



الهيئة العامة للطرق والكباري
الإدارة المركزية (المنطقة المسماة)

مستخلص جاري (١)
عن عملية : إكمال إنشاء تنفيذ أعمال الجسر الترابي والأعمال الصناعية بقطاعات مشروع إنشاء القطر الكهربائي السريع (أكتوبر - أبريل)
لتنفيذ أعمال الجسر الترابي القطاع الثاني (بني مزارع لوط) المسافة من الكم ١٨٠٠٠ إلى الكم ١٨٢٠٠ بطول ٢٠٠ كم اتجاه منطوط (بالأمر المباشر).
تنفيذ شركة أودوك للمقاولات عن المدة من بداية العمل حتى ٢٠٢٤ / ٠٩ / ١٣ بتاريخ : ٢٠٢٣ / ٠٩ / ١٣
العقد رقم : (٢٠٢٤ / ٢٠٢٣ / ٣٧٩)

رقم البند	نوع العمل	الفترة طبقاً للعقد	الوحدة	كمية البند بالعقد	مقدار العمل السابق	مقدار الأعمال التي تمت خلال المدة	جملة مقدار الأعمال	جملة قيمة الأعمال التي تمت	استقطاع او حجز	الباقى بعد الاستقطاع	ملاحظات
		قرش / جنيه			إجراءه	العمل	الأعمال	قرش / جنيه	قرش / جنيه	قرش / جنيه	
١-٣	أعمال تحميل وتوريد ونقل أترية مطابقة للمواصفات وتشغيلها باستخدام آلات التسوية بسمك لا يزيد عن ٥٠ سم حتى مسوب (٢٠ متر) أسفل مسوب الفرمة و بسمك لا يزيد عن ٢٥ سم اعلى من مسوب (٢٠ متر) من مسوب الفرمة لاستكمال المنسوب التصميمي لتشكيل الجسر والأكثاف (نسبة تحمل كاليفورنيا حتى ٢٠%) ورشها بالمياه الأسيوية للوصول إلى نسبة الرطوبة المطلوبة والدمك الجيد بالهراسات للوصول إلى أقصى كثافة جافة (٩٥% من الكثافة الجافة القصوى) ويتم التنفيذ طبقاً للمناسيب التصميمية والقطاعات العرضية النموذجية والرسومات التفصيلية المعتمدة والبند بجميع مشتعلاته طبقاً لأصول الصناعة ومواصفات الهيئة العامة للطرق والكباري وتعليمات المهندسين المشرفين.	٣م		٧٧٠٠٠,٠٠٠	٠,٠٠٠	٣٩٢٧٥,٠٠٠	٣٩٢٧٥,٠٠٠	٢٨١٦٠١٧,٥٠٠	٠,٠٠٠	٢٨١٦٠١٧,٥٠٠	*شهادات تأمين ضد حوادث الطرق طبقاً للمواصفات. *مهندسو المشروع ومدير المشروع متواجدين. *مكاتب جهاز الاشراف والاستشاري متواجدة. *الأجهزة المساهمة متواجدة. *المعدات متواجدة. *البرنامج الزمني الخاص بالعقد. *لوحات المشروع متواجدة. *التقارير (الميداني - الأسبوعي - الشهري) متواجدة. *المستلزمات والمهمات متواجدة. *وسائل تأمين سلامة المرور. *معدات الموقع متواجدة.
٢-٣	السعر في سبتمبر ٢٠٢٣ .	٣م	٧١,٧٠	٧٧٠٠٠,٠٠٠	٠,٠٠٠	٣٩٢٧٥,٠٠٠	٣٩٢٧٥,٠٠٠	٢٨١٦٠١٧,٥٠٠	٠,٠٠٠	٢٨١٦٠١٧,٥٠٠	
٤-٣	علاوة مسافة نقل ٣,٠٠ كم	٣م	١,٥٠	٧٧٠٠٠,٠٠٠	٠,٠٠٠	٣٩٢٧٥,٠٠٠	٣٩٢٧٥,٠٠٠	٢٨١٦٠١٧,٥٠٠	٠,٠٠٠	٢٨١٦٠١٧,٥٠٠	
الإجمالي											
اجمالي قيمة الاعمال المنفذة حتى تاريخ المستخلص											
اجمالي قيمة الاستقطاعات											
اجمالي قيمة الاعمال بعد الاستقطاعات											
ما سبق صرفه											
اجمالي قيمة للمستخلص رقم (١)											

تحريراً في / سنة ٢٠٢٤

سبق صرفها الى

مهندس / احمد عراقي حسين

رئيس الإدارة المركزية للمنطقة المسماة بني سويف

التوقيع

المحاسب

على الحساب

ملاحظة الخاتم

تحريراً في / سنة ٢٠٢٥

المقاول تحريراً في / سنة ٢٠٢٥

بفتح الى المقاول مبلغ

ملاحظة الخاتم

مدير عام المشروعات

م. مصطفى شعبان

م. مهندي

مهندس الاشراف

م. محمود حسين

عن الاستشاري (مستشار)

مدير المشروع

م. محمد عبد الحامد

م. محمد عبد الحامد

مكتب فكري

م. احمد عزب

م. احمد عزب

م. احمد عزب

م. احمد عزب

م. احمد عزب

م. احمد عزب

م. احمد عزب

م. احمد عزب

المقد رقم : () (بتأريخ : / /)		مع شركة		شاملة ضامة
		من بداية العمل حتى		
فرش	جنبة			
		بيان الاصل للتي تمت الاذن		
		محدود		
		مصرح بصرفه		
		سابق صرفه		
		مستحق صرفه		
فرش	جنبة	الاستقطاعات		
		رسم تمهيد اصلي		
		رسم تمهيد اضافي		
		املاك		
		البرادات		
		جملة الاستقطاعات		
		صافي المبلغ المستحق		

قرار كتاب سجل الهجرات والنفقات
المضاء
قرار بان البند المينس مسح بالتصرف
المضاء
اجعلى قيمة المستخلص رقم (١)

علاقات الكتاب الممنوط

1. *Journal of the American Medical Association*, 1997; 278: 1039-1044.

نمبر الفاكس: ٠١١-٤٦٢٣٧٩٨
رقم الهاتف: ٠١١-٤٦٢٣٧٩٨

(٢) مصنف (شبكة) (فنان) (سرف) (رقم)
تکلیف نامتوط

(٤) وترجع في كتاب الميراث رقم ١٤٤٤-٩٦١١-١٢٣٤٤٤-١٠

تمليت النسخة رقم وقررت اني اوافق على هذا الحساب المتقدم به (٩) وقررت اني اوافق على

التمديد سنة + 1

[illegible]

		44-38861-100

[illegible]

قرش	چینه
-----	------

			قعدة للتحويل
--	--	--	--------------

[illegible]

رسم تمغة الترخيص: XXXXXXXXXX

[illegible]

انحرافات

[illegible][illegible]

تحریراتی / سنہ ۲۰		فوجداری			

	جملة قيمة التحصيل
--	-------------------

[illegible]

		المجلس التنفيذي
--	--	-----------------

بقی نس



بخصوص : أعمال الجسر الترابي والأعمال
الصناعية لمشروع القطار الكهربائي السريع (أكتوبر /
أبو سمبل) (القطاع الثاني) في المسافة من كم
١٨٠,٣٥٠ الي كم ١٨٢,٣٥٠ بطول ٢ كم (اتجاه منفلووط)

السيد المهندس / رئيس قطاع التنفيذ والمناطق

تحية طيبة .. وبعد

بالإشارة الي المشروع عاليه تنفيذ شركة اوديك للتوريدات والمقاولات

" عقد رقم ٣٧٩ لسنة ٢٠٢٣/٢٠٢٤

نتشرف بالإحاطة بالاتي :-

- المشروع ليس عليه سيارة محملة
- المشروع ليس عليه عمالة محملة
- لا يوجد بند ائربة في هذا المستخلص تم الحصول عليها طبقا للبرتوكول مع الشركة المصرية
للتعدين

برجاء التكرم بالإحاطة والتفضل بالتوجيه باللازم

وتفضلوا بقبول فائق الاحترام ،،،

تحريرا في : ٢٩ / ١ / ٢٠٢٥

رئيس الإدارة المركزية

المنطقة السادسة (بني سويف)



مهندس

أحمد عراقي حسين

مهندس

مهندس

وزارة النقل
الهيئة العامة للطرق والكباري
المنطقة الأساسية - بنى سويف

السيد المهندس / رئيس قطاع التنفيذ والمناطق

تحية طيبة وبعد،،،

الموضوع بخصوص: أعمال الجسر الترابي والاعمال الصناعية لمشروع القطر الكهربائي السريع
(بنى مزار-منفلوط) القطاع الثاني لتنفيذ المسافة من الكم 180+350 الى 182+350 اتجاه منفلوط

الشركة المنفذة: أوديك للتوريدات والمقاولات .

نتشرف بأن نرفق لسيادتك مستخلص جارى (1).

اتجاه منفلوط عقد رقم (379-2023-2024) .

مرفقات:

- 1- استمارة 50 ع.ح
- 2- محضر استلام الموقع
- 3- اصل مستخلص
- 4- اصل بيان الاعمال
- 5- اصل حصر الاعمال
- 6- صور مكش مسافة النقل

7- اصل البرنامج الزمني

برجاء التكرم بالاحاطة والتنبيه باللازم،،،
وتفضلوا بقبول فائق الاحترام،،،

مدير عام المشروعات بالهيئة
مهندس / مصطفى شعبان البدرى

مستخلص

مهندس الاشراف بالهيئة
مهندس / محمود محمد حسين

مستخلص

بمعد ،،،
رئيس الإدارة المركزية
المنطقة الأساسية بنى سويف
مهندس / احمد عراقي حسين

التوقيع /
أحمد عراقي حسين

[illegible]

وہجہ

كتب المراجعة

رئيس القسم

१५

تفید فی السجل برقم :

(ب) الكاتب المنوط

الاعتماد الإداري ونوع الخصم		نوع الخصم		بيان		المرفقات	
قرش	جنيه	قسم	فرع	نقل	بند	بيان	
٢٨٧٢٩٢٠٠						الصلح الممنون قدره المتخلف رقم (١) عليه أعمال الحرس الزاوي والمحال الصانع للقطر الثاني لخدمة القطر رقم (١) ب السراج الكور والبولي (القطاع الثاني) المأجور رقم ١٨٠٢٥٠ حتر - ١٨٢٢٥ بطول ٢ كم (إليه منطوقه) عقد رقم ٦٧٩ لسنة ٢٠٢٤/١٢/٢٢	
٢٨٧٢٩٢٠٠		إجمالي الأصل					
		قرش	جنيه	بيانات الاستقطاعات			
				عادي	إضافي	دمغة توقيع	
				قرش	جنيه	قرش	
		رسم الدمغة		صافي القيمة المطلوب صرفها			

المختتم ذو التاريخ

→

رئيس المصلحة

سنة الاداء

علامة

الحمد لله رب العالمين في سنة ٢٠٢

(١) إقرار كاتب سجل الحجوزات والتنازلات : _____ الإمضاء : _____
(٢) إقرار بأن القيمة مرتبطة بها على الاعتماد المخصص وأن البند المختص يسمح ولم يسبق الصرف : _____ الإمضاء : _____
(أو) بأن المبلغ مضاف بحساب : _____ بتاريخ _____ الإمضاء : _____

الحتم ذو التاريخ

(ج) قيد في سجل رقم ٥٥ « ع ح » برقم : _____ توقيع الكاتب المنوط بالسجل : _____

(علامات المراجع ورئيس المصلحة)

رو جمع فی ————— سنة ۲۰۲

يعتمد سحب
شيك
إذن صرف

مدير أو رئيس الحسابات

وكيل الحسابات

فی ————— سنہ ۲۰۲۰ بمبلغ

الهيئة العامة للشؤون المطابع الأميرية ٢٠٢٢ - ٢٠٢٣

(١) رقم المسند (وهو رقم القيد في دفتر رقم ٢٢٤ « ج . ع ») ————— إمضاء الكاتب المنوط : —————

(٢) قيد في دفاتر الحسابات المختصة:

(۱)

الحتم ذو التاريخ (٣) سحب

رقم : إضا الكاتب المترو : إضا الكاتب المترو :

(٤) قيد في سجل الشهادات
تحت رقم : إمضاء الكاتب المتروط :

(5) أدرج في كشف الشبهات رقم: امضاء الكاتب المنوط:

(٦) استلمت

شيك

المصارف

امضاء طالب أو كاتب التصدير في _____ سنة ٢٠٢



مذكرة ابضاهيه

المعرض على السيد المهندس / رئيس قطاع التنفيذ والمناطق

المرحوم

بخصوص مشروع أعمال إنشاء الجسر الترابي والاعمال الصناعيه للنطار السريع (أكتوبر - أبو سمبل) القطاع الثاني (بني مزار)
نظرا لما في المسألة من " الكم ١٨٠٠٠٣٥٠ الى الكم ١٨٢٠٠٣٥٠ " بطول ٢ كم (اتجاه - منفلوط) بالأمر المباشر.

- الشركة المنفذة : شركة اوريدك للتوريدات والمقاولات .
- العقد رقم : ٢٠٧٤/٢٠٧٢/٣٧٩ بتاريخ ٢٠٢٣/٩/١٣ .
- تاريخ بدا العمل : ٢٠٢٣/٩/١٦ .
- تاريخ النهي المقرر : ٢٠٢٤/٥/١٥ .
- ايمه العقد الاصلى : ٥٠٧٠٠٠٠٠ (خمسة مليون وسبع مائة ألف جنيها) .

بيرواات المقطعه بتعجيل مقاييسه الاعمال:

- ورد اليه خطاب استشاري القطاع الثاني (مرفق) بخصوص المشروع عليه موضح به اسباب تعديل الكميات المدرجة بالمقاييس المنفذة رقم (١) بالنسبة قيمة امر الاسناد وذلك لوجود تغيير في أسعار البنود المنفذة طبقا لاسعار المقاييسه بتاريخ شهر مارس لسنة ٢٠٢٤ المقاييسه على أسعار البنود (مرفق) المرجوة بالمقاييسه الاصليه وبناءا عليه تم تعديل الكميات المدرجه بالمقاييسه المعدله

البراي

لدى التعطفه الموافقه على تعديل المقاييسه طبقا لالاسعار لما ورد من استشاري المشروع .

برجاء التكرم بالاطم والإحاطه .

والأمر موقوف لمسيرتكم .

وتفضلوا بقبول فائق الاحترام ..

المرحوم

المرحوم
المرحوم

رئيس الإدارة المركزية

المنطقة السادسة (بني سويف)

أحمد محمد حسن

محمود

السيد المهندس / رئيس الاداره المركزيه للمنطقة السادسة ببني سويف

تحية طيبة وبعد ،،،،،

بالاشاره الي مشروع أعمال الجسر الترابي والاعمال الصناعية للخط الثاني لمشروع القطر الكهربائي السريع (6 أكتوبر / أبو سميل) القطاع الثاني (بني مزار / منفلوط) المساقه من كم 180+350 الي كم 182+350 بطول 2 كم (اتجاه منفلوط) عقد رقم (379 / 2023 / 2024) تنفيذ شركة أوديك للمقاولات .

تحيط سيادتكم بأنه :

- تم تعديل اسعار البنود بسبب زيادة أسعار البنود المنفذة طبقا لاسعار المفاوضه بتاريخ شهر مارس لسنة 2024 للمفاوضة علي اسعار البنود الموجودة بالمقايضة الاصلية وبناء عليه تم تعديل الكميات المدرجة بالمقايضة المعدلة .

برجاء التكرم بالإحاطة والتوجيه بما يلزم

وتفضلوا بقبول فائق الاحترام

مكتب الدكتور حسن مهدي

مدير المشروع الاستشاري


م / محمود غريب
مشروع القطار السريع
الخط الثاني من بني مزار / منفلوط

المكتب الفني


م / أحمد عزب



مكتب أ.د. حسن مهدي
للمستشارات الهندسية

مقايضة معدلة رقم (١)



الهيئة العامة للغذاء والدواء
الوطنية

أعمال إنشاء الجسر الترابي للطريق الكهرومائي المربع (أكتوبر / أوسمير)
للقطاع الثاني (بني مزار / منقلاوط) من محطة ١٨٠+٣٥٠ حتى محطة ١٨٢+٣٥٠ اتجاه منقلاوط
تنفيذ شركة / لوديك للتوريدات و المقاولات عقد رقم (٢٠٢٤/٢٠٢٣/٣٧٩)

رقم البند	بيان الأعمال	الوحدة	كمية	سعر الوحدة	الإجمالي
1	أعمال الإنشاء والتكوير				
1-1	بالمتر المسطح أعمال تكوير المواقع من الأشجار والمزروعات والمخلفات في مناطق ذات الطبيعة الزراعية بكثافة يمتد حتى ٣٠ سم و التخلص منها بالمقلب الصومية وذلك لمسافة ٥٠٠ متر . تمهيدا لأعمال الرافع المسامي لكامل حدود المشروع طبقا للشروط والمواصفات وتعليمات المهندس المشرف . - علاوة ٠,٣ جنيه لكل كم زيادة .	م	١,٠٠٠	٨,٣٥	٨,٣٥٠
1-2	بالمتر المسطح أعمال تكوير المواقع من الأشجار والمزروعات والمخلفات والتي يستلزم لها التنفيذ باستخدام (اللودر أو البولدوزر) في مناطق ذات الطبيعة الزراعية بكثافة والبناء بشمل التكوير وإزالة الجذور يمتد لأقل من ٣٠ سم و التخلص منها بالمقلب الصومية وذلك لمسافة ٥٠٠ متر . تمهيدا لأعمال الرافع المسامي لكامل حدود المشروع طبقا للشروط والمواصفات وتعليمات المهندس المشرف . - علاوة ٠,٣ جنيه لكل كم زيادة .	م	١,٠٠٠	١٨,٣٠	١٨,٣٠٠
2	أعمال الحفر				
2-1	بالمتر المكعب أعمال حفر باستخدام المعدات الميكانيكية لجميع أنواع التربة عدا التربة الصخرية وشوية السطح بالآلات التسوية وفرش بالبناء الأسولية للوصول إلى نسبة الرطوبة المطلوبة والتمك الجيد بالهراسات للوصول إلى أقصى كثافة جافة (٩٥% من الكثافة الجافة القصوى) ومحمل على البند تحميل ونقل التربة الزائدة لمسافة ٥٠٠ متر من محور الطريق ويتم التنفيذ طبقا للتسليم التصميمية والقطاعات العرضية النموذجية والرسومات التنفيذية المعتمدة والبناء بجميع مشتاتة طبقا لاصول الصناعة ومواصفات الهيئة العامة للطرق والكبارى وتعليمات المهندس المشرف . - علاوة ١,١ جنيه لكل لمسة نقل لنجح الحفر .	م	١,٠٠٠	٢٩,٢٢	٢٩,٢٢
2-2	بالمتر المكعب أعمال حفر باستخدام المعدات الميكانيكية في التربة المتمسكة عدا التربة الصخرية (باستخدام البولدوزر) وشوية السطح بالآلات التسوية والفرش وشواء الأسولية للوصول إلى نسبة الرطوبة المطلوبة والتمك الجيد بالهراسات للوصول إلى أقصى كثافة جافة (٩٥% من الكثافة الجافة القصوى) ومحمل على البند تحميل ونقل التربة الزائدة لمسافة ٥٠٠ متر من محور الطريق ويتم التنفيذ طبقا للتسليم التصميمية والقطاعات العرضية النموذجية والرسومات التنفيذية المعتمدة والبناء بجميع مشتاتة طبقا لاصول الصناعة ومواصفات الهيئة العامة للطرق والكبارى وتعليمات المهندس المشرف . - علاوة ١,١ جنيه لكل لمسة نقل لنجح الحفر .	م	١,٠٠٠	٣١,٢٠	٣١,٢٠٠
2-3	بالمتر المكعب أعمال حفر بالمعدات الميكانيكية في تربة صخرية ومحمل على البند الاتي ١- تحميل ونقل لنجح الحفر لمسافة لا تقل عن ٥٠٠ متر ٢- إزالة البيوت الجارية باستخدام المعدات الميكانيكية ٣- توريد حربة مطبقة للمواصفات ونشغلها باستخدام آلات التسوية بسك ٧ يزيد عن ٢٥ سم لاستكمال التسوية للتصميمي لتشكيل الجسر والكفاف (نسبة تحمل كالمورنيا حتى ١٠%) ورشها بكمية المياه الأسولية للوصول إلى نسبة الرطوبة المطلوبة والتمك الجيد بالهراسات للوصول إلى أقصى كثافة جافة (٩٥% من الكثافة الجافة القصوى) ويتم التنفيذ طبقا للتسليم التصميمية والقطاعات العرضية النموذجية والرسومات التنفيذية المعتمدة والبناء بجميع مشتاتة طبقا لاصول الصناعة ومواصفات الهيئة العامة للطرق والكبارى وتعليمات المهندس المشرف . - علاوة ١,١ جنيه لكل لمسة نقل لنجح الحفر .	م	١,٠٠٠	٨٠,٢٠	٨٠,٢٠٠
2-4	ذات أجهاد (١٠٠-٢٠٠) حجم/م	م	١,٠٠٠	٨٠,٢٠	٨٠,٢٠٠
2-5	ذات أجهاد (٢٠٠-٣٠٠) حجم/م	م	١,٠٠٠	٩٧,٥٠	٩٧,٥٠٠
2-6	ذات أجهاد (٣٠٠-٤٠٠) حجم/م	م	١,٠٠٠	١١٢,٧٠	١١٢,٧٠٠
2-7	ذات أجهاد (٤٠٠-٥٠٠) حجم/م	م	١,٠٠٠	١٢٩,٦٥	١٢٩,٦٥٠

مدير عام المشروعات
المهندس / مصطفى شحات البدرى
التوقيع /

رئيس الإدارة المركزية للمنطقة الشمالية
(بني مزار)
السيد / محمد أحمد عراقي حسين
التوقيع /

مهندس الهيئة
المهندس / محمود حسين
التوقيع /

الإشراف المشرف
مكتب أ.د. حسن مهدي
مدير المشروع
م / محمود شريف
التوقيع /

مهندس شركة المنطقة
م / أحمد محمد / م / محمد
التوقيع /

مشروع القطار السريع

أ.د. حسن مهدي / السيد / محمد / السيد / محمد / السيد / محمد

محضر استلام موقع

مشروع إنشاء خط القطار الكهربائي السريع (أكتوبر - أوسمبل) من الكم 180+350 حتى الكم 182+350 بطول 2.0 كم تنفيذ شركة أونيك للتوريدات والمقاولات .

أنه في يوم السبت الموافق 2023 / 9 / 16 وبناء على عقد العملية رقم 379 / 2023 / 2024 اتجاه منقوط

اجتمعت اللجنة المشكلة من السادة الاتي اسماءهم بعد وهم :-

عن الهيئة العامة للطرق والكباري (طرف اول)

مهندس الإشراف بالمنطقة السادسة
مدير المشروع الاستشاري (مكتب أ.د/حسن مهدي)
ممثل مكتب الاستشاري مكتب دكتور حسن مهدي
استشاري المساحة (XYZ)

- 1- السيد المهندس / محمود حسين
- 2- السيد المهندس / محمود غريب
- 3- السيد المهندس / احمد عزب
- 4- السيد المهندس / محمد عبدالرحمن سالم

عن الشركة المنفذه (طرف ثاني)

مهندس عن الشركة المنفذه

- 1- السيد المهندس / احمد مرسى ابراهيم ابوريه

وقد قامت اللجنة بالانتقال علي الطبيعة للموقع عالية بالمعاينة الظاهرية علي الطبيعة قام الطرف الاول بتسليم الطرف الثاني الموقع خاليا من العوائق الظاهرية ولا مانع من استلام الموقع والتوقيع في الاعمال ويعتبر تاريخ 2023 / 9 / 16 هو تاريخ استلام الموقع .



وقبل المحضر علي ذلك .

للجنة من الهيئة (طرف اول)

مدير عام المشروعات بالهيئة
مهندس / مصطفى شعبان البدرى

مستفي

بمعد
رئيس الإدارة المركزية
المنطقة السادسة بني سويف
مهندس / احمد عراقي حسين

التوقيع

من المحطة ١٨٠٠٣٢ الى المحطة ١٨٦٠٣٢ الحد
منطوق

الرجوع اسلام الموقع

[illegible][illegible]

	مشروع القطار الكهربائي السريع	 مكتب أ.د. حسن مهدي للاستشارات الهندسية
	إستكمال إستاد أعمال الجسر القرائي والأعمال الصناعية بقطاعات مشروع إنشاء القطار الكهربائي السريع (أكوبر، أبو سمبل)	
	تنفيذ شركة أوديك للمقاولات والتوريدات مستخلص (أ) جاري عن الفترة من سبتمبر ٢٠٢٢ حتى ٢٢ مارس ٢٠٢٤	

بند رقم (١-٣) : أعمال تحميل وتوريد ونقل أثربة مطابقة المواصفات وتشغيلها باستخدام آلات الكسوية بسمك لا يزيد عن ٥٠ سم حتى ملسوب (٢-٠ متر) أسفل ملسوب القرمه و بسمك لا يزيد عن ٢٥ سم اعلي من ملسوب (٢-٠ متر) من ملسوب القرمه الخ

Station	Total FILL Area (m2)	As Built vol FILL	Cum. FILL Vol (m3)		
			LAYER & NO.OF.REQ	QTY (M3)	Total.Qty
180+376	67.09	0.00	FILL LAYER (-1.75)	0.00	43,602.33
180+380	73.57	281.33		281.33	
180+400	72.57	1,461.43		1,742.76	
180+420	74.76	1,473.31		3,216.06	
180+440	70.35	1,451.10		4,667.16	
180+460	64.17	1,345.17		6,012.34	
180+480	70.68	1,348.43		7,360.76	
180+500	76.45	1,471.23		8,831.99	
180+520	79.54	1,559.90		10,391.89	
180+540	85.18	1,647.22		12,039.10	
180+560	114.62	1,997.97		14,037.07	
180+580	116.03	2,306.45		16,343.52	
180+600	112.84	2,289.69		18,632.21	
180+620	113.07	2,259.13		20,891.34	
180+640	118.75	2,318.19		23,209.53	
180+660	116.3	2,350.45		25,559.98	
180+680	124.1	2,403.92		27,963.89	
180+700	116.64	2,407.40		30,371.30	
180+720	111.37	2,280.18		32,651.48	
180+740	96.55	2,079.24		34,730.72	
180+760	88	1,845.50		36,576.21	
180+780	93.66	1,816.59		38,392.80	
180+800	89.69	1,833.53		40,226.33	
180+820	82.79	1,724.79		41,951.12	
180+840	82.33	1,651.18		43,602.30	

عن الاستشاري أ.د حسن مهدي

المكتب الفني م / احمد عزب

التوقيع /

مدير المشروع م / محمود عزب

التوقيع /

مشروع القطار السريع

التوقيع /

م/ محمد عبد الرحمن

التوقيع /

عن الشركة

م/ محمد مرسى / ابراهيم لوريه

التوقيع /



يبدأ رقم (١-٣) : أعمال تحميل وتوريد ونقل أثربة مطابقة للمواصفات وتشغيلها باستخدام آلات التسيبة بسك لا يزيد عن ٥ سم حتى مسلوب (٢- متر) أسفل مسلوب القرمه و بسك لا يزيد عن ٢٥سم اعلى من مسلوب (٢- متر) من مسلوب القرمهالخ

Station	Total FILL Area (m2)	As Built vol FILL	Cum. FILL Vol (m3)		
			LAYER & NO. OF REQ	QTY (M3)	Total Qty
180+860	51.37	1,337.00	FILL LAYER (-3.00)	44,939.31	38,928.75
180+880	89.63	1,409.96		45,349.26	
180+900	102.53	1,921.56		48,270.82	
180+920	98.36	2,008.86		50,279.68	
180+940	110.84	2,091.95		52,371.63	
180+960	101.02	2,118.55		54,490.18	
180+980	117.95	2,189.69		56,679.86	
181+000	130	2,479.49		59,159.35	
181+020	129.54	2,595.39		61,754.74	
181+040	115.93	2,454.75		64,209.48	
181+060	106.76	2,226.95		66,436.43	
181+080	106.21	2,129.74		68,566.17	
181+100	113.33	2,195.39		70,761.56	
181+120	95.74	2,090.65		72,852.22	
181+140	103.02	1,987.63		74,839.85	
181+160	91.82	1,948.44		76,788.29	
181+180	85.19	1,770.13		78,558.41	
181+200	67.25	1,524.40		80,082.82	
181+220	63.06	1,303.07		81,385.89	
181+240	51.45	1,145.15		82,531.04	

عن الاستشاري أ.د حسن مهدي

المكتب الفني م / احمد عزب
مدير المشروع م / محمود كريب



م/محمد عبد الرحمن
م/استشاري (X/2)

عن الشريعة
م/ أحمد فوزي إبراهيم أبو رية
التوقيع / أحمد فوزي

مسرح التفتاز السري

عق استشاري (X/2)
م/محمد عبد الرحمن

عن المراجعة
م/ احمد قريشي / اراهم ابو ريه
التوقيع / المراجعة
٩٠٠-٢٤٩-١٦٢

	مشروع القطار الكهربائي السريع	
	إستكمال إسناد أعمال الجسر الترابي والأعمال الصناعية بقطاعات مشروع إنشاء القطار الكهربائي السريع (أكادير غومسمل)	
	تنفيذ شركة أوديك للمقاولات والتوريدات مستخلص (1) جاري عن الفترة من سبتمبر ٢٠٢٢ حتى ٢٢ مارس ٢٠٢٤	

بند رقم (١-٣) : أعمال تحميل وتقل أترية مطابقة للمواصفات وتشغيلها باستخدام آلات التسوية بسمك لا يزيد عن ٥٠ سم حتى ملسوب (٢-٠ متر) أسفل ملسوب القرمه و بسمك لا يزيد عن ٢٥ سم اعلي من ملسوب (٢-٠ متر) من ملسوب القرمه الخ

Station	Total FILL Area (m2)	As Built vol FILL	Cum. FILL Vol (m3)		
			LAYER & NO.OF.REQ	QTY (M3)	Total.Qty
181+260	84.24	1,356.97	FILL LAYER (-1.75)	83,888.00	9,966.31
181+280	78.61	1,628.58		85,516.58	
181+300	67.44	1,460.59		86,977.17	
181+320	62.91	1,303.59		88,280.77	
181+340	58.35	1,212.67		89,493.43	
181+360	46.21	1,045.67		90,539.10	
181+380	37.57	837.89		91,376.99	
181+400	24.43	620.01		91,997.00	
181+420	25.61	500.34		92,497.34	
181+440	20.58	461.87	FILL LAYER (-2.5)	92,959.21	10,447.11
181+460	41.09	616.70		93,575.91	
181+480	55.52	966.14		94,542.05	
181+500	64.81	1,203.33		95,745.38	
181+520	67	1,318.10		97,063.48	
181+540	81.01	1,480.09		98,543.57	
181+560	102.33	1,833.33		100,376.91	
181+580	154.43	2,567.55		102,944.45	
182+040	78.49	0.00	FILL LAYER (-1.25)	0.00	13,282.60
182+060	81.99	1,604.84		1,604.84	
182+080	85.54	1,675.29		3,280.13	
182+100	81.92	1,674.62		4,954.75	
182+120	82.17	1,640.94		6,595.69	
182+140	86.07	1,682.41		8,278.10	
182+160	77.13	1,632.00		9,910.10	
182+180	61.89	1,390.21		11,300.31	
182+200	42.97	1,048.62		12,348.93	
182+220	21.32	642.88		12,991.81	
182+240	7.76	290.79		13,282.60	

TOTAL FILL VOL

116,227.10

اجمالي كمية خرسانة الميول التي تم خصمها

2,010.20

عن الاستشاري: د. حسن مهدي

الكتب الفني م / احمد عزب

عن استشاري (XYZ)

م / محمد علي احمد

عن الشركة

م / احمد عيسى بن ابراهيم اوريد

مشروع القطار السريع

القطار الكهربائي السريع



عن عملية : تنفيذ الجسر الترابي والأعمال الصناعية بقطاعات مشروع إنشاء القطر الكهربائي
(الكوبر - أسوان)

لتنفيذ أعمال الجسر الترابي لقطاع التلبي (بني مرار - منفلوطة) من الكم ١٨٠٠+٣٥٠ إلى الكم
١٨٢٠+٣٥٠ بطول ٢٠٠ كم

(بالأمر المباشر) تنفيذ : شركة لوبيك للمقاولات



وزارة النقل

الهيئة العامة للطرق والكهوى

المنطقة الأولى المركزية

بيان أعمال عقد رقم (٢٠٢٤/٢٠٢٣/٣٧٩) اتجاه منفلوطة


مستخلص جارى رقم (١) عن الفترة من بداية العمل حتى ٢٠٢٤/٢٠٢٣/٣٧٩

رقم البند	بيان الأعمال	الوحدة	الكمية حسب المقاييس	الكمية للمنقذة فعلياً	الكمية الإجمالية المصروفة سابقاً	الكمية الفعلية الحالية	الكمية المدرجة بالمستخلص
٣	أعمال تحميل وتوريد ونقل أوعية مطبوقة للمواصلات وتشغيلها باستخدام آلات التسوية بسمك لا يزيد عن ٥٠ سم حتى منسوب (٢٠ متر) أسفل منسوب القرمة و بسمك لا يزيد عن ٢٠ سم اعلى من منسوب (٢٠ متر) من منسوب القرمة لاستكمال المنسوب التصميمي لتشكيل الجسر والاكتاف (نسبة تحميل كالفورنيا حتى ٢٠%) ورشها بالمياه الأصوائية للوصول إلى نسبة الرطوبة المطلوبة والتمك الجيد بالهراسات للوصول إلى أقصى كثافة جافة (٩٥% من الكثافة الجافة القصوى) ويتم التنفيذ طبقاً للمناسيب التصميمية والقطاعات العرضية النموذجية والرسومات التفصيلية المعتمدة والبند يجمع محتلاته طبقاً لأصول الصناعة ومواصفات الهيئة العامة للطرق والكهوى وتعليمات المهندس المشرف.	٣م					
١-٢	- في حالة طلب جهاز الإشراف زيادة نسبة الدمك عن ٩٥% بحسب زيادة ١ جنيه على زيادة نسبة الدمك لكل ١% . - مسافة النقل حتى ٢ كم ويتم احتساب علاوة ١.٥ جنيه لكل كم بالزيادة أو النقصان . - السعر يشمل عمل تشوينات و تخليط و اختبارات و نقل لموقع العمل . - و السعر لا يشمل قيمة المادة المحجزة.						
٢-٣	السعر في مشروع علاوة مسافة نقل ١٠ كم						
١-٢							
٣م			٧٧,٠٠٠,٠٠٠	٦٦٦٧٧,٠٠٠	٠	٦٦٦٧٧,٠٠٠	٣٩٢٧٥
٣م			٧٧,٠٠٠,٠٠٠	٦٦٦٧٧,٠٠٠	٠	٦٦٦٧٧,٠٠٠	٣٩٢٧٥

مهندس الإشراف بالهيئة

د. محمود حسن

التوقيع



اعمال الجسر الترابي لمشروع القطار السريع القطاع الثاني (أكتوبر - أسوان) في المسافة من المحطة ١٨٠+٣٥٠ كم الي المحطة ١٨٢+٣٥٠ كم بطول ٢,٠ كم
عقد رقم (٢٠٢٤/٢٠٢٣/٣٧٩) اتجاه (منفلوط)



بيان باجمالي الاعمال التي تمت من بداية العمل حتى تاريخ مستخلص جاري رقم (١)

القطاع	رقم البند بالمقاييس	بيان الاعمال	جاري ١	جاري ٢	جاري ٣	جاري ٤	جاري ٥	جاري ٦	الإجمالي
182+350 - 180+350	٣	اعمال الردم							
	١-٣	اصال تحميل وتوريد ونقل اترية مطابقة للمواصفات وتغليفها باستخدام الات التسوية بسك لا يزيد عن ٥٠ سم حتى منسوب (-٢٠ متر) اسفل منسوب القرمة و بسك لا يزيد عن ٢٥ سم اعلي من منسوب (-٢٠ متر) من منسوب القرمة لاستكمال المنسوب التصميمي لتشكيل الجسر والاكتاف (نسبة تحمل كاليقورنيا حتى ٢٠%) ورشها بالمياه الاصولية للوصول إلى نسبة الرطوبة المطلوبة والدمك الجيد بالهراسات للوصول إلى أقصى كثافة جافة (٩٥% من لكثافة الجافة القصوى) ويتم التنفيذ طبقاً للمناسيب التصميمية والقطاعات العرضية النموذجية والرسومات التفصيلية المعتمدة والبند بجميع مشتملاته طبقاً لأصول الصناعة ومواصفات الهيئة العامة للطرق والكبارى وتعليمات المهندسين المشرفين . - فى حالة طلب جهاز الإشراف زيادة نسبة الدمك عن ٩٥% بحسب زيادة ١ جنيه على زيادة نسبة الدمك لكل ١% . - مسافة النقل حتى ٢ كم و يتم احتساب علاوة ١,٥ جنيه لكل كم بالزيادة او نقصان . - السعر يشمل عمل تشريطات وتخطيط واختبارات ونقل لموقع العمل . - و السعر لا يشمل قيمة المادة المحجيرة .							
	٢-٣	السعر فى سبتمبر ٢٠٢٣ .	٢,٨١٦,٠١٧,٥٠	٠,٠٠	٠,٠٠	٠,٠٠	٠,٠٠	٠,٠٠	٢,٨١٦,٠١٧,٥٠
	٤-٣	علاوة مسافة نقل ٣,٠٠ كم	٥٨,٩١٢,٥٠	٠,٠٠	٠,٠٠	٠,٠٠	٠,٠٠	٠,٠٠	٥٨,٩١٢,٥٠
الاجمالى									
			٢,٨٧٤,٩٣٠,٠٠						

استشارى أ.د حسن مهدى

مهندس الشركة المنفذة

مدير المشروع
م / محمود طوبى

المكتب الفنى
م / احمد عزب

مشروع القطار السريع
القطاع الثاني / منفلوط - أسوان
٢٠٢٣/١٠/٢٠

٢٠٢٣/١٠/٢٠

م / احمد مرسى ابراهيم
مهندس
شركة
الهندسة
والمقاولات
٢٠٢٣/١٠/٢٠



مملكة البحرين
السلطنة

٩٧٥٢٢٨



مختصر معاينة مسافة نال توريد تربة صالحة من معبر بهوار القطاع

مشروع القطر السريع (6 أكتوبر/نوفمبر ٢٠٢١م)

القطاع الملقى بطول 158 كم من 176+700 الى 334+800

تنفيذ شركة : اوديك للمقاولات بطول 2 كم من كم 180+376 الى كم 182+376

بالإشارة الى التكاليف المسددة من الهيئة العامة للطرق والكباري لصالح شركة اوديك للمقاولات بشأن تنفيذ الجسر.

التراخيص والأعمال الصناعية في المسافة الكيلومترية من كم 180+376 الى كم 182+376

بناء على تعليمات السيد المهندس / ربيع قطار التنفيذ والمناطق بالتوريد من معابر خارجية مخصصة بمسافة مؤقتة لمعين اعتماد وترخيص معابر اقرب القطاع

فقد اجتمعت اللجنة يوم الاثنين الموافق 2023 / 12 / 14 وقامت اللجنة المشكلة من:

- | | |
|---------------------------------------|--|
| مهندس الاشراف بالهيئة
مدير المشروع | (1) السيد المهندس / محمود حسين |
| مهندس المكاتب الاستشاري (X, Y, Z) | (2) السيد المهندس / حاتم مبرور |
| مدير مشروع شركة اوديك للمقاولات | (3) السيد المهندس / محمد عبد الرحمن سالم |
| | (4) السيد المهندس / احمد مرسى ابراهيم |

وقامت اللجنة بالذهاب الى مكان المحجر حيث وجد ان المسافة من القطاع (من محطة 180+376 الى 182+376) حتى مكان المحجر (3.00 كم) على ان يتم التوريد بعد عمل اختبارات الصلابة اللازمة و للتأكد من صلاحية المحجر للتوريد.

Station	Latitude (N)	Longitude(E)	Northing	Easting	المنطقة	من
180+376	"N28°31' 15.6	"E30°33' 37.96	3157346.1544	261270.6878	المنطقة	من
182+376	"N28°30' 22.4	"E30°32' 55.79	3155731.5015	260090.4778	المنطقة	من
-	"N28°30'53.77"	"E30°34' 53.69"	3156632.0146	263316.2482	معبر بهوار جامعة الازهر	الى

مما انه يقوم الاستشاري بفصل الكميات المحددة من معبر طارئة مسددة ذلك
المعبر طارئة



استشاري الصلابة (X,Y,Z)





التاريخ : 2025/01/05

اسم المشروع: مشروع القطار الكهربائي السريع قطاع (أكتوبر-أبو سمبل)

الموضوع : اعتماد الهيئة العامة للطرق والكبارى لطلبات امتلاك الاعمال الخاصة بالمشروع

الشركة المنفذة: أودبك للتوريدات و المقاولات في المسافة من 180+350 الى 182+350 بطول 2 كم

عن عقد رقم: (379 / 2023 / 2024) في 13 / 9 / 2023

تم الاطلاع على طلبات الفحص الخاصة بالمشروع المذكور عاليه والمرفقة بمستخلص جارى (1)
لعدد (45) طلب فحص ، وذلك بعد مراجعتها وتوقيعها واعتمادها من استشارى المساحة واستشارى
ضبط الجودة وتنقسم الى:-

عدد (44) طلب فحص لأعمال الرد .

عدد (1) طلب فحص لتسليم AS BUILT .

المهندس / محمود حسين
التوقيع

الإستشاري المشرف
مكتب أ.د حسن مهدي
مدير المشروع

مهندس الشركة المنفذة

م/احمد مرسي

التوقيع / **أوديك**
المندوبين والمقاولات
٧٠٢-٧٥٩-١١١١



مشروع إنشاء القطار الكهربائي (أكتوبر - أسوان)
القطاع الثاني إيني مزار - منفوط من الكم ١٨٠+٢٥٠ الى الكم ١٨٢+٣٥٠ بطول ٢٠٠ كم
تنفيذ : شركة لوديك للتوريدات والمقاولات

مكتب أد/حسن مهدي
للاستشارات الهندسية


الرقم المسلسل	تاريخ الريكويست	تاريخ امضاء المعدل	تاريخ امضاء المساحة	من	الي	الممنسوب	التوصيف	الممنسوب	الطول	السمك
1	01/08/2022	-	01/08/2022	180+300	182+300	-	شبكة ارض تطبيقية	-	2000	-
2	20/11/2022	20/11/2022	-	180+520	181+660	-	محطز احلال	-	1140	-
3	01/01/2023	01/01/2023	-	180+350	180+520	-	محطز احلال	-	170	-
4	01/01/2023	01/01/2023	-	181+920	182+200	-	محطز احلال	-	280	-
5	01/01/2023	01/01/2023	-	182+200	182+300	-	محطز احلال	-	100	-
6	01/01/2023	01/01/2023	-	182+300	182+350	-	محطز احلال	-	50	-
7	04/05/2023	-	04/05/2023	181+760	181+860	-	محطز معاينة لثربة صخرية	-	100	-
8	19/11/2023	19/11/2023	19/11/2023	180+376	181+560	-	محطز معاينة لثربة متماسكة	-	1184	-
9	19/11/2023	19/11/2023	19/11/2023	181+860	182+376	-	محطز معاينة لثربة متماسكة	-	516	-
10	19/12/2023	19/12/2023	19/12/2023	181+560	181+660	-	محطز لثربة سفو	-	100	-
11	25/09/2023	25/09/2023	25/09/2023	182+040	182+376	-	قاع احلال	-	336	-
12	02/10/2023	02/10/2023	02/10/2023	181+260	181+580	-	قاع احلال	-	320	-
13	04/10/2023	04/10/2023	04/10/2023	180+560	180+840	-	قاع احلال	-	280	-
14	11/10/2023	11/10/2023	11/10/2023	180+376	180+560	-	قاع احلال	-	184	-
15-A	01/11/2023	01/11/2023	01/11/2023	180+376	180+560	-	قاع احلال	-	184	-
15	01/11/2023	01/11/2023	01/11/2023	180+840	181+260	-	قاع احلال	-	420	-
16	07/10/2023	09/10/2023	09/10/2023	182+040	182+140	-4.00	استبدال	-4.00	100	متغير
17	15/10/2023	17/10/2023		181+560	181+580	-6.50	استبدال	-6.50	20	متغير
18	16/10/2023	18/10/2023	18/10/2023	182+040	182+160	-3.50	ردم	-3.50	120	0.5
17-A	17/10/2023	19/10/2023	19/10/2023	181+560	181+580	-6.50	استبدال	-6.50	20	متغير
19	21/10/2023	23/10/2023	23/10/2023	180+560	180+720	-5.00	استبدال	-5.00	160	متغير
20	21/10/2023	24/10/2023	24/10/2023	181+560	181+580	-6.00	ردم	-6.00	20	0.3
21	23/10/2023	24/10/2023	24/10/2023	180+720	180+840	-4.50	استبدال	-4.50	120	متغير
22	25/10/2023	25/10/2023	25/10/2023	182+040	182+180	-3.00	ردم	-3.00	140	0.5
23	28/10/2023	29/10/2023	29/10/2023	180+560	180+720	-4.50	ردم	-4.50	160	0.5
24	31/10/2023	31/10/2023	31/10/2023	181+260	181+280	-4.00	استبدال	-4.00	20	متغير
25	31/10/2023	31/10/2023	31/10/2023	180+720	180+840	-4.00	ردم	-4.00	120	0.5
26	02/11/2023	04/11/2023		182+040	182+200	-2.50	ردم	-2.50	160	0.5
26-A	03/11/2023	05/11/2023	06/11/2023	182+040	182+200	-2.50	ردم	-2.50	160	0.5
27	05/11/2023	05/11/2023		181+560	181+580	-5.50	ردم	-5.50	20	0.5
27-A	06/11/2023	08/11/2023	08/11/2023	181+560	181+580	-5.50	ردم	-5.50	20	0.5
28	06/11/2023	08/11/2023		181+260	181+340	-3.50	ردم	-3.50	80	0.5
28-A	08/11/2023	09/11/2023	08/11/2023	181+260	181+340	-3.50	ردم	-3.50	80	0.5
29	13/11/2023	13/11/2023	13/11/2023	180+500	180+720	-4.00	ردم	-4.00	220	0.5
30	14/11/2023	14/11/2023	15/11/2023	180+720	180+840	-3.50	ردم	-3.50	120	0.5

يعتمد
مهندس الهيئة
م/ محمود حسين

عن الاستشاري أد حسن مهدي
مدير المشروع م/ محمود غريب
التوقيع

المكتب الفني
م/ احمد عزب
التوقيع

عن الشركة
م/ احمد مرسي ابراهيم ابوريه
التوقيع





مشروع إنشاء القطار الكهربائي (أكتوبر - أسوان)
القطاع الثاني (بني مزار - منفلوط) من الكم ١٨٠+٣٥٠ إلى الكم ١٨٢+٣٥٠ بطول ٢٠ كم
تنفيذ : شركة أوديك للتوريدات والمقاولات

مكتب أ.د/حسن مهدي
للإستشارات الهندسية


الرقم المسلسل	تاريخ الريكويست	تاريخ امضاء المعمل	تاريخ امضاء المساحة	من	إلى	المسبوب	الوصيف	المسبوب	الطول	السمك
31	16/11/2023	19/11/2023		181+260	181+380	-3.00	ردم	-3.00	120	0.3
32	19/11/2023	20/11/2023	22/11/2023	181+560	181+580	-5.00	ردم	-5.00	20	0.5
33-A	20/11/2023	30/11/2023	22/11/2023	181+280	181+380	-3.00	ردم	-3.00	120	0.5
33	21/11/2023	21/11/2023	22/11/2023	180+380	180+420	-4.00	استبدال	-4.00	40	متغير
34	29/11/2023	30/11/2023	30/11/2023	182+040	182+220	-2.00	ردم	-2.00	180	0.3
35	03/12/2023	04/12/2023	04/12/2023	180+376	180+770	-3.50	ردم	-3.50	344	0.5
36	09/12/2023	09/12/2023		181+280	181+420	-2.50	ردم	-2.50	160	0.5
36-A	09/12/2023	09/12/2023	12/12/2023	181+280	181+420	-2.50	ردم	-2.50	160	0.5
37	09/12/2023	12/12/2023	12/12/2023	180+980	181+040	-6.00	استبدال	-6.00	60	متغير
38	12/12/2023	12/12/2023	12/12/2023	180+720	180+840	-3.00	ردم	-3.00	120	0.5
39	17/12/2023	17/12/2023	19/12/2023	180+880	180+960	-5.50	استبدال	-5.50	80	متغير
40	21/12/2023	21/12/2023	21/12/2023	180+960	181+160	-5.50	ردم	-5.50	200	0.5
41	20/12/2023	20/12/2023	21/12/2023	182+040	182+220	-1.75	ردم	-1.75	180	0.25
42	24/12/2023	27/12/2023	28/12/2023	180+600	180+720	-3.00	ردم	-3.00	120	0.5
43	31/12/2023	31/12/2023	31/12/2023	180+376	180+600	-3.00	ردم	-3.00	224	0.5
44	01/01/2024	02/01/2024		180+880	181+180	-6.00	ردم	-6.00	300	0.5
45	01/01/2024	02/01/2024		182+520	181+580	-4.50	ردم	-4.50	60	0.5
45-A	02/01/2024	04/01/2024	03/01/2024	180+980	181+080	-5.00	ردم	-5.00	300	0.5
45-A	04/01/2024	04/01/2024	04/01/2024	182+520	181+580	-4.50	ردم	-4.50	60	0.5
46	04/01/2024	04/01/2024	04/01/2024	180+700	180+840	-2.50	ردم	-2.50	140	0.5
47	08/01/2024	08/01/2024	08/01/2024	180+580	180+700	-2.50	ردم	-2.50	120	0.5
48	09/01/2024	16/01/2024	-	181+580	181+980	-	AS BUILT	-	400	-
49	23/01/2024	24/01/2024		180+376	180+580	-2.50	ردم	-2.50	204	0.5
49-A	25/01/2024	27/01/2024	26/01/2024	180+376	180+580	-2.50	ردم	-2.50	204	0.5
50	29/01/2024	29/01/2024		180+880	181+000	-4.50	ردم	-4.50	120	0.5
50-A	30/01/2024	30/01/2024		180+880	181+000	-4.50	ردم	-4.50	120	0.5
50-A-A	01/02/2024	07/02/2024	11/02/2024	180+880	181+000	-4.50	ردم	-4.50	120	0.5
51	08/02/2024	08/02/2024	11/02/2024	181+000	181+220	-4.50	ردم	-4.50	220	0.5
52	11/02/2024	11/02/2024		180+540	180+700	-2.00	ردم	-2.00	160	0.5
53	11/02/2024	11/02/2024		181+480	181+580	-4.00	ردم	-4.00	100	0.5
53-A	12/02/2024	12/02/2024	12/02/2024	180+540	180+700	-2.00	ردم	-2.00	160	0.5
54	20/02/2024	21/02/2024	24/02/2024	181+260	181+420	-2.00	ردم	-2.00	160	0.5
54-A	28/02/2024	24/02/2024	24/02/2024	181+480	181+580	-4.00	ردم	-4.00	100	0.5
55	21/02/2024	21/02/2024	24/02/2024	180+376	180+540	-2.00	ردم	-2.00	164	0.5
56	26/02/2024	26/02/2024	27/02/2024	181+000	181+260	-4.00	ردم	-4.00	260	0.5

يعتمد
مهندس الهيئة
م / محمود حسين

عن الاستشاري أ.د حسن مهدي
مدير المشروع م / محمود غريب

المكتب الفني
م / احمد عزب

عن الشركة
م / احمد مرسي ابراهيم ابوريه
التوقيع / احمد مرسي





مشروع إنشاء القطار الكهربائي (أكتوبر - أسوان)
القطاع الثاني (إبلى مزار - منفاوط) من الكم ١٨٠+٣٥٠ إلى الكم ١٨٢+٣٥٠ بطول ٢ كم
تنفيذ : شركة أوديك للتوريدات والمقاولات

مكتب أ.د/حسن مهدي
للإستشارات الهندسية

الرقم المستلم	تاريخ الريكويرست	تاريخ امضاء المعمل	تاريخ امضاء المساحة	من	إلى	المسروب	التوصيف	المسروب	الطول	السمك
57	26/03/2024	27/03/2024		180+840	181+000	-4.00	ردم	-4.00	160	0.5
58	27/02/2024	27/02/2024		182+040	182+240	-3.50	ردم	-3.50	200	0.25
59	27/02/2024	27/02/2024		182+360	182+376	-2.00	استبدال	-2.00	16	متغير
57-A	28/02/2024	03/03/2024		180+840	181+000	-4.00	ردم	-4.00	160	0.5
58-A	04/03/2024	04/03/2024	08/03/2024	182+040	182+240	-3.50	ردم	-3.50	200	0.25
59-A	04/03/2024	04/03/2024	08/03/2024	182+040	182+240	-3.50	استبدال	-3.00	16	متغير
57-ش	08/03/2024	04/03/2024	08/03/2024	180+840	181+000	-4.00	ردم	-4.00	160	0.5
60	05/03/2024	05/03/2024	06/03/2024	181+260	181+420	-1.75	ردم	-1.75	160	0.25
61	05/03/2024	05/03/2024	06/03/2024	181+460	181+580	-3.50	ردم	-3.50	120	0.5
62	05/03/2024	05/03/2024		180+700	180+840	-3.00	ردم	-3.00	140	0.5
62-A	06/03/2024	08/03/2024	08/03/2024	180+700	180+840	-3.00	ردم	-3.00	140	0.5
63	06/03/2024	06/03/2024	06/03/2024	181+100	181+260	-3.50	ردم	-3.50	160	0.5
64	09/03/2024	09/03/2024	09/03/2024	180+840	181+100	-3.50	ردم	-3.50	260	0.5
65	19/03/2024	19/03/2024	20/03/2024	181+440	181+580	-3.00	ردم	-3.00	140	0.5
66	19/03/2024	19/03/2024	20/03/2024	181+100	181+260	-3.00	ردم	-3.00	160	0.5
67	20/03/2024	20/03/2024	20/03/2024	180+700	180+840	-1.75	ردم	-1.75	140	0.25
68	24/03/2024	-	02/04/2024	180+376	182+376	-	AS BUILT	-	2000	-
69	26/03/2024	26/03/2024	27/03/2024	180+376	180+700	-1.75	ردم	-1.75	324	0.25
70	26/03/2024	26/03/2024	27/03/2024	180+840	181+100	-3.00	ردم	-3.00	260	0.5
71	27/03/2024	27/03/2024	28/03/2024	182+040	182+240	-1.25	ردم	-1.25	200	0.25
72	27/03/2024	27/03/2024	28/03/2024	182+360	182+376	-1.75	ردم	-1.75	16	0.25
73	27/03/2024	28/03/2024	28/03/2024	181+420	181+580	-2.50	ردم	-2.50	160	0.5
74	01/04/2024	01/04/2024	02/04/2024	181+100	181+260	-2.50	ردم	-2.50	160	0.5
75	01/04/2024	01/04/2024	02/04/2024	181+260	181+420	-1.50	ردم	-1.50	160	0.25
76	02/04/2024	02/04/2024	02/04/2024	180+840	181+100	-2.50	ردم	-2.50	260	0.5
77	02/04/2024	02/04/2024	02/04/2024	181+420	181+580	-2.00	ردم	-2.00	160	0.5

يعتمد
مهندس الهيئة
م / محمود حسين

مدير المشروع / محمود غريب

من الاستشاري أ.د حسن مهدي
المكتب تقني
م / احمد عزب

عن الشركة
م / احمد مرسى ابراهيم ابوريه
التوقيع /



**RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours**

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أوديك للتوريدات والمقاولات		Designer Company*	DR .Hassan Mahdy (H.M.C)																			
Issued by Contractor	Name	Sign	Date	Time																			
			14/11/2023																				
Received by Employers Representative			<table border="1"> <tr> <td>01</td><td>02</td><td>03</td><td>00</td><td>MM</td><td>YY</td><td>HH</td><td>MM</td> </tr> <tr> <td>KP</td><td>SU</td><td>OT</td><td>14</td><td>11</td><td>23</td><td></td><td></td> </tr> </table>	01	02	03	00	MM	YY	HH	MM	KP	SU	OT	14	11	23						
	01	02	03	00	MM	YY	HH	MM															
KP	SU	OT	14	11	23																		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5																			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	180+720 TO 180+840	تصميم طبقة ردم على منصوب (3.5-)
	E=261067.6917	
	N=3157068.4342	
	E=260996.879	
	N=3156971.555	

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as Indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: GARB SURVEY CONSULTANT (xyz)	Comments by: General consultant (systra)
	- No objection according to the attached reports and Lab. results. - This work was inspected and checked only by xyz and H.M.C. consultant. - you must follow specs and leveling side slope.

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not attend
Contractor Engineer	أحمد	أحمد			A-AWC-R	
Contractor QA/QC*	XYZ	أحمد	15-11-2023	2:45	(A)	
	H.M.C	أحمد	14/11/2023	18:00	A	
GARB**						
Employers Representative	كhaled ali	كhaled ali	5/8/2024		AWC	

* Designer

** Alignment: Bridges: Culvert Only

UNIVERSAL INSPECTION REQUEST



مكتب أمان مهدي
للإستشارات الهندسية



الهيئة العامة للغذاء والدواء



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be completed and ready for inspection at planned time shown

Contractor Company	شركة أ.ه. د.ك. للتوريدات والمقاولات		Designer Company*	DR. Hassan Mahdy (H.M.C)
Issued by Contractor	Name م. / احمد مرسي	Sign [Signature]	Date	Time
Received by Employers Representative	31-A		20/11/2023	

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
180+376 to 182+376	181+260 TO 181+380	تسليم طبقة ردم علي منسوب (3.00-)
	E=260749.0349 N=3156632.4779	E=260678.2222 N=3156535.5988

INSPECTION DETAILS The following will be ready at the Planned Inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate			
Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (XYZ))	Comments by: General consultant (systra)
[Signature]	-No objection, according to the attached reports and Lab. results -This work was inspected and checked only by XYZ and H.M.C. consultants -you must follow specs and landing side logs

INSPECTION RESULT						
Organisation	Name	Sign	Date	Time	Approval Status	Please Mark if Not Attend
Contractor Engineer	[Signature]				A-AWC-R	
Contractor	XYZ	[Signature]	22-11-2023	1:00	(A)	
QA/QC*	H.M.C	[Signature]	20-11-2023	10:00	A	
GARB**						
Employers Representative	Khaleel Ali	[Signature]	5/8/2024		AWC	

* Designer

** Alignment: Bridges/Culvert Only



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة اوريدات والمقاولات		Designer Company*	DR. Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	التوريدات والمقاولات	Date	16/11/2023							
Received by Employers Representative		31	UIR	C1	C2	C3	DO	MM	YY	HH	MM
				RP	SU	OT	16	11	23		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+375 to 182+376	181+260 TO 181+380	تسليم طبقة ردم على منسوب (3.00-)
	E=260749.0349 N=3156632.4779	E=260678.2222 N=3156535.5988

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. (xyz))	Comments by: General consultant (systra)

INSPECTION RESULT						Approval Status	Please tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer							
Contractor	XYZ						
QA/QC*	H.M.C			9-11-2023	12:15	R	
GARB**							
Employers Representative							

* Designer

** Alignment: Bridges: Culvert Only

UNIVERSAL INSPECTION REQUEST



مكتب أنوار منير
للإستشارات الهندسية



مكتب الإستشارات العامة



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أوديك للتعويضات والتأمينات		Designer Company	DR .Hassan Mahdy (H.M.C)											
Issued by Contractor	Name: التوريد المفاولاني		Date	19/11/2023											
Received by Employers Representative	32		UIR	<table border="1"> <tr> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>19</td> <td>11</td> <td>23</td> <td></td> <td></td> </tr> </table>		DD	MM	YY	HH	MM	19	11	23		
DD	MM	YY	HH	MM											
19	11	23													
CODE-1		CODE-2	CODE-3	CODE-4	CODE-5										

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	181+560 TO 181+580	تسليم طبقة ردم على منسوب (5.0-)
	E=260572.0033	
	N=3156390.28	
	E=260560.2012	
	N=3156374.1335	

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB Surveyor: HANAN XYZ)

Comments by: General consultant (systra)

No objection, according to the attached reports and Lab. verifications. This work was inspected and checked only by XYZ and H.M.C. consultant.

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	أحمد				A-AWC-R	
Contractor QA/QC*	XYZ		22-11-2023	1:20	(A)	
	H.M.C		29-11-2023	11:45	A	
GARB**						
Employers Representative	Chaled di		5/8/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أ.د/حسن مهدي
للمشاورات الهندسية



الهيئة العامة للإستشارة



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	 Name: <u>أحمد مرمي</u> Sign: <u>أحمد مرمي</u>		Designer Company*	DR .Hassan Mahdy (H.M.C)	
Issued by Contractor	Date: <u>29/11/2023</u>		Time		
Received by Employers Representative	34		UIR	C1 AP	C2 SU
				C3 OT	DD 29
				MM 11	YY 23
				HH 	MM
CODE -1	CODE -2	CODE -3	CODE -4	CODE -5	

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	182+040 TO 182+220	تسليم طبقة ردم علي منسوب (2.0-)
	E=260288.7528 N=3156002.7634	E=260182.5339 N=3155857.4446

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time



Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

 -No objection, according to the attached reports and Lab. results -This work was inspected and checked only by xyz and H.M.C. on 30/11/2023 -you must follow specs and leveling side slope	 2
---	--

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	أحمد مرمي					
Contractor QA/QC*	XYZ عبد الرحمن الفاروق		30-11-2023	12.130	A	
	H.M.C		30-11-2023	11.30	AWC	
GARB**						
Employers Representative	Khaled Ali		5/12/2023		AWC	

Page 1 of 1

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
الهندسة المدنية



الهيئة العامة للمواصلات



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أوديسا للتوريدات والمقاولات		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	Time							
	من (أدريس مهدي) مهندس مدني ١٢٧-٢٩٩٠		09/12/2023								
Received by Employers Representative		36	UIR	C1	C2	C3	DD	MM	YY	HH	MM
				JP	SU	OT	DB	12	23		
CODE -1		CODE -2		CODE -3		CODE -4		CODE -5			

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
180+375 to 182+375	181+250 TO 181+420	
	E=260749.0349	E=260654.618
	N=3156632.4779	N=3156503.3057
		تسليم طبقة ردم علي منسوب (2.50-)

INSPECTION DETAILS The Following will be ready at the Planned inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate			
Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.{ xyz})	Comments by: General consultant (systra)

INSPECTION RESULT						Approval Status	Release Tick
Organisation	Name	Sign	Date	Time	A-AWC-R		Not Atteny
Contractor Engineer							
Contractor QA/QC*	XYZ						
	H.M.C		9/12/2023	11:15 pm	R		
GARB**							
Employers Representative							

* Designer

** Alignment: Bridges: Culvert Only

UNIVERSAL INSPECTION REQUEST



مكتب أمين مهدي
للإستشارات الهندسية



مكتب أمين مهدي
للإستشارات الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة التوريات والبنادق		Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name: <u>م. أحمد علي</u>	Sign: <u>م. أحمد علي</u>	Date	Time
Received by Employers Representative	37		09/12/2023	
CODE-1		CODE-2	CODE-3	CODE-4
CODE-5		CODE-6	CODE-7	CODE-8

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	180+980 TO 181+040	تسليم طبقة راح علي منسوب (6.00-)
	E=260914.2643 N=3156858.5293	
	E=260878.858 N=3156810.0897	

INSPECTION DETAILS The following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included in appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. (xyz))

Comments by: General consultant (systra)



- you must follow spec and design drawg.
- you must do leveling and cinning
side slope of filling

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick
Contractor Engineer	أحمد علي	أحمد علي			A-AWC-R	Not Attended
Contractor QA/QC*	XYZ	أحمد علي	12-12-2023	12:30	(A)	
GARB**	H.M.C	أحمد علي	12-12-2023	11:00	AWC	
Employers Representative	Khaled Ali	أحمد علي	12/12/2023			

UNIVERSAL INSPECTION REQUEST



مكتب أ.إ.م.ه.م.ه.
للإشراف الهندسية



المكتب الهندسي



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	لوديك للمقاولات والمقاولات		Designer Company*	DR. Hassan Mahdy (H.M.C)	
Issued by Contractor	Name:	Sign:	Date	12/19/2023	
Received by Employers Representative		38	UIR		
CODE -1		CODE -2	CODE -3	CODE -4	CODE -5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	180+770 TO 180+840 E=261067.6917 N=3157068.4342	تسليم طبقة ردم على منسوب (3.00-) E=260996.879 N=3156971.555

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	M5 Reference	

Comments by: (GARBS SURVEY CONSATANT. (xyz))

Comments by: General consultant (sysstra)



- You must follow specs and design line
- You must do leveling and signing side slope of filling layer

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer					A-AWC-R	
Contractor QA/QC*	XYZ		12-12-2023	1:15	(A)	
	H.M.C		12-12-2023	11:45	A	
GARB**						
Employers Representative	Khaled Ali		12/12/2023		ANC	


* Designer

** Alignment: Bridges Culvert Only

UNIVERSAL INSPECTION REQUEST



مكتب أ.إ.ص.م.ه.
للإستشارات الهندسية



شركة أ.إ.ص.م.ه.



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أوديك للتوريدات والمقاولات	Designer Company*	DR. Hassan Mahdy (H.M.C)						
Issued by Contractor	Name: <u>أ.إ.ص.م.ه.</u> Sign: <u>[Signature]</u>	Date	Time						
Received by Employers Representative	39	13/12/2023	2:30						
UIR		C1	C2	C3	DD	MM	YY	HH	MM
		XP	BU	OT	17	12	23	2	30
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	180+880 TO 180+960 E=260973.2748 N=3156939.2619	تسليم طبقة ردم على متسوب (5.5-)
	E=260926.0664 N=3156874.6758	

INSPECTION DETAILS The following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)



- you must follow specs and design drawings
- you must do leveling side slope of filling layer

INSPECTION RESULT						Approval Status	Please Tick if Not Applicable
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	أ.إ.ص.م.ه.	أ.إ.ص.م.ه.					
Contractor	XYZ	أ.إ.ص.م.ه.	19/12/2023	2:30	A		
QA/QC*	H.M.C	أ.إ.ص.م.ه.	17/12/2023	2:30	A		
GARB**							
Employers Representative	Khaled Ali		19/12/2023		AWC		

أ.إ.ص.م.ه.
استشاري الجسر
القنفذ الأول

UNIVERSAL INSPECTION REQUEST



مكتب أراضين مهدي
للإشراف الهندسية



المملكة العربية السعودية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company			Designer Company*	DR. Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	Time							
	20/12/2023	12:30									
Received by Employers Representative		40	UIR								
				C1	C2	C3	DD	MM	YY	HH	MM
				10P	00	01	20	12	23	12	30
	CODE -1	CODE -3	CODE -3	CODE -4	CODE -5						

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	180+960 TO 181+160	تسليم طبقة ردم علي مملوب (5.5-)
	E=260926.0664 N=3156874.6758	E=260808.0454 N=3156713.2106

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time


Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	




Comments by: (GARB SURVEY CONSULTANT (xyz))

Comments by: General consultant (sysra)

	<p>-you must follow spec and design dir.</p> <p>-you must do leveling and dumping.</p> <p>side slope of Piking</p>
---	--

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer					A-AWC-R	
Contractor QA/QC*	XYZ		21-12-2023	11:30	A	
	H.M.C		21/12/2023	12:30	A	
GARB**						
Employers Representative	Khaled al		21/12/2023		B NC	

UNIVERSAL INSPECTION REQUEST		مكتب أمان من للإستشارات الهندسية		الهيئة العامة للغذاء والدواء SAGRA	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours The Work described below will be complete and ready for inspection at planned time shown													
Contractor Company	شركة التورين والمواد				Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name: <u>م. احمد مكي</u> Sign: <u>م. احمد مكي</u>				Date	20/12/2023							
Received by Employers Representative	41				UIR	C1	C2	C3	DD	MM	YY	HH	MM
						KF	UU	OT	20	12	23	2	00
CODE -1		CODE -2		CODE -3		CODE -4		CODE -5					

EXPLANATION OF WORK TO BE INSPECTED			
Area	Element	Item	
180+376 to 182+376	182+040 TO 182+220	تسليم طبقة ردم على منصوب (1.75-)	
	E=260288.7528		E=260182.5339
	N=3156002.7634		N=3155857.4446

INSPECTION DETAILS The following will be ready at the Planned inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE must be included as appropriate			
Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT) <u>م. احمد مكي</u>	Comments by: General consultant (systra) <u>- you must follow specs and design d.no</u> <u>- you must do leveling and lining side slope of filling layer</u>
--	---

INSPECTION RESULT						Approval Status	Please Tick if Not attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	<u>م. احمد مكي</u>	<u>م. احمد مكي</u>					
Contractor	XYZ	<u>م. احمد مكي</u>	20-12-2023	10:00	A		
QA/QC*	H.M.C	<u>م. احمد مكي</u>	20/12/2023	2:00	Aux		
GARB**							
Employers Representative	<u>Kh. Al. Al. Al.</u>	<u>م. احمد مكي</u>	21/12/2023				

UNIVERSAL INSPECTION REQUEST		مكتب أدريس مهدي للإستشارات الهندسية		الهيئة العامة للإستشارات والبحوث	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours							
The Work described below will be complete and ready for inspection at planned time shown.							
Contractor Company	أوديك للتوريدات والمقاولات			Designer Company*	DR .Hassan Mahdy (H.M.C)		
Issued by Contractor	Name	م.م. هادي	Sign	Date	Time		
	2023-12-24			24/12/2023			
Received by Employers Representative	42		UIR	CT	CC	CC	DD
				JP	BU	OT	24
		WM	YY	HH	MM		
CODE-1		CODE-2		CODE-3		CODE-4	

EXPLANATION OF WORK TO BE INSPECTED			
Area	Element	Item	
180+376 to 182+376	180+500 TO 180+720	تسليم طبقة ردم على منسوب (3.00-)	
	E=261138.5043		E=261067.6917
	N=3157165.3133		N=3157068.4342

INSPECTION DETAILS The following will be ready at the Planned inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate			
Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
تم استلام المخطط والمقاولات	-No objection, according to the attached reports and Lab. results.
	-This work was inspected and checked only by xyz and H.M.C consultants.

INSPECTION RESULT						Approval status	Please Tick If Not Attend
Organisation	Name	Sign	Date	Time			
Contractor Engineer	أحمد مرسي	أحمد مرسي					
Contractor QA/QC*	XYZ	محمد مرسي	28-12-2023	3:00	A		
	H.M.C	محمد مرسي	27-12-2023	2:30	A.W.C		
GARB**							
Employers Representative	Khaleel ali		5/8/2024		A.W.C		



UNIVERSAL INSPECTION REQUEST



مكتب أ.د/حسن مهدي
للإشراف الهندسية



الهيئة العامة للغذاء والدواء



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company			Designer Company*	DR. Hassan Mahdy (H.M.C)																
Issued by Contractor	Name أحمد مرسى	Sign 	Date 03/01/2024	Time																
Received by Employers Representative	44-A		UIR	<table border="1"> <tr> <td>01</td> <td>02</td> <td>03</td> <td>00</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>KU</td> <td>OT</td> <td>03</td> <td>01</td> <td>24</td> <td></td> <td></td> </tr> </table>	01	02	03	00	MM	YY	HH	MM	KP	KU	OT	03	01	24		
01	02	03	00	MM	YY	HH	MM													
KP	KU	OT	03	01	24															
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	180+880 TO 181+180 E=260973.2748 E=260796.2433 N=3156939.2619 N=3156697.064	تسليم طبقة ريم على منسوب (5.00-)

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate:

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)



- No objection, according to the attached reports and Lab. results.
- This work was inspected and checked only by xyz and H.M.C.
- you must follow specs

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attended
Contractor Engineer	أحمد مرسى				A-AWC-R	
Contractor QA/QC*	XYZ H.M.C		3-1-2024	16:00	A	
GARB**			3-1-2024	12:30	A	
Employers Representative	Khaled ali		12/8/2024		AWC	



UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
الإشراف الهندسية



المكتب الهندسي للمواصلات العامة



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة التكوينات والمقاولات		Designer Company*	DR ,Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	Time							
	أحمد مرسى	أحمد مرسى	01/01/2024								
Received by Employers Representative		44	UIR	C1	C2	C3	DD	MM	YY	HH	MM
				HP	EU	OT	01	01	24		
CODE -1		CODE -2		CODE -3		CODE -4		CODE -5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	180+880 TO 181+180	تسليم طبقة ردم علي منسوب (5.00-)
	E=260973.2748 N=3156939.2619	E=260796.2433 N=3156697.064

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as Indicated <input type="checkbox"/>
Drawing Reference:	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (sysra)

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	أحمد مرسى	أحمد مرسى				
Contractor QA/QC*	XYZ H.M.C	أحمد مرسى	2/1/2023	11:00	R	
GARB**						
Employers Representative						



UNIVERSAL INSPECTION REQUEST

مكتب ابحاث
الهندسة



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours																							
The Work described below will be completed and ready for inspection at planned time shown																							
Contractor Company	أوتوك للتوريدات والمقاولات			Designer Company*	DR. Hassan Mahdy [H.M.C]																		
Issued by Contractor	Name: 04-117: س.ب.س 888450			Date	04/01/2024																		
Received by Employers Representative	45			UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>04</td> <td>01</td> <td>24</td> <td></td> <td></td> </tr> </table>			C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	04	01	24		
C1	C2	C3	DD	MM	YY	HH	MM																
KP	SU	OT	04	01	24																		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5																			

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
180+376 to 182+376	180+700 TO 180+840	منحرف طرقة رقم على متسوب (2.50-)
	E=261079.4938 N=3157084.5807	

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate			
Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (syatra)
	- No objection, according to the attached reports and lab. results. - This work was inspected and checked only by xyz and H.M.C. - you must follow these and leveling side slopes

INSPECTION RESULT						
Organisation	Name	Sign	Date	Time	Approval A-AWC-R	Please Tick if Not Attend
Contractor Engineer						
Contractor XYZ			4-1-2024	11:30	(A)	
QA/QC* H.M.C			4-1-2024	11:00	Ave	
GARB**						
Employers Representative	Khaled ali		12/8/2024		AWC	



UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للمستشارات الهندسية



المكتب الوطني للمطارات



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company			Designer Company*	DR. Hassan Mahdy (H.M.C)	
Issued by Contractor	Name	Sign	Date	Time	
	م. احمد عرسى	أحمد عرسى	08/01/2024		
Received by Employers Representative	47	UIR	01	02	03
			DD	MM	YY
			08	01	24
			HH	MM	

CODE -1	CODE -2	CODE -3	CODE -4	CODE -5
---------	---------	---------	---------	---------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	180+580 TO 180+700	تسليم طبقة ردم علي منسوب (2.50-)
	E=261150.3064 N=3157181.4598	E=261079.4938 N=3157084.5807

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT. (xyz))

Comments by: General consultant (systra)

تم استلام المراسلة من قبل المهندس أحمد عرسى
- No objection, according to the attached reports and Lab. results.
- This work was inspected and checked only by xyz and H.M.C.
- you must follow the approval status

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval status	Please Tick if Not Attend
Contractor Engineer	أحمد عرسى	أحمد عرسى	8-1-2024	2:30	A	
Contractor QA/QC*	XYZ	أحمد عرسى	8-1-2024	1:15	AWC	
GARB**						
Employers Representative	Khaled Ali	أحمد عرسى	8/1/2024		AWC	

UNIVERSAL INSPECTION REQUEST		مكتب أ.إ.م.م للإشراف الهندسية		الهيئة العامة للغذاء والدواء Ministry of Health	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours The Work described below will be complete and ready for inspection at planned time shown																					
Contractor Company	<div style="border: 2px solid blue; padding: 5px; display: inline-block;"> شركة للتوريدات والمقاولات للتوريدات والمقاولات ٧٠٣ - ١٠٠٠ أحمد داري </div>			Designer Company*	DR. Hassan Mahdy (H.M.C)																
Issued by Contractor	Name	Signature	Date	Time																	
			09/01/2024																		
Received by Employers Representative		48	UIR	<table border="1"> <tr> <td>11</td><td>09</td><td>09</td><td>00</td><td>MM</td><td>YY</td><td>HH</td><td>MM</td> </tr> <tr> <td>AP</td><td>BU</td><td>OT</td><td>VB</td><td>CT</td><td>24</td><td></td><td></td> </tr> </table>	11	09	09	00	MM	YY	HH	MM	AP	BU	OT	VB	CT	24			
11	09	09	00	MM	YY	HH	MM														
AP	BU	OT	VB	CT	24																
CODE -1	CODE -2	CODE -3	CODE -4	CODE -5																	

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
180+376 to 182+376	181+580 TO 181+980 E=260560.2012 N=3156374.1335	من تسليم رفع شبكية المخططات الموضحة E=260324.1591 N=3156051.2029

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate			
Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	


Comments by: (GARB SURVEY CONSATANT. (xyz))	Comments by: General consultant (systra)
<div style="border: 2px solid blue; padding: 5px; display: inline-block;"> استأجر استأجر استأجر </div>	

INSPECTION RESULT					Approval / Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time		
Contractor Engineer	أحمد داري	أحمد داري	16-1-2024	11:00	A	
Contractor QA/QC*	H.M.C	محمود رستم	16-1-2024	11:00	A	
GARB**						
Employers Representative						

UNIVERSAL INSPECTION REQUEST



مكتب أمان مهنى
للإشراف الهندسية



المكتب الهندسى للمياه



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company			Designer Company*	DR. Hassan Mahdy (H.M.C)																	
Issued by Contractor	Name م / احمد مرسي	Sign 	Date	25/01/2024																	
Received by Employers Representative			UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>CD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>AP</td> <td>SU</td> <td>OT</td> <td>25</td> <td>01</td> <td>24</td> <td></td> <td></td> </tr> </table>		C1	C2	C3	CD	MM	YY	HH	MM	AP	SU	OT	25	01	24		
C1	C2	C3	CD	MM	YY	HH	MM														
AP	SU	OT	25	01	24																
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5																	

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	180+376 TO 180+580	تسليم طبقة ردم علي منسوب (2.50-)
	E=261270.6878	
	N=3157346.1544	
	E=261150.3064	
	N=3157181.4598	

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

	<p>- No objection, according to the attached reports and lab. results.</p> <p>- This work was inspected and checked only by IGT and H.M.C.</p> <p>- you must follow specs and leveling side slope</p>
---	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	أحمد مرسي					
Contractor QA/QC*	XYZ		28-1-2024	11:00	(A)	
	H.M.C		27-1-2024	12:30	AWC	
GARB**						
Employers Representative	Khaleed ali		12/8/2024			



UNIVERSAL INSPECTION REQUEST



مكتب أديس مهدي
للإستشارات الهندسية



المكتب الفني للمشروعات



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة أديس مهدي للتوريدات والمقاولات		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name م/ احمد مرسي	Sign [Signature]	Date 28/01/2024 24/1/2024	Time							
Received by Employers Representative	49		UIR	C1 KP	C2 SU	C3 OT	DD 23	MM 01	YY 24	HH	MM
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	180+376 TO 180+580 E=261270.6878 E=261150.3064 N=3157346.1544 N=3157181.4598	تسليم طبقة ردم على منسوب (2.50-)

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz)	Comments by: General consultant (systra)

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	أحمد مرسي	[Signature]				
Contractor QA/QC*	XYZ H.M.C	أحمد مرسي	24/1/24	18:15		
GARB**						
Employers Representative						



UNIVERSAL INSPECTION REQUEST



مكتب أ.إ.إ. من مهن
للإستشارات الهندسية



الهيئة العامة للغذاء والدواء



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أوديك للتوريدات والمقاولات شركة أوديك		Designer Company*	DR. Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	Time							
	التوريدات والمقاولات		28/01/2024	7/2/2024							
Received by Employers Representative	50-A-A		UIR	C1	C2	C3	DD	MM	YY	HH	MM
				10	30	07	06	02	24		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	180+880 TO 181+000	تسليم طبقة ردم على منسوب (4.50-)
	E=260973.2748 N=3156939.2619	E=260902.4622 N=3156842.3828

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. (xyz))	Comments by: General consultant (systra)
تم استلام العمل من قبل الشركة	- No objection, according to the attached reports and lab. results
	- This work was inspected and checked only by xyz and H.M.C.
	- you must follow specs and leveling side slope

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	— زكريا	— زكريا					
Contractor QA/QC*	XYZ H.M.C	— أحمد	11-2-2024	11/00	A		
GARB**			7/2/24	5:00			
Employers Representative	Khaled	—	12/8/2024		AWC		



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company			Designer Company*	DR .Hassan Mahdy (H.M.C)																	
Issued by Contractor	Name: ٧٥٩-١٦٧	Sign: 	Date	29/01/2024																	
Received by Employers Representative	50-A		UIR	<table border="1"> <tr> <td>C1</td><td>C2</td><td>C3</td><td>CD</td><td>MM</td><td>YY</td><td>HH</td><td>MM</td> </tr> <tr> <td>KP</td><td>SU</td><td>OT</td><td>29</td><td>01</td><td>24</td><td></td><td></td> </tr> </table>		C1	C2	C3	CD	MM	YY	HH	MM	KP	SU	OT	29	01	24		
C1	C2	C3	CD	MM	YY	HH	MM														
KP	SU	OT	29	01	24																
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5																	

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
180+376 to 182+376	180+880 TO 181+000		تسليم طبقة ردم علي متمويب (4.50-)
	E=260973.2748	E=260902.4622	
	N=3156939.2619	N=3156842.3828	

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						تحقق
Contractor QA/QC*	XYZ					نسبة العمل
	H.M.C		29/1/24	2800	R	طوبى
GARB**						التفتيش
Employers Representative						المختار الكندياني السري





RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown:

Contractor Company	شركة اوريدك للتوريدات والمقاولات		Designer Company*	DR. Hassan Mahdy (H.M.C)	
Issued by Contractor	Name م. احمد مرسي	Sign [Signature]	Date	29/01/2024	
Received by Employers Representative		50	UIR		
CODE#1		CODE#2	CODE#3	CODE#4	CODE#5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	180+880 TO 181+000 E=260973.2748 N=3156939.2619	تمليم طبقة ردم على منسوب (4.50-) E=260902.4622 N=3156842.3828

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))

Comments by: General consultant (sysra)

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	زكريا مرسي	[Signature]				
Contractor QA/QC*	XYZ H.M.C	احمد مرسي	30/1/24	2315	R	
GARB**						
Employers Representative						



UNIVERSAL INSPECTION REQUEST



مكتب الدراسات
للبنية التحتية



المكتب الفني للمواصلات



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة أوديك للتوريدات والمقاولات		Designer Company*	DR. Hassan Mahdy (H.M.C)																	
Issued by Contractor	Name: <u>أحمد محمد</u>	Sign: <u>[Signature]</u>	Date	08/02/2024																	
Received by Employers Representative		51	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>08</td> <td>02</td> <td>02</td> <td>08</td> <td>02</td> <td>24</td> <td></td> <td></td> </tr> </table>		C1	C2	C3	DD	MM	YY	HH	MM	08	02	02	08	02	24		
C1	C2	C3	DD	MM	YY	HH	MM														
08	02	02	08	02	24																
CODE -1	CODE -2	CODE -3	CODE -4	CODE -5																	

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	181+000 TO 181+220	تسليم طبقة ردم على منسوب (4.50-)
	E=260902.4622	
	N=3156842.3828	
	E=260772.6391	
	N=3156664.771	

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT. (xyz))	Comments by: General consultant (systra)
	<p>- No objection, according to the attached reports and lab. results.</p> <p>- This work was inspected and checked only by xyz and H.M.C.</p> <p>- you must of submitted the following envelope side by side</p>

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Status	Approved	Please Tick if Not Attend
Contractor Engineer	أحمد محمد	أحمد محمد	16/2/2024	10:30	A		
Contractor QA/QC*	XYZ H.M.C	أحمد محمد	16/2/24	11:30	AWC		
GARB**							
Employers Representative	Khaleel	Khaleel	16/2/2024		AWC		

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



المملكة العربية السعودية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة أدريس مهدي للتوريدات والمقاولات		Designer Company*	DR .Hassan Mahdy (H.M.C)																	
Issued by Contractor	Name م. أحمد مرسي	Sign [Signature]	Date	12/02/2024																	
Received by Employers Representative	52-A		UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>AP</td> <td>BU</td> <td>OT</td> <td>12</td> <td>02</td> <td>24</td> <td></td> <td></td> </tr> </table>		C1	C2	C3	DD	MM	YY	HH	MM	AP	BU	OT	12	02	24		
C1	C2	C3	DD	MM	YY	HH	MM														
AP	BU	OT	12	02	24																
CODE -1	CODE -2	CODE -3	CODE -4	CODE -5																	

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
180+375 to 182+376	180+540 TO 180+700		تسليم طبقة ردم علي منسوب (2.00-)
	E=261173.9106	E=261079.4938	
	N=3157213.7529	N=3157084.5807	

INSPECTION DETAILS The following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: GARB SURVEY CONSULTANT (XYZ)	Comments by: General consultant (systra)
	<p>- No objection, according to the attached reports and Lab. results.</p> <p>- This work was inspected and checked only by XYZ and H.M.C.</p> <p>- you must follow specs and leveling side slope</p>

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	زاهد مرسي	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	[Signature]	12/2/2024	2130	A	
	H.M.C	[Signature]	12/2/24	2300	A	
GARB**						
Employers Representative	Khaled Ali	[Signature]	12/8/2024			



UNIVERSAL INSPECTION REQUEST



مكتب أ.إ.ص.م.ه.د
الإشراف الهندسي



المكتب الهندسي



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	لويس للتوريدات والمقاولات		Designer Company*	DR. Hassan Mahdy (H.M.C)
Issued by Contractor	Name: م. احمد مرسي	Sign: [Signature]	Date	Time
Received by Employers Representative	52		11/02/2024	
		UIR	C1 KP	C2 SU
			C3 OT	DD 11
			MM 02	YY 24
			HH	MM
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	180+540 TO 180+700 E=261173.9106 N=3157213.7529	تسليم طبقة ردم علي منسوب (2.00-) E=261079.4938 N=3157084.5807

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

INSPECTION RESULT

Organisation	Name	Sign	Date	Approval Status	Please Tick if Not Attend
Contractor Engineer	[Signature]	[Signature]	[Signature]	True	لم يحضر
Contractor QA/QC*	XYZ	[Signature]	11/2/24	R	نفسه الحاضر
GARB**					المطلوب
Employers Representative					

UNIVERSAL INSPECTION REQUEST



مكتب أ.إ.ص.م
للإستشارات الهندسية



المشروع: ٢٠٢٤/٠٢/١١



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	<p>أ.إ.ص.م للإستشارات الهندسية</p>		Designer Company*	DR .Hassan Mahdy (H.M.C)	
Issued by Contractor	Name	Sign	Date	Time	
	م / احمد مريمي	أ.إ.ص.م	11/02/2024		
Received by Employers Representative	53		UIR		
			C1	C2	C3
			KP	SU	OT
			DO	MM	YY
			11	02	24
			HH	MM	
CODE-1			CODE-2		
CODE-3			CODE-4		
CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	181+480 TO 181+580	تسليم طبقة ردم على منسوب (4.00-)
	E=260619.2117 N=3156454.8661	E=260560.2012 N=3156374.1335

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	أ.إ.ص.م	أ.إ.ص.م				تم الرقابة و تم إعادة
Contractor QA/QC*	XYZ H.M.C	أ.إ.ص.م	11/2/2024	10:00	R	مؤقتة التمشيد / التمشيد / التمشيد / التمشيد / التمشيد /
GARB**						
Employers Representative						



UNIVERSAL INSPECTION REQUEST



مكتب أد/حسن مهدي
للمستشارات الهندسية



الهيئة العامة للطرق
والمواصلات



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة استشارات ومقاولات		Designer Company*	DR :Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	المستشار	Date	20/02/2024						
Received by Employers Representative	54	UIR	C1	C2	C3	DO	MM	YY	HH	MM
			ADP	8U	OT	20	02	24		

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	181+260 TO 181+420 E=260749.0349 N=3156632.4779	تسليم طبقة ردم علي منشوب (2.00-) E=260654.618 N=3156503.3057

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as Indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))	Comments by: General consultant (systra)
تم استلام الموقع في 20/2/2024	-you must follow specs and design draw -you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	ذ.محمد	ذ.محمد				
Contractor QA/QC*	XYZ	ذ.محمد	24-2-2024	8:30	A	
	H.M.C	ذ.محمد	21-2-2024	1:00	A	
GARB**						
Employers Representative	Khaled Ali		17/8/2024		Am/c	

مكتبة أد/حسن مهدي
المستشار
للمستشارات الهندسية
والقانونية

UNIVERSAL INSPECTION REQUEST



مكتب أبحاث
للمواصلات الهندسية



الهيئة العامة
للتنظيمات



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company			Designer Company*	DR. Hassan Mahdy (H.M.C)																
Issued by Contractor	Name أحمد مرسى	Sign أحمد مرسى	Date 26/02/2024	Time																
Received by Employers Representative	55	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>AP</td> <td>SU</td> <td>OT</td> <td>26</td> <td>02</td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	AP	SU	OT	26	02	24			
C1	C2	C3	DD	MM	YY	HH	MM													
AP	SU	OT	26	02	24															

CODE -1	CODE -2	CODE -3	CODE -4	CODE -5
---------	---------	---------	---------	---------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	181+000 TO 181+260 E=260902.4622 E=260749.0349 N=3156842.3828 N=3156632.4779	تسليم طبقة ردم على منسوب (4.00-)

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate:

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	




Comments by: (GARB SURVEY CONSATANT. (xyz))

Comments by: General consultant (systra)

-you must follow specs and design dng.
 -you must do leveling and lining the compacted side slope + filling layer

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	أحمد مرسى	أحمد مرسى				
Contractor	XYZ	أحمد مرسى	27-2-24	11: -	A	
QA/QC*	H.M.C	أحمد مرسى	26-2-2024	3:00	A	
GARB**						
Employers Representative	Khaled	أحمد مرسى	26/2/2024		AWC	

UNIVERSAL INSPECTION REQUEST		مكتب أحمد حسن مهدي للإشراف الهندسي		الهيئة العامة للتأهيل والإشراف	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours						
The Work described below will be complete and ready for inspection at planned time shown						
Contractor Company	التطوير للتوريدات والمقاولات			Designer Company*	DR .Hassan Mahdy (H.M.C)	
Issued by Contractor	Name	اسم: ٢٥٩٠١٢٠	Sign	س.ب. ٩٨٤٥	Date	Time
	م / احمد مرسي				28/02/2024	
Received by Employers Representative		57-A	UIR	C1	C2	C3
				JP	SI	OT
				DO	MM	YY
				28	02	24
				HH	MM	
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5		

EXPLANATION OF WORK TO BE INSPECTED			
Area	Element	Item	
180+376 to 182+376	180+840 TO 181+000	تسليم طبقة ردم علي منسوب (4.00-)	
	E=260996.879		E=260902.4622
	N=3156971.555		N=3156842.3828

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate			
Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA/QC*	XYZ					
	H.M.C		3-3-2024	11:00	R	
GARB**						
Employers Representative						

UNIVERSAL INSPECTION REQUEST



مكتب المهندسين
للمشاورات الهندسية



مكتب المهندسين
للمشاورات الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة التوريد والمقاولات		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	التوريد والمقاولات	Date	26/02/2024							
Received by Employers Representative		57	UIR	C1	C2	C3	DD	MM	YY	HH	MM
				XP	BU	OT	26	02	24		
CODE -1		CODE -2		CODE -3		CODE -4		CODE -5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	180+840 TO 181+000 E=260996.879 N=3156971.555	تسليم طبقة ردم على منسوب (4.00-) E=260902.4622 N=3156842.3828

INSPECTION DETAILS The Following will be ready at the Planned inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attended
Contractor Engineer	زكوة مرسي	زكوة مرسي				
Contractor QA/QC*	XYZ					
	H.M.C	محمد الزكوة	26-2-2024	10:15		
GARB**						
Employers Representative						



UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أوديك للتوريدات والمقاولات		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	Time							
	بن إدريس مهدي		04/03/2024								
Received by Employers Representative		58-A	UIR	C1 KP	C2 SU	C3 OT	DD 04	MM 03	YY 24	HH	MM
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	182+040 TO 182+240	
	E=260288.7528	E=260170.7318
	N=3156002.7634	N=3155841.2981
		تسليم طبقة ردم علي منسوب (1.50-)

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

تم استلام الموقع في 04/03/2024
في 18:30 + 2405 + 6.126

Comments by: General consultant (systra)

-you must follow specs and design dr
-you must do leveling and lining
the compacted side slope + filling
layer

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	أحمد مرسي	أحمد مرسي			A-AWCR	
Contractor QA/QC*	XYZ	محمد إدريس مهدي	5-3-2024	11:30	A	
	H.M.C	محمد إدريس مهدي	4-3-2024	2:15	A	
GARB**						
Employers Representative	Khaled Ali	كhaled Ali	5/3/2024		A	

UNIVERSAL
INSPECTION
REQUEST



مكتب المهندسين
للإستشارات الهندسية



UNIVERSAL INSPECTION REQUEST



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	 Name: <u>م. أحمد مرمي</u> Sign: <u>أحمد مرمي</u>		Designer Company*	DR. Hassan Mahdy (H.M.C)
Issued by Contractor	Date: <u>27/02/2024</u>		Time	
Received by Employers Representative	58		UIR	

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
180+376 to 182+376	182+040 TO 182+240		تمليم طرقة ردم علي منسوب (1.50-)
	E=260288.7528	E=260170.7318	
	N=3156002.7634	N=3155841.2981	

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	<u>أحمد مرمي</u>	<u>أحمد مرمي</u>				
Contractor QA/QC*	XYZ H.M.C	<u>أحمد مرمي</u>	<u>27-2-2024</u>	<u>1:30</u>	<u>R</u>	
GARB**						
Employers Representative						



UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
الاستشارات الهندسية



الهيئة العامة للغذاء والدواء



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة أدريس مهدي للاستشارات الهندسية		Designer Company*	DR. Hassan Mahdy (H.M.C)	
Issued by Contractor	Name	المقاولة	Date	04/03/2024	
Received by Employers Representative		59-A	UIR		

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	182+360 TO 182+376	
	E=260099.9191	E=260090.4778
	N=3155744.4189	N=3155731.5015
		تمليم طبقة ردم علي متمسوب (2.00-)

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as Indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	


Comments by: (GARB SURVEY CONSANTANT (xyz))	Comments by: General consultant (systra)
	- you must follow specs and design drug- - you must do leveling and lining the compacted side slope & filling layer

INSPECTION RESULT					Approval Status	Please tick if Not attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	ز. محمد مرشد	ز. محمد مرشد				
Contractor QA/QC*	XYZ	محمد علي	5-3-2024	12:30	A	
	H.M.C	محمد علي	5-3-2024	1:15	A	
GARB**						
Employers Representative	Khaled ali		5/3/2024		Awc	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
الاستشارات الهندسية



الهيئة العامة للإسكان



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أوديك للتوريدات والمقاولات		Designer Company*	DR. Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	Time							
	أحمد مرسى	أحمد مرسى	27/02/2024								
Received by Employers Representative	59		UIR	C1	C2	C3	DD	MM	YY	HH	MM
				IP	SU	OT	27	02	24		
CODE -1		CODE -2		CODE -3		CODE -4		CODE -5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	182+360 TO 182+376 E=260099.9191 E=260090.4778 N=3155744.4189 N=3155731.5015	تسليم طبقة ردم علي منسوب (2.00-)

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))

Comments by: General consultant (systra)

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	أحمد مرسى	أحمد مرسى			A-AWC-R	
Contractor QA/QC*	XYZ					
	H.M.C	أحمد مرسى	27-2-2024	1:50		
GARB**						
Employers Representative						



UNIVERSAL INSPECTION REQUEST



مكتب أمان مكي
للإستشارات الهندسية



الهيئة العامة للغذاء والدواء



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أحمدك للمقاولات والمقاولات		Designer Company*	DR. Hassan Mahdy (H.M.C)																	
Issued by Contractor	Name للتورين والمقاولات Sign 05/03/2024		Date	Time																	
Received by Employers Representative	50		UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>OD</td> <td>NM</td> <td>YY</td> <td>HH</td> <td>NM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>05</td> <td>03</td> <td>24</td> <td></td> <td></td> </tr> </table>		C1	C2	C3	OD	NM	YY	HH	NM	KP	SU	OT	05	03	24		
C1	C2	C3	OD	NM	YY	HH	NM														
KP	SU	OT	05	03	24																
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5													

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	181+260 TO 181+420 E=260749.0349 N=3156632.4779	تسليم طبقة ردم علي منسوب (1.75-) E=260654.618 N=3156503.3057

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT, (X))	Comments by: General consultant (systra)
ملاحظات: تم فحص الموقع والتأكد من أن العمل جاهز للتحقق. - الفحص الذي	-you must follow specs and design draw -you must do leveling and binning the compacted side slope + filling layer

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not attend
Contractor Engineer	أحمدك	أحمدك			A-AWC-R	
Contractor QA/QC*	XY23		5/3/2024	5:00	A	
	H.M.C		5/3/2024	1:30	A	
GARB**						
Employers Representative	Khaledali		5/3/2024		Amc	

UNIVERSAL INSPECTION REQUEST



مكتب أدامس مهدي
للإشراف الهندسية



الهيئة العامة للطرق
والمواصلات



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة أدامس مهدي للإشراف الهندسية		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Signature	Date	Time						
	702-756-197	أ.م. هادي	05/03/2024							
Received by Employers Representative	61	UIR	C1	C2	C3	DD	MM	YY	HH	NM
			05	03	24					
CODE -1		CODE -2		CODE -3		CODE -4		CODE -5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	181+460 TO 181+580	تمليم طبقة ردم علي منسوب (3.50-)
	E=260631.0138 N=3156471.0126	E=260560.2012 N=3156374.1335

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSANTANT. (xyz))

Comments by: General consultant (systra)

	-you must follow specs and design dries -you must do leveling and lining the compacted side slope & filling layer
--	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	زاهد مرسي	زاهد مرسي			A-AWC-R	
Contractor QA/QC*	XYZ		6-3-2024	4:30	A	
	H.M.C		5/3/2024	2:00	H	
GARB**						
Employers Representative	Khaled ali		6/3/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



شركة أدريس مهدي
للإستشارات الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة أدريس مهدي والمقاولات		Designer Company*	DR ,Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	شركة أدريس مهدي والمقاولات	Date	06/03/2024							
	Signature	أحمد عيسى	Time								
Received by Employers Representative		62-A	UIR	C1	C2	C3	DD	MM	YY	HH	MM
				KP	SU	OT	06	03	24		

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	180+700 TO 180+840 E=261079.4938 N=3157084.5807	تسليم طبقة ردم على منسوب (2.00-) E=260996.879 N=3156971.555

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))	Comments by: General consultant (systra)
تم إجراء المعاينة كمرحلة أولية - الخطة المرفقة	- you must follow specs and design do - you must do leveling and lining the compacted side slope + filling lay

INSPECTION RESULT					Approval Status	Please tick if Not Applicable
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	أحمد عيسى	أحمد عيسى				
Contractor QA/QC*	XYZ	أحمد عيسى	6-3-2024	4:30	A	
	H.M.C	أحمد عيسى	6/3/2024	2:30	A	
GARB**						
Employers Representative	Khaled Ali		6/3/2024		Amrc	

UNIVERSAL INSPECTION REQUEST



مكتب أدامن مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارة



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	<p>س.م.ك. ا.و.د.ب.ك أوديك للتوريدات والمقاولات للتوريدات والمقاولات</p>		Designer Company*	DR .Hassan Mahdy (H.M.C)																	
Issued by Contractor	Name 702-759-197 / م احمد مرسى	Sign [Signature]	Date	05/03/2024																	
Received by Employers Representative	62		UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>ICP</td> <td>SU</td> <td>OT</td> <td>05</td> <td>03</td> <td>24</td> <td></td> <td></td> </tr> </table>		C1	C2	C3	DD	MM	YY	HH	MM	ICP	SU	OT	05	03	24		
C1	C2	C3	DD	MM	YY	HH	MM														
ICP	SU	OT	05	03	24																
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5													

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	<p>180+700 TO 180+840</p> <p>E=261079.4938 E=260996.879 N=3157084.5807 N=3156971.555</p>	تسليم طبقة ردم على منسوب (2.00-)

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as Indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.{ xyz})	Comments by: General consultant (sysra)

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	زاهد مرسى	زاهد مرسى				
Contractor QA/QC*	XYZ H.M.C	محمد مرسى	5/3/2024	1:00	R	
GARB**						
Employers Representative						



UNIVERSAL INSPECTION REQUEST



مكتب أمان من مهدي
للإستشارات الهندسية



الهيئة العامة للغذاء والدواء



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أوتيك للتوكيدات والمقاولات	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name والمقاو Sign ٢٠٢-٢٥٩-١٢٢٢/م.ب/م.ب/أحمد مرسى	Date	06/03/2024																
Received by Employers Representative	63	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SL</td> <td>OT</td> <td>06</td> <td>03</td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SL	OT	06	03	24		
C1	C2	C3	DD	MM	YY	HH	MM												
KP	SL	OT	06	03	24														
CODE-1	CODE-2	CODE-3	CODE-4																
CODE-5																			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	181+100 TO 181+260	تسليم طبقة ردم علي منسوب (3.50-)
	E=260843.4517	
	N=3156761.6501	
	E=260749.0349	
	N=3156632.4779	

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (systa))	Comments by: General consultant (systa)
تم تسليم (الطابع) مرسى 2 مرسى تسليمه القطار الكهربائي السريع - القطار السريع	-you must follow specs and design drug -you must do leveling and binning the compacted side slope & filling layer

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	زاهد مرسى	زاهد مرسى			A-AWC-R	
Contractor QA/QC*	XYZ H.M.C	أحمد مرسى	6/3/2024	4:15	A	
GARB**						
Employers Representative	Khaled ali		6/3/2024		AWC	

UNIVERSAL INSPECTION REQUEST		مكتب الدراسات الهندسية للبنية التحتية		مكتب الدراسات الهندسية للبنية التحتية			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours							
Work described below will be complete and ready for inspection at planned time shown							
Contractor Company				Designer Company*	DR. Hassan Mahdy (H.M.C)		
Issued by Contractor	Name			Date	09/03/2024		
Received by Employer Representative		54	UIR	C1 KP	C2 SU	C3 OT	DD 09
					MM 03	YY 24	HH MM

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
180+375 to 182+375	180+840 TO 181+100	تسليم طبقة ردم علي منسوب (3.50-)
	E=260996.870 N=3156971.55	
	E=260843.4517 N=3156761.6501	

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time			
Planned Inspection Date		Planned Inspection Time	
COMPLIANCE EVIDENCE: Must be included as appropriate			
Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT) (x 10)	Comments by: General consultant (systra)
	- you must follow specs and design draw - you must do leveling and lining the compacted side slope & filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor	XYZ		4-3-2024	21:00	A	
QA/QC*	H.M.C		9/3/2024	12:30	A	
GARB**						
Employers Representative	Khaled Ali		9/3/2024		AWC	

UNIVERSAL INSPECTION REQUEST		مكتب المهندس مهدي للإشراف الهندسية			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours						
The Work described below will be complete and ready for inspection at planned time shown						
Contractor Company	شركة اوريديك		Designer Company*	DR. Hassan Mahdy (H.M.C)		
Issued by Contractor	Name	Sign	Date	Time		
	٧٠٢-٧٥٩-١٦٧	م. احمد مريسي	19/03/2024			
Received by Employers Representative	65		UIR	C1	C2	C3
				DO	MM	YY
				HH	MM	
	code-3	code-2	code-1	code-4	code-5	




EXPLANATION OF WORK TO BE INSPECTED			
Area	Element	Item	
180+376 to 182+376	181+440 TO 181+580	تسليم طبقة ردم علي منسوب (3.00-)	
	E=260642.8159		E=260560.2012
	N=3156487.1592		N=3156374.1335

INSPECTION DETAILS The Following will be ready at the Planned inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate			
Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (systra))	Comments by: General consultant (systra)
تم استلام الموقع في 19/3/2024	- you must follow specs and design drwg
تم تنفيذ شتات الحصى في السطح - التي لاري	- you must do Leveling and Ginning
	the compacted soil slope + filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	م. احمد مريسي					
Contractor QA/QC*	XY		20.3.2024	11:30	A	
GARB**						
Employers Representative	Khaled Ali		20/3/2024		AWC	

UNIVERSAL INSPECTION REQUEST		مكتب أ.أ. حسن مهدي للإستشارات الهندسية		شركة أ.أ. حسن مهدي للإستشارات الهندسية	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours							
The Work described below will be complete and ready for inspection at planned time shown							
Contractor Company	أوديك للتوريدات والمقاولات			Designer Company*	DR. Hassan Mahdy (H.M.C)		
Issued by Contractor	Name	Sign	Date	Time			
	م.أ. أحمد قمرى	(Signature)	19/03/2024				
Received by Employers Representative	66		UIR	C1	C2	C3	DD
				XP	SU	OT	19
							03
							24

EXPLANATION OF WORK TO BE INSPECTED			
Area	Element	Item	
180+376 to 182+376	181+100 TO 181+350	تسليم طبقة ردم علي منسوب (3.00-)	
	E=260843.4517		E=260749.0349
	N=3156761.6501		N=3156632.4779

INSPECTION DETAILS The following will be ready at the Planned inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate			
Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (systra))	Comments by: General consultant (systra)
(Signature)	-you must follow specs and design drwg.
(Signature)	-you must do leveling and lining
(Signature)	the compacted side slope & filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	(Signature)	(Signature)				
Contractor QA/QC*	XYZ	(Signature)	20-3-2024	10:00	A	
	H.M.C	(Signature)	19-3-2024	10:45	A	
GARB**						
Employers Representative	Khaled Ali	(Signature)	20/3/2024		Amc	

UNIVERSAL INSPECTION REQUEST



مكتب أمان نهدي
للإشراف الهندسية



مكتب أمان نهدي
للإشراف الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة التوريدات والمقاولات		Designer Company*	DR. Hassan Mahdy (H.M.C)	
Issued by Contractor	Name	التوريدات والمقاولات	Date	20/03/2024	
	Sign	م.ف. ١٦٧/٢٠٢٤	Time		
Received by Employers Representative	67	UIR	C1	C2	C3
			DO	MM	YY
			20	03	24
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5	

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	180+700 TO 180+840	تسليم طبقة ردم على منسوب (1.75-)
	E=261079.4938 N=3157084.5807	
	E=260996.879 N=3156971.555	

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as Indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB Surveyor CONSTANT +ve)

تم استكمال العمل في الموقع - الفتح الناري

Comments by: General consultant (systra)

-you must follow specs and design dng
-you must do leveling and cinning
the compacted side slope + filling layer

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	أحمد حسن				A-AWC-R	
Contractor QA/QC*	XYZ		20-3-2024	11:50	A	
	H.M.C		20-3-2024	11:40	A	
GARB**						
Employers Representative	Khaleel ali		20/3/2024		Amc	

UNIVERSAL INSPECTION REQUEST



مكتب أد/صن مهدي
للإستشارات الهندسية



الهيئة العامة للغذاء والدواء



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة المقاولات والتشييد		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name للتوريدات والمقاولات	Sign	Date	Time							
	٧٠٣-٧٥٩-١٦٧/ب.ص. ٨٩٨٤٥		26/03/2024								
Received by Employers Representative		59	UIR	C1	C2	C3	DD	MM	YY	HH	MM
				KP	SU	OT	26	03	24		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	180+376 TO 180+700	
	E=261270.6878	E=261079.4938
	N=3157346.1544	N=3157084.5807
		تسليم طبقة ردم على منسوب (1.75-)

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT / xyz)

تم فحص العمل ووجدنا ان العمل مطابق للمواصفات المطلوبة - المرفقات المطلوبة - المرفقات المطلوبة

Comments by: General consultant (systra)

- you must follow specs and design n.dry
- you must do leveling and winning the compacted side slope of filling layer

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick / Not Attend
Contractor Engineer	زكوة مرسي	زكوة مرسي			A-AWC-R	
Contractor QA/QC*	XYZ	محمد بن محمد	27-3-24	11:00	A	
	H.M.C	محمد بن محمد	26/3/2024	11:00	A	
GARB**						
Employers Representative	Khaleel	Khaleel	27/3/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



المجلس الأعلى للمهندسين
المرتبطينين



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أوديك للتوريدات والمقاولات	Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name: شركة أوديك للتوريدات والمقاولات Sign: [Signature] ٧٠٢-٢٥٩-١٦٢	Date	26/03/2024							
Received by Employers Representative	70	UIR	C1 KP	C2 SU	C3 OT	DO 26	MM 03	YY 24	HH	MM
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5						

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	180+840 TO 181+100	تسليم طبقة ردم على منصوب (3.00-)
	E=260996.879	
	N=3156971.555	
	E=260843.4517	
	N=3156761.6501	

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

ملاحظات المهندس
المستشار
المستشار
المستشار

Comments by: General consultant (systra)

-you must follow specs and design draw
- you must do leveling and lining
the compacted side slope of filling layer

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Applicable
Contractor Engineer	زكريا	زكريا			A-AWC-R	
Contractor QA/QC*	XYZ	محمد	27-3-24	11:30	A	
	H.M.C	محمد	26/3/2024	10:30	A	
GARB**						
Employers Representative	Khaled ali	[Signature]	27/3/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أ.د. حسن مهدي
للإشراف الهندسية



الهيئة العامة للتأهيل



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أوديك للتوريدات والمقاولات	Designer Company*	DR. Hassan Mahdy (H.M.C)
Issued by Contractor	Name: شركة أوديك للتوريدات والمقاولات Sign: [Signature] 7-3-2024-167: [Signature]	Date	Time
Received by Employers Representative	71	27/03/2024	

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
180+376 to 182+376	182+040 TO 182+240	تسليم طبقة ردم علي منسوب (1.25-)
	E=260288.7528	
	N=3156002.7634	

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate			
Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as Indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (systra))	Comments by: General consultant (systra)
تم فحص الموقع والتأكد من التسليمات المطلوبة - الفتح للزاري	-you must follow specs and design by -you must do leveling and filling the compacted side slope & filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	ز. ك. م. م.	ز. ك. م. م.				
Contractor QA/QC*	المراد XYZ	ع. م. م.	28-3-2024	8:30	A	
	H.M.C	ع. م. م.	27-3-2024	10:00	A	
GARB**						
Employers Representative	Ahmed Ali		28/3/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أ.د. حسن مهدي
للإستشارات الهندسية



المملكة العربية السعودية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أوديك للتوريدات والمقاولات		Designer Company*	DR. Hassan Mahdy (H.M.C)																			
Issued by Contractor	Name	Sign	Date	Time																			
			27/03/2024																				
Received by Employers Representative			<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>27</td> <td>03</td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	27	03	24						
	C1	C2	C3	DD	MM	YY	HH	MM															
KP	SU	OT	27	03	24																		
CODE-1		CODE-2	CODE-3	CODE-4		CODE-5																	

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	182+360 TO 182+376	
	E=260099.9191	E=260090.4778
	N=3155744.4189	N=3155731.5015
		تسليم طبقة ردم على منسوب (1.75-)

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))

تم استلام المخطط من المصمم
المستوفى القطار الكهربائي السريع - الخط الرابع

Comments by: General consultant (systra)

-you must follow specs and design data
-you must do leveling and filling the compacted side slope of filling layer

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attended
Contractor Engineer	ز. محمد مبرور	ز. محمد مبرور				
Contractor QA/QC*	XYZ	أ. محمد مبرور	28-7-2024	9:30	A	
	H.M.C	محمد مبرور	27-3-2024	10:30	A	
GARB**						
Employers Representative	Khaled ali		28/3/2024		Amr	

UNIVERSAL INSPECTION REQUEST



مكتب أ.د. حسن مهدي
للإستشارات الهندسية



المملكة العربية السعودية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown:

Contractor Company	شركة أود ديمت	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	27/03/2024	Date	Time																
Received by Employers Representative	73	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DO</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>27</td> <td>03</td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DO	MM	YY	HH	MM	KP	SU	OT	27	03	24		
C1	C2	C3	DO	MM	YY	HH	MM												
KP	SU	OT	27	03	24														

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	181+420 TO 181+580	تسليم طبقة ردم علي منسوب (2.5) -
	E=260654.618 N=3156503.3057	E=260560.2012 N=3156374.1335

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSANTANT. (xyz))

Comments by: General consultant (systra)

- you must follow specs and design
- you must do leveling and filling layer
the compacted side slope of filling layer

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	زاهد مرسي	زاهد مرسي			A-AWC-R	
Contractor QA/QC*	XYB		28-7-2024	11:30	A	
	H.M.C		28-7-2024	10:40	A	
GARB**						
Employers Representative	Khalid Ali		28/8/2024		ANC	

UNIVERSAL INSPECTION REQUEST



مكتب أمان من مهنى
للإستشارات الهندسية



الهيئة العامة للإستشارة



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة أوديد للتوريدات والمقاولات		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	لتوريدات المقاولات	Date	01/04/2024							
Received by Employers Representative		74	UIR	C1 KP	C2 SU	C3 OT	DD 01	MM 04	YY 24	HH	MM
CODE -1		CODE -2		CODE -3		CODE -4		CODE -5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	181+100 TO 181+260	تسليم طبقة ردم علي منسوب (2.5-)
	E=260843.4517 N=3156761.6501	E=260749.0349 N=3156632.4779

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (wz))

Comments by: General consultant (systra)

تم العمل على التسليم طبقا للمواصفات - الختم الذي
-you must follow specs and design dr
-you must do leveling and lining
the compacted side slope of filling layer


INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	زاهد مرسي	زاهد مرسي			A-AWC-R	
Contractor QA/QC*	XY		2-4-2024	21:00	A	
GARB**	H.M.C		1-4-2024	9:30	A	
Employers Representative	Khaled Ali		2/4/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أمان من مهابي
للإستشارات الهندسية



الهيئة العامة للإستشارات



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة أوريدات للتوريدات والمقاولات		Designer Company*	DR. Hassan Mahdy (H.M.C)
Issued by Contractor	Name	Sign	Date	Time
	م / أحمد عزمي	أحمد عزمي	01/04/2024	
Received by Employers Representative		75	UIR	

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
180+376 to 182+376	181+260 TO 181+420	تسليم طبقة ردم علي منسوب (1.5-)
	E=260749.0349 N=3156632.4779	E=260654.618 N=3156503.3057

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))	Comments by: General consultant (systra)
 (توقيع) المهندس أحمد عزمي	-you must follow specs and design -you must do leveling and finishing the compacted side slope of filling

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	أحمد عزمي	أحمد عزمي				
Contractor QA/QC*	XY H.M.C	أحمد عزمي	2-4-2024	11:30	A	
GARB**						
Employers Representative	Khaled Ali		2/4/2024		A	

UNIVERSAL INSPECTION REQUEST



BULE Line

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Location Name		Contractor Company		Designer Company	
334+800 الى قسم 176+700		شركة اوريدك للتوريدات والمقاولات		DR. Hassan Mahdy (H.M.C)	
Issued by Contractor	Name	Signature	Date	Time	
	المقاولات والمقاولات	(م.م. احمد محمد عيسى)	02-04-2024		
Contractor UIR Reference	EET-SYS-H.M.C-IR-			Revision (1)	
Received by ER	76	UIR	C1 KP	C2 EW	C3 OT
			D0 02	MM 04	YY 2024
CODE-1	CODE-1	CODE-1	CODE-2		CODE-3

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
(1 KM) FROM 180+376 TO 182+376	180+840 TO 181+100 E=260596.979 N=3156971.535	Middle Embankment (-2.50) E=260843.4517 N=3156761.6501
Inspection Description :		
Inspect fill layer from at level layer (-2.5)		

INSPECTION DETAILS The Following will be ready at the Planned inspection Time

Planned inspection Date	Planned inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by XYZ:

تم اكمال القطع بالحياتة طبق المخطط
اعمال التحويلات

Comments by (H.M.C):

Comments by SYSTRA (EGIS):

-you must follow specs and design draw-
you must do leveling and lining the compacted side slope & filling lower

Approval Status

Organisation	Name	Sign	Date	Time	A-AWC-R
XYZ	محمد الرضا العرابي		24-2024	2:15	A
H.M.C	محمد الرضا العرابي		24-2024	10:00	AWC
GARB*					
Employers Representative	Fhaled ali		24/4/2024		AWC

* Alignment: Bridges, Culvert Only

A= Approved; AWC= Approved with comments; R= Rejected

File Name: NEW COVER.docx

Page 1 of 1

UNIVERSAL INSPECTION REQUEST



BULE Line

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Location Name		Contractor Company		Designer Company																	
334+800 الى 176+700		شركة اوديك شويكس القابضة		DR.Hassan Mahdy (H.M.C)																	
Issued by Contractor	Name	Signature	Date	Time																	
	م. احمد مرسى	02-04-2024																			
Contractor UIR Reference	EET-SYS-H.M.C-IR-			Revision (1)																	
Received by ER		UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>EW</td> <td>OT</td> <td>02</td> <td>04</td> <td>2024</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	EW	OT	02	04	2024				
C1	C2	C3	DD	MM	YY	HH	MM														
KP	EW	OT	02	04	2024																

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
(2 KM) FROM 180+376 TO 182+376	181+420 TO 181+580 E=260554.518 N=3156503.3057	Middle Embankment (-2.00)
Inspection Description: Inspect fill layer from at level layer (-2.0)		

INSPECTION DETAILS The following will be ready at the Planned Inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate			
Checklist Attached <input type="checkbox"/>	Test Results Attached <input type="checkbox"/>	Calibration Attached <input type="checkbox"/>	Other as indicated <input type="checkbox"/>
Drawing Reference	ITP Reference	MS Reference	

Comments by XYZ:	Comments by (H.M.C):	Comments by SYSTRA (EGIS):
		-you must follow specs and design dno. -you must do leveling and winning the compacted shale slope & filling layer

Approval Status					
Organisation	Name	Sign	Date	Time	A-AWC-R
XYZ	عبد الرحمن		24/2024	2:30	A
H.M.C	محمد		24-2024	10:45	AWC
GARB*					
Employers Representative	Khaled		24/2024		AWC

* Alignment: Bridges: Culvert Only

A= Approved; AWC= Approved with comments; R= Rejected

File Name: NEW COVER.docx

Page 1 of 1

مكتب أ.د/حسن مهدي
للإستشارات الهندسية

بيان بتقارير اختبارات صلاحية أتربة للتأسيس
اسم المشروع: مشروع القطار الكهربائي السريع (أكتوبر - أسوان)
القطاع الثاني (بين مزار - منفلوط)



م	تاريخ	المحطة	تصنيف العينة	نسبة الناز من منخل ٢٠٠	مجال اللدونة	أقصى كثافة جافة (الريكتور) جم/سم ^٣	نسبة المياه الاسيولية	قيمة CBR المقمورة	المواد المطلوبة	المعمل
1	2023-06-25	مشون ١٨١+٢٠٠	A-1-b	14.50%	NP	2.141	6.50%	30.10%	لا يوجد	مكتب أ.د.م هشام حلمي
2	2023-10-07	مشون ١٨١+١٠٠	A-1-b	14.50%	NP	2.136	6.50%	32.50%	لا يوجد	مكتب أ.د.م هشام حلمي
3	2023-10-17	مشون ١٨١+١٠٠	A-1-b	14.80%	NP	2.141	6%	30.00%	لا يوجد	مكتب أ.د.م هشام حلمي
4	2023-10-23	مشون ١٨١+١٠٠	A-1-b	14.38%	NP	2.137	6.70%	29.50%	لا يوجد	مكتب أ.د.م هشام حلمي
5	2023-10-28	4.5 - [180+700 to 180+840]	A-1-b	11.90%	NP	2.105	6.60%	52.30%	لا يوجد	مكتب أ.د.م هشام حلمي
6	2023-11-02	مشون ١٨١+٠٠٠	A-1-b	13.60%	NP	2.130	6.50%	57.40%	لا يوجد	مكتب أ.د.م هشام حلمي
7	2023-11-05	مشون ١٨١+١٠٠	A-1-b	14.70%	NP	2.132	6.30%	31.40%	لا يوجد	مكتب أ.د.م هشام حلمي
8	2023-11-29	مشون ١٨١+٠٠٠	A-1-b	12.80%	NP	2.139	6.10%	28.00%	لا يوجد	مكتب أ.د.م هشام حلمي
9	2023-12-03	مشون ١٨١+٢٠٠	A-1-b	13.90%	NP	2.141	6.50%	27.00%	لا يوجد	مكتب أ.د.م هشام حلمي
10	2023-12-12	مشون ١٨١+١٠٠	A-1-b	13.40%	NP	2.131	6.40%	27.90%	لا يوجد	مكتب أ.د.م هشام حلمي
11	2023-12-21	مشون ١٨١+٠٠٠	A-1-b	14.20%	NP	2.143	6.10%	30.00%	لا يوجد	مكتب أ.د.م هشام حلمي
12	2023-12-31	مشون ١٨١+٢٠٠	A-1-b	13.40%	NP	2.147	6%	29.70%	لا يوجد	مكتب أ.د.م هشام حلمي
13	2024-01-04	مشون ١٨١+٠٠٠	A-1-b	12.30%	NP	2.141	6.10%	32.00%	لا يوجد	مكتب أ.د.م هشام حلمي
14	2024-01-08	مشون ١٨٠+٠٠٠	A-1-b	13.00%	NP	2.143	6.40%	30.00%	لا يوجد	مكتب أ.د.م هشام حلمي
15	2024-01-08	محجر يسار المسار (محجر جامعة الأزهر)	A-1-b	13.90%	NP	2.141	6.50%	27.00%	لا يوجد	مكتب أ.د.م هشام حلمي
16	2024-01-18	محجر يسار المسار (محجر جامعة الأزهر)	A-1-b	12.80%	NP	2.139	6.10%	28.00%	لا يوجد	مكتب أ.د.م هشام حلمي
17	2024-01-24	مشون ١٨١+١٠٠	A-1-a	9.00%	3%	2.140	5.30%	40.00%	لا يوجد	معمل جامعة المنيا
18	2024-02-07	مشون ١٨٠+١٠٠	A-1-b	11.40%	NP	2.138	6.00%	35.00%	لا يوجد	مكتب أ.د.م هشام حلمي
19	2024-02-07	مشون ١٨١+٢٠٠	A-1-b	11.00%	3%	2.150	5.40%	43.00%	لا يوجد	معمل جامعة المنيا
20	2024-02-08	مشون ١٨٠+١٠٠	A-1-b	10.10%	NP	2.136	6.50%	35.00%	لا يوجد	مكتب أ.د.م هشام حلمي
21	2024-02-20	مشون ١٨١+٢٠٠	A-1-b	13.10%	NP	2.147	6.30%	38.00%	لا يوجد	مكتب أ.د.م هشام حلمي
22	2024-02-21	مشون ١٨٠+٢٠٠	A-1-b	13.80%	NP	2.146	6.50%	37.60%	لا يوجد	مكتب أ.د.م هشام حلمي
23	2024-02-26	مشون ١٨٠+٢٠٠	A-1-b	14.10%	NP	2.146	6.20%	34.50%	لا يوجد	مكتب أ.د.م هشام حلمي
24	2024-03-04	مشون ١٨٠+١٠٠	A-1-b	13.00%	NP	2.134	6.40%	32.60%	لا يوجد	مكتب أ.د.م هشام حلمي

مدير المشروع
أ.د.م هشام حلمي
م.مروان دياب
التوقيع

الاستشاري المشرف
مهندسين ضبط الجودة
م.مروان دياب
التوقيع

شؤون الشركة
م.م.مروان دياب
التوقيع
٢٠٢٤-٠٣-٠٤



تقرير بنتائج اختبارات صلاحية أترية للناسيس

مقدمة : تم إعداد هذا التقرير بناءا علي طلب شركة /اوديكا

وذلك لتحديد خصائص ومدى صلاحية عينة تراب للإستخدام في طبقات الردم لجسر القطار الكهربائي

مصدر العينة: عند المحطة / مشون (181+200)

- المتدوين: وقد تم توريد العينة بمعرفة م/احمد رشدي. (مهندس الأشراف مكتب د/حسن مهدي)

بتاريخ: 2023/9/25

- بيانات المتدوين: رقم الهاتف = 01150014987

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفلوطة)

تأنيبه : العينة مسؤولة من احضرها

وقد تم عمل الاختبارات الآتية :

1-مختبر الحبيبي

2-حد السيولة واللدونة

3-اختبار البروكتور

4-اختبار CBR

5-اختبار المواد العضوية

وكانت نتائج الاختبارات كالآتي :

م	نوع الاختبار	النتائج	حدود القبول والرفض طبقا للمواصفات
1	تصنيف العينة	A-1-b	(A-1-a) - (A-1-b) - (A-2-4)
2	نسبة الماء من مخل 200	14.50%	لا تزيد عن (15 %)
3	مجال اللدونة	NP	(A-1-a or A-1-b = 5 max) (A-2-4 = 10 max)
4	أقصى كثافة جافة (البروكتور) yd max	2.141 gm/cm3	لا تقل عن 1.88 gm/cm3
5	نسبة الماء الأموية	6.5%	--
6	قيمة CBR المعصورة	30.10%	لا تقل عن 20%
8	المواد العضوية	لا يوجد	لا تزيد عن 1%

• و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للاستخدام في طبقات الردم

يعتمد***

محرر التقرير
م.م. ه.م. ح.م.

مهندس المعمل
م.م. ه.م. ح.م.
التوقيع

مشروع :

قطار أسوان الكهربائي السريع - القطاع الثاني

استشاري أبحاث التربة والاساسات :
أ.د.م. هشام محمد حلمي ..



تقرير بنتائج اختبارات صلاحية أتربة للتأسيس

مقدمة : تم إعداد هذا التقرير بناء على طلب شركة لاوديك

وذلك لتحديد خصائص ومحتوي صلاحية عينة تراب للإستخدام في طبقات الردم لجسر القطاع الكهربائي

مصدر العينة: عند المحطة / مشون (100+181)

- المندوبين: وقد تم توريد العينة بمعرفة م/احمود رشدي. (مهندس الإشراف مكتب د/حسن مهدي)

بتاريخ: 2023/14/7

- بيانات المندوبين: رقم الهاتف = 01150014987

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منقلاوط)

تنبيه : العينة مسؤولة من أحضرها

وقد تم عمل الاختبارات الآتية :

1-الدرج الميبي

2-حد السيولة واللدونة

3-إختبار البروكتور

4-إختبار CBR

5-إختبار المواد العضوية

وكانت نتائج الاختبارات كالآتي :

م	نوع الإختبار	النتائج	حدود القبول والرفض طبقا للمواصفات
1	تصنيف العينة	A-1-b	(A-1-a) - (A-1-b) - (A-2-4)
2	نسبة الماء من مخلل 200	14.50%	لا تزيد عن (15 %)
3	مجال اللدونة	NP	(A-1-a or A-1-b = 6 max) (A-2-4 = 10 max)
4	أقصى كثافة جافة (البروكتور) yd max	2.136 gm/cm3	لا تقل عن 1.88 gm/cm3
5	نسبة المياه الأمولية	6.5%	-
6	قيمة CBR المنصورة	32.50%	لا تقل عن 20%
8	المواد العضوية	لا يوجد	لا تزيد عن 1%

* و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للاستخدام في طبقات الردم

يعتمد

م.م. هشام محمد حلمي

مهندس المعمل

م.م. هشام محمد حلمي

استشاري أبحاث التربة والاساسات :
أ.د.م. هشام محمد حلمي



مشروع :
قطار اسوان الكهربائي السريع - القطاع الثاني

تقرير بنتائج اختبارات صلاحية أنربة للتأسيس

مقدمة : تم إعداد هذا التقرير بناءً على طلب شركة /أوبك

وذلك لتحديد خصائص ومدي صلاحية عينة تراب للاستخدام في طبقات الردم لجسر القطار الكهربائي

مصدر العينة: عند المحطة / مشون (181+100)

- المنسوب: وقد تم توريد العينة بمعرفة م/محمود رشدي. (مهندس الإشراف مكتب د/حسن مهدي)

تاريخ: 2023/10/17

- بيانات المنسوب: رقم الهاتف = 01150014987

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفوط)

تنبيه : العينة مسؤولة من أعضائها

وقد تم عمل الاختبارات الآتية :

- 1- التدرج الحبيبي
- 2- حد السيولة واللينة
- 3- اختبار البرونكتور
- 4- اختبار CBR
- 5- اختبار المواد العضوية

وكشلت نتائج الاختبارات كالتالي :

م	نوع الاختبار	النتائج	حدود القبول والرفض طبقاً للمواصفات
1	تصنيف العينة	A-1-b	(A-1-a) - (A-1-b) - (A-2-4)
2	نسبة الماء من سائل 200	14.80%	لا تزيد عن (15 %)
3	مجال اللينة	NP	(A-1-a or A-1-b = 6 max) (A-2-4 = 10 max)
4	الخصي كثافة جافة (البرونكتور) yd max	2.141 gm/cm3	لا تقل عن 1.88 gm/cm3
5	نسبة الماء الأموية	6%	-
6	قيمة CBR المغمورة	30.00%	لا تقل عن 20%
8	المواد العضوية	لا يوجد	لا تزيد عن 1%

• و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للاستخدام في طبقات الردم

بمعد

محمد شهاب حبيب

مهندس المعمل

م/م
التوقيع



تقرير بنتائج اختبارات صلاحية أتربة للتأسيس

مقدمة : تم إعداد هذا التقرير بناء على طلب شركة /أوديلا

وذلك لتعميد خمساتين ومدي صلاحية عينة تراب للإستخدام في طبقات الردم لجسر لقطار الكهربائي

مصدر العينة: عند المحطة / مشون (181+100)

- المندوب: وقد تم توريد العينة بمعرفة م/محمود رشدي. (مهندس الاشراف مكتب د/حسن مهدي)

بتاريخ: 2023/10/23

- بيانات المندوب: رقم الهاتف = 01150014987

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - ملفوظ)

تنبيه : العينة مسؤولة من احضرها

وقد تم عمل الاختبارات الآتية :

1-الترج الحبيبي

2-حد السيولة واللدونة

3-إختبار البروكتور

4-إختبار CBR

5-إختبار المواد العضوية

وكلت نتائج الاختبارات كالآتي :

م	نوع الإختبار	النتائج	حدود القبول والرفض طبقا للمواصفات
1	تصنيف العينة	A-1-b	(A-1-a) - (A-1-b) - (A-2-4)
2	نسبة الماء من مخل 200	14.38%	لا تزيد عن (15 %)
3	مجال اللدونة	NP	(A-1-a or A-1-b = 6 max) (A-2-4 = 10 max)
4	أقصى كثافة جافة (البروكتور) γd max	2.137 gm/cm3	لا تقل عن 1.88 gm/cm3
5	نسبة المياه الأصولية	6.7%	-
6	قيمة CBR المقصورة	29.50%	لا تقل عن 20%
8	المواد العضوية	لا يوجد	لا تزيد عن 1%

• و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للاستخدام في طبقات الردم

بمعد "

محمد
مهندس

مهندس المعمل
م
التوقيع

استشاري أبحاث التربة والاساسات :
أ.د.م. هشام محمد حلمي



مشروع :
قطار اسوان الكهربائي السريع - القطاع الثاني

تقرير بنتائج اختبارات صلاحية أترية للتأسيس

مقدمة : تم إعداد هذا التقرير بناءا على طلب شركة / أوديك

وذلك لتحديد خصائص ومدي صلاحية هيئة تراب للإستخدام في طبقات الردم لجسر القطار الكهربائي

مصدر العينة : عند المحطة / (١٨٠ + ٩٨٨) (عينة من القطاع)

- الملحق : وقد تم توريد العينة بمعرفة ١ - م / احمد سمير (مهندس الاشراف مكتب د / حسن مهدي) رقم الهاتف = ١١٢١١٦١٢٨٩ .

تاريخ توريد العينة : ٢٨ / ١٠ / ٢٠٢٣

تعيينه على : العينة مسئولة من احضرها

إسم للمشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منقلاوط)

وقد تم عمل الاختبارات الآتية :

١-الكثرج الحبيبي

٢-حد السيولة واللدونة

٣-اختبار البروكتور

٤-اختبار CBR

٥-اختبار المواد العضوية

وكنت نتائج الاختبارات كالآتي :

نوع الاختبار	النتائج	حدود القبول والرفض طبقا للمواصفات
١- تصنيف للعينة	A-1-b	(A-1-a) - (A-1-b) - (A-2-4)
٢- نسبة الماء من منقل 200	11.9%	لا تزيد عن (15 %)
٣- مجال اللدونة	NP	(A-1-a or A-1-b = 6 max) (A-2-4 = 10 max)
٤- أقصى كثافة جافة (البروكتور) yd max	2,105 gm/cm3	لا تقل عن 1.88 gm/cm3
٥- نسبة الماء الأموية	6.6%	---
٦- قيمة CBR المنغورة	52.3%	لا تقل عن 20%
٨- المواد العضوية	لا يوجد	لا تزيد عن 1%

و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للإستخدام في طبقات الردم .

يختم

مهندس المعمل

التوقيع

فني المعمل

التوقيع

استشاري أبحاث التربة والاساسات :
أ.د.م. هشام محمد حلمي



مشروع :
قطر اسوان الكهربائي السريع - القطاع الثاني

تقرير بنتائج اختبارات صلاحية أتربة للتأسييس

مقدمة : تم إعداد هذا التقرير بناءاً على طلب شركة / أوديك

وذلك لتحديد خصائص ومدي صلاحية حينة تراب للإستخدام في طبقات الردم لجسر لقطر الكهربائي

مصدر العينة : (مشون يسار العمار)

- المندوب : وقد تم توريد العينة بمعرفة ١ - م / محمود رشدي (مهندس الاشراف مكتب د/ حسن مهدي) رقم الهاتف = ٠١١٢١٤٦١٢٨١

- تاريخ توريد العينة : ٢٠٢٣/١١/٠٢

- تلبية طلب : العينة مستوفية من أحضرها

اسم المشروع : مشروع القطر الكهربائي السريع (القطاع الثاني) - (بني مزار - منقوط)

وقد تم عمل الاختبارات الآتية :

- ١- التدرج المبيهي
- ٢- الحد السيولة واللدونة
- ٣- إختبار البرونكتور
- ٤- إختبار CBR
- ٥- إختبار المواد العضوية

وكانت نتائج الاختبارات كالآتي :

م	نوع الإختبار	النتائج	حدود القبول والرفض طبقا لخواصات
1	تصنيف العينة	A-1-b	(A-1-a) - (A-1-b) - (A-2-4)
2	نسبة الماء من مختل 200	13.6%	لا تزيد عن (15 %)
3	مجال اللدونة	NP	(A-1-a or A-1-b = 6 max) (A-2-4 = 10 max)
4	أقصى كثافة جافة (البرونكتور) yd max	2.13 gm/cm3	لا تقل عن 1.88 gm/cm3
5	نسبة المياه الأموية	6.5%	---
6	قيمة CBR المنصورة	57.4%	لا تقل عن 20%
8	المواد العضوية	لا يوجد	لا تزيد عن 1%

• و بمقارنة نتائج العينة بمواصفات مشروع القطر السريع فهي صالحة للإستخدام في طبقات الردم .

يعتمد ***

مهندس المعمل
م / م / م
التوقيع /

فني المعمل
محمد علي عيسى
التوقيع /

استشاري أبحاث التربة والاساسات :
أ.د.م. هشام محمد حلمي



مشروع :
قطار اسوان الكهربائي السريع - القطاع الثاني

تقرير بنتائج اختبارات صلاحية أنربة للتأسيس

مقدمة : تم إعداد هذا التقرير بناء على طلب شركة /أونيك
وذلك لتحديد خصائص ومدي صلاحية عينة تراب للإستخدام في طبقات الردم لجسر القطار الكهربائي
مصدر العينة: عند المحطة / مشون (100+181)
- المنفذ: وقد تم توريد العينة بمعرفة /محمود رشدي. (مهندس الأشراف مكتب د/حسن مهدي)

بتاريخ: 2023/11/5

- بيانات المنفذ: رقم الهاتف = 01150014987

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفلوط)

تتبعه : العينة مسؤولة من أحضرها

وقد تم عمل الاختبارات الآتية :

- 1-الكثرج الحبيبي
- 2-حد السيولة واللدونة
- 3-اختبار البروكتور
- 4-اختبار CBR
- 5-اختبار المواد العضوية

وكانت نتائج الاختبارات كالآتي :

م	نوع الاختبار	النتائج	حدود القبول والرفض طبقا للمواصفات
1	تصنيف العينة	A-1-b	(A-1-a) - (A-1-b) - (A-2-4)
2	نسبة الماء من منخل 200	14.70%	لا تزيد عن (15 %)
3	مجال اللدونة	NP	(A-1-a or A-1-b = 6 max) (A-2-4 = 10 max)
4	أقصى كثافة جافة (البروكتور) yd max	2.132 gm/cm3	لا تقل عن 1.88 gm/cm3
5	نسبة الماء الأمية الأصولية	6.3%	-
6	قيمة CBR المفجرة	31.4%	لا تقل عن 20%
8	المواد العضوية	لا يوجد	لا تزيد عن 1%

و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للاستخدام في طبقات الردم

يعتمد

محمد حلمي
مهندس

مهندس المعمل

م. أحمد
التوقيع

مشروع :

قطار اسوان الكهربائي السريع - القطاع الثاني

استشاري أبحاث التربة والاساسات :

أ.د.م. هشام محمد حلمي



تقرير نتائج اختبارات صلاحية أتربة للتأسيس

مقدمة : تم إعداد هذا التقرير بناءا على طلب شركة /أوديك

وذلك لتحديد خصائص ومدي صلاحية عينة تراب للإستخدام في طبقات الردم لجسر القطاع الكهربائي

مصدر العينة : عند المحطة / مشون 181+000

- المندوبين : وقد تم توريد العينة بمعرفة م/محمود الحيني. (مهندس الأشراف مكتب د/حسن مهدي)

بتاريخ : 2023/11/29

- بيانات المندوبين : رقم الهاتف = 01090944342

اسم المشروع : مشروع القطر الكهربائي السريع (القطاع الثاني) - (بني مزار - منقوط)

تتبعه : العينة مسوية من احضرها

وقد تم عمل الاختبارات الآتية :

1-التحرج الحبيبي

2-حد السيولة واللدونة

3-اختبار البروكتور

4-اختبار CBR

5-اختبار المواد العضوية

وكانت نتائج الاختبارات كالآتي :

م	نوع الاختبار	النتائج	حدود القبول والرفض طبقا للمواصفات
1	تصنيف التينة	A-1-b	(A-1-a) - (A-1-b) - (A-2-4)
2	نسبة الماء من منخل 200	12.80%	لا تزيد عن (15 %)
3	مجال اللدونة	NP	(A-1-a or A-1-b = 6 max) (A-2-4 = 10 max)
4	أقصى كثافة جافة (البروكتور) yd max	2.139 gm/cm3	لا تقل عن 1.88 gm/cm3
5	نسبة المياه الأصلية	6.1 %	-
6	قيمة CBR المقررة	28.00%	لا تقل عن 20%
8	المواد العضوية	لا يوجد	لا تزيد عن 1%

و بمقارنة نتائج العينة بمواصفات مشروع القطر السريع فهي صالحة للاستخدام في طبقات الردم

بمعدن

مهندس المعمل

مهندس المعمل

التوقيع

مشروع :

قطار اسوان الكهربائي السريع - القطاع الثاني

استشاري أبحاث التربة والاساسات :
أ.د.م. هشام محمد حلمي



تقرير بنتائج اختبارات صلاحية أترية للتأسيس

مقدمة : تم إعداد هذا التقرير بناء على طلب شركة /أوفيك

وذلك لتحديد خصائص ومدى صلاحية عينة تراب للإستخدام في طبقات الردم لجسر للقطار الكهربائي

مصدر العينة: عند المسطة / مشون 181+200

- المتدوين: وقد تم توريد العينة بمعرفة م/ محمود رشدي. (مهندس الإشراف مكتب د/حسن مهدي)

بتاريخ: 2023/12/3

- بيانات المتدوين: رقم الهاتف = 01121481281

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منقلوط)

تتبعه : العينة مسؤولة من إضرها

وقد تم عمل الاختبارات الآتية :

1- التدرج الحبيبي

2- حد السيولة واللدونة

3- إختبار البروكتور

4- إختبار CBR

5- إختبار المواد العضوية

وكلت نتائج الاختبارات كالتالي :

م	نوع الإختبار	النتائج	حدود القبول والرفض طبقا للمواصفات
1	تصنيف العينة	A-1-b	(A-1-a) - (A-1-b) - (A-2-4)
2	نسبة الماء من مئخل 200	13.90%	لا تزيد عن (15 %)
3	مجال اللدونة	NP	(A-1-a or A-1-b = 6 max) (A-2-4 = 10 max)
4	أقصى كثافة جافة (البروكتور) yd max	2.141 gm/cm3	لا تقل عن 1.88 gm/cm3
5	نسبة المياه الأمولية	6.5 %	-
6	قيمة CBR المعنوية	27.00%	لا تقل عن 20%
8	المواد العضوية	لا يوجد	لا تزيد عن 1%

و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للإستخدام في طبقات الردم

بمعد"

مهندس المعمل
م/ التوقيع

مهندس المعمل

م/ التوقيع

استشاري أبحاث التربة والاماسات :
أ.د.م. هشام محمد حلمي



مشروع :
قطار اسوان الكهربائي السريع - القطاع الثاني

تقرير بنتائج اختبارات صلاحية أتربة للتأسيس

مقدمة : تم إصدار هذا التقرير بناءا على طلب شركة /اوديكا

وذلك لتحديد خصائص ومدى صلاحية هيئة تراب للإستخدام في طبقات الردم لجسر القطار الكهربائي

مصدر العينة: عند المحطة / مشون $181+2^{\circ}$

- المتلوبي: وقد تم توريد العينة بمعرفة م/ محمود رشدي. (مهندس الأشراف مكتب د/حسن مهدي)

بتاريخ: 20223/12/12

- بيانات المتلوبي: رقم الهاتف = 01121461281

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفلوط)

تبيه : العينة مسؤولة من أحضرها

وقد تم عمل الاختبارات الآتية :

- 1-الترج الحبيبي
- 2-حد السيولة واللدونة
- 3-إختبار البروكتور
- 4-إختبار CBR
- 5-إختبار المواد العضوية

وكذلك نتائج الاختبارات كالآتي :

م	نوع الإختبار	النتائج	حدود القبول والرفض طبقا للمواصفات
1	تصنيف الهيئة	A-1-b	(A-1-a) - (A-1-b) - (A-2-4)
2	نسبة الماء من سائل 200	13.40%	لا تزيد عن (15 %)
3	مجال اللدونة	NP	(A-1-a or A-1-b = 6 max) (A-2-4 = 10 max)
4	القصي كثافة جافة (البروكتور) yd max	2.131 gm/cm3	لا تقل عن 1.88 gm/cm3
5	نسبة الماء الأسرولية	6.4 %	-
6	قيمة CBR المنصورة	27.90%	لا تقل عن 20%
8	المواد العضوية	لا يوجد	لا تزيد عن 1%

• و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للاستخدام في طبقات الردم

يعتمد***

محمد زيان مدير
مكتب

مهندس المعمل
التوقيع

استشاري أبحاث التربة والاساسات :
أ.د.م. هشام محمد حاملي



مشروع :
قطار اسوان الكهربائي السريع - القطاع الثاني

تقرير بنتائج اختبارات صلاحية أحربة للناسيس

مقدمة : تم إعداد هذا التقرير بناءا علي طلب شركة /أونيك

وذلك لتحديد خصائص ومدي صلاحية عينة تراب للإستخدام في طبقات الردم لجسر التملار الكهربائي

مصدر العينة: عند المحطة / مشون 18L4000

- المقنن : وقد تم توريد العينة بمعرفة م/ محمود رشدي. (مهندس الأشراف مكتب داهسن مهدي)

بتاريخ: 2023/12/21

- بيانات المتكويين: رقم الهاتف = 01121461281

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفلوط)

تلييه : العينة مسوية من احضرها

وقد تم عمل الاختبارات الآتية :

- 1-الترج الحبيبي
- 2-محد السيونة واللدونة
- 3-إختبار البروكتور
- 4-إختبار CBR
- 5-إختبار المواد العضوية

وكالت نتائج الاختبارات كالتالي :

م	نوع الإختبار	النتائج	حدود القبول والرفض طبقا للمواصفات
1	تصنيف العينة	A-1-b	(A-1-a) - (A-1-b) - (A-2-4)
2	نسبة الماء من مخل 200	14.2%	لا تزيد عن (15 %)
3	محد اللدونة	NP	(A-1-a or A-1-b = 6 max) (A-2-4 = 10 max)
4	أقصى كثافة جافة (البروكتور) yd max	2.143 gm/cm3	لا تقل عن 1.88 gm/cm3
5	نسبة المياه الأموية	6.1 %	--
6	قيمة CBR المقصورة	30.00%	لا تقل عن 20%
8	المواد العضوية	لا يوجد	لا تزيد عن 1%

و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للاستخدام في طبقات الردم

بمعد

احمد محمد عطية

مهندس المعمل

التوقيع

استشاري أبحاث التربة والاساسات :
أ.د.م. هشام محمد حلمي



مشروع :
قطار اسوان الكهربائي السريع - القطاع الثاني

تقرير بنتائج اختبارات صلاحية أترية التأسيس

مقدمة : تم إعداد هذا التقرير بناءا علي طلب شركة /اوديك

وذلك لتحديد خصائص ومدي صلاحية هيئة تراب للاستخدام في طبقات الردم لجسر القطار الكهربائي

مصدر العينة: عند المحطة / مشون $L8L + 200$

- المتدوين: وقد تم توريد العينة بمعرفة م/ محمود رشدي. (مهندس الاشراف مكتب د/حسن مهدي)

بتاريخ: 2023/12/31

- بيانات المتدوين: رقم الهاتف = 01121461281

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منقلاوط)

تتيه : العينة مسوية من احضرها

وقد تم عمل الاختبارات الآتية :

- 1-النتروج الحبيبي
- 2-حد السيولة واللدونة
- 3-اختبار البروكتور
- 4-اختبار CBR
- 5-اختبار المواد العضوية

وكانت نتائج الاختبارات كالآتي :

م	نوع الاختبار	النتائج	حدود القبول والرفض طبقا للمواصفات
1	تصنيف الهيئة	A-1-b	(A-1-a) - (A-1-b) - (A-2-4)
2	نسبة الماء من منخل 200	13.4%	لا تزيد عن (15 %)
3	مجال اللدونة	NP	(A-1-a or A-1-b = 6 max) (A-2-4 = 10 max)
4	أقصى كثافة جافة (البروكتور) yd max	2.147 gm/cm3	لا تقل عن 1.88 gm/cm3
5	نسبة المياه الأموية	6.0 %	--
6	قيمة CBR المنمورة	29.7%	لا تقل عن 20%
8	المواد العضوية	لا يوجد	لا تزيد عن 1%

و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للاستخدام في طبقات الردم

بمقدم

أحمد محمد عطيه

مهندس المعمل

التوقيع



تقرير بنتائج اختبارات صلاحية أتربة للتأسيس

مقدمة : تم إعداد هذا التقرير بناء على طلب شركة /أوديك

وذلك لتحديد خصائص ومدى صلاحية حينة تراب للاستخدام في طبقات الردم لجسر الشطار الكهربائي

مصدر العينة : عند المحطة / 181+000

- المندوبين : وقد تم توريد العينة بمعرفة م/محمود رشدي. (مهندس الأشراف مكتب د/حسن مهدي)

بتاريخ : 2024/1/4

- بيانات المندوبين : رقم الهاتف = 01150014987

اسم المشروع : مشروع الشطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منقوطة)

تتبعه : العينة مسؤولة من أحضرها

وقد تم عمل الاختبارات الآتية :

- 1-التدرج الحبيبي
- 2-محد السيولة واللدونة
- 3-إختبار البروكتور
- 4-إختبار CBR
- 5-إختبار المواد العضوية

وكلفت نتائج الاختبارات كالآتي :

م	نوع الإختبار	النتائج	حدود القبول والرفض طبقا للمواصفات
1	تصنيف العينة	A-1-b	(A-1-a) - (A-1-b) - (A-2-4)
2	نسبة الماء من منخل 200	12.30%	لا تزيد عن (15 %)
3	مجال اللدونة	NP	(A-1-a or A-1-b = 6 max) (A-2-4 = 10 max)
4	أقصى كثافة جافة (البروكتور) yd max	2.141 gm/cm3	لا تقل عن 1.88 gm/cm3
5	نسبة المياه الأصولية	6.1 %	--
6	قيمة CBR المغسورة	32.00%	لا تقل عن 20%
8	المواد العضوية	لا يوجد	لا تزيد عن 1%

• و بمقارنة نتائج العينة بمواصفات مشروع الشطار السريع فهي صالحة للاستخدام في طبقات الردم

يعتمد

أ.د.م. هشام محمد حلمي

مهندس المعمل

التوقيع



تقرير نتائج اختبارات صلاحية أتربة للتأسيس

مقدمة : تم إعداد هذا التقرير بناءً على طلب شركة /أوديك

وذلك، لتحديد خصائص ومدي صلاحية عينة تراب للاستخدام في طبقات الردم لجسر القطار الكهربائي

مصدر العينة : عند المحطة /مثنون (180+000)

- المندوبين : وقد تم توريد العينة بمعرفة م/محمود رشدي. (مهندس الإشراف مكتب د/حسن مهدي)

بتاريخ : 2024/1/8

- بيانات المندوبين : رقم الهاتف = 01150014987

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفلوط)

تنبيه : العينة مسؤولة من احضرها

وقد تم عمل الاختبارات الآتية :

- 1-التدرج الحبيبي
- 2-حد السيولة واللدونة
- 3-إختبار البروكتور
- 4-إختبار CBR
- 5-إختبار المواد العضوية

وكفت نتائج الاختبارات كالاتي :

م	نوع الإختبار	النتائج	حدود القبول والرفض طبقاً للمواصفات
1	تصنيف العينة	A-1-b	(A-1-a) - (A-1-b) - (A-2-4)
2	نسبة الماء من مختل 200	13.00%	لا تزيد عن (15 %)
3	مجال اللدونة	NP	(A-1-a or A-1-b = 6 max) (A-2-4 = 10 max)
4	أقصى كثافة جافة (البروكتور) γd max	2.143 gm/cm3	لا تقل عن 1.88 gm/cm3
5	نسبة المياه الأصولية	6.4 %	—
6	قيمة CBR المغمورة	30.00%	لا تقل عن 20%
8	المواد العضوية	لا يوجد	لا تزيد عن 1%

• و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للاستخدام في طبقات الردم

يعتمد ""

أ.د.م. هشام محمد حلمي

مهندس المعمل

أ.م.م. /
التوقيع



تقرير بنتائج اختبارات صلاحية أتربة للتأسيس

مقدمة : تم إعداد هذا التقرير بناءا علي طلب شركة /إوريدك

وذلك لتحديد خصائص ومدي صلاحية عينة تراب للإستخدام في طبقات الردم لجسر القطاع الكهربائي

بصدر العينة: عند المحطة / محجر بشار المعمار (مكتب جامعة النيل)

المتدوين: وقد تم توريد العينة بمعرفة م/ محمود رشدي. (مهندس الإشراف مكتب د/حسن مهدي)

بتاريخ: 2024/1/8

بيانات المتدوين: رقم الهاتف = 01121461281

سم المشروع : مشروع القطاع الكهربائي السريع (القطاع الثاني) - (بني مزار - منقلاوط)

لبيه : العينة ممولة من احضرها

قد تم عمل الاختبارات الآتية :

- 1-الترج الحبيبي
- 2-حد السيولة واللدونة
- 3-اختبار البروكتور
- 4-اختبار CBR
- 5-اختبار المواد العضوية

وكانت نتائج الاختبارات كالآتي :

م	نوع الاختبار	النتائج	حدود القبول والرفض طبقا للمواصفات
1	تصنيف العينة	A-1-b	(A-1-a) - (A-1-b) - (A-2-4)
2	نسبة الماء من مئثل 200	13.90%	لا تزيد عن (15 %)
3	مجال اللدونة	NP	(A-1-a or A-1-b = 6 max) (A-2-4 = 10 max)
4	أقصى كثافة جافة (البروكتور) yd max	2.141 gm/cm3	لا تقل عن 1.88 gm/cm3
5	نسبة الماء الأمولة	6.5 %	-
6	قيمة CBR المنصورة	27.00%	لا تقل عن 20%
8	المواد العضوية	لا يوجد	لا تزيد عن 1%

• و بمقارنة نتائج العينة بمواصفات مشروع القطاع السريع فهي صالحة للاستخدام في طبقات الردم

محمد علي السيد

مهندس المحمل
/م
التوقيع

يتمتع



تقرير بنتائج إختبارات صلاحية أتربة للتأسيس

مقدمة : تم إعداد هذا التقرير بناءا على طلب شركة / اوريدك

وذلك لتحديد خصائص ومدي صلاحية عينة تراب للإستخدام في طبقات الردم لجسر النطار الكهربائي

بصدر العينة : عند المحطة / محجر يسار المسار (مكبسي بجامعة الشاذلي)

- المندوب : وقد تم توريد العينة بمعرفة م/ محمود الحيني. (مهندس الإشراف مكتب د/حسن مهدي)

بتاريخ : 2024/1/18

- بيانات المندوب : رقم الهاتف = 01090944342

إسم المشروع : مشروع النطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفلوط)

تتبعه : العينة مسولية من احضرها

وقد تم صل الإختبارات الآتية :

- 1-الترج الحبيبي
- 2-حد السيولة واللدونة
- 3-إختبار البروكتور
- 4-إختبار CBR
- 5-إختبار المواد العضوية

وكانت نتائج الإختبارات كالآتي :

م	نوع الإختبار	النتائج	حدود القبول والرفض طبقا للمواصفات
1	تصنيف العينة	A-1-b	(A-1-a) - (A-1-b) - (A-2-4)
2	نسبة الماء من منخل 200	12.80%	لا تزيد عن (15 %)
3	سحل اللدونة	NP	(A-1-a or A-1-b = 6 max) (A-2-4 = 10 max)
4	أقصى كثافة جافة (البروكتور) yd max	2.139 gm/cm3	لا تقل عن 1.88 gm/cm3
5	نسبة المياه الأمولية	6.1 %	-
6	قيمة CBR المغمورة	28.00%	لا تقل عن 20%
8	المواد العضوية	لا يوجد	لا تزيد عن 1%

و بمقارنة نتائج العينة بمواصفات مشروع النطار السريع فهي صالحة للاستخدام في طبقات الردم

محمد شادي حسيدي

مهندس المعمل
/م
التوقيع

يتمتع



مركز الاستشارات الهندسية
Engineering Consultation Center
معمل الطرق والمطارات
Highway & Airport Lab



رؤية الكلية : تسعى الكلية إلى أن تكون مؤسسة تعليمية وباحثة عالية الجودة متميزة بتقديم خدمات مجتمعية للتنمية البيئية والتعليمية

تقرير بنتائج اختبارات صلاحية تربة زلطية (عينة ١)

مقدمة : تم إعداد هذا التقرير بناء على طلب / الهيئة العامة للطرق والكبارى ، وذلك لتحديد خصائص ومحتوى صلاحية عدد واحد عينة تربة زلطية للاستخدام فى جسر مشروع القطار الكهربائى السريع - الخط الثانى (بني مزار - منفلوط) .

مصدر العينة : عند المحطة Sta. 181+100 ، (مشون)

المنسوب : وقد تم توريد العينة بمعرفة م/ محمد شلبى عيد عن الاستشارى الى معمل هندسة الطرق بـ جامعة المنيا

توصيف العينات : العينات عبارة عن تربة حبيبية (تربة زلطية) ...

وقد تم عمل الاختبارات الاتية : ١- التدرج الحبيبي ٢- حد السيولة واللدونة ٣- التصنيف ٤- اختبار البروكتور المعدل و ال C. B. R .

مقابلة : شركة اوديك :: الرقم المرجعي : ٩٣٣٢٤٦٠٣٤١

١- التدرج الحبيبي :

حجم المنخل	٥ بوصة	٤ بوصة	٢,٥	١,٥	٤/٣	رقم ٤	رقم ١٠	رقم ٤٠	أقل من ٢٠٠
المار %	١٠٠	١٠٠	١٠٠	٨٨	٧٦	٥٦	٤٣	٢٥	٩

٢- حد السيولة وحد اللدونة

م	نوع الاختبار	النتائج	مواصفات المشروع
١	حد السيولة	٢٢ %	لا تزيد عن ٢٥ %
٢	مجال اللدونة	٣,٠ %	لا تزيد عن ٦ %
٣	المواد العضوية	لا يوجد	غير مسموح

٣- التصنيف : تم تصنيف التربة طبقاً لنظام الأشتر (AASHTO) وقد وجدت التربة تقع فى الفئة A-1-a وهى عبارة عن تربة حبيبية ولا تحتوى على مواد عضوية.

٤- اختبار الدمك (بروكتور المعدل) و اختبار ال CBR

الاختبار	النتائج	مواصفات المشروع
القصي كثافته جافه yd max	٢,١٤ جم / سم ^٣	لا تقل عن ١,٨٥ جم/سم ^٣
نسبة المياه الاصوليه OMC	٥,٣٠ %	—
قيمة CBR المغمورة	٤٠ %	لا تقل عن ١٥ % L-EMB او ٢٠ % U-EMB
نسبة الانتفاش	٠,٠	غير مسموح

• تقارن النتائج بالشروط الخاصة بالعملية

• التربة تصلح للاستخدام فى ال Up- Embankment و Over Embankment

فنى المعمل مشرف المعمل

أ/ محمد حمدي د/ حمدي بلبع

مركز الاستشارات الهندسية

مركز الاستشارات الهندسية

مركز الاستشارات الهندسية

مركز الاستشارات الهندسية

مركز الاستشارات الهندسية

مركز الاستشارات الهندسية

مركز الاستشارات الهندسية



تقرير بنتائج اختبارات صلاحية أتربة للتأسيس

مقدمة : تم إعداد هذا التقرير بناء على طلب شركة /الوثيرك

وذلك لتحديد خصائص ومدي صلاحية عينة تراب للاستخدام في طبقات الردم لجسر القنطرة الكهربائي

مصنر العينة : عند المحطة /مشون (180+100)

- المندوبين : وقد تم توريد العينة بمعرفة م/محمود رشدي. (مهندس الإشراف مكتب د/حسن مهدي)

بتاريخ : 2024/2/7

- بيانات المندوب : رقم الهاتف = 01150014987

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفلوط)

تنبيه : العينة مسؤولة من احضرها

وقد تم عمل الاختبارات الآتية :

- 1- التدرج الحبيبي
- 2- حد السيولة واللدونة
- 3- اختبار البركتور
- 4- اختبار CBR
- 5- اختبار المواد العضوية

وكانت نتائج الاختبارات كالآتي :

م	نوع الاختبار	النتائج	حدود القبول والرفض طبقا
1	تصنيف العينة	A-1-b	(A-1-b) - (A-2-4)
2	نسبة الماء من منخل 200	11.4%	لا تزيد عن (%)
3	مجال اللدونة	NP	A-1-b = 6 max) I = 10 max)
4	لغسي كثافة جافة (البركتور) yd max	2.138 gm/cm3	لا تقل عن n/cm3
5	نسبة المياه الأمولية	6.0 %	-
6	قيمة CBR المنغورة	35.00%	لا تقل عن %
8	المواد العضوية	لا يوجد	لا تزيد عن %

• و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للاستخدام في طبقات الردم

أحمد حسن علي

مهندس المعمل

التوقيع



رؤية الكلية : تسعى الكلية إلى أن تكون مؤسسة تعليمية وباحثة عالية الجودة متميزة بتقديم خدمات مجتمعية لتنمية البيئة المحيطة

تقرير نتائج اختبارات صلاحية تربة زلطية (عينة ٢)

مقدمة : تم إعداد هذا التقرير بناء على طلب / الهيئة العامة للطرق والكبارى ، وذلك لتحديد خصائص صلاحية عدد واحد عينة تربة زلطية للاستخدام فى جسر مشروع القطار الكهربائى السريع - الخط المزدوج (بنى مزار - منفطوط) .
مصدر العينة : عند المحطة Sta. 181+200 (مشون)
المندوب : وقد تم توريد العينة بمعرفة م/ محمد شلبي عيد عن الاستشارى الى معمل هندسة الطرق بكلية الهندسة - جامعة المنيا
توصيف العينات : العينات عبارة عن تربة حبيبية (تربة زلطية) ...
وقد تم عمل الاختبارات الآتية : ١- التدرج الحبيبي ٢- حد السيولة واللدونة ٣- التصنيف ٤- اختبار البروكور المعدل و ال C. B. R .

الرقم المرجعي : ٩٣٣٢٤٦٠٣٤١ :::

مقابلة : شركة اوديك

١- التدرج الحبيبي :

حجم المنخل	٥ بوصة	٤ بوصة	٢,٥	١,٥	٤/٣	رقم ٤	رقم ١٠	رقم ٤٠	م ٢٠٠
المار %	١٠٠	١٠٠	١٠٠	٨٥	٧٤	٥٩	٤٧	٣١	١١

٢- حد السيولة وحد اللدونة

م	نوع الاختبار	النتائج	مواصفات المشروع
١	حد السيولة	٢٣ %	لا تزيد عن ٢٥ %
٢	مجال اللدونة	٣,٠ %	لا تزيد عن ٦ %
٣	المواد العضوية	لا يوجد	غير مسموح

٣- التصنيف : تم تصنيف التربة طبقا لنظام الأشتو (AASHTO) وقد وجدت التربة تقع فى المجموعة A-1-b وهي عبارة عن تربة حبيبية ولا تحتوى على مواد عضوية.

٤- اختبار الدمك (بروكور المعدل) و اختبار ال CBR

الاختبار	النتائج	مواصفات المشروع
أقصى كثافة جافه yd max	٢,١٥ جم / سم ^٣	لا تقل عن ١,٨٥ جم/سم ^٣
نسبة المياه الاصولية OMC	٥,٤٠ %	---
قيمة CBR المغموره	٤٣ %	لا تقل عن ١٥ % L-EMB او ٢٠ % U-EMB
نسبة الانقماش	١,١	غير مسموح

• تقارن النتائج بالشروط الخاصة بالعملية

• التربة تصلح للاستخدام فى ال Upper Embankement & Lower Embankement

فنى المعمل
مشرف المعمل
د/ محمد حمدي
د/ محمد حمدي
يتمتع
مركز الاستشارات الهندسية
مركز الاستشارات الهندسية
مركز الاستشارات الهندسية



تقرير بنتائج اختبارات صلاحية أتربة للتأسيس

مقدمة : تم إعداد هذا التقرير بناءً على طلب شركة /أوديك/ وذلك لتحديد خصائص ومدي صلاحية عينة تراب للاستخدام في طبقات الردم لجسر القطار الكهربائي

مصدر العينة : عند المحطة بمشون (180+100)

- المندوبين : وقد تم توريد العينة بعرفة م/محمود رشدي. (مهندس الأشراف مكتب د/حسن مهدي)

بتاريخ : 2024/2/8

- بيانات المندوبين : رقم الهاتف = 01150014987

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منقلاوط)

تبنيه : العيلة مسؤولة من احضرها

وقد تم عمل الاختبارات الآتية :

- 1- التدرج السبيبي
- 2- حد السيولة واللدونة
- 3- اختبار البرونكتور
- 4- اختبار CBR
- 5- اختبار المواد العضوية

وكانت نتائج الاختبارات كالآتي :

م	نوع الاختبار	النتائج	حدود القبول والرفض طبقاً
1	تصنيف العينة	A-1-b	(A-1-b) - (A-2-4)
2	نسبة الماء من مئخل 200	10.1%	لا تزيد عن (6)
3	مجال اللدونة	NP	A-1-b = 6 max) l = 10 max)
4	أقصى كثافة جافة (البرونكتور) yd max	2.136 gm/cm3	لا تقل عن n/cm3
5	نسبة المياه الأموية	6.5 %	--
6	قيمة CBR المنمورة	35.00%	لا تقل عن %
8	المواد العضوية	لا يوجد	لا تزيد عن 6

• و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للاستخدام في طبقات الردم

مهندس المعمل

الم
التوقيع

الم
التوقيع



تقرير بنتائج اختبارات صلاحية أتربة للتأسيس

مقدمة : تم إعداد هذا التقرير بناء على طلب شركة /أوليك

وذلك لتحديد خصائص ومذي صلاحية عينة تراب للإستخدام في طبقات الردم لجسر القطار الكهربائي

مصدر العينة : عند المحطة بمشون (181+200)

- المندوب: وقد تم توريد العينة بمعرفة م/محمود رشدي. (مهندس الأشراف مكتب د/حسن مهدي)

تاريخ : 2024/2/20

- بيانات المندوب: رقم الهاتف = 01150014987

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفوط)

تبنيه : العينة مسؤولة من حضرها

وقد تم عمل الاختبارات الآتية :

- 1-الترج الحبيبي
- 2-حد السيولة واللدونة
- 3-إختبار البركتور
- 4-إختبار CBR
- 5-إختبار المواد العضوية

وكانت نتائج الاختبارات كالآتي :

م	نوع الإختبار	النتائج	حدود القبول والرفض طبقاً
1	تصنيف العينة	A-1-b	(A-1-b) - (A-2-4)
2	نسبة الماء من متخل 200	13.1%	لا تزيد عن 6%
3	مجال اللدونة	NP	A-1-b = 6 max) (= 10 max)
4	أقصى كثافة جافة (البركتور) yd max	2.147 gm/cm3	لا تقل عن 1/cm3
5	نسبة المياه الأمولية	6.3 %	--
6	قيمة CBR المغمورة	38.00%	لا تقل عن %
8	المواد العضوية	لا يوجد	لا تزيد عن %

و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للاستخدام في طبقات الردم

استدعته
م/م

مهندس المعمل

م/م
التوقيع



تقرير بنتائج اختبارات صلاحية أتربة للتأسيس

مقدمة : تم إعداد هذا التقرير بناءً على طلب شركة /لوديك

وذلك لتحديد خصائص ومدي صلاحية عينة تراب للاستخدام في طبقات الردم لجسر القطار الكهربائي

مصدر العينة : عند المحطة لمشون (180+200)

- المندوبين : وقد تم توريد العينة بمعرفة م/محمود رشدي. (مهندس الإشراف مكتب د/حسن مهدي)

بتاريخ : 2024/2/21

- بيانات المندوبين : رقم الهاتف = 01150014987

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفلوط)

تتبع : العينة مسؤولة من احضرها

وقد تم عمل الاختبارات الآتية :

- 1-الترج الحبيبي
- 2-حد السيولة واللدونة
- 3-اختبار البروكتور
- 4-اختبار CBR
- 5-اختبار المواد العضوية

وكانت نتائج الاختبارات كالآتي :

م	نوع الاختبار	النتائج	حدود القبول والرفض طبة
1	تصنيف العينة	A-1-b	(A-1-b) - (A-2-4)
2	نسبة الماء من مختل 200	13.8%	لا تزيد عن (6 max)
3	مجال اللدونة	NP	A-1-b = 6 max) = 10 max)
4	أقصى كثافة جافة (البروكتور) γd max	2.146 gm/cm3	لا تقل عن 1/cm3
5	نسبة الماء الأصولية	6.5 %	--
6	قيمة CBR المقصورة	37.6%	لا تقل عن %
8	المواد العضوية	لا يوجد	لا تزيد عن 6

• و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للاستخدام في طبقات الردم

أ.د.م. هشام محمد علي

مهندس المعمل
أ.م.م. النوفع



تقرير بنتائج اختبارات صلاحية أترية للتأسيس

مقدمة : تم إعداد هذا التقرير بناء على طلب شركة /أوديك
وذلك لتحديد خصائص ومدى صلاحية عينة تراب للإستخدام في طبقات الردم لجسر القطار الكهربائي
مصدر العينة : عند المحطة لمشون (180+200)
- المندوب: وقد تم توريد العينة بمعرفة م/محمود رشدي. (مهندس الاشراف مكتب د/حسن مهدي)

بتاريخ : 2024/2/26

- بيانات الملفين: رقم الهاتف = 01150014987
اسم المشروع : مشروع لقطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منقلاوط)
تنبيه : العينة مسؤولة من احضرها

وقد تم عمل الاختبارات الآتية :

- 1- التدرج الحبيبي
- 2- حد السيولة واللدونة
- 3- اختبار البرونكتور
- 4- اختبار CBR
- 5- اختبار المواد العضوية

وكالت نتائج الاختبارات كالاتي :

م	نوع الاختبار	النتائج	حدود القبول والرفض طبق
1	تصنيف العينة	A-1-b	(A-1-b) - (A-2-4)
2	نسبة الماء من منخل 200	14.1%	لا تزيد عن (6)
3	مجال اللدونة	NP	A-1-b = 6 max) = 10 max)
4	أقصى كثافة جافة (البرونكتور) yd max	2.146 gm/cm3	لا تقل عن n/cm3
5	نسبة المياه الأموية	6.2 %	-
6	قيمة CBR المنمورة	34.5%	لا تقل عن %
8	المواد العضوية	لا يوجد	لا تزيد عن %

و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للاستخدام في طبقات الردم

أ.د.م. هشام محمد

مهندس المعمل
التوقيع



تقرير بنتائج اختبارات صلاحية أتربة للتأسيس

مقدمة : تم إعداد هذا التقرير بناءاً على طلب شركة /أوديك وذلك لتحديد خصائص وسدي صلاحية هيئة تراب للاستخدام في طبقات الردم لجسر القطار الكهربائي

مصدر العينة : عند المحطة /مشون (180+100)

- المندوب: وقد تم توريد العينة بمعرفة م/محمود رشدي. (مهندس الأشراف مكتب د/حسن مهدي)

بتاريخ : 2024/3/4

- بيانات المندوب: رقم الهاتف = 01150014987

إسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفلوط)

تتبعه : العينة مسؤولة من أحضرها

وقد تم عمل الاختبارات الآتية :

- 1-الدرجة الحبيبي
- 2-حد السيولة واللدونة
- 3-اختبار البروكتور
- 4-اختبار CBR
- 5-اختبار المواد العضوية

وكانت نتائج الاختبارات كالآتي :

م	نوع الاختبار	النتائج	حدود القبول والرفض طبقاً
1	تصنيف العينة	A-1-b	(A-1-b) - (A-2-4)
2	نسبة الماء من مخل 200	13.00%	لا تزيد عن (6)
3	مجال اللدونة	NP	A-1-b = 6 max) = 10 max)
4	أقصى كثافة جافة (البروكتور) γd max	2.134 gm/cm3	لا تقل عن 1/cm3
5	نسبة المياه الأموية	6.4 %	--
6	قيمة CBR المغمورة	32.6%	لا تقل عن %
8	المواد العضوية	لا يوجد	لا تزيد عن 6

و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للاستخدام في طبقات الردم

أ.د.م. هشام محمد علي

مهندس المعمل
م
التوقيع



W.F. CHEN ET AL.

کتابخانه



اختار أسوان الكرويكي المديح - للطاقم الفني

Determination of field density - ASTM D 1556

Request no.:		From	180+000	to	181+100	Company	ODIK
Station :			Level		- 3.50	DATE	02/04/2024
Description :	FILL LAYER						

Proctor Modified Testing Results:-

Max. dry density (g/cm ³)	O.M.C. %	Degree of Compaction Required %	Bulk Density of Specified sand (g/cm ³)	Sand Weight of Cone (gm)
2.134	8.4	86	1.480	1343

Test No.	1		2		3		4		5		6					
Station of sample	180+860		180+920		180+960		180+985		181+030		181+080					
Wt. Of Sand before test,gm	10280		10155		10000		9910		9835		9715					
Wt. Of Sand after test,gm	7228		7017		6855		6846		6774		6642					
Wt. Of Sand fill hole&cone,gm	3054		3138		3045		3064		3061		3073					
Wt. Of Sand fill cone,gm	1440		1440		1440		1440		1440		1440					
Wt. Of Sand fill hole,gm	1614		1698		1602		1624		1621		1633					
Volume of hole,cm ³	1091		1147		1082		1097		1095		1103					
Wt of sample from hole,gm	2360		2495		2354		2375		2360		2400					
Wet density of soil,gm/cm ³	2.154		2.175		2.176		2.164		2.155		2.178					
No. of container	1	2	3	4	5	6	7	8	9	10	11	12				
Wt. of container,gm	82.4	82.2	82.3	82.5	82.4	82.3	82.4	80.3	81.4	80.7	82.4	81.1				
Wt. Of sample& container before drying,gm	332.5	332.9	346.5	348.9	332.9	310.5	315.7	320.2	342.0	337.9	341.7	330.0				
wt. of container& dried sample,gm	318.3	318.3	331.3	333.2	318.8	295.9	301.7	306.3	327.5	323.7	346.5	314.9				
Water wt.	14.2	14.6	15.2	15.7	14.1	14.6	14.0	13.9	14.5	14.2	15.2	15.1				
Wt. of dried sample,gm	255.9	255.1	269.0	270.7	254.4	233.6	239.3	245.0	256.1	253.0	284.1	253.8				
Moisture content,%	5.55	5.70	5.65	5.80	6.80	6.25	5.85	5.65	5.45	5.40	5.35	5.95				
Average moisture content%	5.6		5.7		5.9		5.8		5.4		5.7					
Dry density,gm/cm ³	2.049		2.057		2.055		2.047		2.044		2.059					
Compaction (%)	96.00%		95.40%		96.30%		95.90%		95.80%		96.50%					
Acceptance	Y		Y		Y		Y		Y		Y					

شركة اودي
للتوريدات والمقاولين
M.E CONTRACTOR
س. ش. م. ع.
٢٠١٠ - ٢٠١١

Abstract

محمود حسن

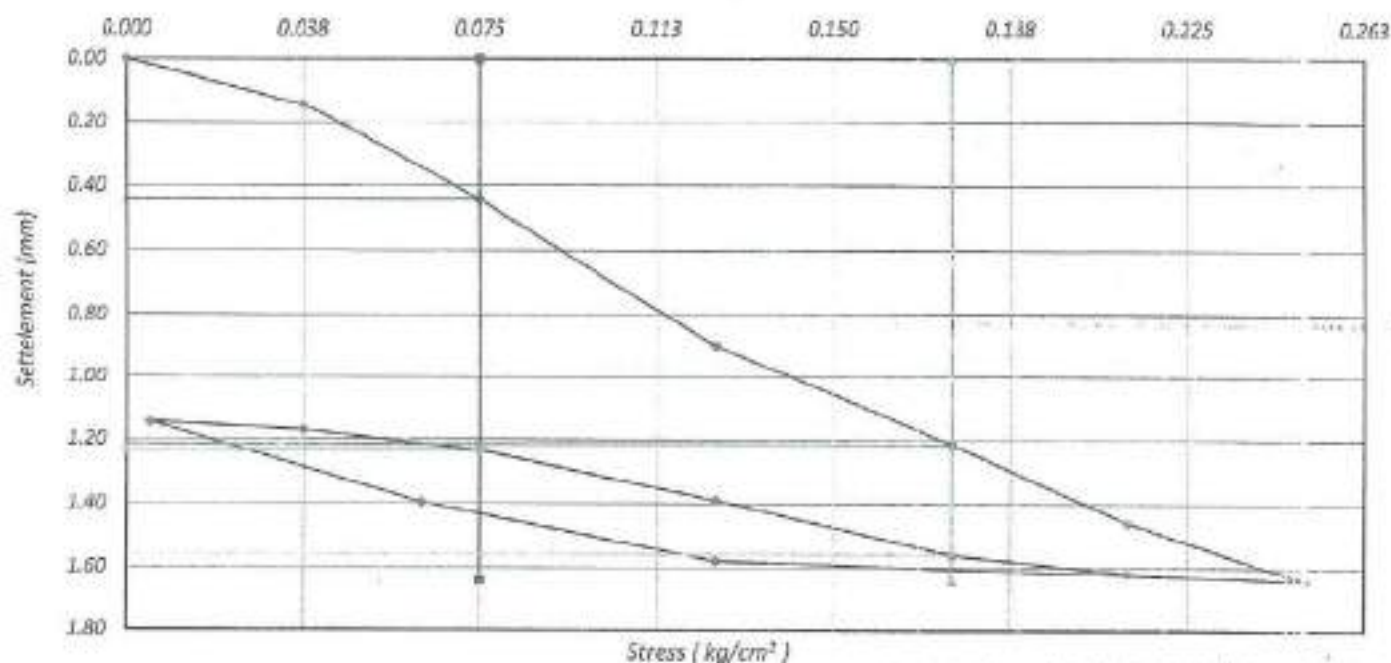


PLATE LOADING TEST RESULTS

PROJECT : القطار الكهربائي السريع (التتويج - أسوان) - قطاع التتويج (بني مزار - منقلاوط)

ST. :	181+260	181+400	Plate Diam. :	60 cm	
level :	-1.5	Location :	181+315	Company :	أوديكا
Date :	Monday	Date :	1/Apr/2024	Soil :	embankment

Stress - Settlement Relationship



	Load (ton)	Stress (M Pa)	Settlement (mm)
Loading	0.00	0.000	0.00
	1.06	0.038	0.14
	2.12	0.075	0.45
	3.54	0.125	0.90
	4.95	0.175	1.22
	6.01	0.213	1.46
	7.07	0.250	1.65
Unloading	3.54	0.125	1.58
	1.77	0.063	1.40
	0.14	0.005	1.15
Loading	1.06	0.038	1.17
	2.12	0.075	1.24
	3.54	0.125	1.39
	4.95	0.175	1.56
	6.01	0.213	1.62

σ_{max}	0.250	Stress (M Pa)	Settlement (mm)
0.30 σ_{max} reloading	0.075		1.24
0.70 σ_{max} reloading	0.175		1.56

$$E_{vd} = 138 \text{ MPa}$$

EV2	138
Specification	Ev2 ≥ 40
Acceptance	Y

مهندس استشاري
شركة استشارية
م. ت. ٨٩٨٤٥٠
م. ت. ٢٣٠٥٢٣٣٩





ECSCO

Egyptian Geotech. & Struc.

Dr. Eng. Hesham M. Helmy



الهيئة القومية للإنفاق



PLATE LOADING TEST RESULTS


PROJECT : القطار الكهربائي السريع (لتكوير - أسوان) - القطاع الثاني (بني مرز - منقوت)

ST : 181+260 181+460 Plate Dim. : 60 cm

Level : -1.5 Location : 181+425 Company : اوديك

Date : Monday Date : 11/Apr/2024 Soil : ENTBAKEMEN

Stress - Settlement Relationship

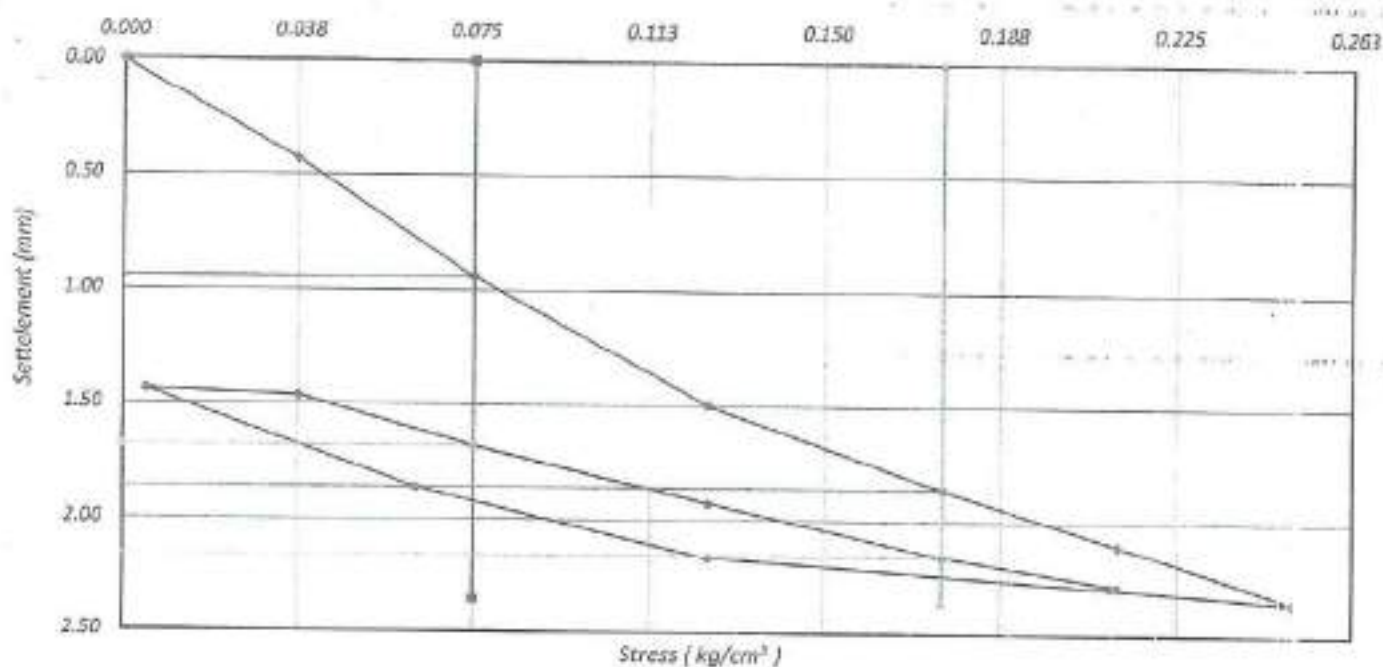

	Load (ton)	Stress (M Pa)	Settlement (mm)
Loading	0.00	0.000	0.00
	1.06	0.038	0.17
	2.12	0.075	0.47
	3.54	0.125	0.93
	4.95	0.175	1.24
	6.01	0.213	1.49
	7.07	0.250	1.67
Unloading	3.54	0.125	1.61
	1.77	0.063	1.42
	0.14	0.005	1.17
Loading	1.06	0.038	1.20
	2.12	0.075	1.26
	3.54	0.125	1.42
	4.95	0.175	1.36
	6.01	0.213	1.55

σ_{max}	0.250	Stress (M Pa)	Settlement (mm)
0.30 σ_{max} reloading	0.075	0.075	1.26
0.70 σ_{max} reloading	0.175	0.175	1.36

$$E_{v2} = 150 \text{ M Pa}$$

EV2	150
Specification	EV2 ≥ 40
Acceptance	Y

شركة اوديك
لتطوير البنية التحتية
والبنية التحتية



Tel: 23052319

مكتب S: عمارة الانفاق والحرم - طريق القاهرة - طريق مصر - طريق القاهرة - طريق مصر



مكتب أ.د/حسن مهدي
للإستشارات الهندسية



الهيئة العامة للإحصاء



مشروع:

قنار لسان كهرلي السريع - قطاع تكلي

Determination of field density - ASTM D 1556

Report no.:	From	181+200	to	181+520	Company	ODIK
Station :		Level	+ 1.50		DATE	61/04/2024
Description :	FILL LAYER					

Proctor Modified Test Results:-

Max. dry density gm/cm ³	O.M.C %	Degree of Compaction Required, %	Bulk Density of Specified sand gm/cm ³	Sand Weight of Cone (gm)
2.124	6.4	85	1.480	960

Test No.	1	2	3	4	5	6	7		
Station of sample	181+280	181+300	181+320	181+340	181+360	181+380	181+400		
Wt. Of Sand before test, gm	11145	11050	10955	10840	10655	10550	10499		
Wt. Of Sand after test, gm	8279	8020	7994	7813	7612	7548	7434		
Wt. Of Sand fill hole & cone, gm	2866	3030	3001	3027	3043	3014	3056		
Wt. Of Sand fill cone, gm	1440	1440	1440	1440	1440	1440	1440		
Wt. Of Sand fill hole, gm	1426	1590	1561	1587	1603	1574	1616		
Volume of hole, cm ³	963	1074	1055	1072	1093	1064	1092		
Wt of sample from hole, gm	2125	2360	2315	2345	2356	2296	2365		
Wet density of soil, gm/cm ³	2.206	2.196	2.194	2.187	2.174	2.158	2.166		
No. of container	1	2	3	4	5	6	7	8	9
Wt. of container, gm	62.4	62.2	62.3	62.5	62.4	62.3	62.4	60.3	61.4
Wt. Of sample & container before drying, gm	279.7	279.9	302.7	307.9	317.6	392.2	300.6	286.1	348.6
wt. of container & dried sample, gm	267.4	267.2	289.2	293.9	303.4	288.3	286.8	274.7	333.6
Water wt.	12.3	12.4	13.5	14.0	14.1	13.9	13.8	13.4	15.1
Wt. of dried sample, gm	208.0	205.0	226.9	231.4	241.0	226.0	224.4	214.4	272.1
Moisture content, %	6.00	6.06	5.96	6.05	5.85	6.16	6.16	6.25	5.55
Average moisture content, %	6.0		6.0		6.0		6.2		5.9
Dry density, gm/cm ³	2.081		2.072		2.070		2.049		2.053
Compaction (%)	97.60%		97.19%		97.00%		96.60%		96.20%
Acceptance	Y		Y		Y		Y		Y

شماره ثبت: ۲۰۲۰-۲۱۹۹-۱۶۶
مكتب أ.د/حسن مهدي
للإستشارات الهندسية

M.E / CONSULTANT

مهندس محمد علي



أشار أمين الإبراهيمي السريع - المندوب الثاني

Formet no.:	Form	101+100	to	101+150	Company	CDK
Station:		level		- 2.50	DATE	01/04/2020
Description:	FILL LAYER					

Max. dry density (g/cm ³)	O.M.C. %	Degree of Compaction Required %	Bulk Density of Specified sand (g/cm ³)	Sand Weight of Core (gr)
2.134	5.4	95	1.420	1640

Test No.	1		2		3		4	
Station of sample	181+120		181+130		181+210		181+240	
Wt. Of Sand before test,gm	10115		10060		10009		9900	
Wt. Of Sand after test,gm	7026		6928		6886		6800	
Wt. Of Sand fill hole&cone,gm	3089		3132		3122		3100	
Wt. Of Sand fill cone,gm	1440		1440		1440		1440	
Wt. Of Sand fill hole,gm	1649		1692		1692		1660	
Volume of hole,cm ³	1114		1143		1143		1122	
Wt of sample from hole,gm	2400		2616		2638		2400	
Wet density of soil,gm/cm ³	2.208		2.209		2.217		2.220	
No. of container	1	2	3	4	5	6	7	8
Wt. of container,gm	62.4	62.2	62.3	62.5	62.4	62.3	62.4	60.3
Wt. Of samples container before drainage,gm	293.8	293.6	314.7	304.4	288.8	297.5	301.0	293.3
wt. of containers & dried sample,gm	260.6	280.1	301.2	290.6	273.7	284.5	267.6	279.8
Water wt.	13.2	13.4	13.5	13.8	15.1	13.0	13.4	13.5
Wt. of dried sample,gm	216.2	217.9	238.9	228.1	211.3	222.2	225.2	219.5
Moisture content,%	6.05	6.15	5.85	6.05	6.25	5.88	5.95	6.15
Average moisture content%	6.1		5.9		6.0		6.1	
Dry density,gm/cm ³	2.561		2.575		2.591		2.583	
Compaction (%)	97.80%		97.40%		98.00%		98.10%	
Acceptance	Y		Y		Y		Y	

謝世英、王國棟、王國華、王國輝

تقریر



المكان المخصص للتأجير المأجور - المصروف - القطاع الثاني

Determination of field density - ASTM D 1556

Request no.:	From:	HL-420	to:	HL-530	Company:	CDK
Status:		(new)		- 330	DATE:	26/03/2024
Description:	FELI LAYER					

Printer Modified: Testing Results

Max. dry density, g/cm ³	O.M.C. %	Degree of Compaction Required, %	Bulk Density of Specified sand, g/cm ³	Sand Weight of Core (gr)
2.145	62	95	1.680	1440

Test No.	1		2		3		4							
Station of sample	181+440		181+590		181+540		181+690							
Wt. Of Sand before test,gm	10320		10150		9965		9680							
Wt. Of Sand after test,gm	7101		6873		6783		6678							
Wt. Of Sand fill hole&cone,gm	3219		3277		3182		3291							
Wt. Of Sand fill cone,gm	1440		1440		1440		1440							
Wt. Of Sand fill hole,gm	1779		1837		1742		1781							
Volume of hole,cm ³	1282		1241		1177		1190							
Wt of sample from hole,gm	2630		2710		2665		2635							
Wet density of soil,gm/cm ³	2.188		2.183		2.171		2.297							
No. of container	1	2	3	4	5	6	7	8						
Wt. of container,gm	62.4	62.2	62.3	62.5	62.4	62.3	62.4	60.3						
Wt. Of sample& container before drying,gm	319.1	316.1	357.6	347.1	347.6	390.5	344.3	328.2						
wt. of container& dried sample,gm	304.8	301.5	341.5	331.5	331.5	344.8	319.1	312.8						
Water wt.	14.3	14.6	15.1	15.6	15.9	15.1	15.2	15.4						
Wt. of dried sample,gm	242.4	238.3	279.6	289.0	269.6	282.6	266.7	282.6						
Moisture content,%	5.90	6.10	5.48	5.80	5.90	5.70	5.70	5.10						
Average moisture content%	6.0		5.6		5.8		5.3							
Dry density,gm/cc ²	2.054		2.068		2.082		2.094							
Compaction (%)	95.28%		96.35%		96.60%		97.10%							
Acceptance	Y		Y		Y		Y							

شركة اوديك
للتوريدات والمقاولات
ت. ٨٩٨٤٥٠ - ف. ٧٠٢-٧٥٩-١٦٧

در کمال حسن

W. S. J. CHONG AND T. H. CHAN

مکملہ سہ ماہی



قطار أسوان القهريالى الممرىع - القطاع الثاني

Request no.:	From	182+369	to	182+376	Company	ODIK
Station:		Level	- 1.75		DATE	17/03/2024
Description:	FILL LAYER					

Max. dry density gm/cm ³	O.N.C. %	Degree of Compaction Required %	Bulk Density of Specified sand, gm/cm ³	Sand Weight of Cone (gm)
2.146	6.2	88	1.480	1543

Test No.	1	
Station of sample	182+370	
Wt. Of Sand before test,gm	10660	
Wt. Of Sand after test,gm	9843	
Wt. Of Sand fill hole&cone,gm	3207	
Wt. Of Sand fill cone,gm	1440	
Wt. Of Sand fill hole,gm	1767	
Volume of hole,cm ³	1194	
Wt of sample from hole,gm	2930	
Wet density of soil,gm/cm ³	2.262	
No. of container	1	2
Wt. of container,gm	62.4	62.2
Wt. Of sample& container before drying,gm	321.4	323.1
wt. of container& dried sample,gm	397.2	398.8
Water wt.	14.2	14.3
Wt. of dried sample,gm	244.8	245.5
Moisture content,%	5.80	5.80
Average moisture content%	5.8	
Dry density,gm/cm ³	2.092	
Compaction (%)	97.06%	
Acceptance	Y	

Acceptance

المستلمة أو ديكت
للتوريدات والمقاولات
تاريخ: 20/05/2017
موقع: [Signature]

1919



مكتب أ.د. إحسن مهدي
للاستشارات الهندسية



الهيئة العامة للمياه والكهرباء



مشروع:

خط أنابيب الكهرباء السريع - المثلج الثاني

Determination of field density - ASTM D 1556

Request no.:	From	182+060	to	182+200	Company	ODIK
Station:		Level	- 3.25	DATE	27/03/2024	
Description:	FILL LAYER					

Proctor Modified Testing Results:-

Max. dry density gm/cm ³	O.M.C. %	Degree of Compaction Required %	Bulk Density of Specified sand gm/cm ³	Sand Weight of Cone (gm)
2.148	6.20	95	1.460	1446

Test No.	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16
Station of sample	182+060	182+080	182+100	182+120	182+140	182+160	182+180	182+200								
Wt. Of Sand before test, gm	10130	10100	10050	9940	9900	9810	9740	9665								
Wt. Of Sand after test, gm	7096	7112	7023	6911	6854	6240	6265	6496								
Wt. Of Sand fill hole&cone, gm	3034	2988	3027	3029	3266	3570	3475	3169								
Wt. Of Sand fill cone, gm	1440	1440	1440	1440	1440	1440	1440	1440								
Wt. Of Sand fill hole, gm	1594	1548	1587	1589	1766	2130	2035	1729								
Volume of hole, cm ³	1077	1046	1072	1074	1193	1439	1375	1168								
Wt of sample from hole, gm	2360	2285	2325	2355	2620	3100	2990	2540								
Wet density of soil, gm/cm ³	2.181	2.185	2.168	2.193	2.196	2.154	2.174	2.174								
No. of container	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16
Wt. of container, gm	62.4	62.2	62.3	62.5	62.4	62.3	62.4	60.3	61.4	60.7	62.4	61.1	62.4	62.1	60.7	60.1
Wt. Of sample& container before drying, gm	353.2	314.4	359.0	345.2	317.3	327.5	312.7	296.9	358.1	331.5	390.1	379.0	296.2	296.4	343.4	368.1
wt. of container& dried sample, gm	337.0	299.9	343.8	329.7	303.1	313.2	299.2	283.3	342.9	317.6	374.2	363.0	283.8	282.4	327.9	352.6
Water wt.	16.2	14.5	15.2	15.5	14.2	14.3	13.5	13.6	15.2	14.9	15.9	16.0	12.4	13.0	15.5	15.5
Wt. of dried sample, gm	274.6	237.7	281.5	267.2	240.7	250.9	235.8	223.0	281.5	256.9	311.8	301.9	221.4	220.3	267.2	292.5
Moisture content, %	5.90	6.10	5.40	5.80	5.80	5.70	5.70	6.10	5.40	5.40	5.10	5.30	5.60	5.90	5.8	5.3
Average moisture content%	5.0		5.6		5.8		5.9		5.6		5.2		5.3		5.6	
Dry density, gm/cm ³	2.058		2.069		2.049		2.071		2.079		2.047		2.056		2.060	
Compaction (%)	95.90%		96.40%		95.50%		96.50%		96.90%		95.40%		95.80%		96.00%	
Acceptance	Y		Y		Y		Y		Y		Y		Y		Y	

شركة اوديك
للتوريدات والمقاولات
ت. ٨٩٨٤٥٠ ف. ٧٠٢٠٧٩٩١١٢٠

أ. د. إحسن مهدي

SE / CONSULTANT

مهندس استشاري



قطار أسوان الكهربائي لسويح - القشاح الثاني

Request no.:		From	100+000	to	101+300	Company	ODJK
Station:			Level		- 1.00	DATE	26/05/2026
Description:	FILL LAYER						

Max. dry density (g/cm ³)	O.M.C. %	Degree of Compaction Required, %	Bulk Density of Specified sand (g/cm ³)	Sand Weight of Core (gm)
2.543	9.5	95	1.480	9443

Test No.	1		2		3		4		5		6					
Station of sample	180+800		190+920		180+980		180+990		181+030		101+060					
Wt. Of Sand before test,gm	16990		16765		16668		16430		16318		16298					
Wt. Of Sand after test,gm	7838		7690		7777		7218		7187		6625					
Wt. Of Sand fill hole&cone,gm	3062		3085		3878		3212		3128		3375					
Wt. Of Sand fill cone,gm	1440		1440		1440		1440		1440		1440					
Wt. Of Sand fill hole,gm	1622		1645		1438		1772		1888		1935					
Volume of hole,cm ³	1096		1112		972		1187		1140		1307					
Wt of sample from hole,gm	2380		2415		2135		2658		2640		2915					
Wet density of soil,gm/cc ³	2.172		2.173		2.197		2.213		2.237		2.230					
No. of container	1	2	3	4	5	6	7	8	9	10	11	12				
Wt. of container,gm	62.4	62.2	62.3	62.6	62.4	62.3	62.4	60.3	61.4	59.7	62.4	61.1				
Wt. Of samples container before drying,gm	267.9	266.5	344.2	253.8	271.4	288.4	277.8	279.8	324.7	274.6	320.0	347.7				
wt. of container& dried sample,gm	265.9	273.1	329.0	242.8	269.2	263.1	288.7	265.6	310.5	262.3	305.6	332.6				
Water wt.	12.0	13.5	15.2	11.0	12.2	15.3	12.2	13.2	14.2	12.3	13.2	15.2				
Wt. of dried sample,gm	193.5	210.9	266.7	180.3	186.8	220.8	203.3	205.3	249.1	201.8	244.4	271.4				
Moisture content,%	6.20	6.40	5.79	6.19	6.20	6.99	6.09	6.40	5.79	6.10	5.40	5.60				
Average moisture content(%)	6.3		5.9		6.1		6.2		5.9		5.5					
Dry density,gm/cm ³	2.043		2.062		2.071		2.064		2.103		2.114					
Compaction (%)	95.20%		95.60%		95.50%		97.10%		99.60%		99.50%					
Acceptance	Y		Y		Y		Y		Y		Y					

تشریکہ او د نیو نیو
MECONTRACTOR
تشریکہ او د نیو نیو
تشریکہ او د نیو نیو

محمد مصطفیٰ صوفی



أحمد بن محمد بن أبي بكر - القضاة

Determination of field density - ASTM D 1556

Request no.:		From	1801376	to	1801701	Company	ODIK
Station :		Level	-1.75			DATE	26/05/2024
Description :	FILL LAYER						

Procter Modified Testers Results:

Max. dry density (g/cm ³)	O.M.C. %	Degree of Compaction Required%	Bulk Density of Specified sand (g/cm ³)	Seed Weight of Cone (gm)
1.148	6.60	95	1.403	11.60

[illegible]

شركة اوديك
للتوريدات والمعدات
ص.ت: ٩٨٤٥ / ب. ص. ٤٠٠٠ / ٤٠٠٠

Signature _____



مكتب أ.د/حسن مهدي
للإستشارات الهندسية



الهيئة العامة للغذاء والدواء



مشروع

قناة آسوان لتهريب السموم - القطاع الثاني

Determination of field density - ASTM D 1556

Request no.:	From	180-375	to	380-700	Company	COIK
Station:		Level	- 1.75	DATE	25/08/2024	
Description:	FILL LAYER					

Proctor Modified Test Results

Max. dry density, gm/cm ³	O.M.C. %	Degree of Compaction Required, %	Bulk Density of Specified sand, gm/cm ³	Sand Weight of Cone (gm)												
2.148	5.50	96	1.460	1440												
Test No.	10		11		12		13									
Station of sample	180+580		180+600		180+620		180+640									
Wt. Of Sand before test, gm	10200		10115		10090		10000									
Wt. Of Sand after test, gm	6755		6981		6873		6568									
Wt. Of Sand fill hole&cone, gm	3404		3134		3217		3434									
Wt. Of Sand fill cone, gm	1440		1440		1440		1440									
Wt. Of Sand fill hole, gm	1964		1694		1777		1994									
Volume of hole, cm ³	1327		1145		1201		1348									
Wt. of sample from hole, gm	2960		2540		2685		2980									
Wet density of soil, gm/cm ³	2.253		2.219		2.237		2.211									
No. of container	1	2	3	4	5	6	7	8								
Wt. of container, gm	62.4	62.2	62.3	62.5	62.4	62.3	62.4	60.3								
Wt. Of sample& container before drying, gm	339.7	318.8	314.1	313.4	283.2	361.5	308.8	267.8								
wt. of container& dried sample, gm	324.5	304.6	317.9	299.2	270.9	345.9	296.4	255.5								
Water wt.	15.2	14.3	16.2	14.2	12.3	15.6	12.4	12.3								
Wt. of dried sample, gm	252.1	242.4	265.6	236.7	208.5	283.6	234.0	195.2								
Moisture content, %	5.80	5.90	6.10	6.00	5.90	5.50	5.30	6.30								
Average moisture content, %	5.8		6.1		5.7		5.8									
Dry density, gm/cm ³	2.129		2.092		2.116		2.090									
Compaction (%)	95.20%		97.50%		98.80%		97.40%									
Acceptance	Y		Y		Y		Y									

شركة اوديك
للتوريدات والمقاولات
ب.ت. ٨٩٨٤٥٠ ٠١٦٧ ٧٠٣٥٥٩

محمد منعم فوزي



قطار اسوان القاهرة السريـح = القطاع الثاني

Request no.:	From	180+700	to	180+840	Company	ODIK
Surface:		level		+ 0.75	DATE	20/05/2024
Description:	FILL LAYER					

Max. dry density g/cm ³	O.M.C. %	Degree of Compaction Required, %	Bulk Density of Specified sand, g/cm ³	Sand Weight of Core (g)
2.147	6.30	95	1.480	1440

[illegible]

THE A. P. CHANDRASEKHAR FELLOWSHIP



قطار مسوار الكهربي المبرمج - (القطار ٤ الثاني).

Request no.:	From	181+100	to	181+250	Company	COIK
Station:		Level		-3.00	DATE	18/08/2024
Description:	FILL LAYER					

Max. dry density gm/cm ³	O.M.C %	Degree of Compaction Required %	Bulk Density of Specified sand, gm/cm ³	Sand (Weight of Cone / gm)
2.547	6.3	95	1.433	1.446

Test No.	1		2		3		4	
Station of sample	181+120		181+180		181+220		181+240	
Wt. Of Sand before test,gm	16320		10190		19045		9860	
Wt. Of Sand after test,gm	6798		9632		6488		5328	
Wt. Of Sand fill hole&cone,gm	3322		3558		3557		3532	
Wt. Of Sand fill cone,gm	1440		1440		1440		1440	
Wt. Of Sand fill hole,gm	2082		2118		2117		2082	
Volume of hole,cms ³	1407		1431		1430		1414	
Wt of sample from hole,gm	3150		3200		3155		3148	
Wet density of soil,gm/cm ³	2.240		2.236		2.206		2.225	
No. of container	1	2	3	4	5	6	7	8
Wt. of container,gm	62.4	62.2	62.3	62.5	62.4	62.3	62.4	60.3
Wt. Of sample& container before drying,gm	316.6	418.7	291.8	318.6	356.9	383.3	397.8	302.6
wt. of container& dried sample,gm	304.1	400.1	278.4	302.9	341.0	365.7	341.7	289.1
Water wt.	14.5	19.6	13.4	15.7	15.9	17.6	16.2	13.5
Wt. of dried sample,gm	241.7	337.9	216.1	240.4	278.8	303.4	279.3	228.8
Moisture content,%	6.0	5.8	6.2	5.7	5.6	5.8	5.8	5.9
Average moisture content%	5.9		6.0		5.7		5.9	
Dry density,gm/cm ³	2.115		2.111		2.087		2.102	
Compaction (%)	98.50%		98.30%		97.20%		97.90%	
Acceptance	Y		Y		Y		Y	

महाराष्ट्र



نظام إمداد الكهرباء للمربع - القطاع الثاني

Request no.:	From	181-440	to	181-580	Company	ODIK
Station :		Level	- 3.00		DATE	19/03/2024
Description:	FILL LAYER					

Max. dry density g/cm ³	O.R.C. %	Degree of Compaction Required, %	Bulk Density of Specified sand g/cm ³	Sand Weight of Conc (gm)
2.147	8.3	95	1.480	1480

شركة اوديك
للتطوير العقاري والمقاولات
س.ت. ٧٠٠٧٥٨١٦٦

M. E. CONSIDIS, T. J. H.

۵۶۳۱۱۹۳



المقرر لمرور المضي على المضي = المضي

Request no.:	From	180+840	to	182+100	Company	ODIK
Station :		Level	= 3.50		DATE	09/03/2024
Description :	FILL LAYER					

Max. dry density g/cm ³	D.N.C. %	Degree of Compaction Required, %	Bulk Density of Specified seed g/cm ³	Seed Weight or Count (g)
1.136	2.50	95	1.600	14.60

[illegible][illegible]

مجلس شورای اسلامی
۱۳۸۲/۰۲/۰۱
مجلس شورای اسلامی



قطر أبو الفوارس القهري السريخ - القلاع الخلفي

Request no.:		From	181+100	to	181+260	Company	CDK
Station :			Level		+ 3.50	DATE	06/03/2024
Description :	FILL LAYER						

Max. dry density g/cm ³	O.M.C %	Degree of Compaction Required %	Bulk Density of Specified sand, g/cm ³	Sand Weight of Core (gm)
2.136	8.50	95	1.410	1443

[illegible]

شركة اوديك
للتوريد والاعمال
٢٠٢-٧٥٩-١٦٧١

محمد عبدالقوی

استشاري أبحاث التربة والاساسات
أ.م.د. هشام محمد حلمي



مشروع:
قطار أسوان الكهربائي السريع - القطاع الثاني

Standard Test Method For Density of Soil and Rock in place By the Sand Replacement Method in a Test Pit " ASTM D4914 M-15 "

Request no.:		From	180+700	to	180+840	Company	لوجيك
Station:		Level	-2.90	DATE	05/03/2024		
Description:	EMBANKMENT Materials						
		1	2	3			
No. of Station →		180+720	180+770	180+820			
1-Mass Of Materials							
Wt of Total Wet Materials	gm	85,306	85,316	85,610			
Wt of Wet Oversize Fraction	gm	30,606	31,113	31,200			
Wt of Wet Control Fraction	gm	54,700	54,203	54,410			
Wt of Dry Oversize Fraction	gm	30,263	30,773	30,794			
Wt of Dry Control Fraction	gm	52,457	51,925	52,325			
2.Determination of moist material							
Molature Content of Control Fraction	%	4.1%	4.2%	4.2%			
Molature Content of Oversize Fraction	%	1.10%	1.10%	1.30%			
3-Volume Of the Test Pit							
Wt Calibrated sand in Pit and template	gm	82,108	82,190	82,195			
Wt of Calibrated sand in template	gm	26,100	26,100	26,100			
Wt of Calibrated sand in test Pit	gm	56,008	56,090	56,095			
Density of Calibrated sand	gm/cm3	1.47	1.47	1.47			
Specific Gravity of Oversize Fraction	gm/cm3	2.530	2.530	2.530			
Volume of the Test Pit	cm3	38,095	38,129	38,150			
Volume of Wet Oversize Fraction	cm3	12,095	12,298	12,332			
Volume of Wet Control Fraction	cm3	26,000	25,831	25,818			
4-Relative Density Calculation							
Wet Density of Control Fraction Gm/cm3		2.10	2.10	2.11			
Dry Density of Control Fraction Gm/cm3		2.02	2.03	2.02			
Q3 4	maximum dry density	2.150	2.150	2.150			
	O.M.C	5.40%	5.40%	5.40%			
Relative Compaction		94.00%	93.66%	94.03%			
remarks		95%	95%	95%			
Pass / Fail		Fail	Fail	Fail			

شركة لوجيك
للتطوير الهندسي والاساسات
ب.م.د. هشام محمد حلمي
٧٠٣-٧٤٩-١١٢

م.ع. استشاري
M.E. CONSULTANT
محمد عبد المنعم لوري

استشاري أبحاث التربة والاساسات
أ.د.م. هشام محمد حلي



مشروع:
قطار أسوان الكهربائي السريع - القطاع الثاني

Standard Test Method For Density of Soil and Rock in place By the Sand Replacement Method in a Test Pit " ASTM D4958-14-16 "

Request no.:	From	180+730	to	180+840	Company	أوديك
Station :		Level	-2.00	DATE	05/03/2024	
Description :	EMBANKMENT Materials					

	1	2	3			
No. of Station →	180+720	180+770	180+820			

1-Mass Of Materials

Wt of Total Wet Materials	gm	85,850	85,340	85,225		
Wt of Wet Oversize Fraction	gm	27,960	27,420	27,350		
Wt of Wet Control Fraction	gm	57,890	57,920	57,875		
Wt of Dry Oversize Fraction	gm	27,088	26,961	26,912		
Wt of Dry Control Fraction	gm	55,247	55,256	55,271		

2.Determination of moist material

Moisture Content of Control Fraction	%	4.5%	4.6%	4.5%		
Moisture Content of Oversize Fraction	%	1.90%	1.60%	1.80%		

3-Volume Of the Test Pit

Wt Calibrated sand in Pit and template	gm	81,200	81,215	81,295		
Wt of Calibrated sand in template	gm	26,100	26,100	26,100		
Wt of Calibrated sand in test Pit	gm	55,100	55,115	55,195		
Density of Calibrated sand	gm/cm3	1.47	1.47	1.47		
Specific Gravity of Oversize Fraction	gm/cm3	2.530	2.530	2.530		
Volume of the Test Pit	cm3	37,483	37,493	37,548		
Volume of Wet Oversize Fraction	cm3	10,870	10,838	10,810		
Volume of Wet Control Fraction	cm3	26,613	26,655	26,737		

4-Relative Density Calculation

Wet Density of Control Fraction Gm/cm3	2.17	2.17	2.16		
Dry Density of Control Fraction Gm/cm3	2.08	2.08	2.07		
Qr 4	maximum dry density	2.159	2.150	2.150	
	O.M.C	5.40%	5.40%	5.40%	
Relative Compaction	96.75%	96.62%	96.34%		
remarks	95%	95%	95%		
Pass / Fail	Pass	Pass	Pass		

شركة أوديك
م.ع. CONTRACTOR
للتوريد والبناء والمقاولات
س.ت: ٨٩٨٤٥٠٠٠٠
ه.ت: ٠٢-٧٥٩٠١٦٦

ECSCO
MTC/CONSULTANT
محمد منعم درويش

استشاري أبحاث التربة والاساسات
أ.د.م. هشام محمد حلمي



مشروع:
قطار أسوان الكهربائي السريع - القطاع الثاني

Standard Test Method For Density of Soil and Rock in place By the Sand Replacement Method in a Test Pit ~ ASTM D4914 M-16 ~

Request no.:		From	181+450	to	181+580	Company	أوديك
Station :		Level	-1.90	DATE	05/03/2024		
Description :	EMBANKMENT Materials						

	1	2	3			
No. of Station →	181+450	181+530	181+580			

1-Mass Of Materials

Wt of Total Wet Materials	gm	85,330	88,815	85,860			
Wt of Wet Oversize Fraction	gm	27,210	27,150	27,130			
Wt of Wet Control Fraction	gm	58,120	58,165	58,230			
Wt of Dry Oversize Fraction	gm	26,892	26,715	26,723			
Wt of Dry Control Fraction	gm	55,535	55,485	55,433			

2. Determination of moist material

Moisture Content of Control Fraction	%	4.5%	4.6%	4.7%			
Moisture Content of Oversize Fraction	%	1.50%	1.00%	1.50%			

3-Volume Of the Test Pit

Wt Calibrated sand in Pit and template	gm	81,600	81,015	81,120			
Wt of Calibrated sand in template	gm	26,100	26,100	26,100			
Wt of Calibrated sand in test Pit	gm	54,900	54,915	55,020			
Density of Calibrated sand	gm/cm ³	1.47	1.47	1.47			
Specific Gravity of Oversize Fraction	gm/cm ³	2.539	2.530	2.538			
Volume of the Test Pit	cm ³	37,347	37,357	37,428			
Volume of Wet Oversize Fraction	cm ³	10,755	10,731	10,728			
Volume of Wet Control Fraction	cm ³	26,592	26,626	26,705			

4-Relative Density Calculation

Wet Density of Control Fraction Gm/cm ³	2.19	2.18	2.18			
Dry Density of Control Fraction Gm/cm ³	2.09	2.09	2.08			
Gr 4	maximum dry density	2.150	2.150	2.150		
	G.M.C	5.40%	5.40%	5.40%		
Relative Compaction		97.28%	97.14%	96.86%		
Remarks		95%	95%	95%		
Pass / Fail		Pass	Pass	Pass		

شركة أوديك
لتطوير البنى التحتية
م.ت: ٨٩٨٤٥٠ ف.٣٠٣٧٤٦١٩٢





طيار لسيان الكهرومائي المبرمج - القطاع الثاني

Request no.:	From	181+260	to	181+470	Company	ODIK
Station :		Level	- 1.75		DATE	05/03/2024
Description :	FILL LAYER					

Wet, dry density g/cm ³	D.M.C %	Degree of Compaction Required, %	Bulk Density of Specified sand, g/cm ³	Sand Weight of Cone (gm)
2.125	5.5	95	1.480	5445

[illegible]

شركة اوديك
للتقنيات والمقاولات
ب.ت.ك. ٢٠٢٠-٢٠٢١

میں نے سیکھ لیا ہے



قطر لواء الكورني السريح - القطاع الثاني

Request no.:	From	132+360	to	182+375	Company	ODK
Station :		Level		- 2.00	DATE	27/02/2014
Description:	FILL LAYER					

Max. dry density, gm/cm ³	O.M.C. %	Degree of Compaction Required %	Bulk Density of Specified sand, gm/cm ³	Sand Weight of Cone (gm)
3.138	6.0	95	1.450	1442

[illegible]

شركة اوديك
لتطوير يدات والمقتنيات
س.ت: ٨٩٨٤٥ * ك.م.ح. ٧٠٢-٣٥٨

MEL CONSULTANT

محمد رفیع



قطار اسوان الكهربائي السريع - القطار الكهربائي

Request no.:	From	182+360	to	182+376	Company	ODIK
Station :		Level	-2.00		DATE	04/03/2024
Description :	FILL LAYER					

Max. dry density (g/cm ³)	O.M.C. %	Degree of Compaction Required, %	Bulk Density of Specified sand, g/cm ³	Sand Weight of Cone (gm)
2.138	8.6	98	1.480	6440

Test No.	1	
Station of sample	182+370	
Wt. Of Sand before test,gm	10960	
Wt. Of Sand after test,gm	8806	
Wt. Of Sand fill hole&cone,gm	3754	
Wt. Of Sand fill cone,gm	1440	
Wt. Of Sand fill hole,gm	2314	
Volume of hole,cm ³	1563	
Wt of sample from hole,gm	3420	
Wet density of soil,gm/cm ³	2.188	
No. of container	1	2
Wt. of container,gm	62.4	62.2
Wt. Of sample& container before drying,gm	379.0	383.1
wt. of container& dried sample,gm	364.5	348.5
Water wt.	14.5	14.8
Wt. of dried sample,gm	362.1	386.3
Moisture content,%	4.8	5.1
Average moisture content%	5.0	
Dry density,gm/cm ³	2.086	
Compaction (%)	97.50%	
Acceptance		

شركة اوديك
للتوريدات والمقاولات
س.ت: ٩٩٤٥٠ ب.ف: ١٦٧-٧٥٩-٧٠٢

MICROGRAPHY

ms Oct 11, 95

**EGSCO**Egyptian Geotech. & Struc.
Dr. Eng. Hesham M. Helmy

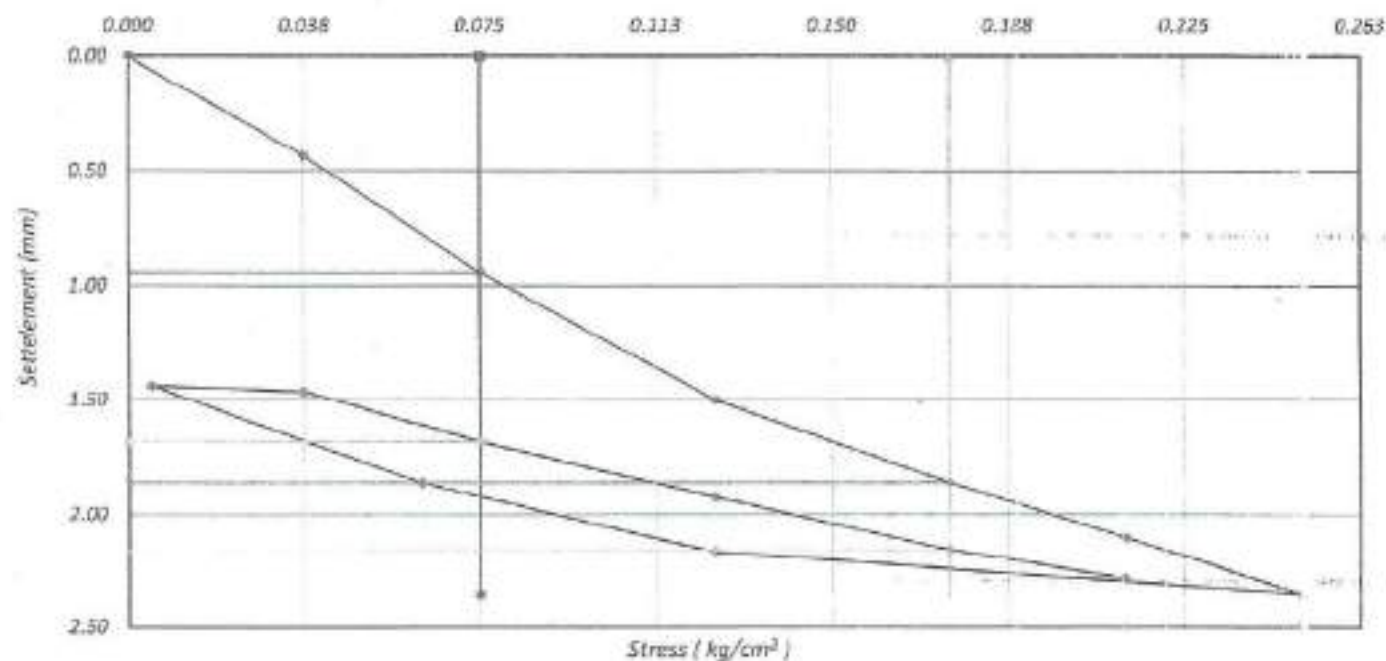
الهيئة القومية للإنشاء

**PLATE LOADING TEST RESULTS****PROJECT :** القطار الكهربائي السريع (القنطرة - أسوان) - القطاع الثاني (يلي مزار - مقلوبة)

ST : 182+040 182+240 Plate Dim. : 60 cm

level : -1.5 Location : 182+110 Company : فوجيات

Date : Monday Date : 4/Mar/2024 Soil : EMBANKMENT

Stress - Settlement Relationship

	Load (ton)	Stress (M Pa)	Settlement (mm)
Loading	0.60	0.000	0.00
	1.66	0.038	0.08
	2.12	0.075	0.38
	3.54	0.125	0.84
	4.93	0.175	1.13
	6.61	0.213	1.40
	7.87	0.250	1.58
Unloading	3.54	0.125	1.52
	1.77	0.063	1.33
	0.14	0.005	1.08
Loading	1.66	0.038	1.11
	2.12	0.075	1.17
	3.54	0.125	1.33
	4.93	0.175	1.56
	6.61	0.213	1.63

Cmax	0.250	Stress (M Pa)	Settlement (mm)
0.30 σ_{max} reloading	0.075	1.17	
0.70 σ_{max} reloading	0.175	1.56	

$$E_{v2} = 115 \text{ M Pa}$$

EV2	115
Specification	Ev2 \geq 40
Acceptance	Y

شركة فوجيات
للتنفيذ والبناء
م.ب. ٨٩٨٤٥
٢٠٣٧٥٥٩٧٠٩٧٠

V.E. CONSULTING

Tel: 23052339

م.ب. ٨٩٨٤٥ : ٢٠٣٧٥٥٩٧٠٩٧٠



EGSCO
Egyptian Geotech. & Struc.
Dr. Eng. Hesham M. Helmy



الهيئة العامة للتخطيط
والتطوير الاقتصادي

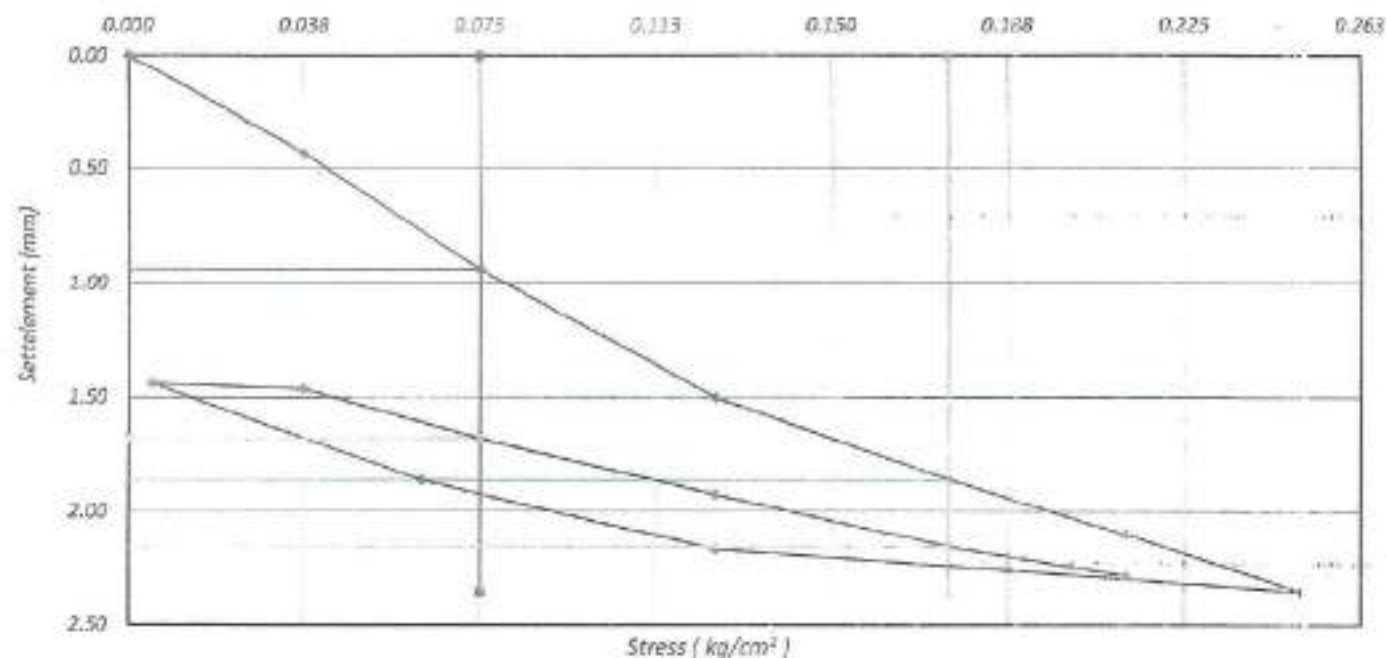


PLATE LOADING TEST RESULTS

PROJECT : تقاسم المهرقاني السريع (التور - اسوان) - القنطرة الكبرى - بني حجاز - متفولة

ST. : 182+040 182+240 Plate Dim. : 60 cm
level : -1.5 Location : 182+320 Company : رابحة
Date : Monday Date : 4/3/2014 Soil : EMBANKMENT

Stress - Settlement Relationship



	Load (ton)	Stress (M Pa)	Settlement (mm)
Loading	0.00	0.000	0.00
	1.06	0.038	0.08
	2.12	0.075	0.39
	3.34	0.125	0.84
	4.95	0.175	1.16
	6.01	0.213	1.40
	7.07	0.250	1.59
Unloading	3.34	0.125	1.32
	1.77	0.063	1.34.00
	0.14	0.005	1.09
Reloading	1.06	0.038	1.11
	2.12	0.075	1.18
	3.34	0.125	1.23
	4.95	0.175	1.56
	6.01	0.213	1.59

G _{max}	0.250	Stress (M Pa)	Settlement (mm)
0.30 G _{max} reloading	0.075		1.18
0.70 G _{max} reloading	0.175		1.56

$$E_{v2} = 118 \text{ M Pa}$$

E _{v2}	118
Specification	Ev2 ≥ 40
Acceptance	Y

شركة اوديك
للتوريدات والمقاولات
7070551500
7070551500

U.S. COMPANY

Tel: 23052330

مكتب: 5 - طابق 5 - المبنى 5 - المنطقة الصناعية - بني حجاز - متفولة



قطار اسوان القاهره الى السبع - القطاع الثاني

Request no.:	From	182+080	to	182+240	Company	ODK
Station :		Level	-3.50		DATE	04/09/2024
Description :	FILL LAYER					

Max. dry density g/cm ³	O.M.C. %	Degree of Compaction Required, %	Bulk Density of Specified sand, g/cm ³	Stand Weight of Cone (gr)
1.425	6.0	95	1.580	1600

[illegible]

شركة اوديك
للتوريدات والمقاولات
ب.ت. ١٩٨٤٥، ج.م.س. ٧٠٢-٧٥٣

W. P. JENNINGS, JR.

گجرات کے لیے



مكتب أد/حسن مهدي
للإستشارات الهندسية



الهيئة العامة للإحصاء



مشروع:

إنشاء أسوار الكهرطاسي السريع - القطاع الثاني

Determination of field density - ASTM D 1556

Request no.:	From	182+080	to	182+240	Company	ODIC
Station :		Level		-1.50	DATE	27/03/2024
Description :	FILL LAYER					

Proctor Modified Testing Results:-

Max. dry density (gm/cm ³)	O.M.C. %	Degree of Compaction Required, %	Bulk Density of Specified sand, gm/cm ³	Sand Weight of Cone (gm)
2.136	8.0	95	1.433	1440

Test No.	1		2		3		4		5		6		7		8			
Station of sample	182+080		182+080		182+100		182+120		182+140		182+160		182+180		182+200			
Wt. Of Sand befor test,gm	10100		9900		9850		9750		9500		9400		9300		9100			
Wt. Of Sand after test,gm	6707		6465		6576		6735		6520		6135		6101		6023			
Wt. Of Sand fill hole&cone,gm	3393		3416		3274		3016		2980		3266		3199		3077			
Wt. Of Sand fill cone,gm	1440		1440		1440		1440		1440		1440		1440		1440			
Wt. Of Sand fill hole,gm	1953		1975		1834		1575		1340		1825		1759		1637			
Volume of hole,cm3	1319		1334		1259		1084		1041		1233		1189		1106			
Wt of sample from hole,gm	2610		2640		2430		2100		2060		2460		2320		2140			
Wet density of soil,gm/cm ³	1.978		1.979		1.961		1.973		1.976		1.995		1.952		1.934			
No. of container	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16		
Wt. of container,gm	62.4	62.2	62.3	62.5	62.4	62.3	62.4	60.3	61.4	60.7	62.4	61.1	62.4	62.1	60.7	60.1		
Wt. Of sample& container befor drying,gm	337.8	318.7	329.2	360.6	281.2	385.9	346.5	247.4	277.2	270.7	278.3	279.6	266.7	283.2	294.3	302.5		
wt. of container& dried sample,gm	330.3	312.2	323.2	352.2	273.8	377.7	339.3	240.9	289.7	283.6	271.0	271.4	269.6	274.9	286.1	293.4		
Water wt.	7.5	6.5	6.0	8.4	7.4	8.2	7.2	6.5	7.5	7.1	7.3	8.2	7.1	8.3	9.2	9.1		
Wt. of dried sample,gm	267.9	250.0	260.9	289.7	211.4	315.4	276.9	180.6	208.3	202.9	208.6	210.3	197.2	212.8	224.4	233.3		
Moisture content, %	2.8	2.6	2.3	2.9	3.5	2.6	2.60	3.60	3.6	3.5	3.5	3.9	3.6	3.9	4.1	3.9		
Average moisture content%	2.7		2.6		3.1		3.1		3.6		3.7		3.8		4.0			
Dry density,gm/cm ³	1.926		1.928		1.903		1.914		1.911		1.924		1.891		1.863			
Compaction (%)	99.16%		99.20%		99.00%		99.60%		99.60%		99.00%		98.00%		87.00%			
Acceptance	N		N		N		N		N		N		N		N			

شركة أوديك
للتوريدات والمقاولات
س.ت: ٨٩٨٤٥٠
هاتف: ٠١٦٢٠٠٠٠٠٠٠٠
فكس: ٠١٦٢٠٠٠٠٠٠٠٠٠

RECEIVED

مكود ٥١٢٢٠٠٠٠٠٠٠٠



تتار: اموزان فناوری های سریع - الفلاح تفتلي

Request no.:	From	180+840	to	181+000	Company	ODK
Station :		Level		+4.00	DATE	04/03/2024
Description :	R/L LAYER					

Max. dry density g/cm ³	O.N.C. %	Degree of Compaction Required, %	Bulk Density of Specified sand, g/cm ³	Sand Weight of Cone (gm)
2.134	1.00	95	1.280	1115

Test No.	1		2		3		4	
Station of sample	180+890		180+920		180+990		180+980	
Wt. Of Sand before test,gm	10329		10210		10116		10009	
Wt. Of Sand after test,gm	6572		6548		6668		6363	
Wt. Of Sand Fill hole&cone,gm	3748		3662		3442		3637	
Wt. Of Sand fill cone,gm	1410		1446		1440		1446	
Wt. Of Sand fill hole,gm	2308		2222		2002		2197	
Volume of hole,cm ³	1568		1501		1363		1485	
Wt of sample from hole,gm	3450		3380		3000		3300	
Wet density of soil,gm/cm ³	2.213		2.232		2.217		2.223	
No. of container	1	2	3	4	5	6	7	8
Wt. of container,gm	62.4	62.2	62.3	62.6	62.4	62.3	62.4	60.3
Wt. Of sample& container before drying,gm	286.6	296.1	317.3	322.1	279.0	263.7	296.7	282.1
wl. of container& dried sample,gm	276.4	285.8	303.0	308.8	268.1	253.2	286.1	281.4
Water wt.	12.2	12.3	14.2	13.3	10.9	10.6	10.6	10.7
Wt. of dried sample,gm	214.0	223.6	240.7	246.3	206.7	190.9	182.7	191.1
Moisture content,%	5.7	5.5	5.9	5.4	5.3	5.5	5.5	5.6
Average moisture content%	5.6		5.7		5.4		5.6	
Dry density,gm/cm ³	2.095		2.112		2.104		2.106	
Compaction (%)	98.00%		98.80%		98.40%		98.50%	
Acceptance	Y		Y		Y		Y	

شركة اوديك
للتوريدات والمقاولات
ص.ت. ٢٩٨٤٥ / ب.ص. ٧٠٢-٧٥٨١٦٧١

© 2000 Blackwell Science Ltd *Journal of Internal Medicine* 247: 395–401

36/11/20



گودرہ کے نام



لبنان الكهربائي السريع - قطاع الطاقة

Request no.2	From	180+340	to	182+000	Company	ODIK
Station :		Level		-4.00	DATE	23/02/2024
Description :	FLL LAYER					

Max. dry density (gm/cc)	O.M.C. %	Degree of Compaction Required, %	Bulk Density of Specified sand, gm/cm ³	Sand Weight of Core (gm)
1.458	5.60	95	1.480	550

[illegible]

PLEASE CONTINUE EARLY

॥ श्रीगणेशाय नमः ॥

استشاري أبحاث التربة والأساسات
أ.د.م. هشام محمد حلمي




مشروع:
قطار أسوان الكهربائي السريع - القطاع الثاني

Standard Test Method For Density of Soil and Rock in place By the Sand Replacement Method in a Test Pit * ASTM D4954 M-16 *

Request no. :	From	181+000	to	181+350	Company	المستفيد	
Station :			level	-6.00	DATE	26/02/2024	
Description :	EMBANKMENT Materials						
	1	2	3	4	5	6	
No. of Station →		181+020	181+070	181+120	181+170	181+220	181+280
1-Mass Of Materials							
Wt of Total Wet Materials	gm	85,400	85,465	85,512	85,624	85,319	85,652
Wt of Wet Oversize Fraction	gm	27,100	27,050	27,115	27,110	27,185	27,200
Wt of Wet Control Fraction	gm	58,300	58,415	58,397	58,514	58,134	58,452
Wt of Dry Oversize Fraction	gm	26,721	26,536	26,708	26,676	26,644	26,710
Wt of Dry Control Fraction	gm	55,618	55,728	55,711	55,881	55,691	55,822
2.Determination of moist material							
Moisture Content of Control Fraction	%	4.6%	4.6%	4.6%	4.5%	4.4%	4.5%
Moisture Content of Oversize Fraction	%	1.40%	1.50%	1.50%	1.60%	1.70%	1.80%
3-Volume Of the Test Pit							
Wt Calibrated sand in Pit and template	gm	81,215	81,115	81,320	81,330	81,320	81,145
Wt of Calibrated sand in template	gm	26,100	26,100	26,100	26,100	26,100	26,100
Wt of Calibrated sand in test Pit	gm	55,115	55,015	55,220	55,230	55,220	55,045
Density of Calibrated sand	gm/cm3	1.47	1.47	1.47	1.47	1.47	1.47
Specific Gravity of Oversize Fraction	gm/cm3	2.530	2.530	2.530	2.530	2.530	2.530
Volume of the Test Pit	cm3	37,493	37,425	37,565	37,571	37,565	37,446
Volume of Wet Oversize Fraction	cm3	10,711	10,692	10,737	10,715	10,713	10,751
Volume of Wet Control Fraction	cm3	26,782	26,733	26,847	26,856	26,851	26,695
4-Relative Density Calculation							
Wet Density of Control Fraction Gm/cm3		2.18	2.19	2.18	2.18	2.17	2.19
Dry Density of Control Fraction Gm/cm3		2.08	2.09	2.08	2.08	2.08	2.10
Q1.4	maximum dry density	2.140	2.140	2.140	2.140	2.140	2.140
	G.M.C	5.30%	5.30%	5.30%	5.30%	5.30%	5.30%
Relative Compaction		97.25%	97.62%	97.17%	97.43%	97.04%	97.31%
remarks		95%	95%	95%	95%	95%	95%
Pass / Fail		Pass	Pass	Pass	Pass	Pass	Pass

شركة أوديك
مستشاري التربة والأساسات
للتنفيذ والمقاولات
ب.ت: ٨٩٨٤٥٠ ب.س: ٧٠٣٠٧٥٩٠١٦٧



استشاري أبحاث التربة والاساسات
أ.د.م. هشام محمد حلمي



مشروع:
قطار أسوان الكهربائي السريع - القطاع الثاني

Standard Test Method For Density of Soil and Rock in place by the Sand Replacement Method in a Test Pit " ASTM D1556 M-16 "

Request no.:	From	180+376	to	180+540	Company	أوديك
Station :			Level	-2.00	DATE	21/02/2024
Description :	EMBANKMENT Materials					

	1	2	3	4		
No. of Station →	180+400	180+450	180+500	180+550		

1-Mass Of Materials

Wt of Total Wet Materials	gm	71,260	71,202	71,308	71,260		
Wt of Wet Oversize Fraction	gm	32,505	32,490	32,300	32,350		
Wt of Wet Control Fraction	gm	38,755	38,712	39,008	38,910		
Wt of Dry Oversize Fraction	gm	31,920	31,875	31,886	31,800		
Wt of Dry Control Fraction	gm	37,011	36,931	37,133	37,158		

2.Determination of moist material

Moisture Content of Control Fraction	%	4.5%	4.6%	4.6%	4.4%		
Moisture Content of Oversize Fraction	%	1.80%	1.90%	1.90%	1.70%		

3-Volume Of the Test Pit

Wt Calibrated sand in Pit and template	gm	71,000	71,120	71,090	71,160		
Wt of Calibrated sand in template	gm	26,100	26,100	26,100	26,100		
Wt of Calibrated sand in test Pit	gm	44,900	45,020	44,990	45,060		
Density of Calibrated sand	gm/cm ³	1.47	1.47	1.47	1.47		
Specific Gravity of Oversize Fraction	gm/cm ³	2.530	2.530	2.530	2.530		
Volume of the Test Pit	cm ³	30,544	30,626	30,605	30,653		
Volume of Wet Oversize Fraction	cm ³	12,848	12,842	12,767	12,787		
Volume of Wet Control Fraction	cm ³	17,696	17,784	17,839	17,866		

4-Relative Density Calculation

Wet Density of Control Fraction Gm/cm ³	2.19	2.18	2.19	2.18		
Dry Density of Control Fraction Gm/cm ³	2.10	2.08	2.09	2.09		
Q: 4	maximum dry density	2.140	2.140	2.140	2.140	
	O.M.C	5.30%	5.30%	5.30%	5.30%	
Relative Compaction		97.93%	97.25%	97.50%	97.48%	
remarks		95%	95%	95%	95%	
Pass / Fail		Pass	Pass	Pass	Pass	

شركة أوديك
لتطوير البنية التحتية والمقاولات
س.ت. ٨٥٠ | ف. ٧ | الهاتف: ٧٠٣-٧٥٩

W.E. CONSULTANT
م.ع. مستشار

استشاري أبحاث التربة والاساسات
أ.د.م. هشام محمد حلمي



مشروع:
قطار أسوان الكهربائي السريع - القطاع الثاني

Standard Test Method For Density of Soil and Rock in place By the Sand Replacement Method in a Test Pit " ASTM D414 N- 15 "

Request no.:		From	181+260	to	181+420	Company	أوديك
Station :		Level	-2.00	DATE	20/02/2024		
Description :	EMBANKMENT Materials						
		1	2	3	4		
No. of Station →		181+280	181+330	181+380	181+420		
1-Mass Of Materials							
Wt of Total Wet Materials	gm	71,410	71,520	71,550	72,000		
Wt of Wet Oversize Fraction	gm	32,600	32,516	32,400	32,200		
Wt of Wet Control Fraction	gm	38,810	39,010	39,150	39,800		
Wt of Dry Oversize Fraction	gm	33,131	32,023	31,914	31,717		
Wt of Dry Control Fraction	gm	37,141	37,333	37,349	38,049		
2.Determination of moist material							
Moisture Content of Control Fraction	%	4.2%	4.3%	4.6%	4.4%		
Moisture Content of Oversize Fraction	%	1.50%	1.50%	1.50%	1.50%		
3-Volume Of the Test Pit							
Wt Calibrated sand in Pit and template	gm	71,120	71,060	71,133	71,235		
Wt of Calibrated sand in template	gm	26,100	26,100	26,109	26,100		
Wt of Calibrated sand in test Pit	gm	45,020	44,960	45,023	45,135		
Density of Calibrated sand	gm/cm ³	1.47	1.47	1.47	1.47		
Specific Gravity of Oversize Fraction	gm/cm ³	2.530	2.530	2.530	2.530		
Volume of the Test Pit	cm ³	30,626	30,583	30,635	30,690		
Volume of Wet Oversize Fraction	cm ³	12,885	12,850	12,806	12,727		
Volume of Wet Control Fraction	cm ³	17,740	17,735	17,828	17,963		
4-Relative Density Calculation							
Wet Density of Control Fraction Gm/cm ³		2.18	2.20	2.20	2.23		
Dry Density of Control Fraction Gm/cm ³		2.10	2.11	2.10	2.12		
C: 4	maximum dry density	2.135	2.139	2.135	2.139		
	D.M.C	6.10%	6.10%	6.10%	6.10%		
Relative Compaction		98.06%	98.50%	98.15%	99.21%		
remarks		95%	95%	95%	95%		
Pass / Fail		Pass	Pass	Pass	Pass		

شركة أوديك
م.ت.م. استشاري
للتطوير والتطوير
٢٠٢٠-٢٠٢٤
٨٩٨٤٥٠

EGSCO
M.E.ACONSULTANT
محمد عتيق سوري

استشاري أبحاث التربة والأساسات
أ.د.م. هشام محمد حلمي



مشروع:
قطار أسوان الكهربائي السريع - القطاع الثاني

Standard Test Method For Density of Soil and Rock in place By the Sand Replacement Method in a Test Pit * ASTM D4514 M-22

Request no.:	From	181+480	to	181+580	Company	أوديك
Station :			Level	-4.00	DATE	20/02/2024
Description :	EMBANKMENT Materials					

	1	2				
No. of Station →	181+500	181+550				

1-Mass Of Materials

Wt of Total Wet Materials	gm	82,250	81,990			
Wt of Wet Oversize Fraction	gm	31,100	31,500			
Wt of Wet Control fraction	gm	51,150	50,490			
Wt of Dry Oversize Fraction	gm	30,540	30,933			
Wt of Dry Control fraction	gm	48,951	48,218			

2.Determination of moist material

Moisture Content of Control Fraction	%	4.3%	4.3%			
Moisture Content of Oversize Fraction	%	1.60%	1.60%			

3-Volume Of the Test Pit

Wt Calibrated sand in Pit and template	gm	79,320	79,320			
Wt of Calibrated sand in template	gm	26,110	26,110			
Wt of Calibrated sand in test Pit	gm	52,210	52,220			
Density of Calibrated sand	gm/cm ³	1.47	1.47			
Specific Gravity of Oversize Fraction	gm/cm ³	2.530	2.530			
Volume of the Test Pit	cm ³	35,517	35,524			
Volume of Wet Oversize Fraction	cm ³	12,292	12,451			
Volume of Wet Control Fraction	cm ³	23,225	23,073			

4-Relative Density Calculation

Wet Density of Control Fraction Gm/cm ³	2.20	2.19			
Dry Density of Control Fraction Gm/cm ³	2.11	2.09			
Gr 4	maximum dry density	2.141	2.141		
	O.M.C	6.50%	6.50%		
Relative Compaction		98.63%	97.81%		
Remarks		95%	95%		
Pass / Fail		Pass	Pass		

شركة أوديك
M.E. CONTRACTOR
للتوريد والبناء والمقاولات
س.ت. ٨٩٨٤٥ ب.ص. ١٦٧-٧٥٩-٧٠٣

M.E./CONSULTANT
محمد رشاد محمد

استشاري أبحاث التربة والأساسات
أ.د.م. هشام محمد حلمي



مشروع:
لطار أسوان الكهربائي السريع - القطاع الثاني

Standard Test Method For Density of Soil and Rock in place By the Sand Replacement Method in a Test Pit * ASTM D4314 M-15 *

Request no.:		From	181+480	to	181+580	Company	أوديك
Station:		Level	-4.00	DATE	11/02/2024		
Description:	EMBANKMENT Materials						
		1	2				
No. of Station →		181+500	181+550				
1-Mass Of Materials							
Wt of Total Wet Materials	gm	80,300	80,360				
Wt of Wet Oversize Fraction	gm	29,000	29,200				
Wt of Wet Control Fraction	gm	51,300	51,160				
Wt of Dry Oversize Fraction	gm	28,566	28,704				
Wt of Dry Control Fraction	gm	49,094	48,656				
2.Determination of moist material							
Moisture Content of Control Fraction	%	4.3%	4.5%				
Moisture Content of Oversize Fraction	%	1.50%	1.70%				
3-Volume Of the Test Pit							
Wt Calibrated sand in Pit and template	gm	78,430	78,400				
Wt of Calibrated sand in template	gm	26,810	26,010				
Wt of Calibrated sand in test Pit	gm	52,420	52,390				
Density of Calibrated sand	gm/cm ³	1.47	1.47				
Specific Gravity of Oversize Fraction	gm/cm ³	2.530	2.530				
Volume of the Test Pit	cm ³	35,660	35,639				
Volume of Wet Oversize Fraction	cm ³	11,462	11,543				
Volume of Wet Control Fraction	cm ³	24,197	24,096				
4-Relative Density Calculation							
Wet Density of Control Fraction Gm/cm ³		2.12	2.12				
Dry Density of Control Fraction Gm/cm ³		2.03	2.08				
Qt 4	maximum dry density	2.141	2.141				
	D.M.C	6.50%	6.50%				
Relative Compaction		94.94%	94.88%				
Remarks		95%	95%				
Pass / Fail		Fail	Fail				

شركة أوديك
التوريدات والمقاولات
٢٠٢-٧٥٩-١٦٧
٨٩٨٤٥٠٠

M.E./CONSULTANT
محمد المصطفى

استشاري أبحاث التربة والأساسات
أ.د.م. هشام محمد حلمي



مشروع
قطار أسوان الكهربائي السريع - القطاع الثاني

Standard Test Method For Density of Soil and Rock in place By the Sand Replacement Method in a Test Pit * ASTM D1556-16 *

Request no.:		From	180+540	to	180+700	Company	أوديك
Station:				Level	-2.80	DATE	12/02/2024
Description:	EMBANKMENT Materials						
		1	2	3	4		
No. of Station →		180+560	180+610	180+660	180+710		
1-Mass Of Materials							
Wt of Total Wet Materials	gm	82,300	82,360	82,340	82,400		
Wt of Wet Oversize Fraction	gm	90,130	90,210	90,620	90,412		
Wt of Wet Control Fraction	gm	52,080	52,050	51,720	51,988		
Wt of Dry Oversize Fraction	gm	29,635	29,666	30,009	29,865		
Wt of Dry Control Fraction	gm	48,841	48,812	48,593	48,597		
2.Determination of moist material							
Moisture Content of Control Fraction	%	4.3%	4.3%	4.5%	4.6%		
Moisture Content of Oversize Fraction	%	1.00%	1.80%	1.80%	1.80%		
3-Volume Of the Test Pit							
Wt Calibrated sand in Pit and template	gm	79,500	79,510	79,260	79,600		
Wt of Calibrated sand in template	gm	26,100	26,100	26,100	26,100		
Wt of Calibrated sand in test Pit	gm	53,400	53,410	53,160	53,500		
Density of Calibrated sand	gm/cm ³	1.47	1.47	1.47	1.47		
Specific gravity of Oversize Fraction	gm/cm ³	2.530	2.530	2.530	2.530		
Volume of the Test Pit	cm ³	36,327	36,333	36,163	36,395		
Volume of Wet Oversize Fraction	cm ³	11,905	11,941	12,109	12,031		
Volume of Wet Control Fraction	cm ³	24,421	24,393	24,060	24,374		
4-Relative Density Calculation							
Wet Density of Control Fraction Gm/cm ³		2.13	2.13	2.15	2.13		
Dry Density of Control Fraction Gm/cm ³		2.04	2.05	2.06	2.04		
Ct 4	maximum dry density	2.139	2.139	2.139	2.139		
	O.M.C	6.10%	6.10%	6.10%	6.10%		
Relative Compaction		95.59%	95.66%	96.17%	95.33%		
remarks		95%	95%	95%	95%		
Pass / Fail		Pass	Pass	Pass	Pass		

شركة أوديك
لتطوير البنية التحتية
س.ت: ١٩٨٤٥٠ ب.مصر الجديدة

M.E/CONSULTANT

م.ع. درة

استشاري أبحاث التربة والاساسات
أ.د.م. هشام محمد حلمي



مشروع:
قطار أسوان الكهربائي السريع - القطاع الثاني

Standard Test Method For Density of Soil and Rock in place by the Sand Replacement Method is a Test Pit "ASTM D4914 M-15"

Request no.:	From	180+540	to	180+760	Company	أوديك
Station :		Level	-2.00	DATE	11/02/2024	
Description :	EMBANKMENT Materials					
	1	2	3	4		
No. of Station →	180+560	180+610	180+660	180+710		
1-Mass Of Materials						
Wt of Total Wet Materials	gm	80,210	80,255	80,341	80,340	
Wt of Wet Oversize Fraction	gm	29,309	29,340	29,355	29,215	
Wt of Wet Control Fraction	gm	51,110	51,115	51,186	51,325	
Wt of Dry Oversize Fraction	gm	26,634	26,674	26,659	26,689	
Wt of Dry Control Fraction	gm	48,563	48,917	48,729	48,964	
2.Determination of moist material						
Moisture Content of Control Fraction	%	4.2%	4.3%	4.6%	4.6%	
Moisture Content of Oversize Fraction	%	1.60%	1.60%	1.70%	1.80%	
3-Volume Of the Test Pit						
Wt Calibrated sand in Pit and template	gm	79,320	79,410	79,200	79,250	
Wt of Calibrated sand in template	gm	26,100	26,300	26,100	26,100	
Wt of Calibrated sand in test Pit	gm	53,220	53,310	53,100	53,150	
Density of Calibrated sand	gm/cm ³	1.47	1.47	1.47	1.47	
Specific Gravity of Oversize Fraction	gm/cm ³	2.530	2.530	2.530	2.530	
Volume of the Test Pit	cm ³	36,204	36,265	36,122	36,156	
Volume of Wet Oversize Fraction	cm ³	11,502	11,518	11,524	11,547	
Volume of Wet Control Fraction	cm ³	24,702	24,748	24,599	24,609	
4-Relative Density Calculation						
Wet Density of Control Fraction Gm/cm ³		2.07	2.07	2.08	2.09	
Dry Density of Control Fraction Gm/cm ³		1.99	1.99	1.99	1.99	
Q _s :	maximum dry density	2.139	2.139	2.139	2.139	
	O.M.C	6.10%	6.10%	6.10%	6.10%	
Relative Compaction		92.83%	92.58%	92.83%	93.22%	
Remarks		95%	95%	95%	95%	
Pass / Fail		Fail	Fail	Fail	Fail	

شركة أوديك
للتوريدات والمقاولات
س.ت: ٩٨٤٥٠ الفاكس: ٧٠٢-٢٥٦٩٦٦

M.E./CONSULTANT

محمد الشرايكة

استشاري أبحاث التربة والاساسات
أ.د.م. هشام محمد حلمي



مشروع:
قطار أسوان الكهربائي السريع - القطاع الثاني

Standard Test Method For Density of Soil and Rock in place By the Sand Replacement Method in a Test Pit " ASTM D4914 M-16 "

Request no.:		From	181+000	to	181+220	Company	أوديك
Station :				level	-4.90	DATE	08/02/2024
Description :	EMBANKMENT Materials						
		1	2	3	4	5	
No. of Station →		181+020	181+070	181+120	181+170	181+220	
1-Mass Of Materials							
Wt of Total Wet Materials	gm	88,150	88,400	88,610	88,516	88,288	
Wt of Wet Oversize Fraction	gm	38,850	38,810	38,574	38,694	38,697	
Wt of Wet Control Fraction	gm	49,300	49,590	50,032	49,822	49,593	
Wt of Dry Oversize Fraction	gm	38,092	38,120	38,025	38,102	38,083	
Wt of Dry Control Fraction	gm	47,517	47,749	47,981	47,758	47,405	
2.Determination of moist material							
Moisture Content of Control Fraction	%	4.2%	4.1%	4.2%	4.2%	4.3%	
Moisture Content of Oversize Fraction	%	1.50%	1.60%	1.80%	1.80%	2.00%	
3-Volume Of the Test Pit							
Wt Calibrated sand in Pit and template	gm	78,220	78,215	78,611	78,590	78,328	
Wt of Calibrated sand in template	gm	26,200	26,200	26,209	26,290	26,200	
Wt of Calibrated sand in test Pit	gm	52,020	52,115	52,412	52,300	52,128	
Density of Calibrated sand	gm/cm ³	1.47	1.47	1.47	1.47	1.47	
Specific Gravity of Oversize Fraction	gm/cm ³	2.530	2.530	2.530	2.530	2.530	
Volume of the Test Pit	cm ³	35,388	35,452	35,654	35,578	35,456	
Volume of Wet Oversize Fraction	cm ³	12,075	12,099	12,089	12,116	12,131	
Volume of Wet Control Fraction	cm ³	23,313	23,354	23,565	23,462	23,325	
4-Relative Density Calculation							
Wet Density of Control fraction Gm/cm ³		2.13	2.13	2.12	2.13	2.12	
Dry Density of Control Fraction Gm/cm ³		2.04	2.05	2.04	2.04	2.04	
Q: 4	maximum dry density	2.141	2.141	2.141	2.141	2.141	
	O.M.C	6.50%	6.50%	6.50%	6.50%	6.50%	
Relative Compaction		95.37%	95.56%	95.16%	95.29%	95.11%	
remarks		95%	95%	95%	95%	95%	
Pass / Fail		Pass	Pass	Pass	Pass	Pass	

شركة أوديك
للتوريدات والمقاولات
م.ع. CONTRACTOR
ت. ٢٠٢-٢٥٥-١٦٧
٢٩٨٤٥

M.E./CONSULTANT

محمد العبدالله



۱۳۸۵



545125



قطار لسون الكهربائي السريع - القطاع الثاني

Request no.:	From	180+000	To	185+000	Company	COIK
Station :		Level	-4.50		DATE	25/01/2024
Destination :	PILL LAYER					

Max. dry density g/cm ³	O.M.C. %	Degree of Compaction Required, %	Bulk Density of Specified sand, g/cm ³	Sand Weight of Cone (gm)
2.143	6.4	95	1.400	5449

[illegible]

RESULTS



مكتب أ.د/حسن مهدي
للإستشارات الهندسية



الجمهورية العراقية
وزارة التخطيط



ملف رقم:

شماره پروانه الترخيص - قطاع الطرق

Determination of field density - ASTM D 1556

Request no.:	From	180+375	to	180+580	Company	ODIK
Station :		Level		- 2.50	DATE	27/03/2024
Description :	FILL LAYER					

Proctor Modified Test Results:

Max. dry density g/cm ³	O.M.C. %	Degree of Compaction Required %	Sub Density of Specified sand g/cm ³	Sand Weight of Cone (gm)
2.143	6.40	96	1.489	1440

Test No.	1	2	3	4	5															
Station of sample	180+400	180+460	180+500	180+520	180+570															
Wt. Of Sand before test, gm	11020	10920	10630	10419	10320															
Wt. Of Sand after test, gm	7519	7489	7150	7021	6782															
Wt. Of Sand fill hole&cone, gm	3501	3431	3480	3389	3538															
Wt. Of Sand fill cone, gm	1440	1440	1440	1440	1440															
Wt. Of Sand fill hole, gm	2061	1991	2040	1940	2098															
Volume of hole, cm ³	1393	1346	1378	1317	1418															
Wt of sample from hole, gm	3106	3004	3190	2950	3150															
Wet density of soil, g/cm ³	2.239	2.233	2.249	2.248	2.222															
No. of container	1	2	3	4	5	6	7	8	9	10										
Wt. of container, gm	82.4	82.2	82.3	82.5	82.4	82.3	82.4	80.3	81.4	80.7										
Wt. Of sample& container before drying, gm	292.0	278.9	288.0	281.6	283.3	292.0	295.7	286.4	327.3	311.6										
wt. of container& dried sample, gm	278.8	267.0	285.5	265.2	270.6	279.2	282.7	273.0	313.2	297.4										
Water wt.	13.2	12.9	12.5	12.4	12.7	12.8	13.0	13.4	14.1	14.2										
Wt. of dried sample, gm	216.4	204.8	223.2	206.7	208.2	216.9	225.3	212.7	251.8	236.7										
Moisture content, %	6.10	6.30	5.60	6.00	6.10	5.90	5.90	6.30	5.60	6.00										
Average moisture content%	6.2	5.8	6.0	6.1	5.8															
Dry density, g/cm ³	2.100	2.111	2.122	2.111	2.100															
Compaction (%)	98.00%	99.50%	99.00%	98.50%	98.00%															
Acceptance	Y	Y	Y	Y	Y															

شركة اوديك
للتوريد والمقاولات
ت. ٠٢٠٧٥٩٠١٦٢٠
ف. ٠٢٠٧٥٩٠١٦٢٠

MOE TECHNICAL REPORT

مورد المراجعة



تقارن أوضاع الكهرباء في السبعينيات - القطاع الثاني

Request no.:		From	180+580	to	180+700	Company	CDK
Station :			Level		+ 2.50	DATE	06/01/2024
Description :	FILL LAYER						

Max. dry density g/cm ³	O.M.C. %	Degree of Compaction Required, %	Bulk Density of Specified sand, g/cm ³	Seed Weight of Cone (gm)
2.141	9.1	91	1.480	1443

सुधामणि



20/11/20

المشروع:

قمار لحدود الكهربي السريخ - التتابع الثاني

Determination of field density - ASTM D 1556

Request no.:	From	181+520	to	181+580	Company	ODIK
Station :		level		- 4.50	DATE	18/01/2024
Description :	FILL LAYER					

Plaster Modified Testina Results:

Max. dry density g/cm ³	O.M.C. %	Degree of Compaction Required %	Bulk Density of Specified sand g/cm ³	Sand Weight of Core (gm)
2.141	6.1	96	1.430	1440

[illegible]

شركة اوديك
AL-ODIK CONSTRUCTORS
للتوريد والبناء
ب.ت. ٩٨٤٥٠ ٩٧٠٠٠٠٠
٧٠٢-٧٥٤-١٩٧

WILL CONULTING

گودارہہ



قطر أسوان الكهربائي السريع - القطاع الثاني

Request No.:		From	1824520	To	1824580	Company	ODIP
Station			Level		+ 4.50	DATE	04/01/2024
Description :	FILL LAYER						

Max. dry density (g/cm ³)	O.M.C. %	Degree of Compaction Required, %	Bulk Density of Specified sand, g/cm ³	Sand Weight of Cons. (gm)
2.341	6.1	85	1.630	1.630

Test No.	1		2	
Station of sample	181+540		181+580	
Wt. Of Sand before test,gm	10218		10160	
Wt. Of Sand after test,gm	6484		6419	
Wt. Of Sand fill hole&cone,gm	3754		3741	
Wt. Of Sand fill cone,gm	1440		1440	
Wt. Of Sand fill hole,gm	2314		2301	
Volume of hole,cm ³	1564		1555	
Wt of sample from hole,gm	3415		3360	
Wat density of soil,gm/cm ³	2.184		2.161	
No. of container	1	2	3	4
Wt. of container,gm	62.4	62.2	62.3	62.5
Wt. Of sample& container before drying,gm	362.8	379.3	396.2	442.1
wt. of container& dried sample,gm	346.2	363.1	380.3	425.1
Water wt.	16.5	16.7	15.9	16.0
Wt. of dried sample,gm	283.8	300.9	318.0	383.6
Moisture content,%	5.85	5.55	5.00	4.40
Average moisture content%	5.7		4.7	
Dry density,gm/cm ³	2.608		2.064	
Compaction (%)	95.50%		96.40%	
Acceptance	Y		Y	

محمد بن عبد الله

استشاري أبحاث التربة والاساسات
أ.د.م. هشام محمد حلمي



مشروع:
فطار أسوان الكهربائي السريع - القطاع الثاني

Standard Test Method For Density of Soil and Rock in place By the Sand Replacement Method in a Test Pit " ASTM D4914 M-15 "

Request No.:		From	180+810	to	181+180	Company	أوديك	
Station :				level	-5.00	DATE	02/01/2024	
Description :	EMBANKMENT Materials							
			1	2	3	4	5	6
No. of Station →			180+900	180+950	181+000	181+050	181+100	181+150
1-Mass Of Materials								
Wt of Total Wet Materials	gm	80,100	80,120	80,660	80,380	80,110	88,300	
Wt of Wet Oversize Fraction	gm	29,550	29,626	29,530	29,452	29,587	38,100	
Wt of Wet Control Fraction	gm	50,550	50,694	51,130	50,928	50,523	50,200	
Wt of Dry Oversize Fraction	gm	29,077	29,152	29,028	29,099	29,148	29,649	
Wt of Dry Control Fraction	gm	48,528	48,365	48,982	48,840	48,401	48,092	
2.Determination of moist material								
Molature Content of Control Fraction	%	4.0%	4.1%	4.2%	4.1%	4.2%	4.2%	
Molature Content of Oversize Fraction	%	1.60%	1.60%	1.70%	1.70%	1.50%	1.50%	
3-Volume Of the Test Pit								
Wt Calibrated sand in Pit and template	gm	78,530	78,600	78,680	78,520	78,700	78,820	
Wt of Calibrated sand in template	gm	26,110	26,110	26,110	26,110	26,110	26,110	
Wt of Calibrated sand in test Pit	gm	52,420	52,490	52,570	52,410	52,590	52,710	
Density of Calibrated sand	gm/cm ³	1.47	1.47	1.47	1.47	1.47	1.47	
Specific Gravity of Oversize Fraction	gm/cm ³	2.530	2.530	2.530	2.530	2.530	2.530	
Volume of the Test Pit	cm ³	35,600	35,707	35,762	35,655	35,776	35,721	
Volume of Wet Oversize Fraction	cm ³	11,686	11,710	11,672	11,641	11,894	13,897	
Volume of Wet Control Fraction	cm ³	23,914	23,998	24,090	24,014	24,081	21,824	
4-Relative Density Calculation								
Wet Density of Control Fraction : gm/cm ³		2.11	2.11	2.12	2.12	2.10	2.11	
Dry Density of Control Fraction : gm/cm ³		2.03	2.03	2.04	2.04	2.01	2.02	
Q.4.	maximum dry density	2.147	2.147	2.147	2.147	2.147	2.147	
	O.M.C	6.00%	6.00%	6.00%	6.00%	6.00%	6.00%	
Relative Compacion		94.41%	94.43%	94.87%	94.89%	93.78%	94.19%	
remarks		95%	95%	95%	95%	95%	95%	
Pass / Fail		Fail	Fail	Fail	Fail	Fail	Fail	

شركة أوديك
للتوريد والبناء
س.ت: ٩٨٤٥٠
ص.ب: ٧٥٥٩٧

M.E./CONSULTANT

محمد رشيد

استشاري أبحاث التربة والاساسات
أ.د.م. هشام محمد حلمي



مشروع:
قطار أسوان الكهربائي السريع - القطاع الثاني

Standard Test Method For Density of Soil and Rock in place by the Sand Replacement Method is a Test Pit " ASTM D1556 M-18 "

Request no.:	From	180+880	to	181+180	Company	u/y/24	
Station :			Level	-5.00	DATE	08/01/2024	
Description :	EMBRANKMENT Materials						
	1	2	3	4	5	6	
No. of Station →	180+900	180+950	181+000	181+050	181+100	181+160	
1-Mass Of Materials							
Wt of Total Wet Materials	gm	70,500	71,420	70,050	70,640	70,124	70,564
Wt of Wet Oversize Fraction	gm	33,610	33,350	33,130	33,653	33,490	33,900
Wt of Wet Control Fraction	gm	36,890	38,070	36,930	36,988	36,674	36,764
Wt of Dry Oversize Fraction	gm	33,274	32,653	32,723	33,215	33,082	33,527
Wt of Dry Control Fraction	gm	35,267	36,624	35,379	35,361	35,024	35,287
2.Determination of moist material							
Moisture Content of Control Fraction	%	4.4%	4.3%	4.2%	4.4%	4.5%	4.1%
Moisture Content of Oversize Fraction	%	1.00%	1.00%	1.10%	1.30%	1.10%	1.40%
3-Volume Of the Test Pit							
Wt Calibrated sand in Pit and template	gm	70,110	70,202	70,090	70,133	70,295	70,055
Wt of Calibrated sand in template	gm	25,700	25,700	25,700	25,700	25,700	25,700
Wt of Calibrated sand in test Pit	gm	44,410	44,502	44,390	44,433	44,595	44,355
Density of Calibrated sand	gm/cm3	1.47	1.47	1.47	1.47	1.47	1.47
Specific Gravity of Oversize Fraction	gm/cm3	2.590	2.530	2.530	2.530	2.530	2.530
Volume of the Test Pit	cm3	30,211	30,273	30,156	30,227	30,296	30,173
Volume of Wet Oversize Fraction	cm3	13,285	13,303	13,091	13,301	13,221	13,380
Volume of Wet Control Fraction	cm3	16,926	17,371	17,066	16,925	17,075	16,814
4-Relative Density Calculation							
Wet Density of Control Fraction Gm/cm3		2.18	2.23	2.16	2.19	2.15	2.19
Dry Density of Control Fraction Gm/cm3		2.09	2.14	2.08	2.09	2.06	2.10
Q4	maximum dry density	2.147	2.147	2.147	2.147	2.147	2.147
	O.M.C	6.00%	6.00%	6.00%	6.00%	6.00%	6.00%
Relative Compaction		97.23%	99.53%	96.73%	97.50%	95.73%	97.83%
remarks		95%	95%	95%	95%	95%	95%
Pass / Fail		Pass	Pass	Pass	Pass	Pass	Pass

شركة أودييك
للتطوير والهندسة
الهندسة المدنية
٢٠٢٠٧٥٩٠٦٧٠
٨٩٨٤٨٥٠٠

M.E./CONSULTANT
م.ع. استشاري

Standard Test Method For Density of Soil and Rock in place by the Sand Replacement Method in a Test Pit. * ASTM D4914 M-16 *

شركة اوديك
للتوريدات والمقاولات
س.ت: ٧٠٢-٧٥٨-١٩٧٧ / ٤٦٨٥٠
(الطبعة)

تحریر: محمد

استشاري ابحاث التربة والاساسات
أ.د.م. هشام محمد حلمي



مشروع:
قطار أسوان الكهربائي السريع - القطاع الثاني

Standard Test Method For Density of Soil and Rock in place By the Sand Replacement Method in a Test Pit * ASTM D4914 M-15 *

Request no.:		From	180+500	to	180+720	Company	أوديك
Station :		Level		-3.00	DATE	27/12/2023	
Description :	EMBANKMENT Materials						
		1	2	3			
No. of Station →		180+620	180+670	180+720			
1-Mass Of Materials							
Wt of Total Wet Materials	gm	85,669	85,560	85,500			
Wt of Wet Oversize Fraction	gm	32,600	33,200	34,250			
Wt of Wet Control Fraction	gm	53,069	52,360	51,250			
Wt of Dry Oversize Fraction	gm	32,111	32,636	33,756			
Wt of Dry Control Fraction	gm	50,734	51,119	49,200			
2.Determination of moist material							
Moisture Content of Control Fraction	%	4.4%	4.2%	4.0%			
Moisture Content of Oversize Fraction	%	1.50%	1.70%	1.50%			
3-Volume Of the Test Pit							
Wt Calibrated sand in Pit and template	gm	81,500	81,650	81,524			
Wt of Calibrated sand in template	gm	26,553	26,503	26,553			
Wt of Calibrated sand in test Pit	gm	54,947	55,097	54,971			
Density of Calibrated sand	gm/cm ³	1.47	1.47	1.47			
Specific Gravity of Oversize Fraction	gm/cm ³	2.550	2.530	2.530			
Volume of the Test Pit	cm ³	37,379	37,481	37,395			
Volume of Wet Oversize Fraction	cm ³	12,885	13,123	13,538			
Volume of Wet Control Fraction	cm ³	24,494	24,358	23,858			
4-Relative Density Calculation							
Wet Density of Control Fraction Gm/cm ³		2.17	2.19	2.15			
Dry Density of Control Fraction Gm/cm ³		2.08	2.10	2.07			
Q4:	maximum dry density	2.143	2.143	2.143			
	O.M.C	6.10%	6.10%	6.10%			
Relative Compaction		96.84%	98.10%	96.39%			
remarks		95%	95%	95%			
Pass / Fail		Pass	Pass	Pass			

شركة اوديك
م.ع. CONTRACTOR
للتوريد والمصاولات
س.ت: ٨٩٨٤٥٠ ج.م. ٢٠٢-٢٥٩-٣٦٧٥

M.E. CONSULTANT

م.ع. استشاري

استشاري أبحاث التربة والأساسات
أ.د.م. هشام محمد حنفي



مشروع:
قطار أسوان الكهربائي السريع - القطاع الثاني

Standard Test Method For Density of Soil and Rock in place By the Sand Replacement Method in a Test Pit " ASTM D4944 M-16 "

Request no.:	From	182+040	to	182+020	Company	أوديك			
Station:		Level	-1.75	DATE	26/12/2023				
Description :	EMBANKMENT Materials								
	1	2	3	4	5	6	7	8	
No. of Station →	182+050	182+070	182+090	182+110	182+130	182+150	182+170	182+190	
1-Mass Of Materials									
Wt of Total Wet Materials	gm	82,600	83,780	83,655	82,950	82,410	83,640	83,710	83,480
Wt of Wet Oversize Fraction	gm	34,110	34,600	34,280	34,910	34,200	33,800	31,675	33,860
Wt of Wet Control Fraction	gm	48,490	49,180	49,375	48,040	48,210	49,840	50,035	49,620
Wt of Dry Oversize Fraction	gm	83,586	83,877	83,796	84,353	83,687	83,218	83,170	83,518
Wt of Dry Control Fraction	gm	46,007	46,672	46,862	45,734	45,800	47,353	47,883	47,080
2.Determination of moist material									
Moisture Content of Control Fraction	%	5.1%	5.1%	4.9%	4.8%	5.0%	5.2%	5.1%	5.3%
Moisture Content of Oversize Fraction	%	1.50%	1.80%	1.70%	1.66%	1.50%	1.40%	1.56%	1.60%
3-Volume Of the Test Pit									
Wt Calibrated sand in Pit and template	gm	80,960	80,420	80,680	80,080	80,140	80,350	81,600	80,455
Wt of Calibrated sand in template	gm	26,500	26,500	26,500	26,500	26,500	26,500	26,500	26,500
Wt of Calibrated sand in test Pit	gm	53,560	53,920	54,180	53,580	53,640	53,850	54,100	53,955
Density of Calibrated sand	gm/cm3	1.48	1.48	1.48	1.48	1.48	1.48	1.48	1.48
Specific Gravity of Oversize Fraction	gm/cm3	2.526	2.520	2.520	2.520	2.528	2.520	2.520	2.520
Volume of the Test Pit	cm3	36,189	36,432	36,608	36,203	36,243	36,385	34,554	36,406
Volume of Wet Oversize fraction	cm3	13,536	13,730	13,643	13,853	13,571	13,369	13,363	13,437
Volume of Wet Control Fraction	cm3	22,653	22,702	22,965	22,350	22,672	23,016	23,191	23,020
4-Relative Density Calculation									
Wet Density of Control Fraction Gm/cm3		2.14	2.17	2.15	2.15	2.13	2.17	2.16	2.16
Dry Density of Control Fraction Gm/cm3		2.04	2.06	2.05	2.05	2.03	2.06	2.05	2.05
Qr 4	maximum dry density	2.181	2.133	2.181	2.181	2.131	2.181	2.181	2.131
	G.M.C	6.40%	6.44%	6.41%	6.40%	6.40%	6.40%	6.40%	6.40%
Relative Compaction		95.57%	96.72%	95.98%	96.25%	95.03%	96.81%	96.33%	96.08%
remarks		95%	95%	95%	95%	95%	95%	95%	95%
Pass / Fail		Pass	Pass	Pass	Pass	Pass	Pass	Pass	Pass

شركة أوديك
التقنية والهندسة
للتنفيذ والتشييد
م.ت. ٤٤٤٤٥٠ - ٧٠٢٠٧٤٥ - ١٩٧٠

M.E./CONSULTANT

محمد عبد الله محمد

استشاري أبحاث التربة والاساسات
أ.د.م. هشام محمد حلي



مشروع:
لطار أسوان الكهربائي السريع - القطاع الثاني

Standard Test Method For Density of Soil and Rock in place by the Sand Replacement Method in a Test Pit " ASTM D4914 M-16 "

Request no.:		From	180+060	to	181+158	Company	لوتور
Station :		Level	-5.10	DATE	21/12/2023		
Description :		SMBRANMENT Materials					
		1	2	3	4		
No. of Station →		180+060	181+030	181+080	181+130		
1-Mass Of Materials							
Wt of Total Wet Materials	gm	84,700	86,500	86,150	85,800		
Wt of Wet Oversize Fraction	gm	33,400	33,050	33,400	33,770		
Wt of Wet Control Fraction	gm	51,300	52,850	52,680	52,140		
Wt of Dry Oversize Fraction	gm	32,865	33,145	32,983	33,297		
Wt of Dry Control Fraction	gm	48,688	49,125	49,603	48,429		
2.Determination of moist material							
Moisture Content of Control Fraction	%	4.8%	5.1%	5.0%	5.2%		
Moisture Content of Oversize Fraction	%	1.60%	1.30%	1.50%	1.40%		
3-Volume Of the Test Pit							
Wt Calibrated sand in Pit and baseplate	gm	81,350	81,420	81,250	81,333		
Wt of Calibrated sand in template	gm	26,500	26,500	26,500	26,500		
Wt of Calibrated sand in test Pit	gm	54,850	54,920	54,750	54,833		
Density of Calibrated sand	gm/cm3	1.48	1.48	1.48	1.48		
Specific Gravity of Control Fraction	gm/cm3	2.520	2.520	2.520	2.520		
Volume of the Test Pit	cm3	37,061	37,108	36,980	37,051		
Volume of Wet Oversize Fraction	cm3	13,254	13,358	13,280	13,401		
Volume of Wet Control Fraction	cm3	23,807	23,755	23,700	23,650		
4-Relative Density Calculation							
Wet Density of Control Fraction Gm/cm3		2.35	2.22	2.22	2.26		
Dry Density of Control Fraction Gm/cm3		2.00	2.12	2.12	2.10		
Q1 &	maximum dry density	2.131	2.131	2.131	2.131		
	O.M.C	6.40%	6.40%	6.40%	6.40%		
Relative Compaction		96.43%	99.34%	99.35%	98.34%		
remarks		95%	95%	95%	95%		
Pass / Fail		Pass	Pass	Pass	Pass		

شركة لوتور
للتوريد والتشييد
ص.ب. ٨٩٨٤٥، ج. ١١٢، ٢٠٢٢٥٩

M.E./CONSULTANT

محمد / السيد

**EGSCO**

Egyptian Geotech. & Struc.

Dr. Eng. Hesham M. Helmy

**PLATE LOADING TEST RESULTS**

PROJECT : القطار الكهربائي السريع (أكتوبر - أسوان) - قطاع الكتي (بني مزار - منقوط)

18-1960

181-160

Plate Dim. :

60 cm

18-1960

Location :

181-100

Company :

أريحا

18-1960


The road

Date :

21/Dec/2023

Soil :

embankment

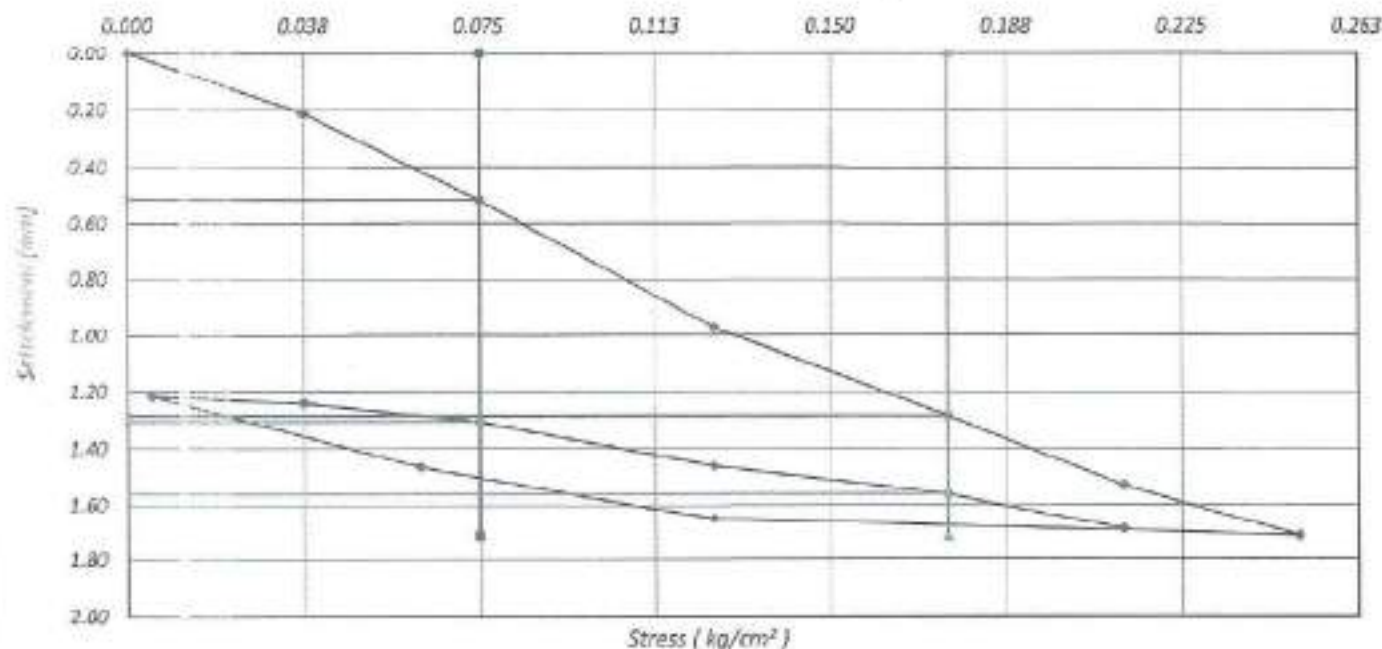Stress - Settlement Relationship

	Load (ton)	Stress (kl Pa)	Settlement (mm)
Loading	0.00	0.000	0.00
	1.06	0.038	0.21
	2.12	0.075	0.52
	3.14	0.125	0.97
	4.95	0.175	1.29
	6.01	0.213	1.53
	7.07	0.250	1.72
Unloading	3.14	0.125	1.65
	1.77	0.063	1.47
	1.14	0.005	1.22
Loading	1.06	0.038	1.24
	2.12	0.075	1.31
	3.14	0.125	1.46
	4.95	0.175	1.56
	6.01	0.213	1.69

G _{max}	0.250	Stress (M Pa)	Settlement (mm)
0.30 G _{max} reloading	0.075		1.31
0.70 G _{max} reloading	0.175		1.56

$$E_{v2} = 176 \text{ M Pa}$$

E _{v2}	176
Specification	E _{v2} ≥ 30
Acceptance	

شركة أوديك
للتوريدات والمقاولات
س.ت: ٨٩٨٤٥ - ٢٠٢-٢٥٥١٦٧

MR. HESHAM M. HELMY

Tel: 23452339

مكتب: 5- عمارات الأمداء والتأمين - طريق النصارى - مدينة نصر - ت: 23452339

استشاري أبحاث التربة والإساسات
أ.د.م. هشام محمد حلمي



مشروع:
قطار أسوان الكهربائي السريع - القطاع الثاني

Standard Test Method For Density of Soil and Rock in place by the Sand Replacement Method in a Test Pit " ASTM D4914 M-16 "

Project no.:	From	180+880	to	180+960	Company	أوديك
Station:			Level	-5.50	DATE	17/12/2023
Description:	EMBANKMENT Materials					
		1	2			
No. of Station →		180+900	180+950			
1-Mass Of Materials						
Wt of Total Wet Materials	gm	81,250	81,320			
Wt of Wet Overse Fraction	gm	30,500	30,540			
Wt of Wet Control Fraction	gm	50,740	50,780			
Wt of Dry Overse Fraction	gm	30,062	30,180			
Wt of Dry Control Fraction	gm	48,254	48,051			
2.Determination of moist material						
Moisture Content of Control Fraction	%	4.9%	5.0%			
Moisture Content of Overse Fraction	%	1.50%	1.50%			
3-Volume Of the Test Pit						
Wt of Calibrated sand in Pit and template	gm	79,220	79,880			
Wt of Calibrated sand in template	gm	36,500	36,500			
Wt of Calibrated sand in test Pit	gm	42,720	43,380			
Density of Calibrated sand	gm/cm ³	1.48	1.48			
Gravimetric Gravity of Overse Fraction	gm/cm ³	2.528	2.520			
Volume of the Test Pit	cm ³	35,822	35,730			
Volume of Wet Overse Fraction	cm ³	12,125	12,159			
Volume of Wet Control Fraction	cm ³	23,499	23,571			
4-Relative Density Calculation						
Wt Density of Control Fraction Gm/cm ³		2.18	2.15			
Wt Density of Control Fraction Gm/cm ³		2.08	2.04			
Q14	maximum dry density	2.161	2.161			
	O.M.C	6.50%	6.50%			
Relative Compaction		96.14%	95.45%			
Remarks		95%	95%			
Test / Fall		Pass	Pass			

شركة أوديك
M.E./CONSULTANT
للتطوير العمراني والمقاولات
ت. ٢٠٢-٧٥٦-١٢٢

M.E./CONSULTANT
مهندس عمراني



استشاري أبحاث التربية والاساسات
أ.د.م. هشام محمد حلمي



مشروع:
قطار أسوان الكهربائي السريع - القطاع الثاني

Standard Test Method For Density of Soil and Rock in place By the Sand Replacement Method in a Test Pit * ASTM D4914 M-10

Report No.:	From	185+720	To	180+840	Company	الملا
Date:		Level	-3.00	DATE	12/12/2023	
Division:	EMBANKMENT Materials					
	1	2	3			
No. of Station →	180+740	180+790	180+840			
1-Mass Of Materials						
It of Total Wet Materials	gm	85,300	85,550	85,400		
It of Wet Oversize Fraction	gm	32,500	32,400	32,300		
It of Wet Control Fraction	gm	52,200	52,150	52,040		
It of Dry Oversize Fraction	gm	32,045	31,940	31,875		
It of Dry Control Fraction	gm	50,933	50,599	50,388		
2.Determination of moist material						
Int. ure Content of Control Fraction	%	4.9%	4.9%	5.0%		
Int. ure Content of Oversize Fraction	%	1.40%	1.42%	1.50%		
3-Volume Of the Test Pit						
It of Calibrated sand in Pit and template	gm	81,650	81,450	81,660		
It of Calibrated sand in template	gm	26,500	26,500	26,300		
It of Calibrated sand in test Pit	gm	55,150	54,950	55,180		
are ity of Calibrated sand	gm/cm3	1.48	1.48	1.48		
are ity Gravity of Oversize Fraction	gm/cm3	2.520	2.520	2.520		
Volume of the Test Pit	cm3	37,264	37,128	37,270		
Volume of Wet Oversize Fraction	cm3	12,897	12,857	12,841		
Volume of Wet Control Fraction	cm3	24,367	24,271	24,429		
4-Relative Density Calculation						
et Density of Control Fraction Gm/cm3		2.18	2.19	2.17		
ry Density of Control Fraction Gm/cm3		2.06	2.09	2.07		
G _{max}	maximum dry density	2.141	2.141	2.141		
	D.M.C	6.50%	6.30%	6.50%		
Relative Compaction		97.21%	97.60%	96.58%		
om inis		95%	95%	95%		
ass / Fail		Pass	Pass	Pass		

شركة اوردريك
S.L. CONTRACTOR
للتوريد والمقاولات
س.ت: ٨٩٨٤٥ - فاكس: ٨٩٨٤٥ - ٨٩٨٤٥

ME/CONSULTANT

Handwritten signature

Standard Test Method For Density of Soil and Rock in place By the Sand Replacement Method in a Test Pit " ASTM D4934 M-16 "

شركة اوديك
للتوريد والمقاولات
س.ت: ٨٩٨٤٥٠ بغداد - العراق

ME/CONSULTANT

محمد بن عبد الله بن محمد

استشاري أبحاث التربة والاساسات
أ.د.م. هشام محمد حلمي



مشروع:
قطار أسوان الكهربائي السريع - القطاع الثاني

Standard Test Method For Density of Soil and Rock in place By the Sand Replacement Method in a Test Pit " ASTM D4914 M-16 "

Request No.:	From:	181+360	To:	181+430	Category:	تاريخ
Station:		Level	-2.80	DATE	09/12/2023	
Description:	EMBANKMENT Materials					
	1	2	3	4		
No. of Station →	181+280	181+330	181+380	181+430		
1-Mass Of Materials						
Wt of Total Wet Materials	gm	86,220	86,280	86,300	86,255	
Wt of Wet Oversize Fraction	gm	29,600	29,580	29,645	29,780	
Wt of Wet Control Fraction	gm	56,620	56,700	56,655	56,475	
Wt of Dry Oversize Fraction	gm	25,155	25,194	25,220	25,260	
Wt of Dry Control Fraction	gm	59,476	59,753	59,813	59,651	
2.Determination of moist material						
Moisture Content of Control Fraction	%	5.3%	5.0%	5.1%	5.0%	
Moisture Content of Oversize Fraction	%	1.57%	1.30%	1.40%	1.30%	
3-Volume Of the Test Pit						
Wt Calibrated sand in Pit and template	gm	82,510	82,550	82,540	82,455	
Wt of Calibrated sand in template	gm	26,500	26,500	26,500	26,500	
Wt of Calibrated sand in test Pit	gm	56,010	56,150	56,040	55,955	
Density of Calibrated sand	gm/cm ³	1.48	1.48	1.48	1.48	
Specific Gravity of Oversize Fraction	gm/cm ³	2.630	2.638	2.620	2.638	
Volume of the Test Pit	cm ³	37,845	37,939	37,845	37,807	
Volume of Wet Oversize Fraction	cm ³	11,746	11,778	11,754	11,617	
Volume of Wet Control Fraction	cm ³	26,099	26,161	26,091	26,190	
4-Relative Density Calculation						
Wet Density of Control Fraction Gm/cm ³		2.17	2.16	2.17	2.17	
Dry Density of Control Fraction Gm/cm ³		2.06	2.06	2.07	2.07	
Q14	maximum dry density	2.139	2.139	2.139	2.139	
	O.M.C	6.10%	6.10%	6.10%	6.10%	
Relative Compaction		96.11%	96.23%	96.64%	96.73%	
remarks		95%	95%	95%	95%	
Pass / Fail		Pass	Pass	Pass	Pass	

شركة اوديك
OUDIK
للتوريد والمقاولات
س.ت: ٨٩٨٤٥٠ ب.ص: ٧١٢٠٧٤٨١٦٧

M.E./CONSULTANT
محمد المنصور

Standard Test Method For Density of Soil and Rock in place By the Sand Replacement Method in a Test Pit " ASTM D4914 96-16 "

Q3: 2023	From	181+250	to	181+420	Company	كرد
10-m			Level	-2.50	DATE	09/12/2023
Location :	EMBRACEMENT Materials					
		1	2	3	4	
No. of Station →		181+280	181+330	181+380	181+430	
1-Mass Of Materials						
1. Total Wet Materials	gm	85,120	85,160	85,135	85,200	
2. Wet Oversize Fraction	gm	30,600	30,150	30,405	30,190	
3. Wet Control Fraction	gm	54,520	55,010	54,730	55,010	
4. Dry Oversize Fraction	gm	20,333	20,118	20,240	20,791	
5. Dry Control Fraction	gm	32,230	32,755	32,481	32,793	
2.Determination of moist material						
1. Moisture Content of Control Fraction	%	4.2%	4.1%	4.2%	4.1%	
2. Moisture Content of Oversize Fraction	%	1.50%	1.18%	1.30%	1.38%	
3-Volume Of the Test Pit						
1. Calibrated sand in Pit and template	gm	23,500	23,100	23,142	23,300	
2. Calibrated sand in template	gm	26,500	26,500	26,500	26,500	
3. Calibrated sand in test Pit	gm	17,000	16,600	16,692	16,700	
4. Density of Calibrated sand	gm/cm3	1.48	1.48	1.48	1.48	
5. G. Gravity of Oversize Fraction	gm/cm3	2.828	2.820	2.820	2.820	
6. Volume of the Test Pit	cm3	18,514	18,243	18,305	18,311	
7. Volume of Wet Oversize Fraction	cm3	12,143	11,955	12,065	11,980	
8. Volume of Wet Control Fraction	cm3	16,371	16,779	16,240	16,331	
4-Relative Density Calculation						
1. Density of Control Fraction Gm/cm3		2.07	2.09	2.09	2.09	
2. Density of Control Fraction Gm/cm3		1.98	2.01	2.00	2.01	
Q3: 4	maximum dry density	2.130	2.139	2.139	2.139	
	O.M.C	6.10%	6.10%	6.10%	6.10%	
Relative Compaction		92.76%	94.01%	93.58%	93.82%	
min. rel		93%	95%	95%	95%	
Pass / Fail		Fail	Fail	Fail	Fail	

شركة محمد امجديك
للتوريدات والمقاولات
س.ت. ٨٩٨٤٥٠ ٠٤.ف. ٢٥٩-٢٠٢٠

M.E./CONSULTANT
[Signature]

استشاري أبحاث التربة والاساسات
أ.د.م. هشام محمد حلي



مشروع:
قطار لسوان الكهربائي السريع - القطاع الثاني

Standard Test Method For Density of Soil and Rock in place By the Sand Replacement Method in a Test Pit " ASTM D4914 M-16 "

Job no.:	From	182+040	to	182+220	Company	أوديك
Lot no.:			Level	-2.00	DATE	30/11/2023
Description:	EMBANKMENT Materials					

No. of Station →	182+060	182+110	182+160	182+210		
------------------	---------	---------	---------	---------	--	--

1-Mass Of Materials

It of Total Wet Materials	gm	84,760	84,315	84,290	84,150	
It of Wet Oversize Fraction	gm	27,410	27,350	27,300	27,160	
It of Wet Control Fraction	gm	56,350	56,965	57,100	56,990	
It of Dry Oversize Fraction	gm	26,550	26,507	26,034	26,807	
It of Dry Control Fraction	gm	58,800	54,079	54,273	54,157	

2.Determination of moist material

Moisture Content of Control Fraction	%	5.0%	5.1%	5.1%	4.9%	
Moisture Content of Oversize Fraction	%	1.54%	1.40%	1.50%	1.30%	

3-Volume Of the Test Pit

It of tamped sand in Pit and template	gm	81,100	81,025	80,290	80,140	
It of Calibrated sand in template	gm	26,000	26,000	26,000	26,000	
It of Calibrated sand in test Pit	gm	55,100	55,025	54,290	54,140	
density of Calibrated sand	gm/cm ³	1.48	1.48	1.48	1.48	
Specific Gravity of Oversize Fraction	gm/cm ³	2.520	2.520	2.520	2.520	
Volume of the Test Pit	cm ³	37,230	37,175	36,682	36,581	
Volume of Wet Oversize Fraction	cm ³	10,677	10,853	10,754	10,778	
Volume of Wet Control Fraction	cm ³	26,553	26,322	25,928	25,803	

4-Relative Density Calculation

Net Density of Control Fraction Gm/cm ³	2.16	2.16	2.21	2.21	
Gross Density of Control Fraction Gm/cm ³	2.05	2.06	2.10	2.11	
Q1 4	maximum dry density	2.132	2.132	2.132	2.132
	OMC	6.34%	6.30%	6.50%	6.30%
Relative Compaction		96.33%	96.60%	98.64%	98.76%
Standard		95%	95%	95%	95%
Result / Pass		Pass	Pass	Pass	Pass

شركة اوديك
م.ع.م. استشاري
لتطوير البنية التحتية
س.ت. ٨٩٨٤٥٠ - الرياض ١١٦٦٦٠٠٠

M.E./CONSULTANT

محمد بن عبد الله

استشاري أبحاث التربة والاساسات
أ.د.م. هشام محمد حليم



مشروع:
قطار أسوان الكهربائي السريع - القطاع الثاني

Standard Test Method For Density of Soil and Rock in place By the Sand Replacement Method in a Test Pit " ASTM D4514 M-16 "

Report no.:	Room	180+380	to	180+420	Company	أونيك
Station:			Level	-1.00	DATE	21/11/2022
Description:	IMBANKMENT Materials					

1

No. of Station →

180+400

1-Mass Of Materials

Wt. of Total Wet Materials	gm	83,450				
Wt. of Wet Oversize Fraction	gm	32,310				
Wt. of Wet Control Fraction	gm	55,890				
Wt. of Dry Oversize Fraction	gm	31,835				
Wt. of Dry Control Fraction	gm	48,359				

2.Determination of moist material

Moisture Content of Control Fraction	%	4.9%				
Moisture Content of Oversize Fraction	%	1.50%				

3-Volume Of the Test Pit

Wt. Calibrated sand in Pit and template	gm	79,440				
Wt. of Calibrated sand in template	gm	26,000				
Wt. of Calibrated sand in test Pit	gm	53,440				
Unit Wt. of Calibrated sand	gm/cm ³	1.48				
Unit Wt. Gravity of Oversize Fraction	gm/cm ³	2.525				
Volume of the Test Pit	cm ³	36,108				
Volume of Wet Oversize Fraction	cm ³	12,825				
Volume of Wet Control Fraction	cm ³	23,283				

4-Relative Density Calculation

Wet Density of Control Fraction Gm/cm ³	2.18					
Dry Density of Control Fraction Gm/cm ³	2.08					
Q4	maximum dry density	2.12				
	0.95C	6.50%				
Relative Compaction	97.71%					
Remarks	95%					
Pass / Fail	Pass					

شركة أونيك
للتوريدات والهندسة
س.ب. ٨٩٨٤٥. ف.ن. ١١٧. ٢٠٢٢٠٤١

M.E./CONSULTANT

محمد عبد الله

استشاري أبحاث التربة والأساسات
أ.د.م. هشام محمد حلمي



مشروع:
قطار أسوان الكهربائي السريع - القطاع الثاني

Standard Test Method For Density of Soil and Rock in place By the Sand Replacement Method in a Test Pit " ASTM D4914 M-10 "

102 2015.06.2	From	101+100	To	101+500	Company	أوديك
001 011		Level	-5.00	DATE:	20/11/2022	
Description:	EMBANKMENT Materials					

1

No. of Station →

101+300

1-Mass Of Materials

Total Wet Materials	gm	86,000				
Wet Oversize Fraction	gm	36,250				
Wet Control Fraction	gm	51,750				
Dry Oversize Fraction	gm	33,665				
Dry Control Fraction	gm	48,915				

2.Determination of moist material

Moisture Content of Control Fraction	%	5.4%				
Moisture Content of Oversize Fraction	%	1.70%				

3-Volume Of the Test Pit

Calibrated sand in Pit and template	gm	81,160				
Calibrated sand in template	gm	26,000				
Calibrated sand in test Pit	gm	55,160				
Density of Calibrated sand	gm/cm ³	1.40				
Density of Oversize Fraction	gm/cm ³	2.520				
Volume of the Test Pit	cm ³	37,270				
Volume of Wet Oversize Fraction	cm ³	13,581				
Volume of Wet Control Fraction	cm ³	23,679				

4-Relative Density Calculation

Wet Density of Control Fraction Gm/cm ³	2.19					
Dry Density of Control Fraction Gm/cm ³	2.07					
Q14	maximum dry density	2.339				
	O.M.C.	6.50%				
Relative Compaction	97.35%					
Remarks	95%					
Test / Fall	Pass					

شركة أوديك
للتوريدات والمقاولات
M.E.CONSULTANT
من: ٢٠٢٠-٧٥٥-١٦٢
٨٩٨٤٥٠

M.E./CONSULTANT

محمد أحمد سمي

استشاري أبحاث التربة والاساسات
أ.د.م. هشام محمد حلمي



مشروع:
قطار أسوان الكهربائي السريع - القطاع الثاني

Standard Test Method For Density of Soil and Rock in place by the Sand Replacement Method in a Test Pit " ASTM D4914 M-16 "

Form No.	From	181+160	to	181+330	Company	أعمال
181-160		Level	-3.00	DATE	20/11/2023	
181-160	EMBANKMENT Materials					
No. of Station →		1	2	3		
		181+280	181+330	181+380		
1-Mass Of Materials						
1. Total Wet Materials	gm	80,360	80,160	80,258		
2. Wet Oversize Fraction	gm	28,050	27,600	27,020		
3. Wet Control Fraction	gm	42,450	52,560	52,600		
4. Dry Oversize Fraction	gm	27,829	27,188	27,235		
5. Dry Control Fraction	gm	45,334	49,679	49,812		
2.Determination of moist material						
6. Moisture Content of Control Fraction	%	5.4%	5.1%	5.3%		
7. Moisture Content of Oversize Fraction	%	1.50%	1.50%	1.50%		
3-Volume Of the Test Pit						
8. Calibrated sand in Pit and template	gm	78,400	78,400	78,450		
9. Calibrated sand in template	gm	26,500	26,500	26,500		
10. Calibrated sand in test Pit	gm	51,900	51,900	51,950		
11. Density of Calibrated sand	gm/cm ³	1.48	1.48	1.48		
12. Specific Gravity of Oversize Fraction	gm/cm ³	2.520	2.520	2.520		
13. Volume of the Test Pit	cm ³	35,088	35,088	35,101		
14. Volume of Wet Oversize Fraction	cm ³	11,131	10,952	10,971		
15. Volume of Wet Control Fraction	cm ³	23,957	24,115	24,129		
4-Relative Density Calculation						
16. Density of Control Fraction Gm/cm ³		2.18	2.18	2.18		
17. Density of Control Fraction Gm/cm ³		2.07	2.07	2.07		
Q14	maximum dry density	2.130	2.130	2.130		
	O.M.C	6.50%	6.50%	6.50%		
18. Relative Compaction		96.96%	97.36%	97.19%		
19. Results		95%	95%	95%		
20. Pass / Fail		Pass	Pass	Pass		

شركة اوديك
لتوريد اسلح و المصنوعات
س.ت: ١٨٤٥ تم بحوزة مصر ٧٠٢٠٧٥٩

M.J.C/CONSULTANT

م.ج.م. استشاري

استشاري أبحاث التربة والاساسات
أ.د. هشام محمد حلمي



مشروع:
خطار لسون الكهربائي السريع - القطاع الثاني

Standard Test Method For Density of Soil and Rock in place by the Sand Replacement Method in a Test Pit " ASTM D4914 M-18 "

TEST NO. :	From	180+740	to	180+840	Company	تاريخ
Location :		Level		-3.50	DATE	14/11/2022
Description :	EMBANKMENT Materials					
		1	2	3		
No. of Station →		180+740	180+790	180+840		
1-Mass Of Materials						
Wt. of Total Wet Materials	gm	75,330	75,120	75,440		
Wt. of Wet Oversize Fraction	gm	30,100	30,250	30,290		
Wt. of Wet Control Fraction	gm	45,130	44,870	45,240		
Wt. of Dry Oversize Fraction	gm	28,698	28,827	28,747		
Wt. of Dry Control Fraction	gm	42,874	42,537	42,842		
2.Determination of moist material						
Moisture Content of Control Fraction	%	5.0%	5.2%	5.3%		
Moisture Content of Oversize Fraction	%	1.50%	1.40%	1.50%		
3-Volume Of the Test Pit						
Wt. Calibrated sand in Pit and template	gm	73,280	73,150	73,280		
Wt. of Calibrated sand in template	gm	25,500	25,500	25,500		
Wt. of Calibrated sand in test Pit	gm	47,780	47,650	47,780		
Density of Calibrated sand	gm/cm ³	1.48	1.48	1.48		
Specific Gravity of Oversize Fraction	gm/cm ³	2.520	2.520	2.520		
Volume of the Test Pit	cm ³	32,284	32,195	32,284		
Volume of Wet Oversize Fraction	cm ³	11,544	12,004	11,544		
Volume of Wet Control Fraction	cm ³	20,811	21,151	21,100		
4-Relative Density Calculation						
Wet Density of Control Fraction gm/cm ³		2.22	2.22	2.18		
Dry Density of Control Fraction gm/cm ³		2.12	2.11	2.12		
Q4	maximum dry density	2.130	2.130	2.130		
	O.M.C	6.50%	6.50%	6.50%		
Relative Compaction		99.31%	99.17%	99.56%		
Remarks		95%	95%	95%		
Pass / Fail		Pass	Pass	Pass		

شركة هندسة
التقنية والهندسة
٢٠٢٠-٧٥٩-١٦٧
س.ب. ٨٩٨٤٥

M.E./CONSULTANT

محمد الشاذلي



مكتب أ.د. حسن مهدي
للإستشارات الهندسية



المشروع: مشروع الطرق



تاريخ: 13/11/2023

موقع: طريق الكورنيش الجديد - 000 م

Determination of field density - ASTM D 1556

Request no.:	180+520	to	180+720	Company	ODIK
Station:	Level		- 4.00	DATE	13/11/2023
Description:	FILL LAYER				

Proctor Modified Test Results:

Max. dry density g/cm^3	G.M.C. %	Degree of Compaction Required, %	Bulk Density of Specified sand g/cm^3	Sand Weight of Core (gm)
2.108	5.8	95	1.480	1440

Test No.	1	2	3	4	5	6	7	8	9	10						
Station of sample	180+520	180+580	180+620	180+640	180+690											
Wt. Of Sand before test, gm	10200	10750	10435	10220	10100											
Wt. Of Sand after test, gm	6481	7063	6803	6639	6482											
Wt. Of Sand fill hole & cone, gm	3719	3687	3632	3581	3648											
Wt. Of Sand fill cone, gm	1440	1440	1440	1440	1440											
Wt. Of Sand fill hole, gm	2279	2247	2192	2141	2208											
Volume of hole, cm^3	1540	1518	1431	1445	1492											
Wt of sample from hole, gm	3400	3320	3200	3155	3298											
Wet density of soil, g/cm^3	2.208	2.186	2.181	2.202	2.211											
No. of container	1	2	3	4	5	6	7	8	9	10						
Wt. of container, gm	62.4	62.1	62.3	62.5	62.4	62.3	62.4	60.3	61.4	60.7						
Wt. Of sample & container before drying, gm	373.1	367.3	380.5	364.1	349.3	322.6	320.9	299.9	345.7	332.8						
Wt. of container & dried sample, gm	386.5	388.9	394.2	338.9	334.6	308.7	313.2	285.7	328.1	317.4						
Water wt.	16.2	18.4	16.3	16.2	14.7	13.8	15.3	14.2	18.6	15.4						
Wt. of dried sample, gm	294.5	306.7	301.8	276.4	273.2	246.4	280.8	226.4	267.7	256.7						
Moisture content, %	5.8	6	5.4	5.5	5.4	5.5	6.1	6.3	6.2	6						
Average moisture content, %	5.8	5.5	5.5	6.2	6.1											
Dry density, g/cm^3	2.088	2.073	2.648	2.073	2.084											
Compaction (%)	99.20%	98.55%	97.30%	98.50%	99.00%											
Acceptance	Y	Y	Y	Y	Y											

مكتب أ.د. حسن مهدي
للإستشارات الهندسية
م.ت: ٨٩٨٤٥٠
٢٠٢٠-٢٠٢٣

NO. 1 LOTUS STREET



علاقہ اقصیٰ، شمال مغربی، جنوب مغربی، جنوب مشرقی، شمال مشرقی

Determination of half-saturation - 25/10/1991

Equipment:	Item:	BU-260	To:	SD-540	Company:	ODK
Station:	Unit:		Line:		Date:	09/21/2002
FILE AVEB						

(Sender: the Wild Trading Society)

Max. dry density (g/cc)	O.M.C. %	Range of Compaction (Standard %)	Soil Variety of Specified sand/gravel	Soil Weight of Core (g)
2.125	6.6	95	LC3	540

Test No.	1		2	
Station of sample	12+200		12+348	
Wt. Of Sand before test,gm	975		975	
Wt. Of Sand after test,gm	646		663	
Wt. Of Sand fill hole,cone,gm	349		312	
Wt. Of Sand fill cone,gm	144		140	
Wt. Of Sand fill hole,gm	203		223	
Volume of hole, cm^3	1389		1386	
Wt of sample from hole,gm	3065		3097	
Wet density of soil, g/cm^3	2.195		2.194	
No. of container	1	2	3	4
Wt. of container gm	62.6	62.2	62.3	62.8
Wt. Of sample& container before drying,gm	362.6	360.6	366.6	354.0
wt. of container& dried sample,gm	368.6	363.8	375.8	366.6
Water wt.	15.2	14.5	13.3	15.6
Wt. of dried sample,gm	294.3	241.7	212.6	240.0
Moisture content,%	5.7	6	6.2	6.3
Average moisture content%	5.9		6.3	
Dry density, gm/cm^3	2.072		2.068	
Compaction (%)	95.60%		95.16%	
Acceptance	Y		Y	

مدير عام
مدير عام
مدير عام

[illegible]



قطار اسوان الكهربائي السريع - القطاع الثاني

Request no.:	From	153+250	to	153+340	Company	ODIR
Station:		Level	- 3.50		DATE	06/11/2023
Description:	FILL LAYER					

Max. dry density, g/cm ³	O.M.C. %	Degree of Compaction Required, %	Bulk Density of Specified sand, g/cm ³	Sand Weight of Cone (g)
1.455	28	80	1.480	1440

Test No.	1		2	
Station of sample	181+280		181+340	
Wt. Of Sand before test,gm	9090		8800	
Wt. Of Sand after test,gm	5321		5670	
Wt. Of Sand fill hole&cone,gm	3679		3130	
Wt. Of Sand fill cone,gm	1440		1440	
Wt. Of Sand fill hole,gm	2239		1690	
Volume of hole,cm ³	1613		1377	
Wt of sample from hole,gm	3000		2500	
Wet density of soil,gm/cm ³	1.883		1.868	
No. of container	1	2	3	4
Wt. of container,gm	52.4	52.2	52.3	52.5
Wt. Of sample& container before drying,gm	248.6	221.4	226.1	246.1
wt. of container& dried sample,gm	232.6	214.4	216.6	236.7
Water wt.	8.0	7.0	7.5	7.4
Wt. of dried sample,gm	179.2	162.3	158.3	176.2
Moisture content,%	4.7	4.6	4.8	4.2
Average moisture content%	4.7		4.5	
Dry density,gm/cm ³	1.885		1.873	
Compaction (%)	90.00%		89.00%	
Acceptance	N		N	

شركة اوديك
للتوريدات والمقاولات
ص.ت: ١٩٨٤٥ (بغداد) ٧٠٣-٢٥٥٤

WEEK CONSULTANT

گنودر استرامم

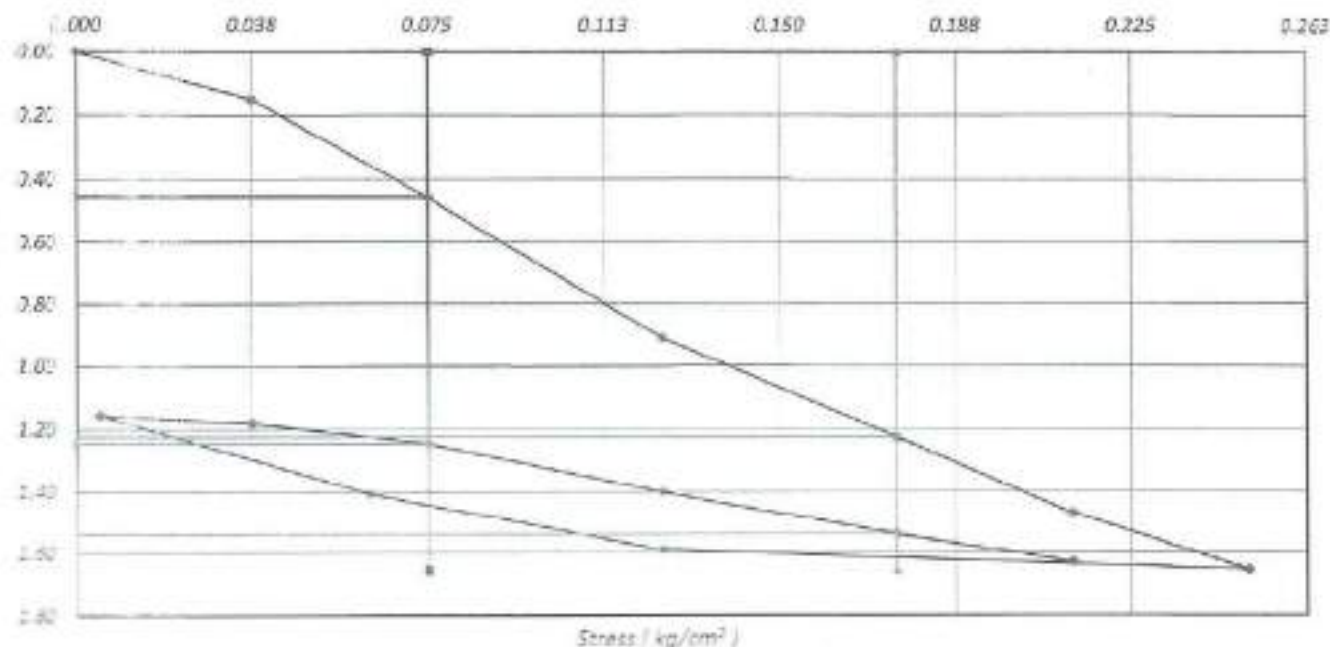


PLATE LOADING TEST RESULTS

القطار الكهربائي السريع (أكتوبر - أسوان) - القطار الثاني (بنى مزار - متكوط)

TR : 1530	181+580	Plate Dia. :	60 cm
15	Location : 181+570	Company :	أريحا
Project No.	Date : 8/Nov/2023	Soil :	entakement

Stress - Settlement Relationship



	Load From	Stress (MPa)	Settlement (mm)
Loading	0.00	0.000	0.00
	1.06	0.038	0.15
	2.12	0.075	0.46
	3.14	0.125	0.91
	4.25	0.175	1.23
	5.01	0.213	1.47
	7.07	0.250	1.66
Unloading	3.34	0.125	1.50
	1.77	0.063	1.41
	2.14	0.005	1.16
Loading	1.06	0.038	1.18
	2.12	0.075	1.25
	3.34	0.125	1.40
	4.25	0.175	1.54
	5.01	0.213	1.63

σ_{\max}	0.250	Stress (MPa)	Settlement (mm)
0.30 σ_{\max} reloading		0.075	1.25
0.70 σ_{\max} reloading		0.175	1.54

$$E_{\nu 1} = 153 \text{ MPa}$$

<i>EV2</i>	<i>153</i>
<i>Specification</i>	<i>Ev2 ≥ 30</i>
<i>Acceptance</i>	<i>Y</i>

شماره ۲۵ او ديك
للتور يدا ت والمهاولات
٧٠٢-٧٥٩-١٢٧٠ ٩٩٨٤٥٠

1998, 1999, 2000, 2001, 2002, 2003, 2004, 2005, 2006, 2007, 2008, 2009, 2010, 2011, 2012, 2013, 2014, 2015, 2016, 2017, 2018, 2019, 2020, 2021, 2022, 2023, 2024, 2025, 2026, 2027, 2028, 2029, 2030, 2031, 2032, 2033, 2034, 2035, 2036, 2037, 2038, 2039, 2040, 2041, 2042, 2043, 2044, 2045, 2046, 2047, 2048, 2049, 2050, 2051, 2052, 2053, 2054, 2055, 2056, 2057, 2058, 2059, 2060, 2061, 2062, 2063, 2064, 2065, 2066, 2067, 2068, 2069, 2070, 2071, 2072, 2073, 2074, 2075, 2076, 2077, 2078, 2079, 2080, 2081, 2082, 2083, 2084, 2085, 2086, 2087, 2088, 2089, 2090, 2091, 2092, 2093, 2094, 2095, 2096, 2097, 2098, 2099, 2100, 2101, 2102, 2103, 2104, 2105, 2106, 2107, 2108, 2109, 2110, 2111, 2112, 2113, 2114, 2115, 2116, 2117, 2118, 2119, 2120, 2121, 2122, 2123, 2124, 2125, 2126, 2127, 2128, 2129, 2130, 2131, 2132, 2133, 2134, 2135, 2136, 2137, 2138, 2139, 2140, 2141, 2142, 2143, 2144, 2145, 2146, 2147, 2148, 2149, 2150, 2151, 2152, 2153, 2154, 2155, 2156, 2157, 2158, 2159, 2160, 2161, 2162, 2163, 2164, 2165, 2166, 2167, 2168, 2169, 2170, 2171, 2172, 2173, 2174, 2175, 2176, 2177, 2178, 2179, 2180, 2181, 2182, 2183, 2184, 2185, 2186, 2187, 2188, 2189, 2190, 2191, 2192, 2193, 2194, 2195, 2196, 2197, 2198, 2199, 2200, 2201, 2202, 2203, 2204, 2205, 2206, 2207, 2208, 2209, 2210, 2211, 2212, 2213, 2214, 2215, 2216, 2217, 2218, 2219, 2220, 2221, 2222, 2223, 2224, 2225, 2226, 2227, 2228, 2229, 2230, 2231, 2232, 2233, 2234, 2235, 2236, 2237, 2238, 2239, 2240, 2241, 2242, 2243, 2244, 2245, 2246, 2247, 2248, 2249, 2250, 2251, 2252, 2253, 2254, 2255, 2256, 2257, 2258, 2259, 2260, 2261, 2262, 2263, 2264, 2265, 2266, 2267, 2268, 2269, 2270, 2271, 2272, 2273, 2274, 2275, 2276, 2277, 2278, 2279, 2280, 2281, 2282, 2283, 2284, 2285, 2286, 2287, 2288, 2289, 2290, 2291, 2292, 2293, 2294, 2295, 2296, 2297, 2298, 2299, 2300, 2301, 2302, 2303, 2304, 2305, 2306, 2307, 2308, 2309, 2310, 2311, 2312, 2313, 2314, 2315, 2316, 2317, 2318, 2319, 2320, 2321, 2322, 2323, 2324, 2325, 2326, 2327, 2328, 2329, 2330, 2331, 2332, 2333, 2334, 2335, 2336, 2337, 2338, 2339, 2340, 2341, 2342, 2343, 2344, 2345, 2346, 2347, 2348, 2349, 2350, 2351, 2352, 2353, 2354, 2355, 2356, 2357, 2358, 2359, 2360, 2361, 2362, 2363, 2364, 2365, 2366, 2367, 2368, 2369, 2370, 2371, 2372, 2373, 2374, 2375, 2376, 2377, 2378, 2379, 2380, 2381, 2382, 2383, 2384, 2385, 2386, 2387, 2388, 2389, 2390, 2391, 2392, 2393, 2394, 2395, 2396, 2397, 2398, 2399, 2400, 2401, 2402, 2403, 2404, 2405, 2406, 2407, 2408, 2409, 2410, 2411, 2412, 2413, 2414, 2415, 2416, 2417, 2418, 2419, 2420, 2421, 2422, 2423, 2424, 2425, 2426, 2427, 2428, 2429, 2430, 2431, 2432, 2433, 2434, 2435, 2436, 2437, 2438, 2439, 2440, 2441, 2442, 2443, 2444, 2445, 2446, 2447, 2448, 2449, 2450, 2451, 2452, 2453, 2454, 2455, 2456, 2457, 2458, 2459, 2460, 2461, 2462, 2463, 2464, 2465, 2466, 2467, 2468, 2469, 2470, 2471, 2472, 2473, 2474, 2475, 2476, 2477, 2478, 2479, 2480, 2481, 2482, 2483, 2484, 2485, 2486, 2487, 2488, 2489, 2490, 2491, 2492, 2493, 2494, 2495, 2496, 2497, 2498, 2499, 2500, 2501, 2502, 2503, 2504, 2505, 2506, 2507, 2508, 2509, 2510, 2511, 2512, 2513, 2514, 2515, 2516, 2517, 2518, 2519, 2520, 2521, 2522, 2523, 2524, 2525, 2526, 2527, 2528, 2529, 2530, 2531, 2532, 2533, 2534, 2535, 2536, 2537, 2538, 2539, 2540, 2541, 2542, 2543, 2544, 2545, 2546, 2547, 2548, 2549, 2550, 2551, 2552, 2553, 2554, 2555, 2556, 2557, 2558, 2559, 2560, 2561, 2562, 2563, 2564, 2565, 2566, 2567, 2568, 2569, 2570, 2571, 2572, 2573, 2574, 2575, 2576, 2577, 2578, 2579, 2580, 2581, 2582, 2583, 2584, 2585, 2586, 2587, 2588, 2589, 2590, 2591, 2592, 2593, 2594, 2595, 2596, 2597, 2598, 2599, 2600, 2601, 2602, 2603, 2604, 2605, 2606, 2607, 2608, 2609, 2610, 2611, 2612, 2613, 2614, 2615, 2616, 2617, 2618, 2619, 2620, 2621, 2622, 2623, 2624, 2625, 2626, 2627, 2628, 2629, 2630, 2631, 2632, 2633, 2634, 2635, 2636, 2637, 2638, 2639, 2640, 2641, 2642, 2643, 2644, 2645, 2646, 2647, 2648, 2649, 2650, 2651, 2652, 2653, 2654, 2655, 2656, 2657, 2658, 2659, 2660, 2661, 2662, 2663, 2664, 2665, 2666, 2667, 2668, 2669, 2670, 2671, 2672, 2673, 2674, 2675, 2676, 2677, 2678, 2679, 26

استشاري أبحاث التربة والاساسات
د.م. هشام محمد حلمي



مشروع:
الطوار أسوان الكهربائي السريع - القطاع الثاني

Standard Test Method For Density of Soil and Back in place By the Sand Replacement Method in a Test Pit " ASTM D4914 M-16 "

From	181+580	to	181+580	Company	أوديك
Soil :		Level	-5.50	DATE	05/11/2023
Location :	EMBANKMENT Materials				

No. of Station →	181+580				
------------------	---------	--	--	--	--

1-Mass Of Materials

Wt of Total Wet Materials	gm	81,215			
Wt of Wet Oversize Fraction	gm	33,500			
Wt of Wet Control Fraction	gm	47,715			
Wt of Dry Oversize Fraction	gm	33,031			
Wt of Dry Control Fraction	gm	45,618			

2.Determination of moist material

Moisture Content of Control Fraction	%	4.4%			
Moisture Content of Oversize Fraction	%	1.40%			

3-Volume Of the Test Pit

Calibrated sand in Pit and template	gm	80,200			
Calibrated sand in template	gm	26,500			
Calibrated sand in test Pit	gm	53,700			
Density of Calibrated sand	gm/cm3	1.45			
Relative Gravity of Oversize Fraction	gm/cm3	2.520			
Volume of the Test Pit	cm3	36,284			
Volume of Wet Oversize Fraction	cm3	13,254			
Volume of Wet Control Fraction	cm3	23,060			

4-Relative Density Calculation

Wt Density of Control Fraction	Gm/cm3	2.08			
Wt Density of Control Fraction	Gm/cm3	1.98			
Q:4	maximum dry density	2.137			
	O.M.C	6.78%			
Relative Compaction		93.93%			
Remarks		95%			
Pass / Fail		Fail			

شركة اوديك
التطوير والتكنولوجيا والهندسة
م.ت. ٤٩٨٤٥٠ ب.ف. ١٢٧-٧٥٩-٢٠٢

M.K./CONSULTANT

م.ك. / استشاري
