

المنطقة السادسة بيني سوف

مذكرة

للعرض على السيد المهندس / رئيس قطاع التنفيذ و المناطق

بخصوص: طلب شركة ابو عجيبة للمقاولات العامة اضافة مدة لعملية"انشاء الجسر الترابي لمشروع القطار الكهربائي السريع
من كم 200+850 الى كم 202+350 " بطول 1.5 كم .

- اسندت الهيئة المشروع عالية الى الشركة المنفذة بالعقد رقم (2024/2023/1229) المورخ في 2024/02/26 بقيمة اجمالية قدرها 11334008 جنيها ولمدة (8) شهور .
- بتاريخ 2024/03/03 تم تسليم الموقع للشركة المنفذة ليكون تاريخ النهو طبقا للعقد الاصلى في 2024/11/02.
- وردنا كتاب الشركة المنفذة تطلب فيه اضافة مدة ستة شهور للعملية لوجود بعض المعوقات التي تسببت في تاخر نهو الاعمال (مرفق) .

الرأي

- التفضل بالإحاطة.
- التكرم بالموافقة على اضافة مدة قدرها (6) شهور من تاريخ إنتهاء العقد في 2024/11/02 ليصبح تاريخ النهو 2025/05/02 وذلك للمبررات الآتية :-
- 1- بناء على قرار مجلس الوزراء بجلسته رقم (254) المنعقدة بتاريخ 2023/08/30 .
- 2- بناء على المذكرة المعروضة على السيد اللواء مهندس رئيس مجلس الادارة بخصوص الموافقة على مد مدة عقود المشروعات (6 أشهر) في ضوء كتاب الوزارة رقم (13793) والمرفق به كتاب دورى السيد اللواء / أمين عام مجلس الوزراء رقم (3-27815) بذات الخصوص (مرفق) .
- 3- تأخر التنفيذ بسبب تحرير سعر الصرف وزيادة تكلفة أسعار المواد الخام وارتفاع اسعار نقلها .
- 4- نقص الدعم الدولارى بالاسواق .
- 5- ارتفاع اسعار قطع الغيار وندرة توافرها بالاسواق .

والأمر مقوض

وتفضلوا سيادتكم بقبول فائق الاحترام

وتفضلوا سيادتكم بقبول فائق الاحترام

تحرير في: 2024/ /

رئيس الإدارة المركزية



طارق يوسف الجزار

صو صو



استشاري أبحاث التربة والاساسات :
أ.د.م. هشام محمد حلمي

مشروع :
قطار اسوان الكهربائي السريع - القطاع الثاني

تقرير بنتائج إختبارات صلاحية أترية للتأسيس

مقدمة : تم إعداد هذا التقرير بناءا علي طلب شركة / ابو عجيبة

وذلك لتحديد خصائص ومدي صلاحية عينة تراب للإستخدام في / طبقات الردم لجسر القطار الكهربائي

مصدر العينة : عند المحطة / تشوينة يمين المسار 202+220

- المندوب : وقد تم توريد العينة بمعرفة 1- م / محمود الحيني رقم الهاتف =01030344342

-تتبيه هام : العينة مسنولة من أحضرها

-تاريخ توريد العينة : 2023/12/14

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفلووط)

وقد تم عمل الإختبارات الآتية :

- 1-الاندرج الحبيبي
- 2-حد السيولة واللدونة
- 3-إختبار البروكتور
- 4-إختبار CBR
- 5-إختبار المواد العضوية

وكانت نتائج الإختبارات كالآتي :

م	نوع الإختبار	النتائج	حدود القبول والرفض طبقا للمواصفات
1	تصنيف العينة	A-1-a	(A-1-a) - (A-1-b) - (A-2-4)
2	نسبة المار من منخل 200	12.3%	لا تزيد عن (15 %)
3	مجال اللدونة	NP	(A-1-a or A-1-b = 6 max) (A-2-4 = 10 max)
4	أقصى كثافة جافة (البروكتور) γd max	2.19 gm/cm3	لا تقل عن 1.88 gm/cm3
5	نسبة الحياة الأمولية	5.8%	---
6	قيمة CBR المغمورة	66.2%	لا تقل عن 20%
8	المواد العضوية	لا يوجد	لا تزيد عن 1%

و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للتأسيس عليها



مهندس المعمل
م /
التوقيع

فني المعمل
أ /
التوقيع

Coarse & Fine Aggregate Grading - ASTM C136 & AASHTO T27

202+220	الموقع : تشوين يمين المنار	19/12/2023	التاريخ :
---------	----------------------------	------------	-----------

نتائج الاختبار :-

رقم المنخل (mm)	رقم المنخل (Inch)	وزن المحجوز على كل منخل	وزن المحجوز التراكمي	المحجوز %	المر %
127	5"	0	0	0%	100%
101.6	4"	0	0	0.00%	100.00%
76.2	3"	0	0	0.00%	100.00%
63.5	2.5"	352	352	6.41%	93.59%
50.8	2"	298	650	11.84%	88.16%
37.5	1.5"	250	900	16.40%	83.60%
25	1"	400	1300	23.69%	76.31%
19	3/4"	364	1664	30.32%	69.68%
12.7	1/2"	255	1919	34.97%	65.03%
9.5	3/8"	451	2370	43.19%	56.81%
4.75	# 4	343	2713	49.44%	50.56%
	المر من منخل # 4	2775			50.56%
	وزن العينة الكلي	5488			
	وزن عينة القاع	500			
2.36	# 10	51	51	54.6%	45.4%
0.425	# 40	154	205	70.2%	29.8%
0.075	# 200	173	378	87.7%	12.3%

NP	السيولة و اللدونة
A-1-a	التصنيف

ملاحظات :



محمد بن علي

مهندس معمل
12
التوقيع

Modified Proctor : ASTM D1557

نوع العينة:	عينة من المشون
تصنيف العينة:	A-1-a

نتائج الاختبار:

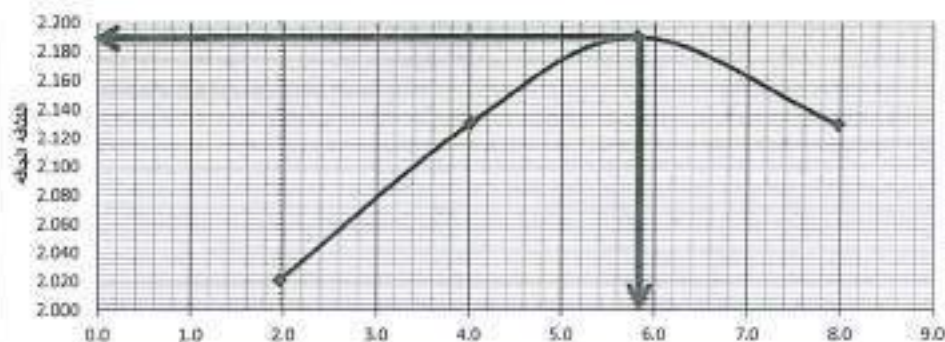
الوزن الجاف	2.190
الوزن المائي	5.8

وزن القالب	5731
حجم القالب	2140

رقم الاختبار	1	2	3	4
وزن القالب + العينة رطبة	10140.0	10472	10689	10650
وزن التربة الرطبة	4409.0	4741	4959	4919
كثافة الرطبة	2.080	2.215	2.317	2.299

رقم البقعة	1	2	3	4	5	6	7	8
وزن البقعة	52	55.8	50.7	52.5	55	53.9	52.4	51.2
وزن البقعة + العينة رطبة	150.0	150.0	150.0	150.0	150.0	150.0	150.0	150.0
وزن البقعة + العينة جافة	148.1	148.2	146	146.4	144.8	144.7	142.6	142.9
وزن الماء	1.9	1.8	4.0	3.6	5.2	5.3	7.4	7.1
وزن العينة جافة	96.1	92.4	95.3	93.9	89.8	90.8	90.2	91.7
المستوى المائي %	2.0	1.9	4.2	3.8	5.8	5.8	8.2	7.7
متوسط المستوى المائي %	2.0	4.0	5.8	8.0				
كثافة الجافة	2.021	2.130	2.190	2.129				

Modified Proctor Chart



ملاحظات:



مهندس المعماري
د. محمد بن أحمد البنا
التوقيع

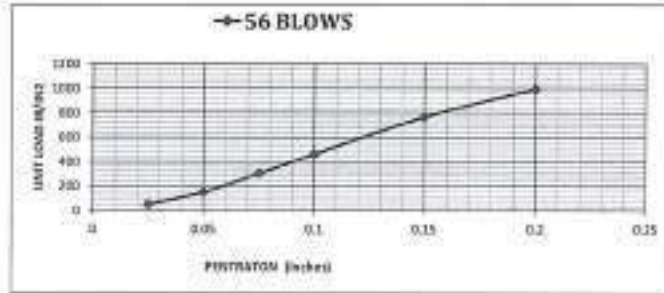
فني مختبر
محمد بن عبد الله
التوقيع

اختبار نسبة تحميل كاتيفورتيا ASTM D1883 (C.B.R)

A-2-a		تصنيف العينة	
عدد الضربات	56	عدد الضربات	56
حجم الكلب (سم ³)	2131	حجم الكلب (سم ³)	2131
وزن الكلب (جم)	6289	وزن الكلب (جم)	6289
وزن الكلب مع وزن العينة رطبة (جم)	92171	وزن الكلب مع وزن العينة رطبة (جم)	92171
وزن العينة رطبة (جم)	4892	وزن العينة رطبة (جم)	4892
الوزن الرطبة (جم/سم ³)	2.291	الوزن الرطبة (جم/سم ³)	2.291
الوزن الجافة (جم/سم ³)	2.168	الوزن الجافة (جم/سم ³)	2.168
نسبة الرطوبة (%)	5.8%	نسبة الرطوبة (%)	5.8%
نسبة التماسك	98.9%	نسبة التماسك	98.9%
نسبة الانكماش	0.14%	نسبة الانكماش	0.14%

حساب نسبة تحميل كاتيفورتيا

7.62	5.08	3.81	2.54	1.95	1.27	0.635	الأحمر لـ 15 ملم
0.3	0.2	0.15	0.1	0.075	0.05	0.025	الأحمر لـ 7.5 ملم
1530.0	1352	1044.0	627.0	411.0	201.0	66.0	الوزن (كجم)
3372.12	2979.808	2300.976	1381.908	905.844	443.004	145.464	الوزن (كجم)
1124.55	993.72	767.34	460.845	302.085	147.735	48.51	الوزن (كجم)



66.2%	قيمة C.B.R
-------	------------

ملاحظات: تم نشر النتائج في اليوم التالي لإتمام الاختبار



في العمل
محمد شهاب السيد
م. شهاب السيد

مهندس العمل
محمد شهاب السيد
م. شهاب السيد



استشاري أبحاث التربة والاساسات :
أ.د.م. هشام محمد حلمي

مشروع :
قطار اسوان الكهربائي السريع - القطاع الثاني

تقرير بنتائج إختبارات صلاحية أترية للتأسيس

مقدمة : تم إعداد هذا التقرير بناء على طلب شركة / ابو عجيبة

وذلك لتحديد خصائص ومدي صلاحية عينة تراب للإستخدام في / طبقات الردم لجسر القطار الكهربائي

مصدر العينة : عند المحطة / تشوينة يمين المسار 202+220

- المندوب: وقد تم توريد العينة بمعرفة 1- م/ محمود الحيني رقم الهاتف =01030344342

- تنبيه هام : العينة مسئولية من أحضرها

- تاريخ توريد العينة : 2023/12/11

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفلوط)

وقد تم عمل الإختبارات الآتية :

- 1- التدرج الحبيبي
- 2- حد السيولة واللدونة
- 3- إختبار البروكتور
- 4- إختبار CBR
- 5- إختبار المواد العضوية

وكانت نتائج الإختبارات كالآتي :

م	نوع الإختبار	النتائج	حدود القبول والرفض طبقا للمواصفات
1	تصنيف العينة	A-1-b	(A-1-a) - (A-1-b) - (A-2-4)
2	نسبة العار من مخل 200	12.9%	لا تزيد عن (15 %)
3	مجال اللدونة	NP	(A-1-a or A-1-b = 6 max) (A-2-4 = 10 max)
4	أقصى كثافة جافة (البروكتور) yd max	2.171 gm/cm3	لا تقل عن 1.88 gm/cm3
5	نسبة المياه الأصلية	6.4%	--
6	قيمة CBR المغمورة	38.2%	لا تقل عن 20%
8	المواد العضوية	لا يوجد	لا تزيد عن 1%

و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للتأسيس عليها



مهندس المعمل
م/م
التوقيع

فني المعمل
م/م
التوقيع

Coarse & Fine Aggregate Grading - ASTM C136 & AASHTO T27

202+220	الموقع : تشوين يمين المسار	16/12/2023	التاريخ :
---------	----------------------------	------------	-----------

نتائج الاختبار :-

رقم المنخل (mm)	رقم المنخل (inch)	وزن المحجوز على كل منخل	وزن المحجوز التراكمي	المحجوز %	المر %
127	5"	0	0	0%	100%
101.6	4"	0	0	0.00%	100.00%
76.2	3"	0	0	0.00%	100.00%
63.5	2.5"	0	0	0.00%	100.00%
50.8	2"	462	462	5.78%	94.22%
37.5	1.5"	348	810	10.14%	89.86%
25	1"	797	1607	20.11%	79.89%
19	3/4"	413	2020	25.28%	74.72%
12.7	1/2"	522	2542	31.81%	68.19%
9.5	3/8"	376	2918	36.52%	63.48%
4.75	# 4	312	3230	40.43%	59.57%
	المر من منخل # 4	4760		59.57%	
	وزن العينة الكلي	7990			
	وزن عينة الناعم	500			
2.36	# 10	54	54	46.9%	53.1%
0.425	# 40	145	199	64.1%	35.9%
0.075	# 200	193	392	87.1%	12.9%

NP	السيولة و اللدونة
A-1-b	التصنيف

ملاحظات :



م. محمد بن عبد الله

مهندس المعمل
م. محمد بن عبد الله
التوقيع

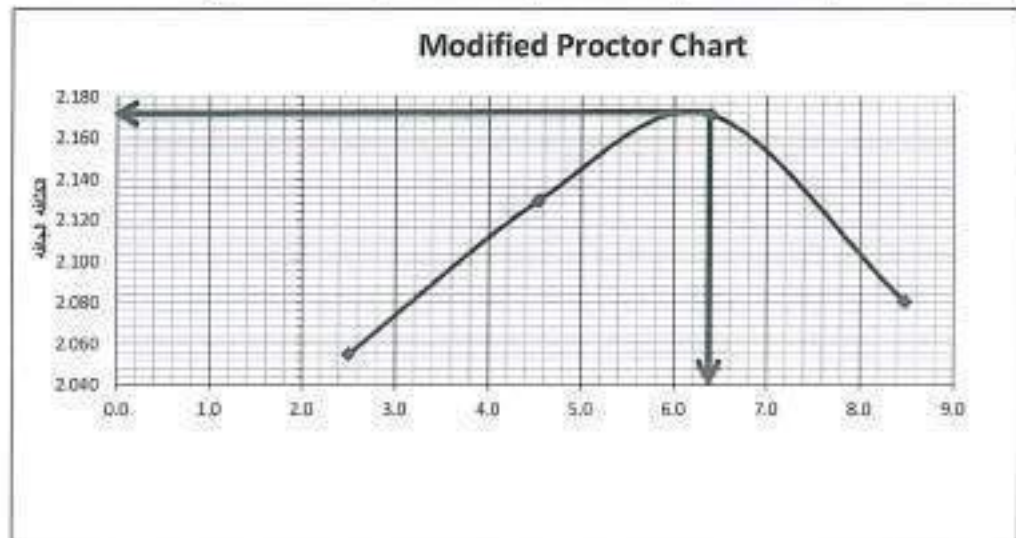
Modified Proctor : ASTM D1557

نوع العينة:	عينة من التشون
تصنيف العينة:	A-1-b
نتائج الاختبار:	
وزن القالب:	5731
حجم القالب:	2140

القيمة القصوى جافه	2.171
القيمة الاسمي	6.4

رقم الاختبار	1	2	3	4
وزن القالب + العينة رطبه	10238.0	10495	10674	10560
وزن القالب الرطبه	4507.0	4764	4943	4829
الكثافه الرطبه	2.105	2.226	2.310	2.257

رقم الحقله	1	2	3	4	5	6	7	8
وزن الحقله	52.3	55.1	25.9	25.5	54.6	52.3	30.4	31.7
وزن الحقله + العينه رطبه	150.0	150.0	150.0	150.0	150.0	150.0	150.0	150.0
وزن الحقله + العينه جافه	147.7	147.6	144.3	144.9	144.3	144.1	140.8	140.8
وزن المياه	2.3	2.4	5.7	5.1	5.7	5.9	9.2	9.4
وزن العينه جافه	95.4	92.5	118.4	119.4	89.7	91.8	110.4	108.9
المحتوى المائي %	2.4	2.6	4.8	4.3	6.4	6.4	8.3	8.6
متوسط المحتوى المائي %	2.5	4.5	6.4	8.5				
الكثافه الجافه	2.055	2.129	2.171	2.080				



ملاحظات:



مهندس المعمل
محمد بن عبد الله
التوقيع
للـ

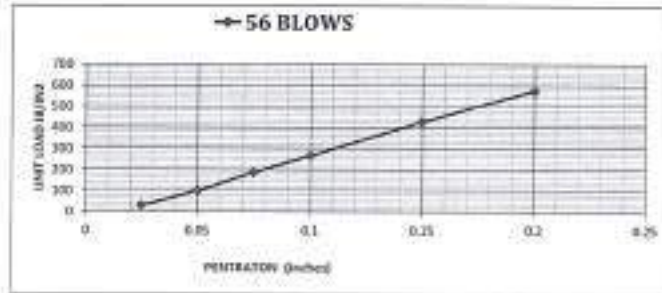
قصر المعمل
محمد بن عبد الله
التوقيع

اختبار نسبة تحمل كاتيلورنيا (C . B . R) ASTM D1883

A-1-b		تصنيف العينة	
56	حد الضربات	56	حد الضربات
5	رقم البقعة	2131	حجم القالب (سم ³)
51.3	وزن البقعة	5280	وزن القالب (جم)
180	وزن البقعة + العينة رطبة جم	10134	وزن القالب + وزن العينة رطبة (جم)
144.2	وزن البقعة + العينة جافة جم	4845	وزن العينة رطبة (جم)
8.8	وزن الماء جم	2.276	الكتلة الرطبة (جم/سم ³)
80.9	وزن العينة جافة جم	2.137	الكثافة جافة (جم/سم ³)
6.4%	المحتوى المائي %	2.171	كتلة الهواء (جم/سم ³)
		88.4%	نسبة الدمك
		0.39%	نسبة الإفراش
			غير قابلة للتفكك

حساب نسبة تحمل كاتيلورنيا

7.62	5.08	3.81	2.54	1.95	1.27	0.635	الاختبار (ب) بالملم
0.3	0.2	0.15	0.1	0.075	0.05	0.025	الاختبار (ب) بالملم
1369.0	780	581.0	360.0	255.0	134.0	39.0	الفرادة kg
3017.276	1719.12	1280.524	793.44	562.02	295.336	85.956	الفرادة بالباوند
1006.215	573.3	427.035	264.6	187.425	98.49	28.665	المعدل (B/M2)



38.2%	قيمة C . B . R
-------	----------------

ملاحظة: تم طرح النتائج في الملف بعد 56 ضربة طبقاً لمواصفة المشروع



في الموقع
م. محمد صالح عبيد
مهندس

مهندس مشرف في عهد اليا
شوقي
4



التاريخ : 2024-9-22

اسم المشروع : مشروع القطار الكهربائي السريع قطاع (أكتوبر - أبو سمبل)
الموضوع : اعتماد الهيئة العامة للطرق والكبارى لطلبات استلام الأعمال الخاصة بالمشروع
الشركة المنفذة : ابوعجيلة للمقاولات العامة والتوريدات العمومية في المسافة
من (200+876) الى (202+376) بطول 1.5 كم.

عقد رقم : - (2023-2022-1968) بتاريخ 2023-5-17

- (2023-2023-142) بتاريخ 2023-8-3

- (2023-2023-143) بتاريخ 2023-8-3

- (2023-2023-499) بتاريخ 2023-10-12

- (2023-2023-1021) بتاريخ 2024-1-18

- (2023-2023-1229) بتاريخ 2024-2-26

- (2024-2024-209) بتاريخ 2024-8-21

تم الإطلاع ظاهريا على طلبات الفحص الخاصة بالمشروع المذكور عاليه والمرفقة بمستخلصات
المذكورة عالية لعدد (77) طلبات فحص وذلك بعد مراجعتها وتوقيعها من استشارى المساحة (XYZ)
واستشارى ضبط الجودة (مكتب أ.د حسن مهدي) وعليه تم اعتمادها

وتنقسم الى :

- (53) طلبات فحص لأعمال الردم .
- (14) طلبات فحص لأعمال الحفر .
- (4) طلبات فحص لأعمال التطهير .

عن الاستشاري (أ.د حسن مهدي)
مشروع القطار السريع

مهندس الاستشاري
أ.د حسن مهدي

يعتمد،،،

مهندس الهيئة العامة للطرق والكبارى

مهندس الهيئة العامة للطرق والكبارى

البرنامج الزمني

أعمال الجسر الترابي لمسار القطر الكهربائي السريع الخط الثاني (الفيوم / بني سويف - أبوسمبل) (مرحلة الجسور والتأسيس والأساس)
القطاع الثاني (بني مزار / متفلوط)

من المحطة ٨٥٠+٢٠٠ الى المحطة ٢٠٢+٣٥٠ بطول ١,٥ كم رقم العقد (٢٠٢٤/٢٠٢٣/١٢٢٩)

أعمال ردم من منسوب ١١٠ م الي - ٩ م من منسوب الفرمة

تاريخ استلام الموقع ٢٠٢٤/٣/٣

مدة تنفيذ العمليه ٨ شهور

تاريخ نهو الاعمال ٢٠٢٤/١١/٢

رقم البند	بيان الاعمال	الوحدة	الكمية	مارس ٢٠٢٤	أبريل ٢٠٢٤	مايو ٢٠٢٤	يونيو ٢٠٢٤	يوليو ٢٠٢٤	أغسطس ٢٠٢٤	سبتمبر ٢٠٢٤	أكتوبر ٢٠٢٤	نوفمبر ٢٠٢٤
٢	أعمال الحفر											
	المنفذ في سبتمبر ٢٠٢٣											
١٥٠٢	بالمتر المكعب اعمال حفر باستخدام المعدات الميكانيكية في السقو وتسوية السطح بالآلات التسوية والريش بالمياه الأصولية للوصول الى نسبة الرطوبة المطلوبة والدمك الجيد بالهراسات للوصول الى أقصى كثافة جافه (95% من الكثافة الجافة القصوى) ومحمل علي البند تحميل ونقل الأتربة الزائدة لمسافة ١,٥ كم. من محور الطريق و الفشة تشمل استخدام المياه في تثبيت السقو و اعداد مدقات على السقو لحركة المعدات ويتم التنفيذ طبقاً للمناسيب التصميمية والقطاعات العرضية النموذجية والرسومات التفصيلية المعتمدة والبند بجميع مشتملاته طبقاً لأصول الصناعة ومواصفات الهيئة العامة للطرق والكباري وتعليمات المهندس المشرف علاوة ١ جنيه / كم لمسافة نقل ناتج الحفر وتصيح ١,١ جنيه / كم ابتداء من ٢٠٢٣/٥/٤.	م³	٣٦.٥٨			٧,٢١١,٦٠	٧,٢١١,٦٠	٧,٢١١,٦٠	٧,٢١١,٦٠			
	المنفذ في سبتمبر ٢٠٢٣											
١٠٣	أعمال تحميل وتوريد ونقل أتربة مطابقة للمواصفات وتشغيلها باستخدام آلات التسوية بسك لا يزيد عن ٥٠ سم حتى منسوب (2٠ متر) أسفل منسوب الفرمة و بسك لا يزيد عن ٢٥ سم اعلي من منسوب (2٠ متر) من منسوب الفرمة لاستكمال المنسوب التصميمي لتشكيل الجسر والأكتاف (نسبة تحمل كاليفورنيا لا تقل عن ١٥%) ورشها بالمياه الأصولية للوصول إلى نسبة الرطوبة المطلوبة والدمك الجيد بالهراسات للوصول إلى أقصى كثافة جافة (٩٥% من الكثافة الجافة القصوى) ويتم التنفيذ طبقاً للمناسيب التصميمية والقطاعات العرضية النموذجية والرسومات التفصيلية المعتمدة والبند بجميع مشتملاته طبقاً لأصول الصناعة ومواصفات الهيئة العامة للطرق والكباري وتعليمات المهندس المشرف. - في حالة طلب جهاز الإشراف زيادة نسبة الدمك عن ٩٥% يحسب زيادة ١ جنيه على زيادة نسبة الدمك لكل ١%. - مسافة النقل حتى ٢ كم و يتم احتساب علاوة ١,٤ جنيه لكل كم بالزيادة او النقصان و تصيح ١,٥ جنيه لكل كم اعتباراً من ٢٠٢٣/٥/٤. -السعر يشمل عمل تشوينات و تخليط واختبارات و نقل لموقع العمل حتي مسافة ٢ كم. - والبند لا يشمل القيمة المحجورية.	م³	٤٩٩٢٠					٩,٩٨٤,٠٠	٩,٩٨٤,٠٠	٩,٩٨٤,٠٠	٩,٩٨٤,٠٠	٩,٩٨٤,٠٠

مهندس الشركة المنفذة

م/ احمد فتوح

التوقيع /



عن الاستشاري أ.د حسن مهدي

م/ احمد عزب

التوقيع /



يعتمد!!!

مهندس الهيئة العامة للطرق والكباري





هيكل تنظيمي للعاملين بمشروع القطار السريع شركة أبو عجيبة للمقاولات العامة

التاريخ : ٢٠٢٢-٩-٢٤

اسم المشروع : مشروع القطار السريع (أكتوبر-أبوسمبل)

رقم العقد: (٢٠٢٤/٢٠٢٣/١٢٢٩)

رقم التليفون	عدد سنوات الخبرة	الوظيفة	الاسم	مستسل
01009742637	10	مدير المشروع	محمد حامد يحي	1
01017199596	5	مدير المكتب الفني	احمد احمد محمود	2
01019930593	5	مدير ضبط الجودة	نادي عادل	3
01114562154	10	مدير السلامة الوقائية	ربيع نوحيد	4
01090254469	5	مهندس التنفيذ	وليد محمود محمد	5
01559856322	5	مهندس صيانة (ميكانيكا وكهرباء)	محمد عماد الدين محمد	6
01223691236	5	مهندس التخطيط والبرمجة الزمنية	احمد قاسم	7
01002612002	5	مراقب تنفيذ (فني مواد)	احمد السيد احمد	8
01063768307			محمد نادي	
01029734478	5	حساب كميات	عبدالعال رجب	9
01064950832	7	مساح	حسين محمد جبريل	10
01033806848	7		محمد جمال	
01092355765	5	فني سلامة مرورية	محمد ابوغنيمه	11
01022245866	5		محمد حسين	

يعتمد!!!
مهندس الهيئة العامة للطرق والكباري

عن الاستشاري أ.د حسن مهدي
م/ احمد عزب
م/ محمود حبيب
التوقيع /
التوقيع /

مهندس الشركة المنفذة

م/ احمد فتح

التوقيع /



بيان المعدات

التاريخ : ٢٠٢٤-٤-١

اسم المشروع : مشروع القطار السريع (أكتوبر-أبوسمبل)
المسافة من كم ٨٥٠+٢٠٠ وحتى كم ٣٥٠+٢٠٢ بطول ١,٥ كم

بالإشارة الى العقد المبرم بين الهيئة العامة للطرق والكباري وشركة أبوعحيلة للمقاولات العامة رقم (٢٠٢٤/٢٠٢٣/١٢٢٩) بتاريخ ٢٠٢٤-٢-٢٦ لتنفيذ المشروع عاليه بالمعدات الآتية :

تاريخ الصنع	العدد	المعدة
2009	3	حفار
2005		
2010	4	لودر
2001		
2015	4	عربية فلاب
2008	5	
2005	2	
2000	1	بلدوزر
2015	1	تأذك مياة
2003	1	جريد
2002	2	هراس

عن الاستشاري أ.د حسن مهدي

م/ عبد الحميد علاء الدين / التوقيع
م/ أحمد عزب / التوقيع



يعتمد
مهندس الهيئة العامة للطرق والكباري

محضر استلام موقع

مشروع إنشاء خط القطار الكهربائي السريع (أكتوبر - أبوسمبل) من الكم 200+850 حتي الكم 202+350 بطول 1.5 كم
تنفيذ شركة أبو عجيبة للمقاولات العامة والتوريدات العمومية.

انه في يوم الاحد الموافق 3 / 3 / 2024 وبناء على عقد العملية رقم 1229 / 2023 / 2024

اجتمعت اللجنة المشكلة من السادة الاتي اسماؤهم بعد وهم :-

عن الهيئة العامة للطرق والكباري (طرف اول)

مدير عام المشروعات

مهندس الإشراف بالمنطقة السادسة

عن الاستشاري (مكتب أ.د/حسن مهدي)

استشاري المساحة (XYZ)

1-السيد المهندس / مصطفى شعبان البديري

2-السيد المهندس / محمود حسين

3- السيد المهندس / أحمد عزب

4- السيد المهندس / محمد عبدالرحمن سالم

عن الشركة المنفذه (طرف ثاني)

مهندس عن الشركة المنفذه

1-السيد المهندس / محمد حامد أبو عجيبة

وقد قامت اللجنة بالانتقال على الطبيعة للموقع عالية بالمعاينة الظاهرية على الطبيعة قام الطرف الاول بتسليم الطرف الثاني
الموقع خاليا من العوائق الظاهرية ولا مانع من استلام الموقع والبدء في الاعمال ويعتبر تاريخ 3 / 3 / 2024 هو تاريخ استلام
الموقع .

وقبل المحضر على ذلك .



اللجنة من الهيئة (طرف اول)



الشركة المنفذه (طرف ثاني)



رئيس الادارة المركزية للمنطقة

السادسة ببني سويف

مهندس / طارق الجزار



مكتب أ.د/حسن مهدي
للإستشارات الهندسية

SYSTRA



مشروع القطار السريع (6 أكتوبر / أبو سمبل)
القطاع الثاني بطول 158 كم من 176+700 كم الى 334+800
تنفيذ شركة : أبو عجيبة للمقاولات العامة بطول 1.5 كم
من كم 200+876 الى كم 202+376

محضر إجمال

اسم الشركة : أبو عجيبة للمقاولات العامة والتوريدات العمومية

القطاع: (201+920) الى (202+376)

أنه في يوم الثلاثاء الموافق 26 / 9 / 2023 قامت اللجنة المكونة من السادة :-

- 1- السيد المهندس/ حاتم مهران
- 2- السيد المهندس/ محمود عبدالرحيم الحيني
- 3- السيد المهندس/ محمد حامد أبو عجيبة

قامت اللجنة بالمعاينة الظاهرية وأخذ عينات وإجراء اختبارات صلاحية للقطاع
من (201+920) احداثي (260168.4582E, 3136445.233N) الى (202+376) احداثي
(260129.6912E, 3135991.0324N) وطبقاً لنتيجة العينة المرفقة تبين أن التربة غير صالحة

للتأسيس (سفو) ويلزم إزالتها وذلك حسب توصيات استشاري التربة وتوصيات سيفكون جروب .

ملحوظات : ...
التوقيع : ...

لجنة
مجلس
مجلس

عن مكتب أ.د/حسن مهدي
مدير المشروع
م. محمود علي

عن الشركة المنفذة
م. محمد علي

استشاري أبحاث التربة والاساسات :
أ.د.م. هشام محمد حلمي



مشروع :
قطار اموان الكهربائي السريع - القطاع الثاني

تقرير بنتائج اختبارات صلاحية أتربة للتأسيس

مقدمة : تم إعداد هذا التقرير بناءا علي طلب شركة / ابو عجيلة

و ذلك لتحديد خصائص ومدي صلاحية حينة تراب كأرض طبيعية تصلح للتأسيس

مصدر العينة : عند المحطة / ٢٠١+٩٢٠ (الارض طبيعية)

- المندوبين : وقد تم توريد العينة بمعرفة م/ محمود الحيني . (مهندس اشراف د/ حسن المهدي) رقم الهاتف = ١١٥٩٤٠٠١٠٨

بتاريخ : ٢٠٢٣/٩/٢١

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفلوط)

- التوصيف الظاهري للعينة : كتبان رملية ناعمة (سفو)

وقد تم عمل الاختبارات الآتية :

- ١-التدرج الحبيبي
- ٢-حد السيولة واللدونة
- ٣-اختبار البروكتور
- ٤-اختبار CBR
- ٥-اختبار المواد العضوية

وكانت نتائج الاختبارات كالآتي :

م	نوع الاختبار	النتائج	ملاحظات
1	تصنيف العينة	A-3	
2	نسبة الماء من منخل 200	4.6%	
3	مجال اللدونة	عديمة اللدونة	
4	أقصى كثافة جافة (البروكتور) yd max	1.858 gm/cm3	
5	نسبة المياه الأصلية	10.13 %	
6	قيمة CBR المغمورة	8.50 %	
8	المواد العضوية	لا يوجد	

• و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي غير صالحة للتأسيس عليها او للاستخدام في طبقات الردم



احمد حسن عطيه
م.م

مهندس المعمول
م.م
التوقيع

Coarse & Fine Aggregate Grading - ASTM C136 & AASHTO T27

التاريخ :	26/09/2023
الموقع : St =201+920	ارض طبيعية

نتائج الاختبار :-

رقم المنخل (mm)	رقم المنخل (inch)	وزن المحجوز على كل منخل	وزن المحجوز التراكمي	المحجوز %	العار %
127	5"	0	0	0%	100%
101.6	4"	0	0	0.00%	100.00%
76.2	3"	0	0	0.00%	100.00%
63.5	2.5"	0	0	0.00%	100.00%
50.8	2"	0	0	0.00%	100.00%
37.5	1.5"	0	0	0.00%	100.00%
25	1"	0	0	0.00%	100.00%
19	3/4"	0	0	0.00%	100.00%
12.7	1/2"	0	0	0.00%	100.00%
9.5	3/8"	0	0	0.00%	100.00%
4.75	# 4	0	0	0.00%	100.00%
	العار من منخل # 1	500			100.00%
	وزن العينة الكلي	500			
	وزن عينة الناعم	500			
2.36	# 10	0	0	0.0%	100.0%
0.425	# 40	63	63	12.6%	87.4%
0.075	# 200	414	477	95.4%	4.6%
السيولة و اللدونة		N.P			
التصنيف		A-3			

ملاحظات : توصيف العينة : كثران رملية ناعمة (Sand Dunes)



امه حسن عبيد
المهندس

مهندس المعماري
م. طه
التوقيع

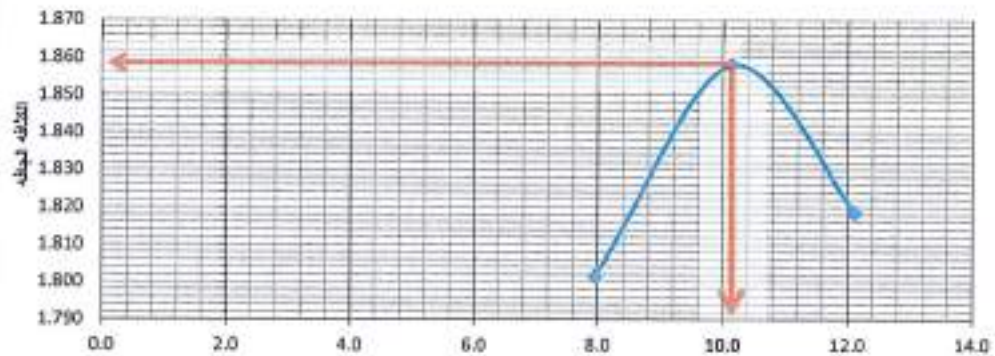
Modified Proctor : ASTM D1557

نوع العينة:	عينة قشبان رملية
تصنيف العينة:	A-3
نتائج الاختبار:	
وزن قالب	5731
حجم القالب	2140
الوزن كـلـكـه جـانـه	1.858
البيـاء الاسـوائـيه	10.13

رقم الاختبار	1	2	3
وزن القالب + العينة رطبه	9893.0	10110	10094
وزن التربه الرطبه	4162.0	4379	4383
كثافه الرطبه	1.945	2.046	2.039

رقم الجفـه	1	2	3	4	5	6
وزن الجفـه	53.65	55.31	54.35	54.15	55.14	53.4
وزن القالب + العينة رطبه	150.0	150.0	150.0	150.0	150.0	150.0
وزن الجفـه + العينة جافه	142.81	143.12	141.22	141.16	139.81	139.5
وزن البياء	7.2	6.9	8.8	8.8	10.2	10.5
وزن العينة جافه	88.96	87.61	86.87	87.01	84.67	86.1
المحتوى المائى %	8.1	7.8	10.1	10.2	12.0	12.2
متوسط المحتوى المائى %	8.0	10.1	12.1			
كثافه الجافه	1.801	1.858	1.818			

Modified Proctor Chart



ملاحظات:



احمد حسن عطيه
احمد حسن عطيه

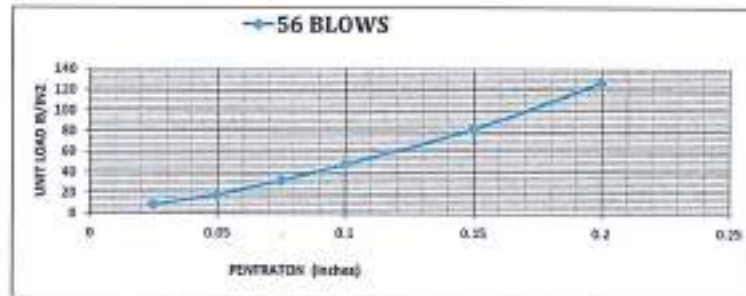
مهندس المعمل
د. محمد فاضل محمد البنا
التوقيع /
محمد فاضل محمد البنا

اختبار نسبة تحميل كاليفورنيا (C . B . R) ASTM D1883

A-3		تصنيف العينة	
عدد الضربات	56	عدد الضربات	56
حجم القالب (سم ³)	2121	حجم القالب (سم ³)	2121
وزن القالب (جم)	3260	وزن القالب (جم)	3260
وزن القالب موزن العينة رطبة (جم)	3611	وزن القالب موزن العينة رطبة (جم)	3611
وزن العينة رطبة (جم)	4322	وزن العينة رطبة (جم)	4322
كثافة الرخية (جم/سم ³)	2.028	كثافة الرخية (جم/سم ³)	2.028
القيمة كثافة جافة (جم/سم ³)	1.842	القيمة كثافة جافة (جم/سم ³)	1.842
كثافة المروكتر (جم/سم ³)	1.850	كثافة المروكتر (جم/سم ³)	1.850
نسبة الماء	99.1%	نسبة الماء	99.1%
نسبة التفتش	0.00%	نسبة التفتش	0.00%

حساب نسبة تحميل كاليفورنيا

7.62	5.08	3.81	2.54	1.95	1.27	0.635	الاختراق بالملم
0.3	0.2	0.15	0.1	0.075	0.05	0.025	الاختراق بالمليمتر
230.0	173	112.0	65.0	44.0	25.0	12.0	الفرادة kg
506.92	381.292	246.848	143.26	96.976	55.1	26.448	الفرادة بالاونز
169.05	127.155	82.32	47.775	32.34	18.375	8.82	المعمل IB1N2



8.5%	قيمة C . B . R
------	----------------

ملاحظات: تم إجراء اختبار في الماء لمدة ١٦ ساعة قبل توصلة المشروع



احمد حسن عطيه
المهندس

مهندس العمل
١٢
التوقيع
مهندس علي محمد الهنا

استشاري أبحاث التربة والاساسات :
أ.د.م. هشام محمد حلمي



مشروع :
قطار اسوان الكهربائي السريع - القطاع الثاني

تقرير بنتائج اختبارات صلاحية أترية للتأسيس

مقدمة : تم إعداد هذا التقرير بناءا على طلب شركة / ابو عجيله
وذلك لتحديد خصائص ومدي صلاحية عينة تراب كارض طيبعية تصلح للتأسيس

مصدر العينة : عند المحطة / 202+220 أرض طبيعية

- المندوبين : وقد تم توريد العينة بمعرفة 1- م/ محمود الحيني (مهندس الإشراف مكتب د/ حسن مهدي) رقم الهاتف = 01159400108

تاريخ توريد العينة : 2023/10/14

-العينة مسئوليه من أحضرها.

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفلوط)

وقد تم عمل الاختبارات الآتية :

- 1-التدرج الحبيبي
- 2-حد السيولة واللدونة
- 3-إختبار البروكتور
- 4-إختبار CBR
- 5-إختبار المواد العضوية.

وكانت نتائج الاختبارات كالآتي :

م	نوع الإختبار	النتائج	ملاحظات
1	تصنيف العينة	A-3	-
2	مجال اللدونة	---	-
3	أقصى كثافة جافة (البروكتور) yd max	2.02 gm/cm3	-
4	نسبة المياه الأمولية	8.4%	-
5	قيمة CBR المغمورة	15.7	-
6	المواد العضوية	لا يوجد	-

• يتم اتباع التعليمات العامة لميفيكون استشاري التربة .



مهندس المعمل
أ.د.م. هشام محمد حلمي
التوقيع

فني المعمل
أ.د.م. هشام محمد حلمي
التوقيع

Coarse & Fine Aggregate Grading - ASTM C136 & AASHTO T27

التاريخ :	18-10-23	الموقع : St :202+220	ارض طبيعيه
-----------	----------	----------------------	------------

نتائج الاختبار :-

رقم المنخل (mm)	رقم المنخل (inch)	وزن المحجوز على كل منخل	وزن المحجوز التراكمي	المحجوز %	المر %
127	5"	0	0	0%	100%
101.6	4"	0	0	0.00%	100.00%
76.2	3"	0	0	0.00%	100.00%
63.5	2.5"	0	0	0.00%	100.00%
50.8	2"	0	0	0.00%	100.00%
37.5	1.5"	0	0	0.00%	100.00%
25	1"	136	136	2.15%	97.85%
19	3/4"	30	166	2.62%	97.38%
12.7	1/2"	174	340	5.37%	94.63%
9.5	3/8"	178	518	8.19%	91.81%
4.75	# 4	226	744	11.76%	88.24%
	المر من منخل # 4	5582			88.24%
	وزن العينة الكلي	6326			
	وزن عينة التاعم	500			
2.36	# 10	31	31	17.2%	82.8%
0.425	# 40	90	121	33.1%	66.9%
0.075	# 200	342	463	93.5%	6.5%
السبولة و اللدونة		N.P			
التصنيف		A-3			

ملاحظات :



مهندس المعمل
أ/ محمد حمد عتيه
التوقيع

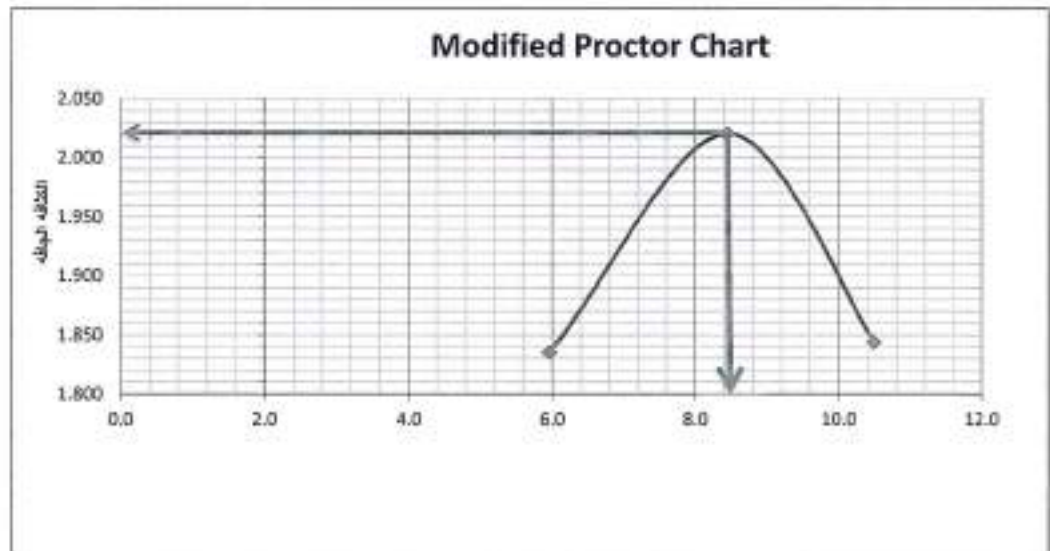
مهندس المعمل
أ/ محمد حمد البنا
التوقيع

Modified Proctor : ASTM D1557

نوع العينة:		عينة أرض طبيعية
تصنيف العينة:		A-3
نتائج الاختبار:		
وزن القالب	5731	الوزن كجالة جافة
حجم القالب	2140	الحجم الأسولي
		2.020
		8.4

رقم الاختبار	1	2	3
وزن القالب + العينة رطبة	9892.0	10420	10090
وزن القالب + العينة الجافة	4161.0	4689	4359
الوزن الرطبة	1.944	2.191	2.037

رقم الحقل	1	2	3	4	5	6
وزن الحقل	55	52.9	25.7	25.2	53.8	51.3
وزن الحقل + العينة رطبة	150.0	150.0	150.0	150.0	150.0	150.0
وزن الحقل + العينة جافة	144.4	144.6	140.2	140.4	141	140.5
وزن الماء	5.6	5.2	9.8	9.6	9.0	9.5
وزن العينة جافة	89.4	91.9	114.5	115.2	87.2	89.2
المحتوى المائي %	6.3	5.7	8.6	8.3	10.3	10.7
متوسط المحتوى المائي %	6.0	8.4	10.5			
الوزن الجاف	1.835	2.020	1.844			



ملاحظات :



أحمد محمد خضير
المهندس

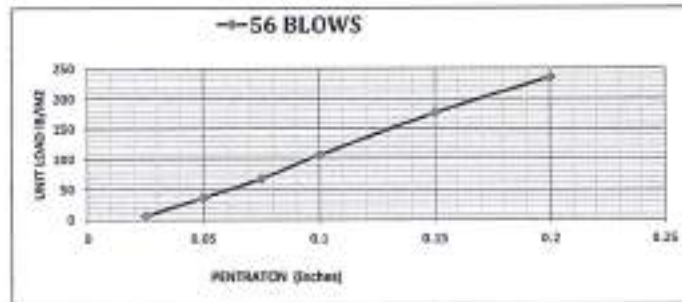
مهندس العمل
د. محمد بن محمد
التوقيع

اختبار نسبة تحميل كاليورنيا ASTM D1883 (C.B.R)

تصنيف العينة		A-3	
عدد الضربات	56	عدد الضربات	56
حجم القالب (سم ³)	2531	رقم الوقت	4
وزن القالب (جم)	5289	وزن الوقت	52.5
وزن القالب موزن العينة رطبه (جم)	3900	وزن الوقت «العينة رطبه جم	160
وزن العينة رطبه (جم)	4611	وزن الوقت «العينة جافة جم	142.48
الكثافة الرطبة (جم/سم ³)	2.184	وزن الماء جم	7.55
الكثافة الجافة (جم/سم ³)	1.398	وزن العينة جافة جم	90.0
كثافة البرونز (جم/سم ³)	2.020	المحتوى المائي %	8.4%
نسبة الدمك	98.8%		
نسبة ولفش	1.20%	غير قابلة للتفتش	

حساب نسبة تحمل كاليورنيا

7.52	5.08	3.81	2.54	1.95	1.27	0.635	الاختبار في العمق
0.3	0.2	0.15	0.1	0.075	0.05	0.025	الاختبار في عمق نسبة
530.0	320	240.0	145.0	92.0	49.0	8.0	التراب kg
1168.12	705.28	528.96	319.58	202.768	107.996	17.632	التراب بالبرونز
389.55	235.2	176.4	106.575	67.62	36.015	5.88	شمل 18/802



15.7%	قيمة C.B.R
-------	------------

ملاحظات: تم نشر النتائج في اليوم لمدة 25 ساعة قبل المراجعة المتوقعة



المهندس
أ. م. أحمد ح. عتيق
المهندس
أ. م. عيسى

المهندس
أ. م. مصطفى ع. ص. ص. ص.
المهندس
أ. م. عيسى

محضر مسافة نقل

مشروع القطار الكهربائي السريع (6 أكتوبر-اسوان) القطاع الثاني

انه في يوم الاثنين الموافق 2022/9/5 قامت اللجنة المذكورة من :-

(1) السيد المهندس / مصطفى محمد عبدالحمد مهندس المشروع الهيئة العامة للطرق والكباري

(2) السيد المهندس / محمد عبدالرحمن سالم مهندس المكتب الاستشاري (X,Y,Z)

(3) السيد المهندس / محمد حامد أبو عجيبة مدير المشروع شركة اورعجلة للمقاولات المتكاملة والتوريدات

وقد تم التوجه بالذهاب الى مكان المقاب حيث وجد ان المسافة من قطاع (من محطة 200+800 حتى 202+300)

على مكان المقاب 3 كم وذلك بسبب تعثر وجود مداف بسبب وجود مراوغ حول القطاع

وهذا محضر منا بذلك

التوقيع



م / مصطفى محمد عبدالحمد

م / محمد عبدالرحمن سالم

م / محمد حامد أبو عجيبة

الإدارة المركزية بالمنطقة السادسة بنى سويف

اعتماد

م / طارق يوسف الجزان





مكتب أ.د/حسن مهدي
للإستشارات الهندسية

SYSTRA



محضر معاينة مسافة نقل توريد تربة صالحة من محجر (ابو هشيمة)

مشروع القطار السريع (6 أكتوبر / أبو سمبل)
القطاع الثاني بطول 158 كم من 700+176 كم الى 800+334
تنفيذ شركة : أبو عجيبة للمقاولات العامة بطول 1.5 كم
من كم 876+200 الى كم 376+202

بالإشارة الى التكاليف الصادر من الهيئة العامة للطرق والكباري لصالح شركة ابو عجيله للمقاولات العامة و التوريدات العمومية بشأن تنفيذ الجسر الترابي والأعمال الصناعية بمشروع القطار الكهربائي السريع (اكتوبر - أسوان) في المسافة الكيلومترية 200+876 الى العلامة الكيلومترية 202+ 376

بناءً على تعليمات السيد المهندس / رئيس قطاع التنفيذ والمناطق بالتوريد من محاجر خارجية مرخصة بصفة مؤقتة لحين اعتماد وترخيص محاجر أخرى اقرب للقطاع

فقد اجتمعت اللجنة يوم الاثنين الموافق 2023/8/28 قامت اللجنة المشكلة من :-

مهندس الإشراف بالهيئة

مدير المشروع

مهندس المكتب الاستشاري (X,Y,Z)

مدير المشروع شركة أبو عجيبة للمقاولات المتكاملة والتوريدات

(1) السيد المهندس / محمد السيد شعبان

(2) السيد المهندس / حاتم مهران

(3) السيد المهندس / محمد عبدالرحمن سالم

(4) السيد المهندس / محمد حامد أبو عجيلة

وقامت اللجنة بالذهاب الي مكان المحجر (ابومشيمه) حيث وجد ان المسافة من القطاع (من محطة 200+876 حتي 202+376) حتي مكان المحجر (49 كم) وذلك بسبب تعذر وجود محجر قريب علي ان يتم التوريد بعد عمل اختبارات الصلاحية اللازمة والتأكد من صلاحية مواد المحجر للتوريد .

Easting	Northing	Longitude (E)	Latitude (N)	Station		الشركة	
260126.0446	3137487.7094	30° 33' 10.74 "	28° 20' 30.11 "	200+876	البداية	أبو عجيله	من
260129.6907	3135991.0284	30° 33' 11.98 "	28° 19' 41.52 "	202+376	النهاية	للغزلات العامة	
270048.623	3178136.045	30° 38' 45.6 "	28° 42' 36.3 "	-	-	محجر ابو هشيمة	الي

هذا المحضر اعتماد مؤقت لحين اعتماد محجر بجوار القطاع ، ولا يعد إثبات لتوريد أية كميات من المحجر المذكور ، ويجب على استشاري ضبط الجودة متابعة وحصر أي كميات يتم توريدها من المحجر المذكور ومتابعة صلاحية المحجر بصفة دورية مستمرة ومقارنتها بصلاحية المواد المنشونة لتوريدها على القطاع .

وأقفل المحضر على ذلك ۞۞۞

استثماري العسكرة (X,Y,Z)

م/محمد عبدالرحمن سالم

عن الشركة المنلذة

م/محمد حامد أبو عطية

يعتمد

مهندس الهيئة العامة للطرق والكبارى

تسمية ختم: ختم من الطين - ختم الطين

بِسْمِ اللَّهِ الرَّحْمَنِ الرَّحِيمِ

4-09-141-193

اسم المشروع : مشروع انشاء خط القطار الكهربائي السريع (أكتوبر - أبوسمبل)
الموضوع : اعتماد الهيئة العامة للطرق والكباري لطلبات استلام الاعمال الخاصة بالمشروع
الشركة المنفذة : شركة أبو عجيبة للمقاولات العامة والتوريدات العمومية من الكم 200+850
حتى الكم 202+350 .

محضر استلام بيانات مائية

انه في يوم الاحد الموافق 1 / 4 / 2024 تم عمل مستخلص جاري (1) اعمال ردم من
منسوب -11م الي -9م من منسوب القرمة والبنونات المائية المقدمه من الشركة المصرية
للتعدين الى شركة ابو عجيبة للمقاولات العامة علي كامل مسئولية الشركة المنفذة وتفرغ ارقامها
في بيان موقع من مسئول الشركة.
وبيانها كالآتي :-

1- محجر ابو هشيمة بواقع عدد 942 بون مائي.

وتم الاطلاع عليها من قبل استشاري المشروع ومهندس الاشراف من الهيئة واستلام البيان
الموقع من الشركة وارجاع اصل البنونات المائية للشركة وعلي مسئوليتها الكاملة من صحتها
وعدها وخلافه لحين إعادة تقديمها للهيئة اثناء مراجعة وعمل المستخلص الختامي للعملية.
وعلي ذلك جري التوقيع.

1- مهندس الشركة المنفذة

التوقيع / 



2- عن الاستشاري (مكتب أ.د/حسن مهدي)

السيد المهندس / أحمد عزب

3- الهيئة -مهندس الإشراف م/محمود محمد حسين

التوقيع /

م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارثة	رسوم المرور والميزان (جنيه)	المحجر
107	2023/08/19	1659184	2673-5926	60			سلطان أبو هشيمة
108	2023/08/19	15786087	5728-7138	60			سلطان أبو هشيمة
109	2023/08/20	67776508	5127-8731	60			سلطان أبو هشيمة
110	2023/08/20	67776520	6874-5472	60			سلطان أبو هشيمة
111	2023/08/20	15786057	2546-5241	60			سلطان أبو هشيمة
112	2023/08/21	67776511	9637-2564	60			سلطان أبو هشيمة
113	2023/08/21	67776702	9271-7932	60			سلطان أبو هشيمة
114	2023/08/21	15783768	4823-3418	60			سلطان أبو هشيمة
115	2023/08/21	15783709	2533-1482	60			سلطان أبو هشيمة
116	2023-08-21	22418424	2789-9254	60			سلطان أبو هشيمة
117	2023-08-21	22417567	7391-5268	60			سلطان أبو هشيمة
118	2023-08-21	22419695	1932-9164	60			سلطان أبو هشيمة
119	2023-08-21	22417554	22417554	60			سلطان أبو هشيمة
120	2023/08/22	67776852	4958-1478	60			سلطان أبو هشيمة
121	2023/08/22	67776840	2673-5926	60			سلطان أبو هشيمة
122	2023/08/22	15780909	5748-7182	60			سلطان أبو هشيمة
123	2023/08/22	15780739	7548-7184	60			سلطان أبو هشيمة
124	2023-08-22	22417594	1658-9287	60			سلطان أبو هشيمة
125	2023-08-22	22417564	1658-6287	60			سلطان أبو هشيمة
126	2023-08-22	24602410	5973-7489	60			سلطان أبو هشيمة
127	2023/08/23	67776846	5728-7138	60			سلطان أبو هشيمة
128	2023/08/23	67776903	6497-6854	60			سلطان أبو هشيمة
129	2023/08/23	15797899	5748-7138	60			سلطان أبو هشيمة
130	2023/08/23	15765731	7159-3657	60			سلطان أبو هشيمة
131	2023-08-23	21279793	5973-7489	60			سلطان أبو هشيمة
132	2023-08-23	22417578	5973-7489	60			سلطان أبو هشيمة
133	2023/08/24	67776514	2546-5241	60			سلطان أبو هشيمة
134	2023/08/24	67776505	4823-3418	60			سلطان أبو هشيمة
135	2023/08/24	1686159	3967-8437	60			سلطان أبو هشيمة
136	2023/08/24	15798649	8291-1679	60			سلطان أبو هشيمة
137	2023-08-24	22419884	7489-5973	60			سلطان أبو هشيمة
138	2023-08-24	22419735	7489-5973	60			سلطان أبو هشيمة
139	2023-08-24	6751433	8263-6394	60			سلطان أبو هشيمة
140	2023/08/26	67776708	2533-1482	60			سلطان أبو هشيمة
141	2023/08/26	67776711	5748-7182	60			سلطان أبو هشيمة
142	2023/08/26	15798369	2533-1482	60			سلطان أبو هشيمة
143	2023/08/26	15787824	7138-5748	60			سلطان أبو هشيمة
144	2023/08/27	67776849	7548-7184	60			سلطان أبو هشيمة
145	2023/08/27	67776714	5748-7138	60			سلطان أبو هشيمة
146	2023/08/27	15787924	5589-5784	60			سلطان أبو هشيمة
147	2023/08/27	15795948	2533-1482	60			سلطان أبو هشيمة
148	2023-08-27	5440053	5362-4927	60			سلطان أبو هشيمة
149	2023-08-27	5442196	8341	20			سلطان أبو هشيمة
150	2023-08-27	13195149	8193-4973	60			سلطان أبو هشيمة
151	2023/08/28	67776502	7159-3657	60			سلطان أبو هشيمة
152	2023/08/28	67776837	8291-1679	60			سلطان أبو هشيمة
153	2023/08/28	15797349	3967-8437	60			سلطان أبو هشيمة
154	2023/08/28	15783149	6853-9672	60			سلطان أبو هشيمة
155	2023-08-28	18999009	3651	20			سلطان أبو هشيمة
156	2023/08/29	67776705	2533-1482	60			سلطان أبو هشيمة
157	2023/08/29	67776699	7138-5748	60			سلطان أبو هشيمة
158	2023/08/29	15783141	4973-8193	60			سلطان أبو هشيمة
159	2023/08/29	1686159	7413-6925	60			سلطان أبو هشيمة

مهندس إشراف الهيئة
م/محمود حسين

عن مكتب الاستشاري أ.د/ حسن مهدي
م/ احمد عزب

أ.د/ حسن مهدي



م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارثة	رسوم المرور والميزان (جنيه)	المحجر
54	2023/08/08	67776665	2673-5926	60			سلطان أبو هشيمة
55	2023/08/08	67776659	5728-7138	60			سلطان أبو هشيمة
56	2023/08/08	1687394	4823-3418	60			سلطان أبو هشيمة
57	2023/08/08	1659781	2533-1482	60			سلطان أبو هشيمة
58	2023/08/09	67776638	6497-6854	60			سلطان أبو هشيمة
59	2023/08/09	67776641	2546-5241	60			سلطان أبو هشيمة
60	2023/08/09	1687956	5748-7182	60			سلطان أبو هشيمة
61	2023/08/09	16893428	7548-7148	60			سلطان أبو هشيمة
62	2023-08-09	22417176	9271-1687	60			سلطان أبو هشيمة
63	2023-08-09	22416941	5317-8651	60			سلطان أبو هشيمة
64	2023-08-09	22417689	3257-2756	60			سلطان أبو هشيمة
65	2023-08-09	22417136	5391-8953	60			سلطان أبو هشيمة
66	2023-08-09	22417151	7316-9865	60			سلطان أبو هشيمة
67	2023/08/10	67776635	2533-1482	60			سلطان أبو هشيمة
68	2023/08/10	67776632	5748-7182	60			سلطان أبو هشيمة
69	2023/08/10	1687237	5748-7138	60			سلطان أبو هشيمة
70	2023/08/10	1659375	7159-3657	60			سلطان أبو هشيمة
71	2023-08-10	22417170	8614-7142	60			سلطان أبو هشيمة
72	2023-08-10	22416954	1687-9271	60			سلطان أبو هشيمة
73	2023-08-10	22417141	1687-9271	60			سلطان أبو هشيمة
74	2023-08-10	22417131	4156-3286	60			سلطان أبو هشيمة
75	2023/08/11	16893413	8291-1679	60			سلطان أبو هشيمة
76	2023/08/11	1686948	2533-1482	60			سلطان أبو هشيمة
77	2023-08-11	22417688	9752-1648	60			سلطان أبو هشيمة
78	2023-08-11	22416914	3864-8465	60			سلطان أبو هشيمة
79	2023-08-11	22417190	8764-6249	60			سلطان أبو هشيمة
80	2023-08-11	22417599	1758-5469	60			سلطان أبو هشيمة
81	2023/08/12	67776629	7548-7184	60			سلطان أبو هشيمة
82	2023/08/12	67776626	5748-7138	60			سلطان أبو هشيمة
83	2023/08/12	1686771	7138-5748	60			سلطان أبو هشيمة
84	2023/08/12	1686773	5589-5784	60			سلطان أبو هشيمة
85	2023/08/13	67776623	7138-5748	60			سلطان أبو هشيمة
86	2023/08/13	67776548	7159-3657	60			سلطان أبو هشيمة
87	2023/08/13	1686397	3967-8437	60			سلطان أبو هشيمة
88	2023/08/13	1659153	6853-9674	60			سلطان أبو هشيمة
89	2023/08/14	67776551	8291-1679	60			سلطان أبو هشيمة
90	2023/08/14	67776544	5589-5784	60			سلطان أبو هشيمة
91	2023/08/14	6754795	4973-8193	60			سلطان أبو هشيمة
92	2023/08/14	6754962	7413-6925	60			سلطان أبو هشيمة
93	2023/08/15	67776563	3967-8437	60			سلطان أبو هشيمة
94	2023/08/15	67776596	6853-9672	60			سلطان أبو هشيمة
95	2023/08/15	1656852	7163-2139	60			سلطان أبو هشيمة
96	2023/08/15	1656175	6391-2854	60			سلطان أبو هشيمة
97	2023/08/16	67776557	4973-8193	60			سلطان أبو هشيمة
98	2023/08/16	67776620	7413-6925	60			سلطان أبو هشيمة
99	2023/08/16	1659375	4659-4679	60			سلطان أبو هشيمة
100	2023/08/16	1656823	6874-5472	60			سلطان أبو هشيمة
101	2023/08/17	67776554	7163-2139	60			سلطان أبو هشيمة
102	2023/08/17	67776675	6391-2854	60			سلطان أبو هشيمة
103	2023/08/17	1659369	9637-2564	60			سلطان أبو هشيمة
104	2023/08/17	1684085	7958-1478	60			سلطان أبو هشيمة
105	2023/08/19	67776614	4659-4679	60			سلطان أبو هشيمة
106	2023/08/19	67776617	7239-5639	60			سلطان أبو هشيمة

مهندس اشراف الهيئة
م/محمود حسين

عن مكتب الاستشاري أ.د/ حسن مهدي
م/ احمد عزب
أحمد عزب



مكتب أ.د. حسن مهدي
للإستشارات الهندسية

مشروع إنشاء القطار الكهربائي (أكتوبر - أسوان)
القطاع الثاني (بني مزار - منفلوط) من الكم 200+850 إلى الكم 202+350 بطول 1.5 كم
تنفيذ : شركة أبو عجيبة للمقاولات العامة والتوريدات العمومية
عقد رقم (2024-2023-1229)



م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارثة	رسوم المرور والميزان (جنيه)	المحجر
1	2023/08/01	67776931	3967-8437	60			سلطان أبو هشيمة
2	2023/08/01	67776937	6853-9672	60			سلطان أبو هشيمة
3	2023/08/01	16578697	6853-9672	60			سلطان أبو هشيمة
4	2023/08/01	16576573	4973-8193	60			سلطان أبو هشيمة
5	2023-08-01	22418474	1758-5419	60			سلطان أبو هشيمة
6	2023-08-01	22418237	5198-6814	60			سلطان أبو هشيمة
7	2023-08-01	22418212	9449-2983	60			سلطان أبو هشيمة
8	2023-08-01	22416980	2514-1687	60			سلطان أبو هشيمة
9	2023/08/02	67776934	4973-8193	60			سلطان أبو هشيمة
10	2023/08/02	67776940	7413-6925	60			سلطان أبو هشيمة
11	2023/08/02	1684271	7413-6925	60			سلطان أبو هشيمة
12	2023/08/02	1684085	7163-2139	60			سلطان أبو هشيمة
13	2023-08-02	22417194	7142-8614	60			سلطان أبو هشيمة
14	2023/08/03	67776943	7163-2139	60			سلطان أبو هشيمة
15	2023/08/03	67776946	6391-2139	60			سلطان أبو هشيمة
16	2023/08/03	1686781	6391-2854	60			سلطان أبو هشيمة
17	2023/08/03	1659752	4659-4679	60			سلطان أبو هشيمة
18	2023-08-03	22417672	4523-7419	60			سلطان أبو هشيمة
19	2023-08-03	22417691	7698-6912	60			سلطان أبو هشيمة
20	2023-08-03	22417198	7316-9865	60			سلطان أبو هشيمة
21	2023-08-03	22417669	7142-8614	60			سلطان أبو هشيمة
22	2023/08/04	67776723	4659-4679	60			سلطان أبو هشيمة
23	2023/08/04	67776726	7239-5639	60			سلطان أبو هشيمة
24	2023/08/04	1683562	7239-5639	60			سلطان أبو هشيمة
25	2023/08/04	1682383	6874-5472	60			سلطان أبو هشيمة
26	2023/08/05	67776729	5127-8731	60			سلطان أبو هشيمة
27	2023/08/05	67776732	6874-5472	60			سلطان أبو هشيمة
28	2023/08/05	1686982	9637-2564	60			سلطان أبو هشيمة
29	2023/08/05	1687582	7958-1478	60			سلطان أبو هشيمة
30	2023-08-05	22417155	7435-3127	60			سلطان أبو هشيمة
31	2023-08-05	22417210	1687-9271	60			سلطان أبو هشيمة
32	2023-08-05	22417152	6381-1265	60			سلطان أبو هشيمة
33	2023-08-05	22417667	3257-2756	60			سلطان أبو هشيمة
34	2023-08-05	22417167	5312-5341	60			سلطان أبو هشيمة
35	2023/08/06	67776899	9637-2564	60			سلطان أبو هشيمة
36	2023/08/06	67776653	9271-7932	60			سلطان أبو هشيمة
37	2023/08/06	1687672	2673-5926	60			سلطان أبو هشيمة
38	2023/08/06	1687192	5728-7138	60			سلطان أبو هشيمة
39	2023-08-06	22417153	9154-3267	60			سلطان أبو هشيمة
40	2023-08-06	22417297	1483-1785	60			سلطان أبو هشيمة
41	2023-08-06	22417113	4157-8726	60			سلطان أبو هشيمة
42	2023-08-06	22416915	8729-8217	60			سلطان أبو هشيمة
43	2023-08-06	22417133	1973-2945	60			سلطان أبو هشيمة
44	2023/08/07	67776672	7958-1478	60			سلطان أبو هشيمة
45	2023/08/07	67776668	4823-3418	60			سلطان أبو هشيمة
46	2023/08/07	1687352	6497-6854	60			سلطان أبو هشيمة
47	2023/08/07	1687482	2546-5241	60			سلطان أبو هشيمة
48	2023-08-07	22417692	246-9784	60			سلطان أبو هشيمة
49	2023-08-07	22417144	5837-1754	60			سلطان أبو هشيمة
50	2023-08-07	22417661	2568-9123	60			سلطان أبو هشيمة
51	2023-08-07	22416970	3864-8465	60			سلطان أبو هشيمة
52	2023-08-07	22417160	8249-7192	60			سلطان أبو هشيمة
53	2023-08-07	22417682	9417-3529	60			سلطان أبو هشيمة

مهندس إشراف الهيئة
م/محمود حسين

عن مكتب الاستشاري أ.د/ حسن مهدي
م/ احمد عزب

أ.د. حسن مهدي



م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارثة	رسوم المرور والميزان (جنيه)	المحجر
160	2023-08-29	13195694	5923	20			سلطان أبو هشيمة
161	2023/08/30	67776696	5589-5748	60			سلطان أبو هشيمة
162	2023/08/30	67776662	3967-8437	60			سلطان أبو هشيمة
163	2023/08/30	1686753	5127-8731	60			سلطان أبو هشيمة
164	2023/08/30	1686764	5874-5472	60			سلطان أبو هشيمة
165	2023-08-30	6750892	9186-7416	60			سلطان أبو هشيمة
166	2023-08-30	18998479	9237-3417	60			سلطان أبو هشيمة
167	2023/08/31	67776656	6853-9672	60			سلطان أبو هشيمة
168	2023/08/31	67776611	4973-8193	60			سلطان أبو هشيمة
169	2023/08/31	1686717	9637-2564	60			سلطان أبو هشيمة
170	2023/08/31	1686794	9271-7932	60			سلطان أبو هشيمة
171	2023/09/01	67777014	8179-5312	60			سلطان أبو هشيمة
172	2023/09/01	67776679	8392-2867	60			سلطان أبو هشيمة
173	2023/09/01	67776613	4263-1562	60			سلطان أبو هشيمة
174	2023/09/01	67777011	6341-2456	60			سلطان أبو هشيمة
175	2023/09/01	1688194	7958-1487	60			سلطان أبو هشيمة
176	2023/09/01	1688146	2673-5926	60			سلطان أبو هشيمة
177	2023-09-01	18998808	3532	20			سلطان أبو هشيمة
178	2023-09-01	20440075	8764-6249	60			سلطان أبو هشيمة
179	2023-09-01	18997880	1859-7163	60			سلطان أبو هشيمة
180	2023-09-01	13196714	1936-1785	60			سلطان أبو هشيمة
181	2023-09-01	18996881	3651	20			سلطان أبو هشيمة
182	2023/09/02	67776806	8392-2867	60			سلطان أبو هشيمة
183	2023/09/02	6776812	4263-1562	60			سلطان أبو هشيمة
184	2023/09/02	67776818	6341-2456	60			سلطان أبو هشيمة
185	2023/09/02	67776999	5394-7563	60			سلطان أبو هشيمة
186	2023/09/02	67776602	7413-6925	60			سلطان أبو هشيمة
187	2023/09/02	67776608	7163-2139	60			سلطان أبو هشيمة
188	2023/09/02	1687180	5728-7138	60			سلطان أبو هشيمة
189	2023/09/02	1684085	6497-6854	60			سلطان أبو هشيمة
190	2023-09-02	22417631	9256-9264	60			سلطان أبو هشيمة
191	2023/09/03	67777026	7137-1282	60			سلطان أبو هشيمة
192	2023/09/03	67777029	9658-8274	60			سلطان أبو هشيمة
193	2023/09/03	67777032	4123-1256	60			سلطان أبو هشيمة
194	2023/09/03	67777035	3729-7285	60			سلطان أبو هشيمة
195	2023/09/03	67776537	3729-7285	60			سلطان أبو هشيمة
196	2023/09/03	67776605	6391-2854	60			سلطان أبو هشيمة
197	2023/09/03	67776593	4659-4679	60			سلطان أبو هشيمة
198	2023/09/03	15789863	2546-5248	60			سلطان أبو هشيمة
199	2023/09/03	15795948	4823-3418	60			سلطان أبو هشيمة
200	2023-09-03	13195565	1936-1785	60			سلطان أبو هشيمة
201	2023-09-03	18996760	3971-8547	60			سلطان أبو هشيمة
202	2023/09/04	8644250	8374-3714	60			سلطان أبو هشيمة
203	2023/09/04	8644249	8919-5767	60			سلطان أبو هشيمة
204	2023/09/04	67776866	6374-9683	60			سلطان أبو هشيمة
205	2023/09/04	67776830	8231-9258	60			سلطان أبو هشيمة
206	2023/09/04	67776827	8413-6983	60			سلطان أبو هشيمة
207	2023/09/04	67776599	7239-5639	60			سلطان أبو هشيمة
208	2023/09/04	67776774	5127-8731	60			سلطان أبو هشيمة
209	2023/09/04	15795967	2533-1482	60			سلطان أبو هشيمة
210	2023/09/04	15784191	5748-7182	60			سلطان أبو هشيمة
211	2023-09-04	13195580	1936-1785	60			سلطان أبو هشيمة
212	2023/09/05	67776824	4476-8517	60			سلطان أبو هشيمة

مهندس إشراف الهيئة
م/محمود حسين

عن مكتب الاستشاري أ.د/ حسن مهدي
م/ احمد عزب

أحمد عزب



2

مجلس الشورى
م/م
1997
100-741-199

م/ احمد عزب

م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارثة	رسوم المرور والميزان (جنه)	المحجر
319	2023-09-14	18998188	7912-5746	60			سلطان أبو هشيمة
320	2023/09/15	67776834	2546-5248	60			سلطان أبو هشيمة
321	2023/09/15	67776831	4823-3418	60			سلطان أبو هشيمة
322	2023-09-15	13196619	1936-1785	60			سلطان أبو هشيمة
323	2023-09-15	6674609	1982-7376	60			سلطان أبو هشيمة
324	2023-09-15	18998294	4735-4973	60			سلطان أبو هشيمة
325	2023/09/16	67776558	6158-8357	60			سلطان أبو هشيمة
326	2023/09/16	67776645	9186-4847	40			سلطان أبو هشيمة
327	2023/09/16	67776772	7189-6463	60			سلطان أبو هشيمة
328	2023/09/16	67776597	1282-7137	60			سلطان أبو هشيمة
329	2023/09/16	67776600	7214-9365	60			سلطان أبو هشيمة
330	2023/09/16	67776795	4659-4679	60			سلطان أبو هشيمة
331	2023/09/16	67776801	7239-5639	60			سلطان أبو هشيمة
332	2023/09/16	67776828	2533-1482	60			سلطان أبو هشيمة
333	2023/09/16	67776825	5748-7182	60			سلطان أبو هشيمة
334	2023-09-16	8423361	9396-9783	60			سلطان أبو هشيمة
335	2023-09-16	21278101	7381-7348	60			سلطان أبو هشيمة
336	2023-09-16	22418480	3529-9417	60			سلطان أبو هشيمة
337	2023-09-16	13196666	1936-1785	60			سلطان أبو هشيمة
338	2023-09-16	13196637	1936-1785	60			سلطان أبو هشيمة
339	2023-09-16	8423360	1859-7163	60			سلطان أبو هشيمة
340	2023-09-16	18998271	1982-2786	60			سلطان أبو هشيمة
341	2023/09/17	67776603	3692-4622	60			سلطان أبو هشيمة
342	2023/09/17	67776606	1692-7968	60			سلطان أبو هشيمة
343	2023/09/17	67776609	8691-3762	60			سلطان أبو هشيمة
344	2023/09/17	67776612	7285-3729	60			سلطان أبو هشيمة
345	2023/09/17	67776673	2867-8392	60			سلطان أبو هشيمة
346	2023/09/17	67776804	6874-5472	60			سلطان أبو هشيمة
347	2023/09/17	67776807	9637-2564	60			سلطان أبو هشيمة
348	2023/09/17	67776822	7548-7184	60			سلطان أبو هشيمة
349	2023-09-17	8423391	8465-2475	60			سلطان أبو هشيمة
350	2023-09-17	8423515	2378-2359	60			سلطان أبو هشيمة
351	2023-09-17	8423395	4361-3184	60			سلطان أبو هشيمة
352	2023-09-17	8423513	6379-8246	60			سلطان أبو هشيمة
353	2023-09-17	8423532	7356-2681	60			سلطان أبو هشيمة
354	2023-09-17	8423541	2987-1836	60			سلطان أبو هشيمة
355	2023-09-17	18998196	4678-7562	60			سلطان أبو هشيمة
356	2023-09-17	8423367	4356-7892	60			سلطان أبو هشيمة
357	2023-09-17	8423537	2756-3257	60			سلطان أبو هشيمة
358	2023-09-17	8423510	9648-7518	60			سلطان أبو هشيمة
359	2023-09-17	24602407	5869-1736	60			سلطان أبو هشيمة
360	2023-09-17	22418416	1265-6381	60			سلطان أبو هشيمة
361	2023-09-17	22417593	5973-7489	60			سلطان أبو هشيمة
362	2023-09-17	13196650	1936-1785	60			سلطان أبو هشيمة
363	2023-09-17	22418485	5312-5341	60			سلطان أبو هشيمة
364	2023/09/18	67776615	9253-3285	60			سلطان أبو هشيمة
365	2023/09/18	67776618	8691-3762	60			سلطان أبو هشيمة
366	2023/09/18	67776552	7916-7848	60			سلطان أبو هشيمة
367	2023/09/18	67776555	7139-8423	60			سلطان أبو هشيمة
368	2023/09/18	67776594	6397-4727	60			سلطان أبو هشيمة
369	2023/09/18	67776810	9271-7932	60			سلطان أبو هشيمة
370	2023/09/18	67776644	7958-1478	60			سلطان أبو هشيمة
371	2023-09-18	189978806	1826-2319	60			سلطان أبو هشيمة

مهندس اشراف الهيئة
م/محمود حسين

عن مكتب الاستشاري أ.د/ حسن مهدي
م/ احمد عزب

أحمد عزب

مهندس الاستشارة
م/ محمد جاسم أبو عجيبة
أبو عجيبة للاستشارات الهندسية
1999-1998-1997

م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارتة	رسوم المرور والميزان (جنيه)	المحجر
372	2023-09-18	18997809	6942-9853	60			سلطان أبوهشيمة
373	2023-09-18	8423588	4937-6983	60			سلطان أبوهشيمة
374	2023-09-18	18997849	1217-8729	60			سلطان أبوهشيمة
375	2023-09-18	18997811	1736-5869	60			سلطان أبوهشيمة
376	2023-09-18	18997819	4378-4965	60			سلطان أبوهشيمة
377	2023-09-18	8423583	6381-1295	60			سلطان أبوهشيمة
378	2023-09-18	8423552	4973-8193	60			سلطان أبوهشيمة
379	2023-09-18	8423599	2645-2716	60			سلطان أبوهشيمة
380	2023-09-18	18997805	1754-5837	60			سلطان أبوهشيمة
381	2023-09-18	8423573	2593-4378	60			سلطان أبوهشيمة
382	2023-09-18	8423566	4637-5319	60			سلطان أبوهشيمة
383	2023-09-18	8423581	8439-8612	60			سلطان أبوهشيمة
384	2023-09-18	18997801	8476-2943	60			سلطان أبوهشيمة
385	2023-09-18	18997830	1854-1654	60			سلطان أبوهشيمة
386	2023-09-18	8423554	9271-7932	60			سلطان أبوهشيمة
387	2023-09-18	8423551	1948-7653	60			سلطان أبوهشيمة
388	2023-09-18	8423563	6721-9657	60			سلطان أبوهشيمة
389	2023-09-18	8423546	6874-5472	60			سلطان أبوهشيمة
390	2023-09-18	8423358	2179-9274	60			سلطان أبوهشيمة
391	2023-09-18	8423572	1687-8317	60			سلطان أبوهشيمة
392	2023-09-18	8423560	7215-5248	60			سلطان أبوهشيمة
393	2023-09-18	18997823	8975-2931	60			سلطان أبوهشيمة
394	2023-09-18	18997817	6573-1843	60			سلطان أبوهشيمة
395	2023-09-18	18997821	2645-7698	60			سلطان أبوهشيمة
396	2023-09-18	18997804	5329-8314	60			سلطان أبوهشيمة
397	2023-09-18	8423548	9637-2564	60			سلطان أبوهشيمة
398	2023-09-18	8423565	6713-4895	60			سلطان أبوهشيمة
399	2023-09-18	8423575	2819-1824	60			سلطان أبوهشيمة
400	2023-09-18	8423586	9417-3529	60			سلطان أبوهشيمة
401	2023-09-18	18997820	7921-5216	60			سلطان أبوهشيمة
402	2023-09-18	8423595	1986-2975	60			سلطان أبوهشيمة
403	2023-09-18	8423570	1896-1856	60			سلطان أبوهشيمة
404	2023-09-18	18997825	9173-7135	60			سلطان أبوهشيمة
405	2023/09/19	67776542	2867-8392	60			سلطان أبوهشيمة
406	2023/09/19	67776561	6574-8739	60			سلطان أبوهشيمة
407	2023/09/19	67776546	9253-3285	60			سلطان أبوهشيمة
408	2023/09/19	67776549	2365-2381	60			سلطان أبوهشيمة
409	2023/09/19	67776621	15062-4263	20			سلطان أبوهشيمة
410	2023/09/19	67776655	2673-5926	60			سلطان أبوهشيمة
411	2023/09/19	67776681	5728-7138	60			سلطان أبوهشيمة
412	2023-09-19	18997865	7352	20			سلطان أبوهشيمة
413	2023-09-19	22417811	5216-8921	60			سلطان أبوهشيمة
414	2023-09-19	13196673	1936-1785	60			سلطان أبوهشيمة
415	2023-09-19	18997835	3248-3176	60			سلطان أبوهشيمة
416	2023-09-19	18997878	9417-3529	60			سلطان أبوهشيمة
417	2023-09-19	8423600	9271-2599	60			سلطان أبوهشيمة
418	2023-09-19	18997864	1982-2789	60			سلطان أبوهشيمة
419	2023-09-19	18997856	9518-8945	60			سلطان أبوهشيمة
420	2023-09-19	18997848	7359-2459	60			سلطان أبوهشيمة
421	2023-09-19	13196683	7653-2979	60			سلطان أبوهشيمة
422	2023-09-19	18997854	5973-7489	60			سلطان أبوهشيمة
423	2023-09-19	18997837	7142-8614	60			سلطان أبوهشيمة
424	2023-09-19	18997885	1843-6573	60			سلطان أبوهشيمة

مهندس إشراف الهيئة
م/محمود حسين

عن مكتب الاستشاري أ.د/ حسن مهدي
م/ احمد عزب

أشرف



م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارثة	رسوم المرور والميزان (جنيه)	المحجر
425	2023-09-19	18997897	6874-5472	60			سلطان أبو هشيمة
426	2023-09-19	18997891	8217-8729	60			سلطان أبو هشيمة
427	2023/09/20	67776624	4713-8553	60			سلطان أبو هشيمة
428	2023/09/20	67776627	8576-9695	60			سلطان أبو هشيمة
429	2023/09/20	67776630	8739-9749	60			سلطان أبو هشيمة
430	2023/09/20	67776633	1692-7968	60			سلطان أبو هشيمة
431	2023/09/20	67776591	1282-7137	60			سلطان أبو هشيمة
432	2023/09/20	67776678	6497-6854	60			سلطان أبو هشيمة
433	2023/09/20	67776720	2546-5241	60			سلطان أبو هشيمة
434	2023/09/21	67776636	6158-8357	60			سلطان أبو هشيمة
435	2023/09/21	67776639	9186-4847	60			سلطان أبو هشيمة
436	2023/09/21	67776642	7189-6463	60			سلطان أبو هشيمة
437	2023/09/21	67776718	1282-7137	60			سلطان أبو هشيمة
438	2023/09/21	67776660	7214-9365	60			سلطان أبو هشيمة
439	2023/09/21	67776693	4823-3418	60			سلطان أبو هشيمة
440	2023/09/21	67776717	2533-1482	60			سلطان أبو هشيمة
441	2023-09-21	18998312	1785-1936	60			سلطان أبو هشيمة
442	2023-09-21	13196690	1936-1785	60			سلطان أبو هشيمة
443	2023/09/22	67776532	3692-4622	60			سلطان أبو هشيمة
444	2023/09/22	67776535	1692-7968	60			سلطان أبو هشيمة
445	2023/09/22	67776538	8691-3762	60			سلطان أبو هشيمة
446	2023/09/22	67776541	2867-8329	60			سلطان أبو هشيمة
447	2023/09/22	67776867	2867-8392	60			سلطان أبو هشيمة
448	2023/09/22	67776690	5748-7182	60			سلطان أبو هشيمة
449	2023/09/22	67776684	8548-7184	60			سلطان أبو هشيمة
450	2023/09/23	67776911	9253-3285	60			سلطان أبو هشيمة
451	2023/09/23	67776914	8691-3762	60			سلطان أبو هشيمة
452	2023/09/23	67776917	7916-7848	60			سلطان أبو هشيمة
453	2023/09/23	67776920	7139-8423	60			سلطان أبو هشيمة
454	2023/09/23	67776923	6397-4727	60			سلطان أبو هشيمة
455	2023/09/23	67776687	5748-7138	60			سلطان أبو هشيمة
456	2023/09/23	67776650	7159-3657	60			سلطان أبو هشيمة
457	2023-09-23	22418109	9634-4351	60			سلطان أبو هشيمة
458	2023-09-23	22418126	7163-1859	60			سلطان أبو هشيمة
459	2023-09-23	22418117	9783-9356	60			سلطان أبو هشيمة
460	2023-09-23	22417885	2983-9479	60			سلطان أبو هشيمة
461	2023/09/24	67776927	2867-8392	60			سلطان أبو هشيمة
462	2023/09/24	67776930	6574-8739	60			سلطان أبو هشيمة
463	2023/09/24	67776936	9253-3285	60			سلطان أبو هشيمة
464	2023/09/24	67776933	2365-2381	60			سلطان أبو هشيمة
465	2023/09/24	67776939	5637	20			سلطان أبو هشيمة
466	2023/09/24	67776928	8291-1679	60			سلطان أبو هشيمة
467	2023/09/24	67776884	2533-1482	60			سلطان أبو هشيمة
468	2023-09-24	22417807	1853-3698	60			سلطان أبو هشيمة
469	2023-09-24	22418102	9536	20			سلطان أبو هشيمة
470	2023-09-24	22417980	9539-8462	60			سلطان أبو هشيمة
471	2023-09-24	22417976	8945-5398	60			سلطان أبو هشيمة
472	2023-09-24	22418132	5816-9157	60			سلطان أبو هشيمة
473	2023-09-24	22417577	7698-6912	60			سلطان أبو هشيمة
474	2023/09/25	67776942	8576-9695	60			سلطان أبو هشيمة
475	2023/09/25	67776722	6158-8357	60			سلطان أبو هشيمة
476	2023/09/25	67776725	9186-4847	60			سلطان أبو هشيمة
477	2023/09/25	67776728	7189-6463	60			سلطان أبو هشيمة

مهندس اشراف الهيئة
م/محمود حسين

عن مكتب الاستشاري أ.د/ حسن مهدي
م/ احمد عزب

أ.د/ حسن مهدي



م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارتة	رسوم المرور والميزان (جنيه)	المحجر
478	2023/09/25	67776731	1282-7137	60			سلطان أبو هشيمة
479	2023/09/25	67776898	7214-9365	60			سلطان أبو هشيمة
480	2023/09/25	67776887	7138-5748	60			سلطان أبو هشيمة
481	2023/09/25	67776890	5589-5784	60			سلطان أبو هشيمة
482	2023/09/26	67776667	8691-3762	60			سلطان أبو هشيمة
483	2023/09/26	67776754	7189-6463	60			سلطان أبو هشيمة
484	2023/09/26	67776757	9186-4847	60			سلطان أبو هشيمة
485	2023/09/26	67776649	3692-4622	60			سلطان أبو هشيمة
486	2023/09/26	67776652	1692-7968	60			سلطان أبو هشيمة
487	2023/09/26	67776658	8691-3762	60			سلطان أبو هشيمة
488	2023/09/26	67776664	7285-3729	60			سلطان أبو هشيمة
489	2023/09/26	67776670	2867-8392	60			سلطان أبو هشيمة
490	2023/09/27	67776677	9253-3285	60			سلطان أبو هشيمة
491	2023/09/27	67776680	8691-3762	60			سلطان أبو هشيمة
492	2023/09/27	67776760	6158-8357	60			سلطان أبو هشيمة
493	2023/09/27	67776763	1692-7968	60			سلطان أبو هشيمة
494	2023/09/27	67776683	7916-7848	60			سلطان أبو هشيمة
495	2023/09/27	67776686	7139-8423	60			سلطان أبو هشيمة
496	2023/09/27	67776689	6397-4727	60			سلطان أبو هشيمة
497	2023/09/27	67776692	2867-8392	60			سلطان أبو هشيمة
498	2023-09-27	6754657	2642-9127	60			سلطان أبو هشيمة
499	2023-09-27	13196727	1936-1785	60			سلطان أبو هشيمة
500	2023-09-27	22419638	5312-5341	60			سلطان أبو هشيمة
501	2023-09-27	22419798	3698-1853	60			سلطان أبو هشيمة
502	2023-09-27	22417644	7894-7416	60			سلطان أبو هشيمة
503	2023/09/28	67776766	8739-9749	60			سلطان أبو هشيمة
504	2023/09/28	67776769	8576-9695	60			سلطان أبو هشيمة
505	2023/09/28	67776695	6574-8739	60			سلطان أبو هشيمة
506	2023/09/28	67776698	2365-2381	60			سلطان أبو هشيمة
507	2023/09/28	67776701	15062-4263	60			سلطان أبو هشيمة
508	2023/09/28	67776704	9258-3285	60			سلطان أبو هشيمة
509	2023/09/28	67776707	5837	20			سلطان أبو هشيمة
510	2023/09/28	67776929	1428-7148	60			سلطان أبو هشيمة
511	2023/09/28	67776926	1482-2533	60			سلطان أبو هشيمة
512	2023-09-28	16556218	6254-4221	60			سلطان أبو هشيمة
513	2023-09-29	16558594	1428-5631	60			سلطان أبو هشيمة
514	2023/09/30	67776922	7182-5748	60			سلطان أبو هشيمة
515	2023/09/30	67776919	5784-5589	60			سلطان أبو هشيمة
516	2023/09/30	67776916	7138-5748	60			سلطان أبو هشيمة
517	2023/09/30	67776913	5784-5589	60			سلطان أبو هشيمة
518	2023/09/30	67776910	1679-8291	60			سلطان أبو هشيمة
519	2023/09/30	67776907	7138-5748	60			سلطان أبو هشيمة
520	2023/09/30	67776904	7138-5748	60			سلطان أبو هشيمة
521	2023-09-30	16558532	8341-9157	60			سلطان أبو هشيمة
522	2023-09-30	16558599	4791	20			سلطان أبو هشيمة
523	2023/10/01	67776748	1282-7137	60			سلطان أبو هشيمة
524	2023/10/01	67776751	7214-9365	60			سلطان أبو هشيمة
525	2023/10/01	67776745	3692-4622	60			سلطان أبو هشيمة
526	2023/10/01	67776742	1692-7968	60			سلطان أبو هشيمة
527	2023/10/02	67776739	7285-3729	60			سلطان أبو هشيمة
528	2023/10/02	67776736	2867-8392	60			سلطان أبو هشيمة
529	2023/10/02	67776733	9253-3285	60			سلطان أبو هشيمة
530	2023/10/02	67776947	8691-3762	60			سلطان أبو هشيمة

مهندس اشراف الهيئة
م/محمود حسين

عن مكتب الاستشاري أ.د/ حسن مهدي
م/ احمد عزب

أ.د/ حسن مهدي



م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارتة	رسوم المرور والميزان (جنيه)	المحجر
531	2023/10/03	67777086	7916-7848	60			سلطان أبو هشيمة
532	2023/10/03	67777083	7139-8423	60			سلطان أبو هشيمة
533	2023/10/03	67777080	6397-4727	60			سلطان أبو هشيمة
534	2023/10/03	67777098	2867-8392	60			سلطان أبو هشيمة
535	2023-10-03	16556651	1572-3756	60			سلطان أبو هشيمة
536	2023/10/04	67777077	6574-8739	60			سلطان أبو هشيمة
537	2023/10/04	67777074	9253-3285	60			سلطان أبو هشيمة
538	2023/10/04	67777071	2365-2381	60			سلطان أبو هشيمة
539	2023/10/04	67777068	15062-4263	60			سلطان أبو هشيمة
540	2023/10/05	67776945	6156-8357	60			سلطان أبو هشيمة
541	2023/10/05	67776715	1282-7137	60			سلطان أبو هشيمة
542	2023/10/05	67776691	4622-3692	60			سلطان أبو هشيمة
543	2023/10/05	67776694	9365-7214	60			سلطان أبو هشيمة
544	2023-10-06	24602544	5619-9123	60			سلطان أبو هشيمة
545	2023-10-06	20440321	1842-8348	60			سلطان أبو هشيمة
546	2023-10-06	5886304	2348-3898	60			سلطان أبو هشيمة
547	2023-10-06	16558666	8341	20			سلطان أبو هشيمة
548	2023/10/07	67776697	7137-1282	60			سلطان أبو هشيمة
549	2023/10/07	67776700	6463-7189	60			سلطان أبو هشيمة
550	2023/10/07	67776703	4847-9186	60			سلطان أبو هشيمة
551	2023/10/07	67776706	8357-6158	60			سلطان أبو هشيمة
552	2023-10-07	16558688	5923	20			سلطان أبو هشيمة
553	2023-10-07	20440210	3248-5177	60			سلطان أبو هشيمة
554	2023-10-07	22416923	9154-3267	60			سلطان أبو هشيمة
555	2023/10/08	67776580	7968-1692	60			سلطان أبو هشيمة
556	2023/10/08	67776583	9749-8739	60			سلطان أبو هشيمة
557	2023/10/08	67776897	32285-9253	60			سلطان أبو هشيمة
558	2023/10/08	67776648	8739-6574	60			سلطان أبو هشيمة
559	2023/10/08	67776651	8392-2867	60			سلطان أبو هشيمة
560	2023-10-08	22418430	2139-7163	60			سلطان أبو هشيمة
561	2023-10-08	22416925	3928-6417	60			سلطان أبو هشيمة
562	2023-10-08	22416916	8614-7142	60			سلطان أبو هشيمة
563	2023-10-08	22418423	6438-8465	60			سلطان أبو هشيمة
564	2023-10-08	22418602	4378-4965	60			سلطان أبو هشيمة
565	2023-10-08	6751810	7163-1859	60			سلطان أبو هشيمة
566	2023/10/09	67776657	4727-6397	60			سلطان أبو هشيمة
567	2023/10/09	67776663	8423-7139	60			سلطان أبو هشيمة
568	2023/10/09	67776666	7848-7916	60			سلطان أبو هشيمة
569	2023/10/09	67776669	3762-8691	60			سلطان أبو هشيمة
570	2023-10-09	2895288	3798-2348	60			سلطان أبو هشيمة
571	2023-10-09	22417283	7238-5824	60			سلطان أبو هشيمة
572	2023-10-09	22416921	5341-5312	60			سلطان أبو هشيمة
573	2023-10-09	22416920	1687-9271	60			سلطان أبو هشيمة
574	2023/10/10	67776884	6953-5392	60			سلطان أبو هشيمة
575	2023/10/10	67777017	3729-7258	60			سلطان أبو هشيمة
576	2023/10/10	67776682	3729-7285	60			سلطان أبو هشيمة
577	2023/10/10	67776803	3285-9253	60			سلطان أبو هشيمة

مهندس اشراف الهيئة
م/محمود حسين

عن مكتب الاستشاري أ.د/ حسن مهدي
م/ احمد عزب

أ.د. حسن مهدي



م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارثة	رسوم المرور والميزان (جنيه)	المحجر
578	2023-10-10	22416928	7921-5216	60			سلطان أبوهشيمة
579	2023/10/11	67776815	2381-2365	60			سلطان أبوهشيمة
580	2023/10/11	67776886	5394-7563	60			سلطان أبوهشيمة
581	2023/10/11	67777065	7137-1282	60			سلطان أبوهشيمة
582	2023/10/11	67777059	4123-1256	60			سلطان أبوهشيمة
583	2023-10-11	8424540	9673-5428	60			سلطان أبوهشيمة
584	2023-10-11	22416810	9362-6315	60			سلطان أبوهشيمة
585	2023-10-11	22419185	1658-6287	60			سلطان أبوهشيمة
586	2023/10/12	67777053	3729-7285	60			سلطان أبوهشيمة
587	2023/10/12	67777047	8919-5736	60			سلطان أبوهشيمة
588	2023/10/12	67777041	8231-9258	60			سلطان أبوهشيمة
589	2023/10/12	67776710	447-8517	60			سلطان أبوهشيمة
590	2023-10-12	6751195	6482-6581	60			سلطان أبوهشيمة
591	2023-10-12	22417553	5973-7489	60			سلطان أبوهشيمة
592	2023-10-12	24602629	6287-1658	60			سلطان أبوهشيمة
593	2023-10-12	22419204	1658-6287	60			سلطان أبوهشيمة
594	2023-10-12	8424160	5198-6814	60			سلطان أبوهشيمة
595	2023-10-12	22419859	5973-7489	60			سلطان أبوهشيمة
596	2023/10/13	67776501	9695-8576	60			سلطان أبوهشيمة
597	2023/10/13	67776513	8553-4713	60			سلطان أبوهشيمة
598	2023/10/13	67776510	5695-2864	60			سلطان أبوهشيمة
599	2023/10/13	67776504	2365-1729	60			سلطان أبوهشيمة
600	2023-10-13	22417539	5973-7489	60			سلطان أبوهشيمة
601	2023-10-13	2895442	2348-3798	60			سلطان أبوهشيمة
602	2023/10/14	67777075	2983-4312	60			سلطان أبوهشيمة
603	2023/10/14	67777069	1867-3657	60			سلطان أبوهشيمة
604	2023/10/14	67776892	3729-7285	60			سلطان أبوهشيمة
605	2023/10/14	67776857	9886-7524	60			سلطان أبوهشيمة
606	2023-10-14	13196978	5923	20			سلطان أبوهشيمة
607	2023-10-14	20439865	9752-1648	60			سلطان أبوهشيمة
608	2023/10/15	67776769	7172-44852	60			سلطان أبوهشيمة
609	2023/10/15	67776882	8553-4713	60			سلطان أبوهشيمة
610	2023/10/15	67776776	3762-8691	60			سلطان أبوهشيمة
611	2023/10/15	67776842	4622-3692	60			سلطان أبوهشيمة
612	2023-10-15	8425835	9173-7135	60			سلطان أبوهشيمة
613	2023/10/16	67776785	7137-1282	60			سلطان أبوهشيمة
614	2023/10/16	67776773	4847-9186	60			سلطان أبوهشيمة
615	2023/10/16	67776598	7968-1692	60			سلطان أبوهشيمة
616	2023/10/16	67776604	3285-9253	60			سلطان أبوهشيمة
617	2023-10-16	8425890	5428-9673	60			سلطان أبوهشيمة
618	2023/10/17	67776788	8392-2867	60			سلطان أبوهشيمة
619	2023/10/17	67776794	8423-7139	60			سلطان أبوهشيمة
620	2023/10/17	67776800	3762-8691	60			سلطان أبوهشيمة
621	2023/10/17	67777023	2983-4312	60			سلطان أبوهشيمة

مهندس اشراف الهيئة
م/محمود حسين

عن مكتب الاستشاري أ.د/ حسن مهدي

م/احمد عزب
أحمد عزب



م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارتة	رسوم المرور والميزان (جنيه)	المحجر
622	2023/10/18	67776676	3285-9253	60			سلطان أبو هشيمة
623	2023/10/18	67776610	2381-2365	60			سلطان أبو هشيمة
624	2023/10/18	67776809	3729-7285	60			سلطان أبو هشيمة
625	2023/10/18	67777008	7138-5748	60			سلطان أبو هشيمة
626	2023-10-18	13196833	5362-4927	60			سلطان أبو هشيمة
627	2023-10-18	13196851	5879-6437	60			سلطان أبو هشيمة
628	2023/10/19	67776889	4519-8289	60			سلطان أبو هشيمة
629	2023/10/19	67777062	9658-8274	60			سلطان أبو هشيمة
630	2023/10/19	67777056	3729-7285	60			سلطان أبو هشيمة
631	2023/10/19	67777050	8374-3714	60			سلطان أبو هشيمة
632	2023-10-19	6751184	9272-2179	60			سلطان أبو هشيمة
633	2023-10-20	16556761	9362-6315	60			سلطان أبو هشيمة
634	2023/10/21	67777044	6374-9683	60			سلطان أبو هشيمة
635	2023/10/21	67777038	8413-6983	60			سلطان أبو هشيمة
636	2023/10/21	67776713	5464-3972	60			سلطان أبو هشيمة
637	2023/10/21	67776901	3729-7285	60			سلطان أبو هشيمة
638	2023-10-21	13196871	1428-5631	60			سلطان أبو هشيمة
639	2023-10-21	13196875	4613-1854	60			سلطان أبو هشيمة
640	2023-10-21	16556781	8724-9328	60			سلطان أبو هشيمة
641	2023/10/22	67776507	9892-7561	60			سلطان أبو هشيمة
642	2023/10/22	67776519	5993-7534	60			سلطان أبو هشيمة
643	2023/10/22	67776836	1684-4638	60			سلطان أبو هشيمة
644	2023/10/22	67776845	4622-3692	60			سلطان أبو هشيمة
645	2023-10-22	20441491	3267-4921	60			سلطان أبو هشيمة
646	2023/10/23	67776851	3564-8316	60			سلطان أبو هشيمة
647	2023/10/23	67776854	8919-5736	60			سلطان أبو هشيمة
648	2023/10/23	67776863	8714-5371	60			سلطان أبو هشيمة
649	2023/10/23	67776869	8231-9258	60			سلطان أبو هشيمة
650	2023-10-23	16556744	8629-9426	60			سلطان أبو هشيمة
651	2023-10-23	16555634	7524-4179	60			سلطان أبو هشيمة
652	2023-10-23	20441482	8721-9752	60			سلطان أبو هشيمة
653	2023-10-23	22418486	3127-7435	60			سلطان أبو هشيمة
654	2023-10-23	22418246	7519-5316	60			سلطان أبو هشيمة
655	2023-10-23	22419808	1658-6287	60			سلطان أبو هشيمة
656	2023/10/24	67776896	7419-8627	60			سلطان أبو هشيمة
657	2023/10/24	67776779	7968-1692	60			سلطان أبو هشيمة
658	2023/10/24	67776782	9365-7214	60			سلطان أبو هشيمة
659	2023/10/24	67776646	6463-7189	60			سلطان أبو هشيمة
660	2023-10-24	16555729	4937-6983	60			سلطان أبو هشيمة
661	2023-10-24	16555839	6398-3581	60			سلطان أبو هشيمة
662	2023/10/25	67776592	8357-6158	60			سلطان أبو هشيمة
663	2023/10/25	67776601	9749-8739	60			سلطان أبو هشيمة
664	2023/10/25	67776607	8739-6574	60			سلطان أبو هشيمة
665	2023/10/25	67776791	4727-6397	60			سلطان أبو هشيمة

مهندس اشراف الهيئة
م/محمود حسين

عن مكتب الاستشاري أ.د/ حسن مهدي
م/ احمد عزب

مهندس الاستشارة
م/ محمد خير محمد
أبو عجيبة
بني مزار - منفوط
ب. ص. 119-161-603

م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارثة	رسوم المرور والميزان (جنيه)	المحجر
666	2023/10/25	67776797	7848-7916	60			سلطان أبوهشيمة
667	2023-10-26	13195286	5362-4927	60			سلطان أبوهشيمة
668	2023-10-27	13197032	1428-5631	60			سلطان أبوهشيمة
669	2023-10-27	13195865	5362-4927	60			سلطان أبوهشيمة
670	2023-10-29	13197056	5879-6437	60			سلطان أبوهشيمة
671	2023-10-30	13197067	1428-5631	60			سلطان أبوهشيمة
672	2023-10-31	21279874	4937-6983	60			سلطان أبوهشيمة
673	2023-11-02	16555580	1983-4937	60			سلطان أبوهشيمة
674	2023-11-02	16555575	1943-1624	60			سلطان أبوهشيمة
675	2023-11-02	18997337	3412-7382	60			سلطان أبوهشيمة
676	2023-11-02	13197087	87762-5946	60			سلطان أبوهشيمة
677	2023-11-03	21278857	7142-8614	60			سلطان أبوهشيمة
678	2023-11-03	21278853	6439-1829	60			سلطان أبوهشيمة
679	2023-11-03	16558687	2596	20			سلطان أبوهشيمة
680	2023-11-03	5885794	3798-2348	60			سلطان أبوهشيمة
681	2023-11-04	21278907	2748-2385	60			سلطان أبوهشيمة
682	2023-11-04	21278902	1826-2316	60			سلطان أبوهشيمة
683	2023-11-04	21278867	5746-7912	60			سلطان أبوهشيمة
684	2023-11-04	21278891	8945-9518	60			سلطان أبوهشيمة
685	2023-11-04	21278898	1572-3756	60			سلطان أبوهشيمة
686	2023-11-05	21278936	7142-8614	60			سلطان أبوهشيمة
687	2023-11-05	21278962	7142-8614	60			سلطان أبوهشيمة
688	2023-11-05	21278926	9362-6315	60			سلطان أبوهشيمة
689	2023-11-05	21278972	5268-7391	60			سلطان أبوهشيمة
690	2023-11-05	21278952	5837-1754	60			سلطان أبوهشيمة
691	2023-11-05	21278958	2479-8465	60			سلطان أبوهشيمة
692	2023-11-05	16557303	8762-5946	60			سلطان أبوهشيمة
693	2023-11-05	21278951	3845-8359	60			سلطان أبوهشيمة
694	2023-11-05	21278943	7283-2643	60			سلطان أبوهشيمة
695	2023-11-06	21278948	2564-9637	60			سلطان أبوهشيمة
696	2023-11-06	21279209	3845-8359	60			سلطان أبوهشيمة
697	2023-11-06	21278993	7142-8614	60			سلطان أبوهشيمة
698	2023-11-06	21278995	3789-6493	60			سلطان أبوهشيمة
699	2023-11-06	21278989	7163-1859	60			سلطان أبوهشيمة
700	2023-11-07	21279381	7142-8614	60			سلطان أبوهشيمة
701	2023-11-08	16555545	2195-4628	60			سلطان أبوهشيمة
702	2023-11-08	21279376	7142-8614	60			سلطان أبوهشيمة
703	2023-11-09	21279034	5619-736	60			سلطان أبوهشيمة
704	2023-11-10	21279055	7142-8614	60			سلطان أبوهشيمة
705	2023-11-10	18997327	1359-2194	60			سلطان أبوهشيمة
706	2023-11-10	22419629	7139-1432	60			سلطان أبوهشيمة
707	2023-11-10	6751101	5694-2467	60			سلطان أبوهشيمة
708	2023-11-11	21279076	8614-7142	60			سلطان أبوهشيمة
709	2023-11-11	22417518	3698-1853	60			سلطان أبوهشيمة

مهندس اشرف الهيئة
م/محمود حسين

عن مكتب الاستشاري أ.د/ حسن مهدي
م/ احمد عزب

9/11



م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارثة	رسوم المرور والميزان (جنيه)	المحجر
710	2023-11-12	21279093	7831-8236	60			سلطان أبو هشيمة
711	2023-11-12	22418945	1824-2952	60			سلطان أبو هشيمة
712	2023-11-12	21279292	8614-7145	60			سلطان أبو هشيمة
713	2023-11-13	21279277	7142-8614	60			سلطان أبو هشيمة
714	2023-11-14	5440981	8193-8346	60			سلطان أبو هشيمة
715	2023-11-14	21279135	7142-8614	60			سلطان أبو هشيمة
716	2023-11-15	21279177	6832-1592	60			سلطان أبو هشيمة
717	2023-11-15	21279759	5312-5341	60			سلطان أبو هشيمة
718	2023-11-16	18997617	6432-3512	60			سلطان أبو هشيمة
719	2023-11-16	18997646	3971-8547	60			سلطان أبو هشيمة
720	2023-11-17	18997688	4726-9417	60			سلطان أبو هشيمة
721	2023-11-17	22419743	7941-2386	60			سلطان أبو هشيمة
722	2023-11-17	22419841	4381	20			سلطان أبو هشيمة
723	2023-11-17	24602597	3529-9417	60			سلطان أبو هشيمة
724	2023-11-17	21279272	6439-1829	60			سلطان أبو هشيمة
725	2023-11-18	22419680	1265-6381	60			سلطان أبو هشيمة
726	2023-11-19	18997268	2134-7439	60			سلطان أبو هشيمة
727	2023-11-19	18997267	2195-4628	60			سلطان أبو هشيمة
728	2023-11-19	18997235	7831-8276	60			سلطان أبو هشيمة
729	2023-11-19	22418320	5317-8651	60			سلطان أبو هشيمة
730	2023-11-19	22419689	2467-7389	60			سلطان أبو هشيمة
731	2023-11-19	24602518	5619-9123	60			سلطان أبو هشيمة
732	2023-11-19	22418976	4965-4378	60			سلطان أبو هشيمة
733	2023-11-20	18997288	8217-8729	60			سلطان أبو هشيمة
734	2023-11-20	18997402	7261	20			سلطان أبو هشيمة
735	2023-11-20	18997412	1654-1854	60			سلطان أبو هشيمة
736	2023-11-21	18997300	6381-1265	60			سلطان أبو هشيمة
737	2023-11-21	18997435	9413-6519	60			سلطان أبو هشيمة
738	2023-11-21	5885331	2348-2134	60			سلطان أبو هشيمة
739	2023-11-21	18997437	9479-2983	60			سلطان أبو هشيمة
740	2023-11-22	18997508	9752-8721	60			سلطان أبو هشيمة
741	2023-11-23	18997558	5619-736	60			سلطان أبو هشيمة
742	2023-11-23	22419785	4628-2195	60			سلطان أبو هشيمة
743	2023-11-23	24599404	9645-8169	60			سلطان أبو هشيمة
744	2023-11-23	22418405	3412-7382	60			سلطان أبو هشيمة
745	2023-11-23	5442770	4613-4971	60			سلطان أبو هشيمة
746	2023-11-24	22419775	7482-5619	60			سلطان أبو هشيمة
747	2023-11-24	13197064	2596	20			سلطان أبو هشيمة
748	2023-11-24	22418482	5854	20			سلطان أبو هشيمة
749	2023-11-24	22419151	3671-8926	60			سلطان أبو هشيمة
750	2023-11-24	22418490	5391-8953	60			سلطان أبو هشيمة
751	2023-11-25	24602498	2789-9254	60			سلطان أبو هشيمة
752	2023-11-25	24601403	7462-2579	60			سلطان أبو هشيمة
753	2023-11-25	18997581	9674-8548	60			سلطان أبو هشيمة

مهندس اشراف الهيئة
م/محمود حسين

عن مكتب الاستشاري أ.د/ حسن مهدي
م/ احمد عزب

أحمد عزب



م	التاريخ	رقم اليون	رقم العربية	الكمية	رقم الكارتة	رسوم المرور والميزان (جنيه)	المحجر
754	2023-11-26	22418463	4257-4235	60			سلطان أبو هشيمة
755	2023-11-26	24602511	3267-9154	60			سلطان أبو هشيمة
756	2023-11-26	22418464	8926-3671	60			سلطان أبو هشيمة
757	2023-11-27	22419824	9427-5943	60			سلطان أبو هشيمة
758	2023-11-27	22419827	4628-2195	60			سلطان أبو هشيمة
759	2023-11-27	22418217	8651-5317	60			سلطان أبو هشيمة
760	2023-11-27	18997025	8567-2639	60			سلطان أبو هشيمة
761	2023-11-28	22418955	8713	20			سلطان أبو هشيمة
762	2023-11-28	18997064	5216-7921	60			سلطان أبو هشيمة
763	2023-11-29	8354095	5352-7693	60			سلطان أبو هشيمة
764	2023-11-29	18996808	7958-1478	60			سلطان أبو هشيمة
765	2023-11-29	18997092	9165-4768	60			سلطان أبو هشيمة
766	2023-11-30	18997715	3172-7348	60			سلطان أبو هشيمة
767	2023-11-30	18997718	2596	20			سلطان أبو هشيمة
768	2023-11-30	18997716	8612-5412	60			سلطان أبو هشيمة
769	2023-12-01	24602577	1982-2786	60			سلطان أبو هشيمة
770	2023-12-01	24602522	7391-5268	60			سلطان أبو هشيمة
771	2023-12-01	22419657	7462-2579	60			سلطان أبو هشيمة
772	2023-12-01	22419832	3412-7382	60			سلطان أبو هشيمة
773	2023-12-01	2895129	2348-3798	60			سلطان أبو هشيمة
774	2023-12-01	8676285	6853-9672	60			سلطان أبو هشيمة
775	2023-12-02	22416905	9256-9264	60			سلطان أبو هشيمة
776	2023-12-02	22419670	9869-1736	60			سلطان أبو هشيمة
777	2023-12-02	24602521	1393-7415	60			سلطان أبو هشيمة
778	2023-12-02	22419833	7482-5619	60			سلطان أبو هشيمة
779	2023-12-02	22419232	3127-8435	60			سلطان أبو هشيمة
780	2023-12-02	22416917	6713-4895	60			سلطان أبو هشيمة
781	2023-12-02	18996893	5359-3845	60			سلطان أبو هشيمة
782	2023-12-02	18996887	7163-1859	60			سلطان أبو هشيمة
783	2023-12-02	18997704	7912-3259	60			سلطان أبو هشيمة
784	2023-12-02	18996719	7214-6485	60			سلطان أبو هشيمة
785	2023-12-02	18996708	9163-1928	60			سلطان أبو هشيمة
786	2023-12-03	18996738	1687-9271	60			سلطان أبو هشيمة
787	2023-12-03	5442740	8346-8793	60			سلطان أبو هشيمة
788	2023-12-03	18996755	2983-9479	60			سلطان أبو هشيمة
789	2023-12-03	22418407	8651-5317	60			سلطان أبو هشيمة
790	2023-12-03	24599427	1687-9271	60			سلطان أبو هشيمة
791	2023-12-03	6751832	3127-8435	60			سلطان أبو هشيمة
792	2023-12-03	22417161	1658-6287	60			سلطان أبو هشيمة
793	2023-12-03	633222	9749-4998	60			سلطان أبو هشيمة
794	2023-12-03	8676987	9672-6853	60			سلطان أبو هشيمة
795	2023-12-03	22416929	1726-1432	60			سلطان أبو هشيمة
796	2023-12-03	18996753	2635-7584	60			سلطان أبو هشيمة
797	2023-12-03	18996889	7518-9648	60			سلطان أبو هشيمة

م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارثة	رسوم المرور والميزان (جنه)	المحجر
798	2023-12-04	18996796	9271-1687	60			سلطان أبو هشيمة
799	2023-12-04	18996766	7381-7348	60			سلطان أبو هشيمة
800	2023-12-04	20440272	1658-6287	60			سلطان أبو هشيمة
801	2023-12-04	22417242	1658-6287	60			سلطان أبو هشيمة
802	2023-12-04	22417286	8945-5398	60			سلطان أبو هشيمة
803	2023-12-04	22416932	7894-7516	60			سلطان أبو هشيمة
804	2023-12-04	22417597	6438-8465	60			سلطان أبو هشيمة
805	2023-12-04	5441116	8132-6983	60			سلطان أبو هشيمة
806	2023-12-04	21277906	5943-9427	60			سلطان أبو هشيمة
807	2023-12-04	18996785	9154-3267	60			سلطان أبو هشيمة
808	2023-12-04	18996771	1265-6381	60			سلطان أبو هشيمة
809	2023-12-04	18996797	7489-5973	60			سلطان أبو هشيمة
810	2023-12-04	18996776	5973-7489	60			سلطان أبو هشيمة
811	2023-12-04	21277907	7942-1564	60			سلطان أبو هشيمة
812	2023-12-04	18996780	2479-8465	60			سلطان أبو هشيمة
813	2023-12-04	18996791	6713-4895	60			سلطان أبو هشيمة
814	2023-12-04	18996768	9362-6331	60			سلطان أبو هشيمة
815	2023-12-04	18996798	5428-9673	60			سلطان أبو هشيمة
816	2023-12-04	18996800	7142-8614	60			سلطان أبو هشيمة
817	2023-12-05	21277914	7698-6912	60			سلطان أبو هشيمة
818	2023-12-05	24602496	5782	20			سلطان أبو هشيمة
819	2023-12-05	22418410	7413-6925	60			سلطان أبو هشيمة
820	2023-12-05	24602434	4378-4965	60			سلطان أبو هشيمة
821	2023-12-05	22417600	5312-5341	60			سلطان أبو هشيمة
822	2023-12-05	18998461	5973-7489	60			سلطان أبو هشيمة
823	2023-12-05	18996769	9426-8629	60			سلطان أبو هشيمة
824	2023-12-05	18996763	6439-5724	60			سلطان أبو هشيمة
825	2023-12-05	21277928	3652-4791	60			سلطان أبو هشيمة
826	2023-12-05	21277911	3257-2756	60			سلطان أبو هشيمة
827	2023-12-05	21277920	9637-2564	60			سلطان أبو هشيمة
828	2023-12-05	21277933	7942-1564	60			سلطان أبو هشيمة
829	2023-12-05	18996772	4791-3652	60			سلطان أبو هشيمة
830	2023-12-05	21277910	9865-7316	60			سلطان أبو هشيمة
831	2023-12-05	21278506	3127-7435	60			سلطان أبو هشيمة
832	2023-12-05	21277929	1265-6381	60			سلطان أبو هشيمة
833	2023-12-05	21277925	9154-3267	60			سلطان أبو هشيمة
834	2023-12-05	21277934	2479-8465	60			سلطان أبو هشيمة
835	2023-12-05	21277926	1859-7163	60			سلطان أبو هشيمة
836	2023-12-05	21277932	8614-7142	60			سلطان أبو هشيمة
837	2023-12-05	21278505	2983-9479	60			سلطان أبو هشيمة
838	2023-12-05	21277918	2983-9479	60			سلطان أبو هشيمة
839	2023-12-05	21278964	9634-4351	60			سلطان أبو هشيمة
840	2023-12-05	21277917	6832-1592	60			سلطان أبو هشيمة
841	2023-12-05	18997446	3698-1853	60			سلطان أبو هشيمة

مهندس اشراف الهيئة
م/محمود حسين

عن مكتب الاستشاري أ.د/ حسن مهدي
م/ احمد عزب

أ.د/ حسن مهدي



م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارتة	رسوم المرور والميزان (جنيه)	المحجر
842	2023-12-06	21277946	6439-5724	60			سلطان أبو هشيمة
843	2023-12-06	21277950	1678-9271	60			سلطان أبو هشيمة
844	2023-12-06	21277936	6713-4895	60			سلطان أبو هشيمة
845	2023-12-06	21277947	8945-5398	60			سلطان أبو هشيمة
846	2023-12-07	18996758	8437-3967	60			سلطان أبو هشيمة
847	2023-12-08	5441192	8132-6983	60			سلطان أبو هشيمة
848	2023-12-09	21278569	9163-1928	60			سلطان أبو هشيمة
849	2023-12-10	21278586	1823-6541	60			سلطان أبو هشيمة
850	2023-12-11	8423934	5216-7921	60			سلطان أبو هشيمة
851	2023-12-11	21279081	7896	20			سلطان أبو هشيمة
852	2023-12-12	21278216	4319-2935	60			سلطان أبو هشيمة
853	2023-12-12	5441353	2139-7167	60			سلطان أبو هشيمة
854	2023-12-12	18997766	6912-7698	60			سلطان أبو هشيمة
855	2023-12-12	18996862	9853-6942	60			سلطان أبو هشيمة
856	2023-12-13	21278236	8729-8217	60			سلطان أبو هشيمة
857	2023-12-14	21278343	9362-6315	60			سلطان أبو هشيمة
858	2023-12-14	21278363	1948-7653	60			سلطان أبو هشيمة
859	2023-12-16	21278127	9256-9264	60			سلطان أبو هشيمة
860	2023-12-17	21278403	1754-2761				سلطان أبو هشيمة
861	2023-12-18	22418033	7316-9865	60			سلطان أبو هشيمة
862	2023-12-18	21278468	1736-5869	60			سلطان أبو هشيمة
863	2023-12-18	22418020	6498-7839	60			سلطان أبو هشيمة
864	2023-12-18	22418036	7826-4157	60			سلطان أبو هشيمة
865	2023-12-18	22418014	9637-2564	60			سلطان أبو هشيمة
866	2023-12-18	22418016	2947-1529	60			سلطان أبو هشيمة
867	2023-12-19	22417832	6573-1843	60			سلطان أبو هشيمة
868	2023-12-19	22418059	9256-9264	60			سلطان أبو هشيمة
869	2023-12-19	22418022	9479-2983	60			سلطان أبو هشيمة
870	2023-12-19	22417805	3628-1269	60			سلطان أبو هشيمة
871	2023-12-19	22417810	9713-4895	60			سلطان أبو هشيمة
872	2023-12-19	22417817	3652-4791	60			سلطان أبو هشيمة
873	2023-12-19	22417821	2931-8975	60			سلطان أبو هشيمة
874	2023-12-19	22417822	9356-9183	60			سلطان أبو هشيمة
875	2023-12-19	22418055	1564-7945	60			سلطان أبو هشيمة
876	2023-12-20	22417854	3257-2756	60			سلطان أبو هشيمة
877	2023-12-20	22418081	7921-5216	60			سلطان أبو هشيمة
878	2023-12-21	22417712	2761-1754	60			سلطان أبو هشيمة
879	2023-12-22	22417891	1687-9271	60			سلطان أبو هشيمة
880	2023-12-22	22417723	8614-7142	60			سلطان أبو هشيمة
881	2023-12-23	22418119	7142-8614	60			سلطان أبو هشيمة
882	2023-12-24	22417979	4156-3286	60			سلطان أبو هشيمة
883	2023-12-24	22418147	8614-7142	60			سلطان أبو هشيمة
884	2023-12-25	22417958	6912-7698	60			سلطان أبو هشيمة
885	2023-12-25	22418163	246-9784	60			سلطان أبو هشيمة

مهندس إشراف الهيئة
م/محمود حسين

عن مكتب الاستشاري أ.د/ حسن مهدي
م/ احمد عزب

أحمد عزب



م	التاريخ	رقم اليون	رقم العربية	الكمية	رقم الكارتة	رسوم المرور والميزان (جنيه)	المحجر
886	2023-12-25	22418161	8614-7142	60			سلطان أبو هشيمة
887	2023-12-25	22417961	7142-8614	60			سلطان أبو هشيمة
888	2023-12-25	8677149	6853-9672	60			سلطان أبو هشيمة
889	2023-12-25	22418174	4157-7829	60			سلطان أبو هشيمة
890	2023-12-26	21278377	4768-9165	60			سلطان أبو هشيمة
891	2023-12-26	22417946	8764-6249	60			سلطان أبو هشيمة
892	2023-12-27	22417638	2947-1529	60			سلطان أبو هشيمة
893	2023-12-27	22417657	9183-9356	60			سلطان أبو هشيمة
894	2023-12-27	22417616	4157-7826	60			سلطان أبو هشيمة
895	2023-12-27	22417654	8614-7142	60			سلطان أبو هشيمة
896	2023-12-28	22417450	6417-3928	60			سلطان أبو هشيمة
897	2023-12-28	22417414	7413-6925	60			سلطان أبو هشيمة
898	2023-12-28	22417448	4157-7826	60			سلطان أبو هشيمة
899	2023-12-28	16556222	2176-9247	60			سلطان أبو هشيمة
900	2023-12-28	22417426	8614-7142	60			سلطان أبو هشيمة
901	2023-12-28	22417413	2579-1863	60			سلطان أبو هشيمة
902	2023-12-29	21279514	7942-1564	60			سلطان أبو هشيمة
903	2023-12-29	22417458	6925-7413	60			سلطان أبو هشيمة
904	2023-12-29	22417487	2931-8975	60			سلطان أبو هشيمة
905	2023-12-29	22417470	9417-3529	60			سلطان أبو هشيمة
906	2023-12-29	22417489	5341-5312	60			سلطان أبو هشيمة
907	2023-12-29	22417472	9734-9762	60			سلطان أبو هشيمة
908	2023-12-29	22417479	8614-7142	60			سلطان أبو هشيمة
909	2023-12-30	18997721	1754-5837	60			سلطان أبو هشيمة
910	2023-12-30	22417021	7413-6925	60			سلطان أبو هشيمة
911	2023-12-30	22417031	3512-6432	60			سلطان أبو هشيمة
912	2023-12-30	22417030	1534	20			سلطان أبو هشيمة
913	2023-12-30	22417038	8794-7516	60			سلطان أبو هشيمة
914	2023-12-30	22417035	4157-7826	60			سلطان أبو هشيمة
915	2023-12-30	22417034	4273	20			سلطان أبو هشيمة
916	2023-12-30	22417953	7142-8614	60			سلطان أبو هشيمة
917	2023-12-30	22417007	3516-1852	60			سلطان أبو هشيمة
918	2023-12-30	22417008	9274-2179	60			سلطان أبو هشيمة
919	2023-12-31	22417069	5472-6874	60			سلطان أبو هشيمة
920	2023-12-31	22417066	2596	20			سلطان أبو هشيمة
921	2023-12-31	22417091	1687-9271	60			سلطان أبو هشيمة
922	2023-12-31	22417094	1754-5837	60			سلطان أبو هشيمة
923	2023-12-31	22417070	1572-3756	60			سلطان أبو هشيمة
924	2023-12-31	22417949	5317-8651	60			سلطان أبو هشيمة
925	2023-12-31	22417077	7142-8614	60			سلطان أبو هشيمة
926	2023-12-31	22417202	8614-7142	60			سلطان أبو هشيمة
927	2023-12-31	22417080	4289-9241	60			سلطان أبو هشيمة
928	2023-12-31	22417046	1859-7163	60			سلطان أبو هشيمة
929	2023-12-31	22417019	9637-2564	60			سلطان أبو هشيمة

مهندس اشراف الهيئة
م/محمود حسين

عن مكتب الاستشاري أ.د/ حسن مهدي
م/ احمد عزب

أحمد عزب





عقد رقم (2023-2022-1229)						
م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارثة	رسوم المرور والميزان (جنيه)
930	2023-12-31	22417310	1658-6287	60		سلطان أبوهشيمة
931	2023-12-31	22417205	7238-5824	60		سلطان أبوهشيمة
932	2023-12-31	22417092	5619-736	60		سلطان أبوهشيمة
933	2023-12-31	22417358	7896	60		سلطان أبوهشيمة
934	2023-12-31	22417270	1363-7415	60		سلطان أبوهشيمة
935	2023-12-31	22417941	2819-6754	60		سلطان أبوهشيمة
936	2023-12-31	22417067	2756-3257	60		سلطان أبوهشيمة
937	2023-12-31	22417375	5398-8945	60		سلطان أبوهشيمة
938	2023-12-31	22417037	3652-4791	60		سلطان أبوهشيمة
939	2023-12-31	22417072	7214-1864	60		سلطان أبوهشيمة
940	2023-12-31	22417081	2195-2167	60		سلطان أبوهشيمة
941	2023-12-31	22417265	5128-9236	60		سلطان أبوهشيمة
942	2023-12-31	22417010	6731-4181	60		سلطان أبوهشيمة
	الإجمالي			55280		

7-13-18



	مشروع القطار الكهربائي السريع	 الهيئة العامة للغمرات مكتب أ.د/حسن مهدي للإستشارات الهندسية
	إستكمال إسناد أعمال الجسر الترابي والأعمال الصناعية بقطاعات مشروع إنشاء القطار الكهربائي السريع (أكتوبر-أبوسمبل)	
	تنفيذ شركة أبو عجيله للمقاولات العامة والتوريدات العمومية مستخلص (١) جارى	

الحصر الإجمالي لكميات القطاع حتى تاريخ ٢٠٢٤/٤/١

Station	Total Cut Area(m2)	Cum. Cut Vol(m3)	As Built vol.cut		
				CUT VOL(m3)	Total.Qty
200+876.01	580.84	0	cut	0	529753.21
200+880.00	586.05	2,325.62		2,325.62	
200+900.00	630.8	14,494.09		12,168.47	
200+920.00	667.79	27,479.99		12,985.90	
200+940.00	665.5	40,812.95		13,332.96	
200+960.00	635.92	53,827.17		13,014.23	
200+980.00	655.55	66,741.85		12,914.68	
201+000.00	650.46	79,801.90		13,060.05	
201+020.00	610.45	92,410.94		12,609.04	
201+040.00	622.17	104,737.11		12,326.16	
201+060.00	621.82	117,176.99		12,439.89	
201+080.00	624.05	129,635.71		12,458.71	
201+100.00	616.97	142,045.96		12,410.26	
201+120.00	615.77	154,373.38		12,327.42	
201+140.00	617.82	166,709.30		12,335.92	
201+160.00	623.52	179,122.78		12,413.48	
201+180.00	614.79	191,505.94		12,383.16	
201+200.00	633.1	203,984.90		12,478.96	
201+220.00	599.85	216,314.49		12,329.59	
201+240.00	499.13	227,304.33		10,989.84	
201+260.00	445.74	236,753.04		9,448.72	
201+280.00	450.78	245,718.30		8,965.26	
201+285.93	449.56	248,387.80		2669.5	
201+300.00	460.6	254,790.75		6,402.95	
201+320.00	478.13	264,178.05		9,387.30	
201+340.00	476.54	273,724.79		9,546.74	
201+360.00	473.02	283,220.47		9,495.68	
201+380.00	467.7	292,627.66		9,407.19	
201+400.00	480.96	302,114.23		9,486.57	
201+420.00	473.9	311,662.81		9,548.58	
201+440.00	516.53	321,567.07		9,904.26	
201+460.00	579.3	332,525.35		10,958.28	
201+465.93	585.45	335,978.82		3453.48	
201+480.00	583.85	344,204.87		8,226.04	
201+500.00	576.27	355,806.07		11,601.20	
201+520.00	563.45	367,203.19		11,397.13	
201+540.00	521.62	378,053.86		10,850.67	
201+560.00	446.24	387,732.49		9,678.63	
201+580.00	417	396,364.88		8,632.38	
201+600.00	431.82	404,853.04		8,488.16	
201+620.00	454.9	413,720.28		8,867.24	
201+640.00	461.11	422,880.41		9,160.14	

عن الاستشاري أ.د حسن مهدي

م/ عبد الحميد علاء الدين م/ احمد عزب

عن استشاري المساحة

م/ محمد عبدالرحمن م/ محمد

عن الشركة

م/ محمد حامد أبو عجيله م/ محمد

١٤





مكتب أ.د. حسن مهدي
للاستشارات الهندسية

حضر كمية الاحلال في السفو ابتداء من شهر سبتمبر ٢٠٢٣

CUT

عن الاستشاري أ.د. حسين مهدي

عن استشاري المصاحفة

عن الشركة

م/ احمد عزب م/ محمود غريب

م/محمد عبدالرحمن

م / احمد ختيخ

[Handwritten signature]

11/11/11

10780
ABUAGLA
609-161-199

	مشروع القطار الكهربائي السريع	 مكتب المهندسين للإستشارات الهندسية
	إستكمال أعمال الجسر الترابي لمسار القطار الكهربائي السريع الخط الثاني (الفيوم / بني سويف - أيا سمبل) (مرحلة الجسور والأساس والأسياس) القطاع الثاني (بني مزار / منقلاوط)	
	تنفيذ شركة أبو عجيبة للمقاولات العامة والتوريدات العمومية كميات حتي مستخلص جاري (١) جاري لعقد رقم (٢٠٢٥/٢٠٢٤/٢٠٩) بتاريخ 2024/4/1 ASBUILT	

بند رقم (١-٣) : أعمال تحميل وتوريد ونقل أتربة مطابقة للمواصفات وتشغيلها باستخدام آلات التسوية بسمك لا يزيد عن ٥٠ سم حتى منسوب (-2 متر) أسفل منسوب الفرمة و بسمك لا يزيد عن ٢٥ سم اعلي من منسوب (-2 متر) من منسوب الفرمة لإستكمال المنسوب التصميمي الخ

Station	Total Fill Area(m2)	Cum. Fill Vol(m3)	As Built vol.Fill			
			Fill VOL(m3)	Total.Qty	Fill VOL(m3) ابتداء من ٢٠٢٤/٢/٢٢	اجمالي الكميات ابتداء من ٢٠٢٤/٢/٢٢
201+920.00	202.61	2026.07	2026.07	100122.28	582.22	9669.67
201+940.00	227.66	6,328.78	4,302.71		1,170.55	
201+960.00	248.2	11,087.40	4,758.61		1,162.28	
201+980.00	274.47	16,314.06	5,226.57		1,140.36	
202+000.00	262.01	21,578.88	5,364.82		1,142.87	
202+020.00	243.79	26,736.89	5,058.01		1,149.44	
202+040.00	194.01	31,114.85	4,377.95		1,134.32	
202+060.00	362.48	36,679.73	5,564.88		561.35	
202+080.00	341.72	43,721.80	7,042.07		0.00	
202+100.00	314.56	50,284.61	6,562.81		0.00	
202+120.00	301.56	56,445.77	6,161.16		0.00	
202+140.00	0	59,461.36	3,015.59		0.00	
202+160.00	0	59,461.36	0.00		0.00	
202+180.00	0	59,461.36	0.00		0.00	
202+200.00	0	59,461.36	0.00		0.00	
202+220.00	317.97	62,641.01	3,179.66		162.54	
202+240.00	312.67	68,947.36	6,306.35		325.06	
202+260.00	320.6	75,280.03	6,332.66		321.62	
202+280.00	330.13	81,787.33	6,507.30		322.02	
202+300.00	335.88	88,447.44	6,660.11		328.98	
202+320.00	141.42	93,220.38	4,772.95		166.06	
202+340.00	132.47	95,959.23	2,738.85		0.00	
202+360.00	116.74	98,451.35	2492.11		0	
202+376.01	91.94	100,122.29	1,670.94		0.00	

عن الإستشاري أد حسن مهدي
مدير المشروع
م / محمود هريش
م / أحمد عزب

المساحة
م/ محمد عبدالرحمن
١٨/٤

عن الشركة
م / احمد فتح
م / أحمد
١٢
١٩٧٨
ABUAGLA
ب ض ١٠٩ - ١٠٩ - ٦٠٩

	مشروع القطار الكهربائي السريع إستكمال أعمال الجسر الترابي لمسار القطار الكهربائي السريع الخط الثاني (الفيوم / بني سويف - أبو سمبل) (مرحلة الجسور والتأسيس والأساس) القطاع الثاني (بني مزار / متفلوط) تنفيذ شركة أبو عجيبة للمقاولات العامة والتوريدات العمومية حصر اجمالي لكميات الردم	الهيئة القومية للإتفاق مكتب أ.د/حسن مهدي للإستشارات الهندسية
--	--	--

بند رقم (١-٣) : أعمال تحميل وتوريد ونقل أتربة مطابقة للمواصفات وتشغيلها باستخدام آلات التسوية بسمك لا يزيد عن ٥٠ سم حتى منسوب (-2 متر) أسفل منسوب القرمه و بسمك لايزيد عن ٢٥سم اعلي من منسوب (-2٠ متر) من منسوب القرمه لاستكمال المنسوب التصميميالخ

Station	Total Fill Area(m2)	Cum. Fill Vol(m3)	Fill	As Built vol.Fill	Total.Qty
				Fill VOL(m3)	
201+920.00	202.61	2026.07	Fill	2026.07	100122.28
201+940.00	227.66	6,328.78		4,302.71	
201+960.00	248.2	11,087.40		4,758.61	
201+980.00	274.47	16,314.06		5,226.67	
202+000.00	262.01	21,678.88		5,364.82	
202+020.00	243.79	26,736.89		5,058.01	
202+040.00	194.01	31,114.85		4,377.95	
202+060.00	362.48	36,679.73		5,564.88	
202+080.00	341.72	43,721.80		7,042.07	
202+100.00	314.56	50,284.61		6,562.81	
202+120.00	301.56	56,445.77		6,161.16	
202+140.00	0	59,461.36		3,015.59	
202+160.00	0	59,461.36		0.00	
202+180.00	0	59,461.36		0.00	
202+200.00	0	59,461.36		0.00	
202+220.00	317.97	62,641.01		3,179.66	
202+240.00	312.67	68,947.36		6,306.35	
202+260.00	320.6	75,280.03		6,332.66	
202+280.00	330.13	81,787.33		6,507.30	
202+300.00	335.88	88,447.44		6,660.11	
202+320.00	141.42	93,220.38		4,772.95	
202+340.00	132.47	95,959.23		2,738.85	
202+360.00	116.74	98,451.35		2492.11	
202+376.01	91.94	100,122.29		1,670.94	
اجمالي كميات الردم المصروفة سابقا					0
اجمالي كميات الردم الفعلية الحالية بعد خصم سمك خرسانه الميول					100122.28
كمية خصم سمك خرسانه الميول					911

عن الاستشاري المساحة
م/محمد عبد الرحمن
م/احمد عزب
م/محمود غريب
عن الاستشاري أ.د/حسن مهدي



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name [Signature]	Sign [Signature]	Date 15-8-2022
Received by Employers Representative		Time 2	
		UIR	
		C1 KP	C2 EW
		C3 OT	DD 15
		MM 8	YY 22
		HH	MM
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 202+376	
	E=260126.0446 N=3137487.7094	E=260129.6912 N=3135991.0324
Inspection description[Disinfection Of Trees Cutting From st (200+876) to st (202+376)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

تصوير وازالة الحما
بواسطة فريق العمل

- Trees No. was checked only by xyz and under their own responsibility
- you must follow specs and design dr

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	[Signature]	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	[Signature]	15-8-2022		A	
	H.M.C	[Signature]	15-8-2022		A	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024		AWC	

* Designer

** Alignment: Bridges: Culvert Only

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name [Signature]	Sign [Signature]	Date 15-8-2022
Received by Employers Representative	UIR	C1 KP	C2 EW
		C3 OT	DD 15
		MM 8	YY 22
		HH 22	MM 22
CODE-1	CODE-2	CODE-3	CODE-4

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 202+376	
	E=260126.0446 N=3137487.7094	E=260129.6912 N=3135991.0324
Inspection description[Disinfection Of Trees Cutting From st (200+876) to st (202+376)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

تصوير وازالة الاشجار بواسطة فريق العمل	- Trees No. was checked only by xyz and under their own responsibility - you must follow specs and design dr
---	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	[Signature]	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	[Signature]	15-8-2022		A	
	H.M.C	[Signature]	15-8-2022		A	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024		AWC	

* Designer

** Alignment: Bridges: Culvert Only

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيل للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
	20-10-2022	3								
Received by Employers Representative			C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	20	10	22		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5						

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+686 E=260126.0446 E=260172.2356 N=3137487.7094 N=3136679.1711	
Inspection description/ تطهير بعد قطع الاشجار Disinfection of crops and trees cutting from st (200+876) to st (201+686)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
---	--

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA/QC*	XYZ		20-10-2022	14:30	A	
	H.M.C		20/10/2022	15:00	A	
GARB**						
Employers Representative						

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
	أبو عجلة	[Signature]	20-10-2022	4						
Received by Employers Representative			C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	20	10	22		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5						

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+686 TO 201+846	
	E=260172.2356 N=3136679.1711	E=260170.8362 N=3136519.1841
Inspection description/		
Disinfection of crops and trees cutting from st (201+686) to st (201+846) / تم تعقيم بعد قطع الأشجار		

منطقة قطع

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
[Signature]	

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	أبو عجلة	[Signature]				
Contractor QA/QC*	XYZ	[Signature]	20-10-2022	16:00	A	
	H.M.C	[Signature]	20/10/2022	16:30		
GARB**						
Employers Representative						

[illegible]

INSPECTION DETAILS	
Planned Inspection Date	Planned Inspection Time
The Following will be ready at the Planned Inspection Time	
COMPLIANCE EVIDENCE	
Must be included as appropriate	
☐ Checklist Attached ☐ Drawing Reference ☐ Test Results Attached ☐ ITP Reference	☐ Calibration Attached ☐ MS Reference ☐ Other as indicated

Comments by: General consultant (systa) - Levels and coordinates were checked only by xyz and under their own responsibility - you must follow spec, design drawing	Comments by: (GAR8 SURVEY CONSULTANT: (xyz)) 
---	--

INSPECTION RESULT		Approval Status		Please Tick if	
		Not Attend			
Organisation	Name	Sign	Date	Time	A-AWC-R
Contractor Engineer	20-10-2022 14:30				
Contractor	XYZ		20-10-2022 14:30		
QA/QC*	H.M.C		20/10/2022 14:30		
GARB**					
Employers Representative	Khaled ah		23/10/2024		AWC

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)					
Issued by Contractor	Name	Sign	Date					
			25-10-2022					
Received by Employers Representative	Name	Sign	Time					
			6					
C1		C2	C3	DD	MM	YY	HH	MM
KP		EW	OT	25	10	22		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+466 TO 201+666	
	E=260165.8013	E=260172.0505
	N=3136899.0593	N=3136699.1703
Inspection description/		
As-Built for rock surface from st (201+466) to st (201+666)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)



-Levels and coordinates were checked only by xyz and under their own responsibility
-This work was inspected only by xyz and H.M.C
-you must follow spec and geo-technical report

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer					A-AWC-R	
Contractor QA/QC*	XYZ		25-10-2022	13:00	A	
	H.M.C		25/10/2022	13:00	A	
GARB**						
Employers Representative	Khaled ali		23/9/2024			



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
			29-10-2022	7						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	29	10	28		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	200+876 TO 201+466		
	E=260126.0446	E=260165.8013	
	N=3137487.7094	N=3136899.0593	
Inspection description[الرفع المساحي + المعاينة للطرح المقصود (المسوح الأول) As-Built for rock surface from st (200+876) to st (201+466)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. (xyz))

Comments by: General consultant (systra)

(as built) م.عبدالله السويح - الخبير	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C. - you must follow specs and design drawings.
---	--

INSPECTION RESULT

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time			
Contractor Engineer							
Contractor QA/QC*	XYZ		29-10-2022	12:00	A		
	H.M.C		29/10/22		A		
GARB**							
Employers Representative	Khaleed ali		23/9/2024				

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	مكتب أديسن مهدي للإستشارات الهندسية		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
			2-11-2022	8						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	2	11	22		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+036 TO 201+086	
	E=260137.1186 N=3137328.0971	E=260140.5793 N=3137278.217
<u>Inspection description/</u> As-Built for rock surface from st (201+036) to st (201+086)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
2/11/2022	

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C - you must follow spec and geo-technical report

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time			
Contractor Engineer							
Contractor QA/QC*	XYZ			2-11-2022	17:30	A	
	H.M.C			2/11/2022	13:30	A	
GARB**							
Employers Representative	Khaled ali			23/9/2024			

Page 1 of 1

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عبيدة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
	محمد أبو بكر		6-11-2022	10						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	6	11	2022		
CODE-1		CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+156 TO 201+246	
	E=260145.4242 N=3137208.3848	E=260151.6535 N=3137118.6007
Inspection description/		
الرفع المساحي + معاينة سطح صخري (المنسوب الثالث)		
As-Built for rock surface from st (201+156) to st (201+246)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))

Comments by: General consultant (systra)

- Levels and Coordinates were checked only by xyz and under their own responsibility.

- This work was inspected only by xyz and H.M.C.

you must follow specs and geo-technical report

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	محمد أبو بكر				A-AWC-R	
Contractor QA/QC*	XYZ		6-11-2022	14:00	A	
	H.M.C		6/11/2022	14:30	A	
GARB**						
Employers Representative	Khaled Ali		23/11/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name أبو عجلة	Sign أبو عجلة	Date 7-12-2022																
Received by Employers Representative			Time 13																
		UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>EW</td> <td>OT</td> <td>7</td> <td>12</td> <td>23</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	EW	OT	7	12	23		
C1	C2	C3	DD	MM	YY	HH	MM												
KP	EW	OT	7	12	23														
CODE-1	CODE-2	CODE-3	CODE-4																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+286 TO 201+386	
	E=260154.422 N=3137078.6966	E=260161.1582 N=3136978.9239
<u>Inspection description</u> As-Built for rock surface from st (201+286) to st (201+386)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT: (xyz))

Comments by: General consultant (systra)



- Levels and coordinates were checked only by xyz and under their own responsibility
 - This work was inspected only by xyz and H.M.C.
 - you must follow specs and geo-technical report

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	أبو عجلة	أبو عجلة			A-AWC-R	
Contractor QA/QC*	XYZ	أبو عجلة	7-12-2022	14:00	A	
	H.M.C	أبو عجلة	7/12/2022	14:30	A	
GARB**						
Employers Representative	Khaleel ali	أبو عجلة	23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR ,Hassan Mahdy (H.M.C)
Issued by Contractor	Name Sign 13-12-2022	Date	Time 14
Received by Employers Representative	UIR	C1 KP	C2 EW
		C3 OT	DD 13
		MM 12	YY 22
		HH	MM
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+386 TO 201+426	
	E=260161.1582 N=3136978.9239	E=260163.6041 N=3136938.9988
Inspection description: الرفع المساحي + معاينة سطح صخره (المستوي الثالث) As-Built for rock surface from st (201+386) to st (201+426)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
	- Levels and coordinates were checked only by systra and under their own responsibility - This work was inspected only by systra and H.M.C - you must follow specs and geo-technical report

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer							
Contractor QA/QC*	XYZ		13-12-2022	12:16	A		
	H.M.C		13/12/2022	12:17	A		
GARB**							
Employers Representative	Khaled al.		23/12/2022				

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)					
Issued by Contractor	Name	Sign	Date	Time					
	13-12-2022	16							
Received by Employers Representative	C1	C2	C3	DD	MM	YY	HH	MM	
									13
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5	

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+036	
	E=260126.0446 N=3137487.7094	E=260137.1186 N=3137328.0971
Inspection description: As-Built for rock surface from st (200+876) to st (201+036)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSANTANT.(xyz))	Comments by: General consultant (systra)
	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C - you must follow spec and geotechnical rep.

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer						
Contractor QA/QC*	XYZ		13-12-2022	13:30	A	
	H.M.C		13/12/2022	14:00	A	
GARB**						
Employers Representative	Phaked ali		23/12/2022		A	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR ,Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
			2023-1-3	17						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	3	1	23		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED


Area	Element		Item
From 200+876 To 202+376	200+876 TO 201+666		
	E=260126.0446	E=260172.0505	
	N=3137487.7094	N=3136699.1703	
Inspection description/			
As-Built for cut from st (200+876) to st (201+666)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
2023/1/3	

COMPLIANCE EVIDENCE Must be Included as appropriate


Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
	- Levels and coordinates were checked only by XYZ and under their own responsibility - you must follow specs and design drawings

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor	XYZ		3-1-2023	19:00	A	
QA/QC*	H.M.C		3/1/2023	19:00		
GARB**						
Employers Representative	Khaled ali		23/9/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name  Sign 	Date	Time
Received by Employers Representative	UIR	13-6-2023	18
		C1 KP	C2 EW
		C3 OT	DD 13
		MM 6	YY 23
		HH	MM
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+660 E=260126.0446 N=3137487.7094	E=260171.9793 N=3136705.1798
Inspection description As-Built for cut from st (200+876) to st (201+660)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time



Planned Inspection Date	Planned Inspection Time
12/6/2023	

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)


- Levels and coordinates were checked only by xyz and under their own responsibility

- you must follow spec and design dwg.

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA/QC*	XYZ		13-6-2023	9:00	A	
	H.M.C		13/6/2023			
GARB**						
Employers Representative	Khaled Ali		23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله والمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name Sign 24-8-2023	Date	Time 19
Received by Employers Representative	Sign 23	Time	

CODE -1	CODE -2	CODE -3	CODE -4	CODE -5
---------	---------	---------	---------	---------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+840 E=260126.0446 N=3137487.7094	E=260170.9813 N=3136525.1923
Inspection description: As-Built for cut from st (200+876) to st (201+840)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
24/8/2023	

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

 asbuilt
 قطاع الطرق

 - Levels and coordinates were checked only by xyz and under their own responsibility
 - you must follow specs and design dwg.

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer					A-AWC-R	
Contractor QA/QC*	XYZ		26-8-2023	10:00	A	
	H.M.C		26/8/2023	10:15	A	
GARB**						
Employers Representative	Khaled ali		23/8/2023			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name وليد فاضل Sign [Signature]	Date	9-11-2023
Received by Employers Representative	UIR	REQ.NUM	20
		C1 KP	C2 SU
		C3 OT	DD 9
		MM 11	YY 23
		HH	MM
CODE -1		CODE -2	
CODE -3		CODE -4	
CODE -5			

EXPLANATION OF WORK TO BE INSPECTED


Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description/ تشييد قاع إحلال from st (202+220) to st (202+300)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
	- levels and coordinates were checked only by xyz and under their own responsibility - No objection according to the attached reports and lab. results.

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time		A-AWC-R	
Contractor Engineer	وليد فاضل	[Signature]	19-11-2023	10:00	(A)		
Contractor QA/QC*	XYZ	[Signature]	9/11/2023	11:00	A		
GARB**							
Employers Representative	Khaled ali	[Signature]	23/9/2024				

* Designer

** Alignment: Bridges; Culvert Only

UNIVERSAL INSPECTION REQUEST



مكتب أ.د. حسن مهدي
للإشراف الهندسية



الهيئة العامة للأشغال العامة
General Authority of Public Works



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name وليد محمد محمود	Date	18-11-2023
Received by Employers Representative	Sign [Signature]	REQ. NUM	21
UIR	UIR	C1 KP	C2 SU
		C3 QT	DD 18
		MM 11	YY 23
		HH 23	MM 23
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+280 TO 202+300	
	E=260141.2938 N=3136086.3373	E=260139.0278 N=3136066.4661
Inspection description:		
من (10-متر) تسليم طبقة (10-متر) from st (202+280) to st (202+300)		

INSPECTION DETAILS The Following will be ready at the Planned inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))

مكتب أ.د. حسن مهدي
للإشراف الهندسية

Comments by: General consultant (systra)

- No objection, according to the attached reports and lab. results.
- you must follow specs and design dwg.

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمد محمود	[Signature]	18/11/2023	10:10	A	يقم صيانة - الطريق قبل العملات
Contractor QA/QC*	XYZ	[Signature]	18-11-2023	13:30	A	
	H.M.C	[Signature]	18/11/2023	11:30	AWC	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عبيدة للمقاولات 2023	Designer Company*	DR ,Hassan Mahdy (H.M.C)															
Issued by Contractor	Name Signature 20-11-2023	Date	REQ. NUM 22															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>21</td> <td>11</td> <td>23</td> <td>2</td> <td>30</td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	21	11	23	2	30
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT	21	11	23	2	30											
CODE-1	CODE-2	CODE-3	CODE-4															
CODE-5																		

EXPLANATION OF WORK TO BE INSPECTED


Area	Element	Item
From 200+876 To 202+376	202+000 TO 202+120	
	E=260164.6561 N=3136365.3242	E=260156.5571 N=3136245.6007
Inspection description/ تشغيل قاع إحلال from st (202+000) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was checked only by xyz and H.M. - you must follow speed and design drawing and geo-technical report

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time			
Contractor Engineer	وليد محمد	وليد محمد					
Contractor QA/QC*	XYZ	محمد	21-11-2023	3:15	(A)		
	H.M.C	عبدالله	21/11/2023	3:00	A		
GARB**							
Employers Representative	Khaled ali		23/11/2024		Any		

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown:

Contractor Company	أبو عجمية للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name:  Sign: 	Date	REQ. NUM						
Received by Employers Representative	UIR	22-11-2023	23						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT	22	11	23		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description/		
منطقة ردم منسوب (-9.5) متر from st (202+220) to st (202+300)		



INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))	Comments by: General consultant (systra)
	- No objection, according to the attached reports and Lab. results. - you must follow specs and design drawings

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time			
Contractor Engineer	وليد محمد						
Contractor QA/QC*	XYZ		22-11-2023	3:45	(A)		
	H.M.C		22/11/2023	11:00	A		
GARB**							
Employers Representative	Fhaled ali		23/11/2023				

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإشراف الهندسية



الهيئة العامة للإشراف
على الطرق



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة المقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name	Sign	Date	REQ.NUM
	أحمد محمد	أحمد محمد	25-11-2023	24
Received by Employers Representative	شركة المقاولات العامة		UIR	
			C1 C2 C3 DO MM YY HH MM	
			KP SU OT 25 11 23	

CODE-1 CODE-2 CODE-3 CODE-4 CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+000 TO 202+020	
	E=260164.6561 N=3136365.3242	E=260163.5058 N=3136345.3573
Inspection description/		
منطقة ردم منسوب (13) متر from st (202+000) to st (202+020)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (systa))



Comments by: General consultant (systa)

- No objection, according to the attached reports and lab. results.
- you must follow specs and design drawings

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	أحمد محمد	أحمد محمد			A-AWC-R	
Contractor QA/QC*	XYZ	أحمد محمد	25-11-2023	12:30	(A)	
	H.M.C	أحمد محمد	25/11/23	11:00	A	
GARB**						
Employers Representative	Khaled ali	أحمد محمد	23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name [Signature]	Sign [Signature]	Date 28-11-2023
Received by Employers Representative	UIR	REQ NUM 25	
		C1 KP	C2 SU
		C3 OT	DD 28
		MM 11	YY 23
		HH 11	MM 00
CODE-1	CODE-2-109	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300 E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description منسوب (9-متر) from st (202+220) to st (202+300)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

تم استلام استبيان المعاينة
والتأكد من أن العمل جاهز للمعاينة

- No objection, according to the attached reports and lab. results
- you must follow specs and design dng.

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمد	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	عبد الله الدلاوي	28/11/2023	3:30	A	
	H.M.C	عبد الله العتيبي	28/11/2023	11:00	A	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	Name		Sign	Designer Company*	DR .Hassan Mahdy (H.M.C)				
Issued by Contractor	29-11-2023		REQ.NUM		26				
Received by Employers Representative	C1		C2	C3	DO	MM	YY	HH	MM
	KP		SU	OT	29	11	23		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5	

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+060 TO 202+080		
	E=260160.9658	E=260159.576	
	N=3136305.4382	N=3136285.4865	
Inspection description[			
from st (202+060) to st (202+080) طبقة ردم منسوب (-11) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))	Comments by: General consultant (systra)
 المهندس خالد علي - الهندس العام	- No objection, according to the attached reports and lab. results. - you must follow specs and design draw

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد فريد	وليد فريد				
Contractor XYZ	خالد علي	خالد علي	29-11-2023	11:15	(A)	
Contractor QA/QC*	H.M.C	محمد أحمد	29-11-2023	12:45	A	
GARB**						
Employers Representative	Khaled ali	خالد علي	29/11/2023		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name وليد محمود محمد	Date	29-11-2023						
Received by Employers Representative	Sign [Signature]	REQ.NUM	27						
Received by Employers Representative	UIR	C1 KP	C2 SU	C3 OT	DD 29	MM 11	YY 23	HH	MM
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+080 TO 202+120	
	E=260159.576 N=3136285.4865	E=260156.5571 N=3136245.6007
Inspection description[منطقة ردم منسوب (10.5) متر from st (202+080) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

مكتب أد/حسن مهدي
للإستشارات الهندسية

-No objection, according to the attached reports and lab. results
-you must follow specs and design dwg

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمود محمد	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	[Signature]	29-11-2023	11:30	(A)	
	H.M.C	[Signature]	29-11-2023	12:30	A11	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024			

UNIVERSAL INSPECTION REQUEST



مكتب أ.د/حسن مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
SYSTRA



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	157137 أبو عجلة للتقانات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name وليد محمد Sign [Signature] Date 30-11-2023	REQ. NUM	28
Received by Employers Representative	UIR	C1 KP	C2 SU
		C3 OT	DD 30
		MM 11	YY 23
		HH	MM

CODE-1

CODE-2

CODE-3

CODE-4

CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+000 TO 202+020 E=260164.6561 N=3136365.3242	E=260163.5058 N=3136345.3573
Inspection description: ردم طبقة ردم منسوب (-12.5) متر from st (202+000) to st (202+020)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (XYZ)) [Signature] [Stamp]	Comments by: General consultant (systra) - No objection, according to the attached reports and lab. results. - you must follow spec and design draw
---	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمد	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	[Signature]	30-11-2023	13:00	A	
	H.M.C	[Signature]	30/11/2023	12:30pm	A	
GARB**						
Employers Representative	Khaled Ali	[Signature]	23/9/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 57537	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name [Signature]	Date	2-12-2023																
Received by Employers Representative	Sign [Signature]	REQ.NUM	29																
UIR		<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>2</td> <td>12</td> <td>23</td> <td></td> <td></td> </tr> </table>		C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	2	12	23		
C1	C2	C3	DD	MM	YY	HH	MM												
KP	SU	OT	2	12	23														
CODE-1	CODE-2	CODE-3	CODE-4																
CODE-5	CODE-6	CODE-7	CODE-8																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description[from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (-8.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))

Comments by: General consultant (systra)

تم استلام نتائج الاختبار
من مختبر اختبار السريعة - الخط الثاني

- No objection, according to the attached reports and lab. results.
- you must follow specs and design dr

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمد	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	عبد الرحمن الوالد	21/12/2023	3:15	A	
	H.M.C	أحمد مصطفى	21/12/23	3:00	AWC	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/12/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name 157537	Sign	Date 3-12-2023
Received by Employers Representative		UIR	REQ.NUM 30
		C1 KP	C2 SU
		C3 OT	DD
		MM	YY 23
		HH	MM

CODE-1

CODE-2

CODE-3

CODE-4

CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+100 E=260160.9658 N=3136305.4382	E=260158.1064 N=3136265.5406
Inspection description منطقة ردم مسوب (-10.5) متر from st (202+060) to st (202+100)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz)) مستشاري المساحة مستشاري المساحة مستشاري المساحة	Comments by: General consultant (systra) - No objection, according to the attached reports and lab. results. - you must follow specs and design d.
--	--

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA\QC*	XYZ		3-12-2023	4:15	(A)	
	H.M.C		3/12/2023	2:30 PM	AWC	
GARB**						
Employers Representative	Khaled ali		28/9/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown.

Contractor Company	شركة البترول العالمية		Designer Company*	DR. Hassan Mahdy (H.M.C)																
Issued by Contractor	Name وليد عيسى	Sign [Signature]	Date 5-12-2023	REQ. NUM 31																
Received by Employers Representative	[Signature]		UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DO</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>23</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DO	MM	YY	HH	MM	KP	SU	OT			23		
C1	C2	C3	DO	MM	YY	HH	MM													
KP	SU	OT			23															
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147	E=260139.0278
	N=3136146.003	N=3136066.4661
<u>Inspection description:</u> from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (8-متر)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT-(xyz))

[Signature]

مهندس الاستشارات الهندسية - الخلد

Comments by: General consultant (systra)

- No objection, according to the attached reports and lab. results.
- you must follow specs and design dwg.

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد عيسى	[Signature]	6-12-2023	10:30	(A)	يتم اضافة لسانه قبل اكمال التوازي
Contractor QA/QC*	XYZ	[Signature]	6-12-2023	10:30	(A)	
	H.M.C	[Signature]	5/12/2023	4:15PM	AWC	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024		AWC	



UNIVERSAL INSPECTION REQUEST



مكتب أ.إ.م.ن
للإشراف الهندسية



الهيئة العامة
للإشراف الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR. Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ. NUM						
	أحمد محمد	أحمد محمد	13-12-2023	35						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			XP	SU	OT	13	12	23	3	00
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5						

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+060 TO 202+120		
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007	
Inspection description/ منطقة ردم طليقة ردم منسوب (9- متر from st (202+060) to st (202+120)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARIB SURVEY CONSATANT. (xyz))

Comments by: General consultant (systra)

أحمد محمد

- No objection, according to the attached reports and lab. results.
- you must follow specs and design drawings.

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	أحمد محمد	أحمد محمد	13-12-2023	4:00	(A)		
Contractor QA/QC*	XYZ	أحمد محمد	13-12-2023	4:00	(A)		
	H.M.C	أحمد محمد	13-12-2023	3:00	AWC		
GARB**							
Employers Representative	Khaled ali	أحمد محمد	23/12/2023		AWC		

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للتعليم
التقني والتدريب المهني



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR. Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ. NUM						
	وليد فلاح	وليد فلاح	17-12-2023	37						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT				23	
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007	
Inspection description:			
من (202+060) to st (202+120) طبقة ردم ملسوب (8.5) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by (GARB SURVEY CONSULTANT xyz)	Comments by: General consultant (systra)
استاذ المهندس مستوى التفتيش الكفائي الذي -315	-No objection, according to the attached reports and lab. results. -you must follow specs and design dwg

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد فلاح	وليد فلاح				تم اتمام العمل
Contractor QA/QC*	XYZ		17-12-2023	13:00	A	قبول
	H.M.C	محمد بن عبد الله	17-12-2023	11:00	Amc	الموافق
GARB**						
Employers Representative	Khaled ali		20/12/24		Amc	



UNIVERSAL INSPECTION REQUEST



مكتب المدعى
للإشراف الهندسية



المكتب الهندسي
للإشراف الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company			Designer Company*	DR. Hassan Mahdy (H.M.C)																
Issued by Contractor	Name	Sign	Date	REQ. NUM																
			19-12-2023	38																
Received by Employers Representative			<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>AP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>YY</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	AP	SU	OT			YY			
C1	C2	C3	DD	MM	YY	HH	MM													
AP	SU	OT			YY															
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5																

EXPLANATION OF WORK TO BE INSPECTED


Area	Element	Item
From 200+876 To 202+576	202+220 TO 202+300	
	E=260147.5147	E=260139.0278
	N=3136146.003	N=3136066.4661
Inspection description (from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (7.0) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	M5 Reference	

Comments by: (GARB SURVEY CONSULTANT: XYZ)	Comments by: General consultant (systra)
	- No objection, according to the attached reports and lab. results. - you must follow specs and design drug

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA/QC*	XYZ		19-12-2023	3:30	A	
	H.M.C		19-12-2023	11:30	A	
GARB**						
Employers Representative	Khaled ali		23/9/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)				
Issued by Contractor	Name	Sign	Date				
	وليد محمور محمد		20-12-2023				
Received by Employers Representative		REQ.NUM	39				
C1	C2	C3	DD	MM	YY	HH	MM
	KP	SU	OT			23	

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description/		
من (8-) متر from st (202+060) to st (202+120) طبقة ردم منسوب		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time


Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)



- No objection, according to the attached reports and Lab. results.
- You must follow specs and design draw

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمور محمد				A-AWC-R	
Contractor QA/QC*	XYZ		20-12-2023	3:40	A	
	H.M.C		20-12-2023	1:45	A	
GARB**						
Employers Representative	Khaled ali		23/9/2024		A	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name Sign 21-12-2023	Date	REQ.NUM 40															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>21</td> <td>12</td> <td>23</td> <td>11</td> <td>30</td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	21	12	23	11	30
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT	21	12	23	11	30											
CODE-1	CODE-2	CODE-3	CODE-4															
CODE-5	CODE-6	CODE-7	CODE-8															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description: from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (6-متر)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT: xyz)	Comments by: General consultant (systra)
	- No objection, according to the attached reports and lab. results. - you must follow specs and design d.

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمد	وليد محمد				
Contractor QA/QC*	XYZ	عبد الرحمن العرابي	21-12-2023	11:00	A	
	H.M.C	سيد احمد محمد	21/12/23	11:30	A	
GARB**						
Employers Representative	Khaled ali		23/12/2023		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب المهندس
للإشراف الهندسية



الهيئة العامة للطرق
والمواصلات



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name وليد محمود محمد	Sign 	Date 23-12-2023	REQ.NUM 41																
Received by Employers Representative			<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>23</td> <td></td> <td></td> </tr> </table>		C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			23		
C1	C2	C3	DD	MM	YY	HH	MM													
KP	SU	OT			23															
CODE-1		CODE-2	CODE-3	CODE-4	CODE-5															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description: from st (202+220) to st (202+300) تسليم طبقة ردم ملسوب (-5.5) متر		

INSPECTION DETAILS The following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
	- No objection, according to the attached reports and lab. results. - you must follow specs and design dr.

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود محمد					
Contractor QA/QC*	XYZ		23/12/2023	1:00	A	
	H.M.C		23/12/2023	12:00	A	
GARB**						
Employers Representative	Khaled ali		23/12/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
SHARER



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	DR .Hassan Mahdy (H.M.C)	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name: وليد محمود Sign: [Signature] Date: 23-12-2023	REQ.NUM	42															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>23</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			23		
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT			23													
CODE-1	CODE-2	CODE-3	CODE-4															
CODE-5	CODE-6	CODE-7	CODE-8															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+920 TO 202+000	
	E=260168.4582 N=3136445.233	E=260164.6561 N=3136365.3242
Inspection description:		
from st (201+920) to st (202+000)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
مستشار عام مستشار عام مستشار عام	- Levels and coordinates were checked only by XYZ and under their own responsibility - This work was checked only by XYZ and - you must follow specs and design H.M.C

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمود	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	[Signature]	23/12/2023	12:00	A	
	H.M.C	[Signature]	23/12/2023	11:00	A	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024			

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للمستشارات الهندسية



الهيئة العامة للإسكان
General Housing Authority



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name: <u>وليد محمود</u> Sign: <u>[Signature]</u>	Date	REQ.NUM																
Received by Employers Representative		23-12-2023	43																
		<table border="1"> <tr> <td>G1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>23</td> <td>12</td> <td>23</td> <td></td> <td></td> </tr> </table>	G1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	23	12	23			
G1	C2	C3	DD	MM	YY	HH	MM												
KP	SU	OT	23	12	23														
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description/ منسوب (7.5-) متر from st (202+060) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT. (xyz))	Comments by: General consultant (systra)
<u>[Signature]</u>	- No objection, according to the attached reports and lab. results. - you must follow specs and design draw

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	<u>وليد محمود</u>	<u>[Signature]</u>				
Contractor QA/QC*	XYZ	<u>[Signature]</u>	23-12-2023	4:15	A	
	H.M.C	<u>[Signature]</u>	23/12/23	4:00	AWC	
GARB**						
Employers Representative	<u>Khaled Nale</u>	<u>[Signature]</u>	23/12/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أراضين مهدي
للإستشارات الهندسية



الهيئة العامة للإعتماد
والتقنين



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	المشروعات العامة		Designer Company*	DR. Hassan Mahdy (H.M.C)																
Issued by Contractor	Name وليد محمود	Sign 	Date 25-12-2023	REQ. NUM 44																
Received by Employers Representative			<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DO</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>23</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DO	MM	YY	HH	MM	KP	SU	OT			23			
C1	C2	C3	DO	MM	YY	HH	MM													
KP	SU	OT			23															
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
<u>Inspection description:</u> متر طبقة ردم منسوب (7) - متر from st (202+060) to st (202+120)		

INSPECTION DETAILS The following will be ready at the Planned inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT. xyz) Comments by: General consultant (systra)

	- No objection, according to the attached reports and lab. results. - you must follow specs and design data
--	--

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود					
Contractor QA/QC*	XYZ	عبد الرحمن الخولي	25-12-2023	4:13	A	
	H.M.C	محمد كعود	25-12-2023	4:10	AWC	
GARB**						
Employers Representative	Khaled ali		23/9/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أديسن مهندسي
الاستشارات الهندسية



الهيئة العامة للإستثمار



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أيم جلوبل للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	وليد محمود	وليد محمود	28-12-2023	46						
Received by Employers Representative		VIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT				23	

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
From 200+876 To 202+376	201+980 E=260165.727 N=3136385.3	
Inspection description: منطقة ردم منسوب (-14) متر from st (201+980)		

INSPECTION DETAILS The Following will be ready at the Planned inspection Time	
Planned inspection Date	Planned inspection Time


COMPLIANCE EVIDENCE Must be included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))	Comments by: General consultant (systra)
 - No objection, according to the attached reports and lab. results. - you must follow specs and design drawings	

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود	وليد محمود				
Contractor QA/QC*	XYZ	عبد الرحمن العبدان	28-12-2023	13:00	A	
	H.M.C	محمود بشارة	28-12-2023	11:00		
GARB**						
Employers Representative	Khaled ali		23/9/2024		ANC	

UNIVERSAL
INSPECTION
REQUEST








RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours
The Work described below will be complete and ready for inspection at planned time shown

Contractor Company

Name

Designer Company*

Date

DR. Hassan Mahdy
(H.M.C)

28-12-2023

Issued by Contractor

Sign

REQ.NUM

47

Received by Employers Representative

Sign

C1

C2

C3

DO

MM

YY

HH

MM

CODE-1

CODE-2

CODE-3

CODE-4

CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area

Element

Item

From 200+876 To 202+376

202+060 TO 202+120

E=260160.9658

E=260156.5571

N=3136305.4382

N=3136245.6007

Inspection description:

from st (202+060) to st (202+120) طبقة ردم منسوب (-6.5) متر

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date

Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached

Test Results Attached

Calibration Attached

Other as indicated

Drawing Reference

ITP Reference

MS Reference

Comments by: (GARB SURVEY CONSULTANT-xyz)

Comments by: General consultant (systra)

- No objection, according to the attached reports and lab. results.
- you must follow specs and design dmy.

INSPECTION RESULT

Approval Status

Please Tick if Not Attend

Organisation

Name

Sign

Date

Time

A-AWC-R

Contractor Engineer

Contractor QA/QC*

XYZ

28-12-2023

1:00

A

H.M.C

28-12-2023

1:00

A

GARB**

Employers Representative

Icholed ali

23/9/2024

Ame



UNIVERSAL INSPECTION REQUEST



مكتب المهندس
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	157533 مكتب المهندس للإستشارات الهندسية		Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name وليد محرم	Sign 	Date 2-1-2024	REQ.NUM 48
Received by Employers Representative	 UIR		C1 KP	C2 SU
			C3 OT	DD MM YY 24
	CODE-1	CODE-2	CODE-3	CODE-4
				CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
<u>Inspection description/</u> from st (202+220) to st (202+300) تسليم طبقة ردم مسسوب (4.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))

Comments by: General consultant (systra)

تم تسليم طبقة ردم مسسوب (4.5) متر
مستوفى القياسات التسريبية - الفتح الذري

-No objection, according to the attached reports and lab. results.
-you must follow specs and design draw

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محرم				A-AWC-R	
Contractor QA/QC*	XYZ	غير ملحق بالصلاحيات	2-1-2024	10:40	A	
	H.M.C	محمود عبد الحليم	2-1-2024	10:30	A	
GARB**						
Employers Representative	Khaled ali		23/1/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company			Designer Company*	DR. Hassan Mahdy (H.M.C)																
Issued by Contractor	Name	Sign	Date	REQ. NUM																
			2-1-2024	49																
Received by Employers Representative			UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			24		
C1	C2	C3	DD	MM	YY	HH	MM													
KP	SU	OT			24															
CODE-1		CODE-2		CODE-3																
				CODE-4																
				CODE-5																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+060 TO 202+120		
	E=260160.9658	E=260156.5571	
	N=3136305.4382	N=3136245.6007	
<u>Inspection description</u> from st (202+060) to st (202+120) طبقة ردم منسوب (-6) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))

Comments by: General consultant (systra)

- No objection, according to the attached reports and lab. results
 - you must follow specs and design drawings

INSPECTION RESULT

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time			
Contractor Engineer							
Contractor QA/QC*	XYZ		2-1-2024	11:40	A		
	H.M.C		2-1-2024	11:50	AWC		
GARB**							
Employers Representative	Khaleed ali		2/1/2024				

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	المشروعات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name وليد محجور	Sign 	Date 2-1-2024																
Received by Employers Representative	UIR	REQ NUM 50																	
		<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			24			
C1	C2	C3	DD	MM	YY	HH	MM												
KP	SU	OT			24														
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+960 TO 202+000	
	E=260166.717 N=3136405.271	E=260164.6561 N=3136365.1247
<u>Inspection description</u> from st (201+960) to st (202+000) طبقة ردم منسوب (-13.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. (xyz)) 	Comments by: General consultant (systra) -No objection, according to the attached reports and lab. results. -you must follow specs and design dr
---	--

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محجور					
Contractor QA\QC*	XYZ	عبد الرحمن الشرايحي	2-1-2024	11:15	A	
	H.M.C	عبد الرحمن الشرايحي	2-1-2024	11:00	AUC	
GARB**						
Employers Representative	Khaled ali		23/9/2024		AUC	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



المهنة العامة الإستشارية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	[Signature]		6-1-2024	51						
Received by Employers Representative	[Signature]	UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT				24	
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+960 TO 202+000		
	E=260166.717 N=3136405.271	E=260164.6561 N=3136365.3242	
<u>Inspection description</u> from st (201+960) to st (202+000) طبقه ردم منسوب (-13) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: [GARB SURVEY CONSATANT. (xyz)]	Comments by: General consultant (systra)
[Signature]	- No objection, according to the attached reports and Lab. results.
[Signature]	- you must follow specs and design drag

INSPECTION RESULT

					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمدي	[Signature]				
Contractor QA/QC*	XYZ	عبد الرحمن العرابي	6-1-2024	4:20	A	[Signature]
	H.M.C	محمود عولمة	6/1/2023	4:15	AWC	
GARB**						
Employers Representative	Khaled ali	[Signature]	29/9/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للاستشارات الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	[Signature]		6-1-2024	52						
Received by Employers Representative	[Stamp]	UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT				24	
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5						

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+060 TO 202+120		
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007	
Inspection description/			
from st (202+060) to st (202+120) طبقة ردم منسوب (5.5) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
[Signature]	- No objection, according to the attached reports and lab results. - you must follow spec and design

INSPECTION RESULT

					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	[Signature]	[Signature]				
Contractor QA/QC*	XYZ	[Signature]	6-1-2024	5:00	A	
	H.M.C	[Signature]	6/1/2024	4:40	Awc	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024		Anrc	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 137537	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name: <u>وليد محمد</u> Sign: <u>[Signature]</u>	Date	10-1-2024
Received by Employers Representative	UIR	C1 KP	C2 SU
		C3 OT	DD MM YY HH MM
			23
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+300 TO 202+376	
	E=260139.0278 N=3136066.4661	E=260129.6912 N=3135991.0324
Inspection description/		
from st (202+300) to st (202+376)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))

Comments by: General consultant (systra)

تم التحقق من المستويات والارتفاعات فقط بواسطة XYZ والمسئولية تقع على عاتقهم فقط.

- levels and coordinates were checked only by xyz and under their own responsibility
- you must follow specs and design and geo-technical report.


- This work was inspected only by xyz and H.M.C

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمد	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	[Signature]	10-1-2024	10:30	A	
	H.M.C	[Signature]	10-1-2024	10:30	AWC	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name:  Sign: 	Date	REQ. NUM
Received by Employers Representative	UIR	15-1-2024	55
		C1 C2 C3 DD MM YY HH MM	
		KP SU OT	20
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED


Area	Element	Item
From 200+876 To 202+376	202+300 TO 202+340	
	E=260139.0278 E=260134.2574	
	N=3136066.4661 N=3136026.7517	
Inspection description/		
from st (202+300) to st (202+340) ردم منسوب (8.5) متر		


INSPECTION DETAILS The following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT - (xyz))	Comments by: General consultant (systra)
	-you must follow specs and design drug- -you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	علي محمد					
Contractor QA/QC*	XYZ	عبد الرحمن العزاد	16-1-2024	8:30	A	
	H.M.C	صمودي	15/1/2024	4:30pm	H	
GARB**						
Employers Representative	Khaled ali		26/1/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أ.إ.ص.ن مهدي
للإستشارات الهندسية





الهيئة العامة للإستشارات
والبحوث الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 1075377	Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name:  Sign: 	Date	15-1-2024						
Received by Employers Representative	UIR	REQ. NUM	56						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT			24		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300 E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description/ تسليم طبقة ردم منسوب (4) متر from st (202+220) to st (202+300)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	


Comments by: (GARB SURVEY CONSANTANT.(xyz))

Comments by: General consultant (systra)



-you must follow specs and design by
-you must do leveling and lining
the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود محمد		16-1-2024			
Contractor QA/QC*	XYZ	عبد الرحمن الزينادي	16-1-2024	9:18	A	
	H.M.C	محمد علي	15/1/2024	5:16	A	
GARB**						
Employers Representative	Khaled ali		16/1/2024		AWC	



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name [Signature] Sign [Signature]	Date	REQ.NUM 57																
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			24			
C1	C2	C3	DD	MM	YY	HH	MM												
KP	SU	OT			24														
CODE-1	CODE-2	CODE-3	CODE-4																
			CODE-5																

EXPLANATION OF WORK TO BE INSPECTED


Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description/		
منطقة ردم منسوب (4.5) متر from st (202+060) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT-xyz)	Comments by: General consultant (systra)
 مشروع القمم الكبريتات السريعة - القمم الثاني	- you must follow specs and design drug. - you must do landing and lining the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد عمار	[Signature]				
Contractor QA\QC*	XYZ	[Signature]	16-1-2024	3:30	A	
	H.M.C	[Signature]	16/1/24	3:00	AWC	
GARB**						
Employers Representative	Khaled ali	[Signature]	16/1/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name: 157537 Sign: وليد خلافة وليد محمود	Date	17-1-2024						
Received by Employers Representative	UIR	REQ.NUM	58						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT	17	1	24	4	00
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300 E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description/ منسوب (3.5-) متر from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (3.5-) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: GARB SURVEY CONSULTANT (xyz)	Comments by: General consultant (systra)
تم فحص الموقع ووجدنا أن العمل مطابق للمواصفات المطلوبة - الفحص النهائي	-you must follow specs and design dng -you must do leveling and lining the compacted side slope & filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد خلافة وليد محمود					
Contractor QA/QC*	XYZ	عبد الرحمن العرابي	17-1-2024	5:10	A	
	H.M.C	عبد الرحمن العرابي	17/1/2024	4:00	A	
GARB**						
Employers Representative	Khaled Ali		17/1/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أدهم مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR. Hassan Mahdy (H.M.C)
Issued by Contractor	Name: 137537 Sign: وليد محمد	Date	REQ. NUM
Received by Employers Representative	UIR	20-1-2024	59
		C1 C2 C3 DO MM YY HH MM	
		KP SU OT	24
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+300 TO 202+360	
	E=260139.0278 N=3136066.4661	E=260131.7531 N=3136006.9091
Inspection description:		
منسوب (8-متر) from st (202+300) to st (202+360) تسليم طبقة ردم منسوب		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: GARB SURVEY CONSATANT. (xyz)	Comments by: General consultant (systra)
مستشار الاستشارات العامة	- you must follow specs and design dwg.
مستشار الاستشارات العامة	- you must do leveling and lining
مستشار الاستشارات العامة	the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	علي محمد	علي محمد	20/1/2024	10:00	A	
Contractor QA/QC*	YXZ	علي محمد	20/1/2024	9:00	A	
	H.M.C	علي محمد				
GARB**						
Employers Representative	Khaled ali	علي محمد	20/1/2024		Amr	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والمصممات الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name: <u>علي محمد</u> Sign: <u>علي محمد</u>	Date	REQ.NUM
Received by Employers Representative	UIR	18-1-2024	60
		C1 C2 C3 DD MM YY HH MM	
		KP SU OT	24
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+920 TO 202+000	
	E=260168.4582 N=3136445.233	E=260164.6561 N=3136365.3242
Inspection description:		
منسوب (12.5) متر from st (201+920) to st (202+000)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
تم العمل على الخطوط المرسومة - you must follow specs and design dwg	- you must follow specs and design dwg
مستوى التربة: 12.5 متر - you must do leveling and lining	- you must do leveling and lining
مستوى التربة: 12.5 متر - the compacted side slope of filling layer	- the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	علي محمد	علي محمد	20-1-2024	11:15	A	
Contractor QA/QC*	XYZ	علي محمد	20-1-2024	11:15	A	
	H.M.C	علي محمد	20-1-2024	3:45	A	
GARB**						
Employers Representative	Khaled ali	علي محمد	20/1/2024	Amrc		

UNIVERSAL INSPECTION REQUEST



مكتب أ.د. حسن مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR. Hassan Mahdy (H.M.C)
Issued by Contractor	Name: Sign:	Date	REQ.NUM
Received by Employers Representative	UIR	18-1-2024	61
		C1 C2 C3 DO MM YY HH MM	
		KP SU OT	23
CODE-1	CODE-2	CODE-3	CODE-4
CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+020 TO 202+060	
	E=260163.5058 N=3136345.3573	E=260160.9658 N=3136305.4382
Inspection description/		
منسوب (12.5-) متر from st (202+020) to st (202+060)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT: xyz)	Comments by: General consultant (systra)
	- you must follow specs and design dr - you must do leveling and lining - the compacted side slope of filling layer

INSPECTION RESULT

					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	ر.م.ح. محمد					
Contractor QA/QC*	XYZ		21-1-2024	5:15	A	
	H.M.C		21-1-2024	5:00	A	
GARB**						
Employers Representative	Ali		20/1/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أ.د. حسن مهدي
للإستشارات الهندسية




المهنة العامة للإنشاءات



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name:  Sign:  Date: 21-1-2024	REQ. NUM	62
Received by Employers Representative	UIR	C1 KP	C2 SU
		C3 OT	DD MM YY HH MM
			24

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+300 TO 202+376	
	E=260139.0278 N=3136066.4661	E=260129.6912 N=3135991.0324
Inspection description(		
منسوب (7.5) متر from st (202+300) to st (202+376) تسليم طبقة ردم منسوب (7.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time


Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate


Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

	-you must follow specs and design dng -you must do leveling and lining the compacted side slope + filling layer
---	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمد				A-AWC-R	
Contractor QA/QC*	XYZ	عبد الرحمن الابرار	21-1-2024	5:10	A	
	H.M.C	شودا	21-1-2024	5:28	A	
GARB**						
Employers Representative	Khaled ali		21/1/2024		A	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجمية للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name:  Sign: 	Date	22-1-2024																
Received by Employers Representative	UIR	REQ.NUM	63																
		<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>20</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			20			
C1	C2	C3	DD	MM	YY	HH	MM												
KP	SU	OT			20														
CODE-1	CODE-2	CODE-3	CODE-4																
CODE-5																			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+920 TO 202+040	
	E=260168.4582 N=3136445.233	E=260162.2757 N=3136325.3952
Inspection description:		
منسوب (12-) متر from st (201+920) to st (202+040)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	


Comments by: (GARB SURVEY CONSATANT. (xyz))

Comments by: General consultant (systra)



-you must follow specs and design dwg
-you must do leveling and lining
the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمد					
Contractor QA/QC*	XYZ	عبد الرحمن الخياط	23-1-2024	9:00	A	
	H.M.C	محمود العبدوي	22-1-2024	5:15	AWC	
GARB**						
Employers Representative	Khaled		23/1/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	REQ. NUM							
	وليد محمود	وليد علاف	27-1-2024	65							
Received by Employers Representative			UIR	C1	C2	C3	DD	MM	YY	HH	MM
				KP	SU	OT			23		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+875 To 202+376	201+920 TO 202+060		
	E=260168.4582	E=260160.9658	
	N=3136445.233	N=3136305.4382	
Inspection description/			
من 200+875 إلى 202+376 من st (201+920) إلى st (202+060) طبقة ردم منسوب (-11.5) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time


Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)



-you must follow specs and design dng
-you must do leveling and lining
the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد علاف	وليد علاف					
Contractor QA/QC*	XYZ	أحمد محمد	27-1-24	5:00	A		
	H.M.C	محمود محمد	27-1-24	4:15	A		
GARB**							
Employers Representative	Khaled ali		27/1/2024				

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	REQ.NUM							
	رئيس محوري	رئيس خلاف	30-1-2024	66							
Received by Employers Representative			UIR	C1	C2	C3	DD	MM	YY	HH	MM
				KP	SU	OT				24	
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+300 TO 202+376		
	E=260139.0278	E=260129.6912	
	N=3136066.4661	N=3135991.0324	
<u>Inspection description:</u> from st (202+300) to st (202+376) تسليم طبقة ردم منسوب (6.5) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
	-you must follow specs and design drug -you must do leveling and lining the compacted sube slp & filling layer

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد محوري	وليد خلاف					يتم صيانة
Contractor QA/QC*	XYZ	محمد رافع	30-1-2024	4:00	(A)		القطار في التور
	H.M.C	محمد منتصر فوزي	30-1-24	12:30	AWC		
GARB**							
Employers Representative	Khated ali		30/1/2024				

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



شركة أديس مهدي
للإستشارات الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	وليد محمود	وليد عارف	18-2-2024	68						
Received by Employers Representative	[Stamp]	UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT			24		
CODE-3		CODE-2	CODE-3	CODE-4		CODE-5				

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+300 TO 202+376		
	E=260139.0278	E=260129.6912	
	N=3136066.4661	N=3135991.0324	
<u>Inspection description:</u>			
منسوب (6-) متر from st (202+300) to st (202+376)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT - xyz)

تم استلام العمل (الطريق) من قبل فريق العمل
وتم التحقق من التسليم - انظر المرفق

Comments by: General consultant (systra)

- you must follow specs and design durg
- you must do leveling and lining
the compacted side slope of filling layer

INSPECTION RESULT

					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود	وليد عارف				
Contractor QA/QC*	XYZ	عبد الرحمن العلي	19-2-2024	11:30	A	
	H.M.C	محمد مشهور	19-2-2024	12:00	A	
GARB**						
Employers Representative	rehaled ale	[Signature]	19/2/2024		Arre	

UNIVERSAL INSPECTION REQUEST



مكتب أ.إ.ص.ن مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	REQ.NUM							
	وليد محمود	وليد محمود	22-2-2024	69							
Received by Employers Representative	[Signature]	[Signature]	UIR	C1	C2	C3	DD	MM	YY	HH	MM
				KP	SU	OT			24		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+920 TO 202+060		
	E=260168.4582 N=3136445.233	E=260160.9658 N=3136305.4382	
Inspection description/			
منطقة ردم منسوب (10.5-) متر from st (201+920) to st (202+060)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))

مستشار الاستشارات الهندسية
أ.إ.ص.ن مهدي

Comments by: General consultant (systra)

-you must follow specs and design details
-you must do leveling and lining
the compacted side slope & filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود	وليد محمود				
Contractor QA/QC*	XYZ	عبد الرحمن الوائلي	24-2-2024	3:30	A	
	H.M.C	محمد منعم فوزي	24-2-2024	11:00	A	
GARB**						
Employers Representative	Khaled ali	[Signature]	24/2/2024		Amr	

UNIVERSAL INSPECTION REQUEST



مكتب أديسن مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والمصممات الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أديسن مهدي للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	وليد طاي و وليد محمد		23-3-2024	74						
Received by Employers Representative	UIR		C1	C2	C3	DO	MM	YY	HH	MM
			KP	SU	OT			24		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+920 TO 202+060		
	E=260168.4582 N=3136445.233	E=260160.9658 N=3136305.4382	
Inspection description:			
منطقة ردم منسوب (10- متر) from st (201+920) to st (202+060)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
تم اتمام العمل في المنطقة (الطريق) - انظر المرفق	- you must follow specs and design drawings - you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد طاي و وليد محمد						
Contractor QA/QC*	XYZ	محمد علي (الطريق)	23-3-2024	12:15	A		
	H.M.C	محمد مشهور مؤذن	23/3/2024	12:00	A		
GARB**							
Employers Representative	Khaled ali		23/3/2024		Amr		

UNIVERSAL INSPECTION REQUEST



مكتب أ.د. حسن مهدي
للإستشارات الهندسية



الهيئة العامة للإعانة
SHARER



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name: Sign:	Date	REQ. NUM						
Received by Employers Representative	UIR	31-3-2024	75						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT			24		
CODE -1	CODE -2	CODE -3	CODE -4	CODE -5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+920 TO 202+060 E=260168.4582 N=3136445.233	E=260160.9658 N=3136305.4382
Inspection description: منطقة ردم منسوب (9.5) متر from st (201+920) to st (202+060)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))

Comments by: General consultant (systra)

تم فحص الموقع والتأكد من أن العمل مطابق للمواصفات المطلوبة.

-you must follow specs and design draw
-you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود محمد					
Contractor QA/QC*	XYZ عبد الرحمن الطرناوي		1-4-2024	12:00	A	
	H.M.C	محمود علي	31-3-2024	11:00	A	
GARB**						
Employers Representative	Khakdali		1/4/2024		Done	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name:  Sign: 	Date	REQ.NUM						
Received by Employers Representative	UIR	1-4-2024	76						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT			24		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description(		
منسوب (3-متر) from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (3-متر)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate



Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))

Comments by: General consultant (systra)

تأكد من التسليم طبقاً للمواصفات - القياسات
- you must follow specs and design dra
- you must do leveling and lining
the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	أبو عجلة					
Contractor QA/QC*	XYZ		1-4-2024	11:30	A	
	H.M.C		1-4-2024	11:00	A	
GARB**						
Employers Representative	Khaled ali		1/4/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours The Work described below will be complete and ready for inspection at planned time shown								
Contractor Company	أبو عجيبة للمقاولات العامة 157537			Designer Company*	DR .Hassan Mahdy (H.M.C)			
Issued by Contractor	Name	Sign	Date	Time				
			1-4-2024	77				
Received by Employers Representative	UIR 	C1	C2	C3	DD	MM	YY	
		KP	SU	OT			24	
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
From 200+876 To 202+376	201+920 TO 202+376	
	E=260168.4582	E=260129.6912
	N=3136445.233	N=3135991.0324
Inspection description: As-Built for Fill from st (201+920) to st (202+376)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time	
Planned Inspection Date	Planned Inspection Time
1/4/2024	

COMPLIANCE EVIDENCE Must be included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz)) 	Comments by: General consultant (systra)
--	--

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	أحمد	أحمد				
Contractor QA/QC*	XYZ	أحمد	2-4-2024	9:00	A	
	H.M.C	أحمد	2-4-2024	9:30	A	
GARB**						
Employers Representative						

