



المشروع القومي

القطار الكهربائي السريع (أكتوبر / أبو سمبل)

العينة العامة للطرق والكباري

المنطقة السادسة - بنى سويف

بخصوص : أعمال تنفيذ نفق تقاطع مسار
الخط الثاني للقطار الكهربائي السريع (أكتوبر / أبو سمبل)
مع الطريق الدائري الأقليمي عند كم ٣٢.٦٥٠ بنظام الخوازيق
السد المتلاصقة

السيد المهندس / رئيس قطاع التنفيذ والمناطق

تحية طيبة .. وبعد

بالإشارة الي المشروع عاليه تنفيذ شركه المنشات والمعدات الحديثه

عقد رقم ١٤٢٠ لسنة ٢٠٢٣/٢٠٢٤

تشرف بالإحاطة بالاتي :-

- المشروع عليه عدد (٢) سيارة محمله وهى غير متواجدة حتى تاريخ نهاية الاعمال
- المشروع ليس عليه عمالة محملة

برفاء التكرم بالإحاطة والتفضل بالتوجيه باللازم
وتفضلوا بقبول فائق الاحترام ،،،

تحرير في : ٩/٩/٢٠٢٤

رئيس الادارة المركزية

المنطقة السادسة (بني سويف)

مهندس /

طارق يوسف العزاز



بخصوص : مشروع أعمال تنفيذ نفق تقاطع مسار الخط الثاني للقطار الكهربائي السريع (٦ اكتوبر - الأقصر - أسوان - أبو سمبل) مع الطريق الدائري الأقليمي عند كم ٣٢,٦٥٠ بنظام خوازيق السندي المتلاصقة

تنفيذ: شركة المنشآت والمعدات الحديثة

عقد رقم: العقد رقم (١٤٢٠) لسنة ٢٠٢٣ / ٢٠٢٤

السيد المهندس / رئيس قطاع التنفيذ والمناطق

تحية طيبة وبعد ،،،

نتشرف بأن نرفق طيه المستخلص الجاري رقم (٢ جاري) عن العمليه عاليه من أصل وثلاثة صور وباقى المرفقات

برجاء التكرم بالأحاطة والتفضل بالتنبيه باللازم ،،،

وتفضلوا بقبول فائق الاحترام ،،،

المرفقات:

أصل المستخلص + عدد ٣ صورة

أصل إستماره ٥٠ ع.ح.

أصل الحصر

بيان الأعمال

رئيس الإداره المركزية

مهندس / طارق يوسف الجزار

معظم

مستخلص رقم (٠٢) جاري عن الفترة من بدء العملية حتى ٢٠٢٤/٠٨/١٠
تنفيذ شركة المنشآت و المعدات الحديدة

- مكتب جهاز الاتصال متواجدة
- التقليدي (المبدىء) - الاسيوى -
- الشهري (متواجد)
- البرنامج الزمني متواجد
- لوحات المشروع متواجدة
- المنهجوس متواجدون
- المسرفون متواجدون
- المعدات متواجدة
- وسائل تأمين شاملة المرور متواجدة
- الحالات الاشدية والتحذيرية متواجدة
- ثقافة التأمين متواجدة

- ويفعل السامي متراجدة
مدد (٢٠) سيرة غير متوارد
عن تاريخ كل من إسلام

96

فرض جنبه اقر بان هذا الحساب صحيح و مضبوط وأن المبالغ المقيدة ظهرية و قدرها سبق صرفها للمقاول،	فرض جنبه تحريرا في/...../.....
على الحساب / نهائيا غير الواردة يخص بشرطه ملحوظة المذكورة:	يدفع للمقاول مبلغ 

رق والكباري
مدير عام المشروعات
مختار التوقيع :

اسم العميل :

عملية / مشروع القطار الكهربائي السريع من اكتوبر الى ابو سمبل / أعمال انشاء العمل الصناعي تقاطع مسار القطار السريع
مع طريق الدائرى الاقليمى بالكيلو (٣٢+٦٥٠) بنظام خوازيق السندي المتلاصقة

اسم المقاول :

العقد رقم (١٤٢٠) لسنة ٢٠٢٤/٢٠٢٣

مستخلص رقم (٠٢)

رقم ومقدار التصدية :

بند الميزانية :

شركة المنتجات والمعدات الحديثة

فرش

قيمة الاعمال

جنية

قرش

بيان المتصروف من المقاول

٦٩٦٨٦٤٠

٨٤

بيان الاعمال التي تمت الان

٦٩٦٨٦٤٠

١١

محـ وـ زـ

٦٩٦٨٦٤٠

٤٤

مـصـرـ بـصـرـفـهـ

٦٩٦٨٦٤٠

١١

سـابـقـ صـرـفـهـ

٦٩٦٨٦٤٠

٤٤

مـسـتـحـقـ صـرـفـهـ

٦٩٦٨٦٤٠

٤٤

جمـلـةـ الـاسـقـطـاعـاتـ

٦٩٦٨٦٤٠

٤٤

صـافـىـ الـعـبـاـغـ الـمـسـتـحـقـ

٦٩٦٨٦٤٠

٤٤

الـشـيكـاتـ

٦٩٦٨٦٤٠

٤٤

حساب مصلحة الضرائب

٦٩٦٨٦٤٠

٤٤

حساب التأمينات الاجتماعية

٦٩٦٨٦٤٠

٤٤

الـصـافـىـ النـهـانـىـ

٦٩٦٨٦٤٠

٤٤

جملة الاستقطاعات

٥٥ تأمين اعمال

٦٦٦٦٥ جنية

٨٠ فرش

رسم الدمنة

٩٧٩٥٥٢

٢٠

حساب الارباح التجارية والصناعية

١٦٦٦١٥

٩٠

تكليف معمل

—

—

١٥ مصاريف ادارية

—

—

٤٠ صريره قيمة مضافة

—

—

— [٢٢٥٠٠] - يتم بيع مائمه وخرير الفوج
رفيق عدم تواجد (٢٠٢٢) مسمى لمنه (٦٥٠) ميو

مدير عام الشئون المالية والإدارية

روجع حسابياً،

رقم	بيان العمل	الكمية بالمقاييس	الوحدة	الأعمال المنفذة			بيان العمل
				مقدار الأعمال المائية تمت خلال المدة	مقدار الأعمال السليق أجراوة	مقدار الأعمال التي تمت الان	
أعمال الجسات والحفير والردم							
٨							بالنور الطولى تغطية جسات في جميع انواع التربة عدا الصخريه وعلى ان يتم تحديد (Q unconfined) لكل طبقة طبقاً لتقدير التربة والبنيد يشمل تقل ملائكته الجهات وجريعه متضمنها إلى الموقع كالتلوف المحيطة بالموقع ودفع جميع الكارات اللازمة من مكان تنقلها الى الموقع ثم تنقلها الى الموقع كالتلوف المحيطة بالموقع ودفع جميع الكارات الاشراف وكل ما يلزم لتهي العمل كاملاً طبقاً لاصول الصناعة والشروب والمواصفات وتعليمات المهندس المشرف.
٩	جاهد تربة أقل من كجم/سم³ و RQD أقل من % 60	١٥٠,٠٠	م.م³	١٢٧٥٠	١٥٠,٠٠	١٤٢٥٠	جاهد
أعمال الخوازيق والاختباراتها :-							
١٠							بالبعد تقل خارجي (وجه قبلي) وتركيز وفك ماكينة الخوازيق الى الموقع ثم ذفتها ونقلتها (خارج الموقع) بعد الانتهاء من كافة الاعمال والسعر يشمل المعدات والادوات اللازمة لفك و التركيب بالموقع و كل تفاصيل التفريز والبنيد شامل مما جبعه طبقاً لاصول الصناعة والمواصفات و تعليمات المهندس المشرف.
١١		٢,٠٠	عدد	٠,٨٥	٠,١٠	٠,٩٥	جاهد
١٢							بالنور الطولى تغطية خوازيق بـ قطر ٢٠ سم وحمل التشغيل طبقاً لدراسات والمواصلات مع استخدام سمنت بورتلاندي عادي او مقاوم للتأثيرات طبقاً لتأثير الاستشاري بحيث لا يقل محتوى الاسمنت عن كجم المتر المكعب ولا رتبة درجة المقاومة بـ ٤٨ يوم من التقطيع على ان يتم ازالة الخوازيق الطبعي ونقل مخلفات الحفر والتكسير الى المقلب العمومي والسعر يشمل جميع اعمال التهوية كاملاً والبنيد شامل مما جبعه طبقاً لاصول الصناعة والرسومات والمواصفات و تعليمات المهندس المشرف.
١٣							كامل طبل الخازق
١٤	خوازيق بـ قطر ٢٠ سم	٢٠٥٦٠٠	م.م³	٢٩٠٦٥	٢٩٠١٤	٤٨٥,٧٧	جاهد
١٥							بالنور الطولى تغطية خوازيق سند بـ قطر ٨٠ سم من المتنبوات طبقاً لدراسات والمواصلات على ان يتم جميع الاعمال طبقاً للشروط والمواصفات الفنية والرسومات وحسب تعليمات المهندس المشرف.
١٦	أعمال خوازيق بـ قطر ٨٠ سم	٤,٤٨٤,٠٠	م.م³	١٦٣٤	٢١٢	٧٧٨٦	جاهد
١٧							بالبعد عمل شجرة تحمل على خارق غير اعمال ووضع العمل المتصبغي (%) ٤٠ - ولفلة تشمل الالواح المعدنية الموقعة واجهة عمل الشجرة المائية او خلاصه على جزءه التحمل الوصول الى حمل التحمل المطلوب وازالة مدة اخرى بعد الانتهاء من تجربة التحمل باستخدام المعدات اللازمة والسعر يشمل جميع الكارات اللازمة لارقام الارقام وتزويده الازفة لتجربة التجربة و اداء الاشراف واعادةها من جهاز الاشراف وكل ما يلزم لتهي العمل تهوا تماماً طبقاً لاصول الصناعة والشروب والمواصفات الفنية وطبقاً و تعليمات المهندس المشرف. البنيد غير شكل خارق التجربة وغير شامل حديد التسلسلي.
١٨							باتلن توريد وتركيب ورس حديد تسليح B500 DWR لزادة المرونة (Durility) في الحديدة المستخدم مقاومة الاهتزازات الشائكة عن السرعات المائية للطاير لزوج جميع المعاشر الاشتراكية الكوري طوال حتى ١٦ ميليجير والسعر يشمل التقنيق طبقاً للوحات والرسومات التفصيفية "A5" والتفاصيل وكل المعدات اللازمة مثل الحديد والجذب المشكل داخل الموقع والمعدات الالزامية لتوسيب وقطع الجديه واسفل كل ما يلزم لتهي العمل تهوا كاملاً طبقاً لاصول الصناعة و تعليمات المهندس المشرف
التشويشات							
١٩	باتلن توريد وتركيب ورس حديد تسليح B500 DWR	١,٨٩٠,٠٠	طن	١٢٠,٣٩	٨٨٠,٨١	٢٠٣,٤٠	جاهد
٢٠							

الهيئة العامة للطرق والكباري
مدير المشروع
م/ الشافعى مددوح السيد

~~Frank~~

شركة بيت الهندسة
مشروع تطوير مسار
الخطار السريع مع الطريق الدائري
الإقليمي والإقليمي ٣٣ + ١٥٠ - ٦٤٣٧٢٩٥٨

Transmittal Of Quantity Survey

Date: 12/08/2024

Request no: TQS-MSE-AHE-00002-REV.00

Project No. & Title: Intersection between Regional Ringroad and HSR @ ST. 32+650

Employer:



Engineer:



Contractor:



1. Document type

- Quantity Survey

2. Submittal details

Item no.	Description of items submitted/ quantity	Ref.	Contract doc. Ref. & compliances
	حصر مستخلص جاري ٢ حتى ٢٠٢٤/٨/١٠		

These are transmitted for:

- Your information Approval Review & comment Other

Submitted by: Eng / Kareem Wahdan

Signature:



3. Engineer's Representative comments:

Approved

Approved as noted

Revise & resubmit

Rejected

Others

تم إعداد وتحاليل المطالبات
المقدمة

Signature:



Date: 12/08/2024

Applying this stamp does not constitute acceptance of the Contract or constitute authorization of any change to Contract Document.



بالناء الطولى تنفيذ جلسات فى جميع انواع التربية عدا المخبرية وعلى أن يتم تحديد (Q unconfined) لكل طبقة طبقاً لتقرير التربية والبند يشمل نقل ماكينة الجسات وجميع مستلزماتها إلى الموقع منها كانت الظروف المحيطة بالموقع ودفع جميع الكارتات اللازمة من مكان نقلها إلى الموقع ثم نقلها خارج الموقع بعد الانتهاء من كافة الاعمال واستخراج التقارير واعتمادها من جهة الاشراف وكل ما يلزم لتهو العمل كاملاً طبقاً لأصول الصناعة والشروط والمواصفات وتليمين المهندس المشرف.

اسم المجموعة : اعمال الجسات و الحفر و الردم

رقم اليد: _____

مهندس الاستشاري




بيان الاعم

رقم الب

10

اسم المجموعة: اعمال الخوارق و الاختبارات

مهندس الاستشارى





شركة بيت الهندسة
Arab House of Engineering
Lahcen and Partners

وزارة النقل
الهيئة العامة للطرق
للهواء والآبار والثوار
والكباري
المنطقة السادسة

عملية / مشروع القطار الكهربائي السريع من اكتوبر الى ابو سليم / أعمال إنشاء نفق تقاطع مسار القطار السريع مع الطريق
الداورى الأقليمى بالكيلو (٣٢+٦٥٠)

بالمتر الطولى تنفيذ خوازيق بـ ٤٠٠ سم وحمل التشغيل طبقاً للرسومات والمواصفات مع استخدام استنت بورتلاندى عادى او مقاوم للتغيرات طبقاً
لتقرير الاستشارى بحيث لا يقل محتوى الاستنت عن ٤٥٠ كجم للمتر المكعب ولا تقل رتبة الفرسانة بعد ٢٨ يوم من الصب بالطبيعة عن ٣٥٠ كجم/سم٢
على ان يتم ازالة روؤس الخوازيق الطبا ونقل مخلفات الحفر والتكسير الى المقلب العمومي والسرير يشمل الاحوال المساجحة (واتساع لا يشمل حديد
السلنج) ونها العمل تهوا كاملاً والبند شامل مما جمبعه طبقاً لأصول الصناعة والرسومات والمواصفات وتعليمات المهندس المشرف شامل اختبارات
الموجات الصوتية على كامل طول الخازوق

بيان الاختبارات:


رقم الاختبار:

اسم المجموعة: خوازيق الخرسانة ٢

الرقم:

رقم الخازوق	المحور	النوع	متسوب الأرض الطبيعية	متسوب قاع الحفر	طول الخازوق	توقيت الصب
TEST PLIE	-	CONCRETE	101.34	66	35.34	26/02/2024
P-02	A01	CONCRETE	100	66	34	03/05/2024
P-03	A01	CONCRETE	100	66	34	08/05/2024
P-04	A01	CONCRETE	100	66	34	05/05/2024
P-05	A01	CONCRETE	100	66	34	09/05/2024
P-06	A01	CONCRETE	100	66	34	06/05/2024
P-07	A01	CONCRETE	100	66	34	12/05/2024
P-08	A01	CONCRETE	100	66	34	07/05/2024
P-20	A02	CONCRETE	100	66	34	22/05/2024
P-22	A02	CONCRETE	100	66	34	27/05/2024
P-21	A02	CONCRETE	100	66	34	27/06/2024
P-23	A02	CONCRETE	100	66	34	28/06/2024
P-24	A02	CONCRETE	100	66	34	10/06/2024
P-25	A02	CONCRETE	100	66	34	01/08/2024
P-26	A02	CONCRETE	100	66	34	12/06/2024
الإجمالي						
511.34						



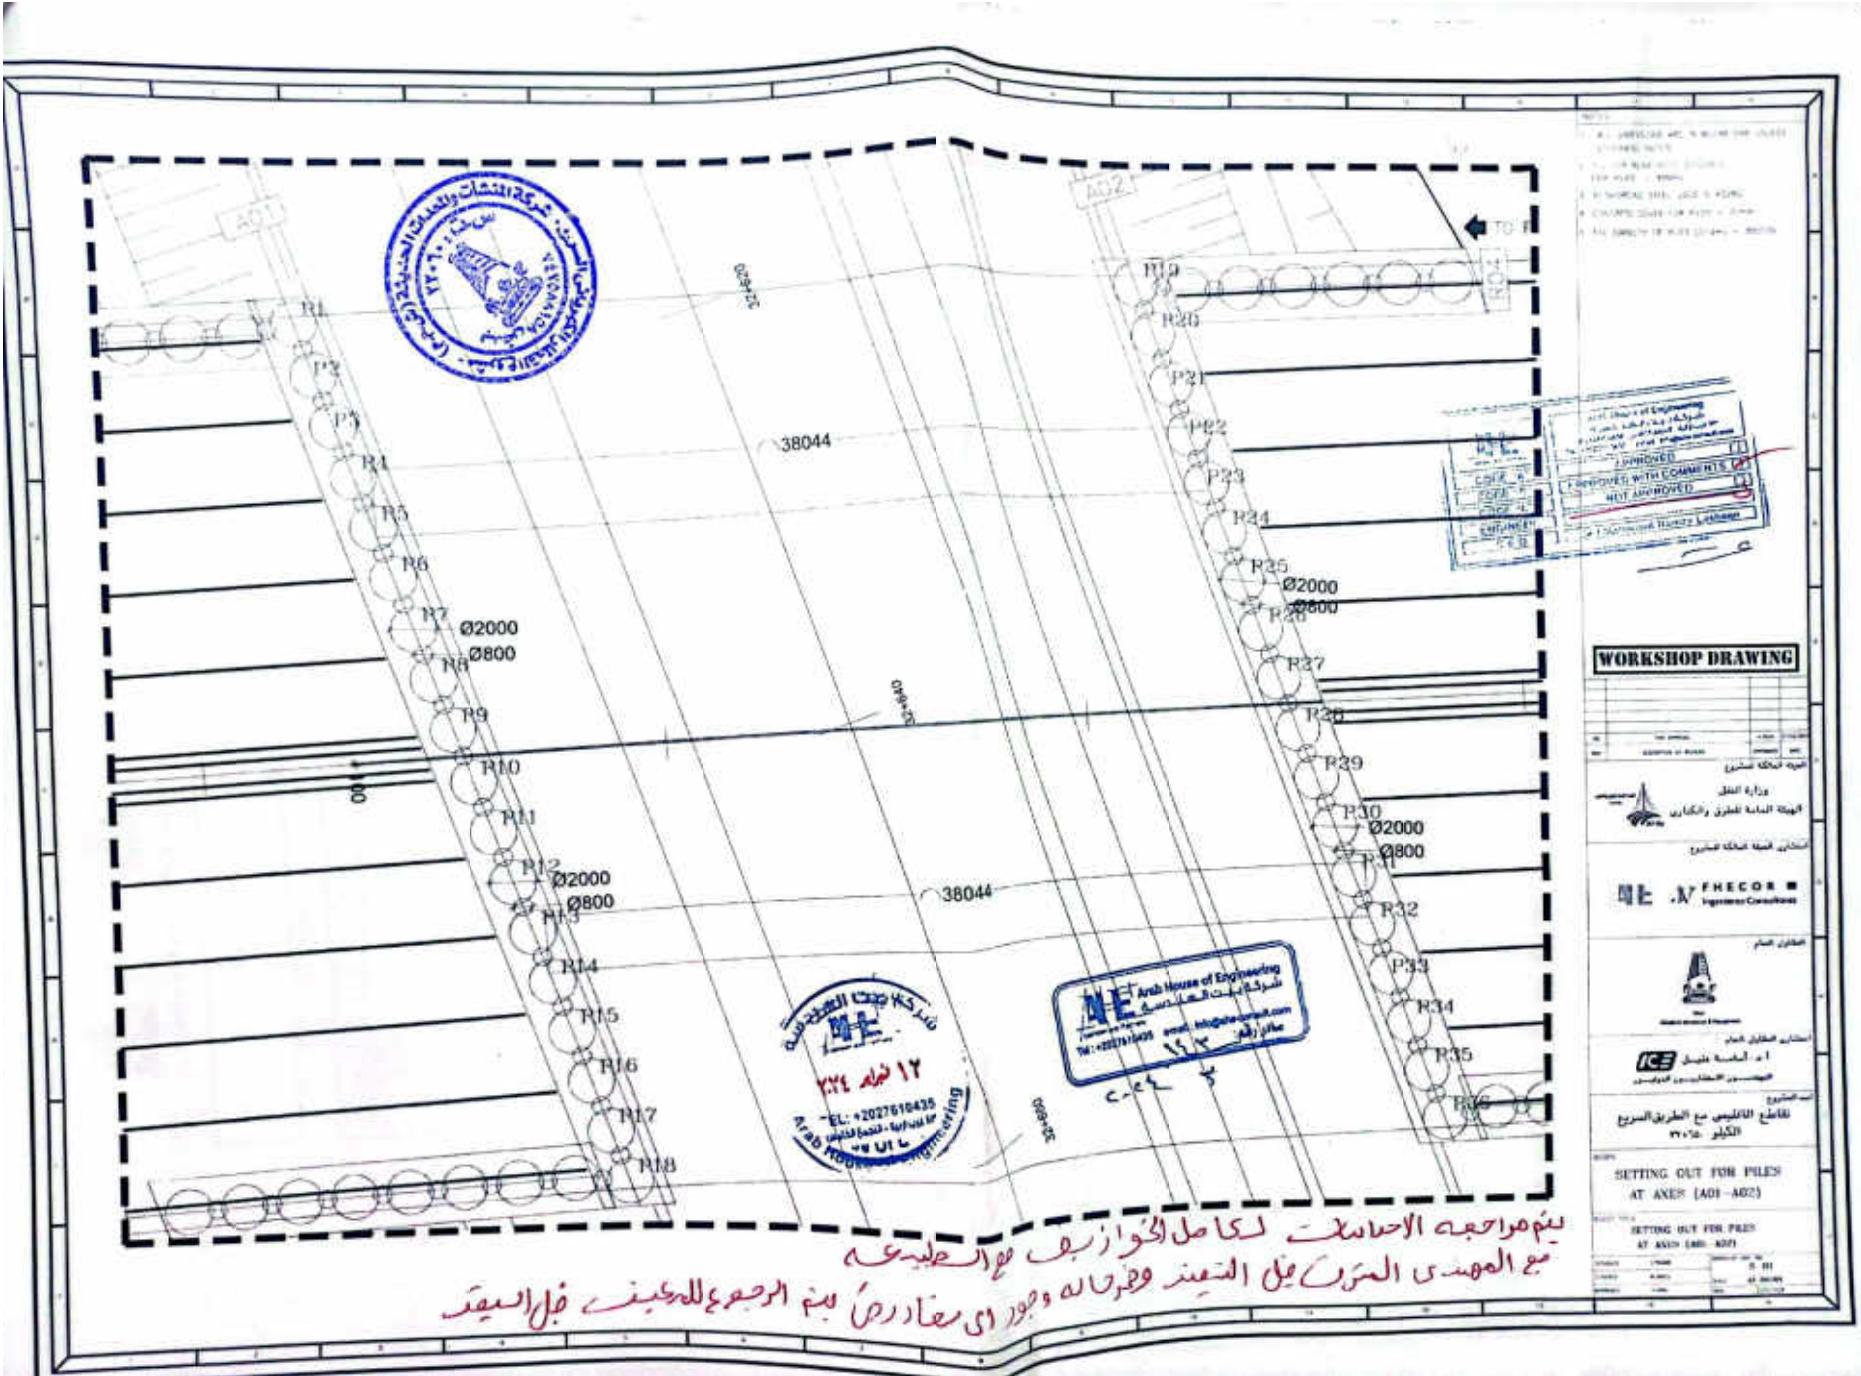



www.IBM.com/ibm



عملية / مشروع القطار التهرباني السريع من المكتوبر إلى أبو سليم / أعمال إنشاء نفق تقاطع مسار القطار السريع مع الطريق الدائري الأفقي بالكتلتين (٢٢٥ + ٦٥٠) م





الى اعلاه
بيان الاعمال
قلم الاعمال


رقم الخازوق	المحور	النوع	منسوب الأرض الطبيعية	متوسط قاع الحفر	طول الخازوق	توقيت الصب	اسم المجموعة	بيان خوازيق سد بفتر ٨٠ سم من الينتوبيات طبقاً للرسومات والمواصفات على أن تم جمع الأعمال طبقاً للشروط والمواصفات التالية والرسومات وحسب تعليمات المهندس المشرف.
1	P01	BENTONITE A00	100	66	34	25/04/2024		
2	P-02	BENTONITE A01	100	66	34	29/04/2024		
3	P-03	BENTONITE A01	100	66	34	26/04/2024		
4	P-04	BENTONITE A01	100	66	34	29/04/2024		
5	P-05	BENTONITE A01	100	66	34	27/04/2024		
6	P-06	BENTONITE A01	100	66	34	30/04/2024		
7	P-07	BENTONITE A01	100	66	34	28/04/2024		
8	P-08	BENTONITE A01	100	66	34	30/04/2024		
9	P-18	BENTONITE A02	100	66	34	12/05/2024		
10	P-19	BENTONITE A02	100	66	34	15/05/2024		
11	P-20	BENTONITE A02	100	66	34	12/05/2024		
12	P-21	BENTONITE A02	100	66	34	17/05/2024		
13	P-22	BENTONITE A02	100	66	34	13/05/2024		
14	P-23	BENTONITE A02	100	66	34	17/05/2024		
15	P-24	BENTONITE A02	100	66	34	14/05/2024		
16	P-25	BENTONITE A02	100	66	34	19/05/2024		
17	P-35	BENTONITE A01	100	66	34	08/08/2024		
18	P-36	BENTONITE A01	100	66	34	06/08/2024		
19	P-37	BENTONITE A01	100	66	34	08/08/2024		
20	P-38	BENTONITE A01	100	66	34	05/08/2024		
21	P-39	BENTONITE A01	100	66	34	07/08/2024		
22	P-40	BENTONITE A01	100	66	34	05/08/2024		
23	P-41	BENTONITE A01	100	66	34	06/08/2024		
24	P-42	BENTONITE A01	100	66	34	04/08/2024		

816,00

جمالی



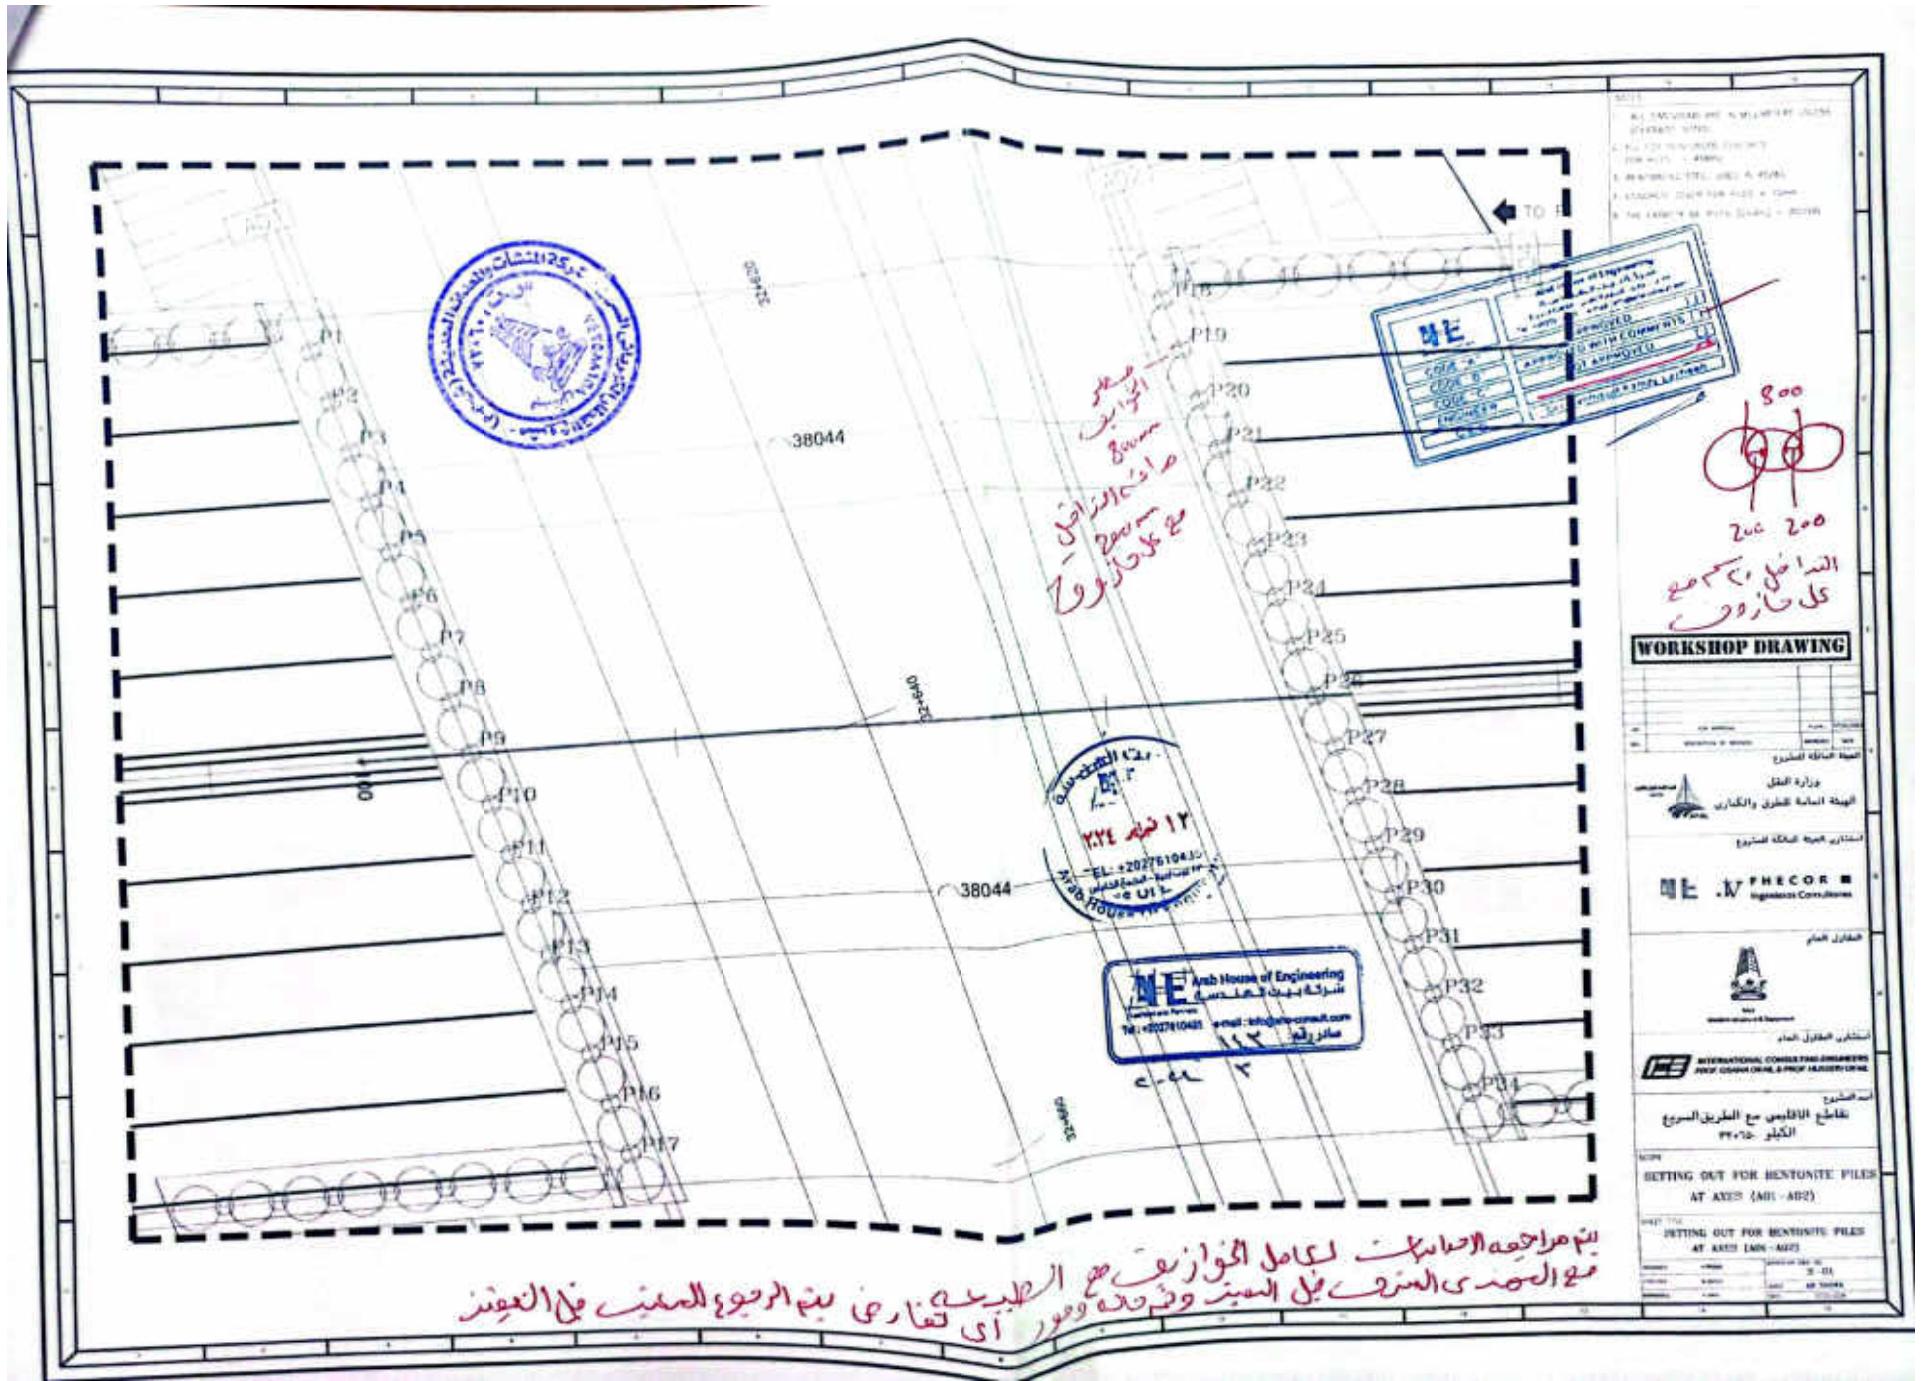

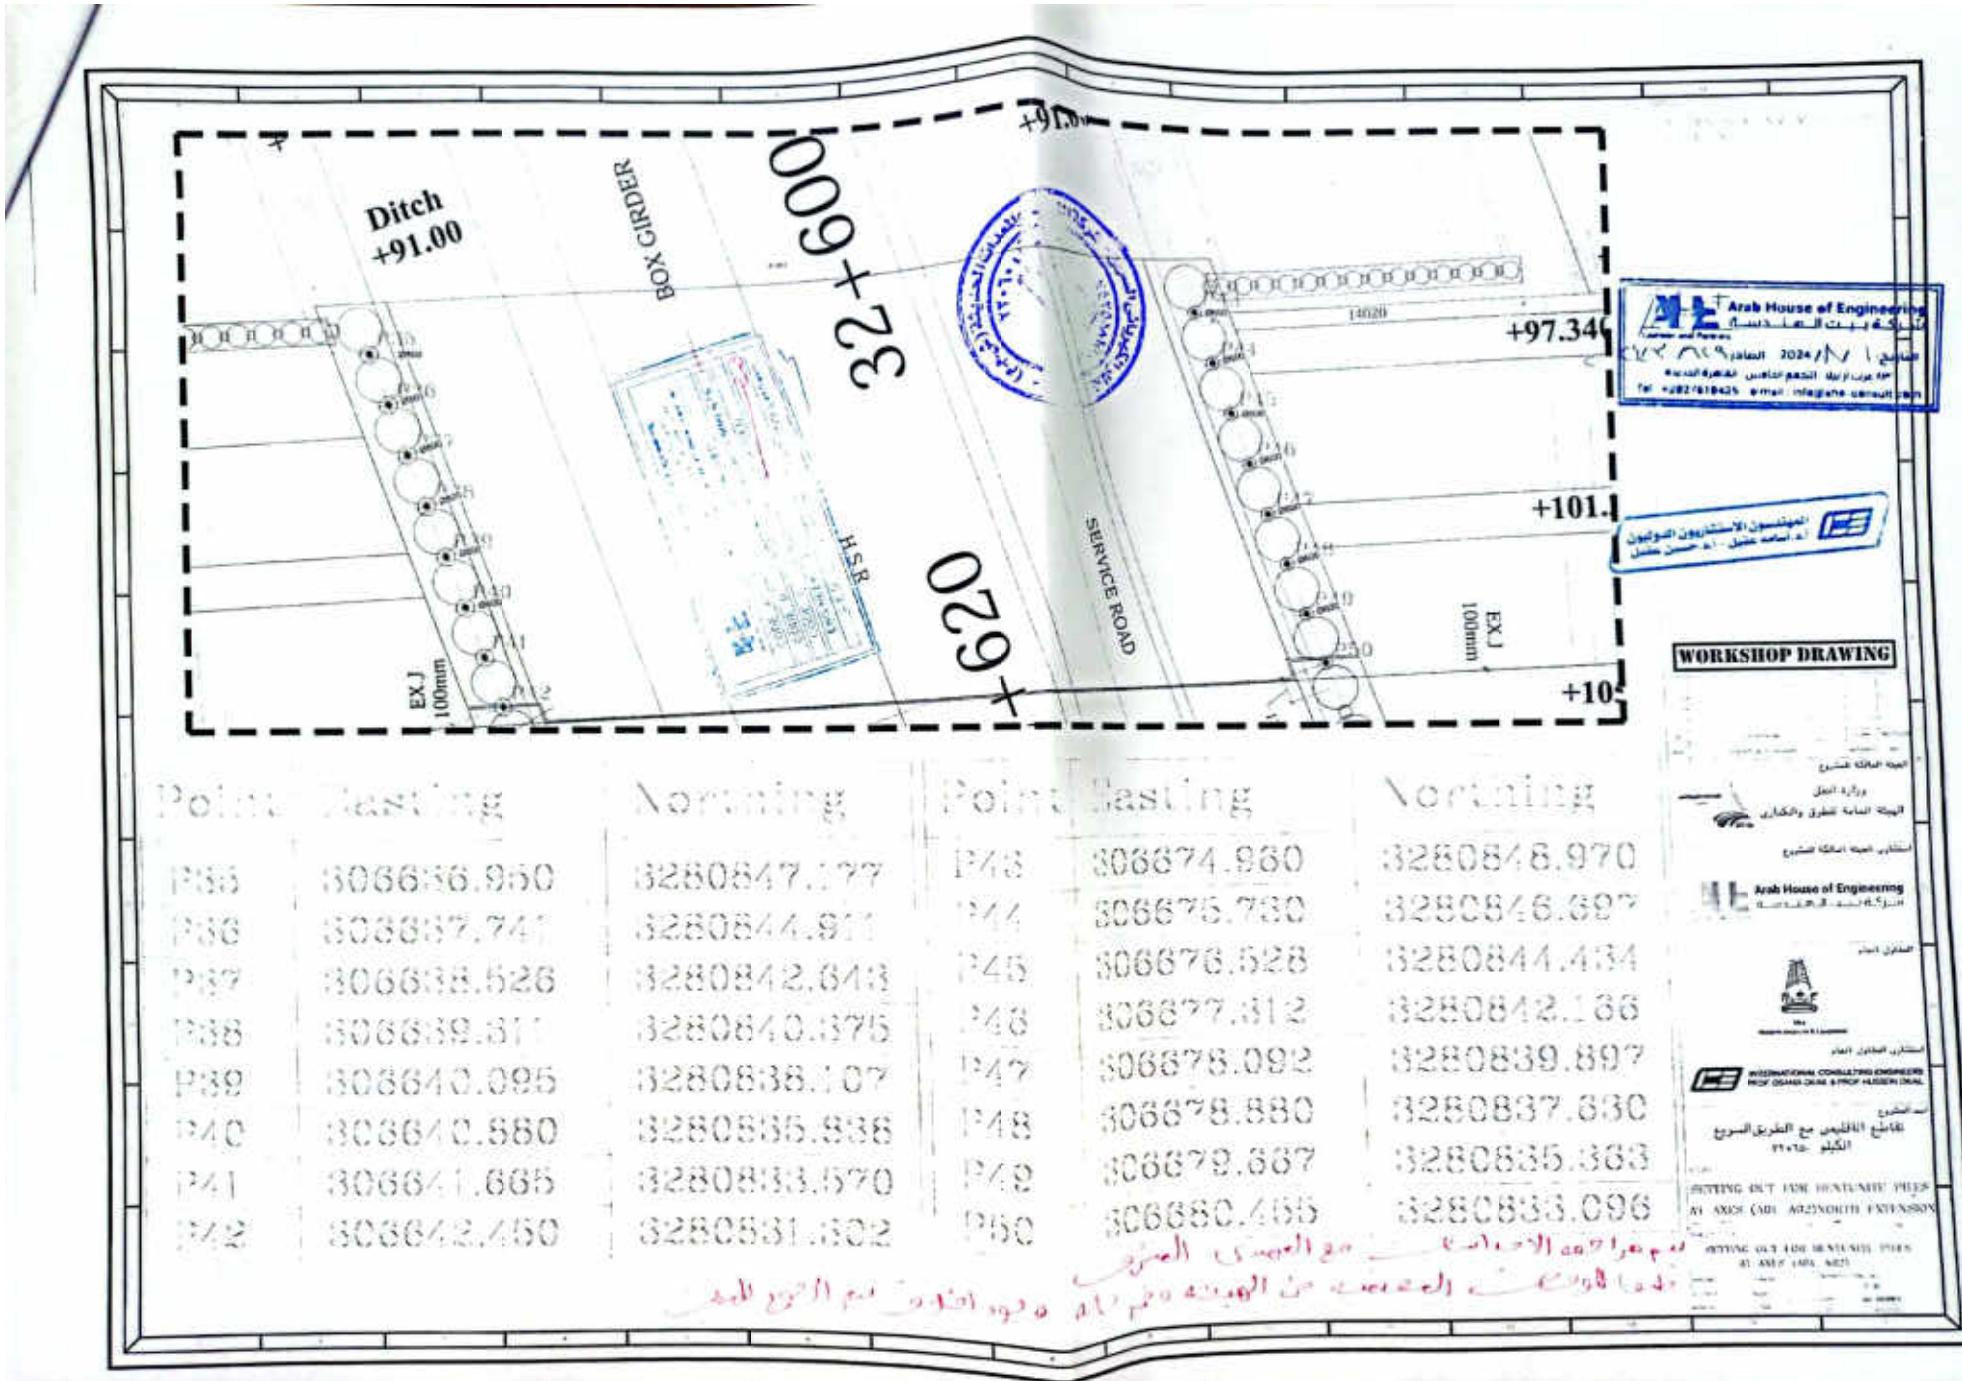

عملية / مشروع القطار الكهربائي السريع من اكتوبر إلى أبو سعيل /
أعمال إنشاء نفق تقاطع مسار القطار السريع مع الطريق الدائري
الإقليمي، بالكيلو (٣٦٤٦٥) ٣٢٤٦٥

بالالعدد عمل تجربة تحمل على خازوق غير عامل وبضعف العمل التصميمي (٢٠٠٪) والفلنة تشمل الالواح المعدنية الموقته واجهزه القباب والمعدات والبلوکات الخرسانية او خلافه اعلى تجربة التحميل للوصول الى حمل التهرب المطلوب وازانته مرة اخري بعد الانتهاء من تجربة التحمل باستخدام المعدات اللازمة والسعر يشتمل على جميع الكارتات اللازمة لزوم اعمال الردم وتوريد الاجهزه الضروريه لاجراء التجربة واعداد التقارير واعتمادها من جهاز الاشراف وكل ما يتلزم لنهاي الاعمال نهيا تماما طبقا لاصول المصانع والشروط والمواصفات الفنية وطبقا وتعليمات المهندس المشرف. البند غير شامل خازوق التجربة وغير شامل حديد التسلیح

اسم المجموعة : أعمال الخوازيق والاختباراتها

12

بيان الاعمال:

رقم المذكرة:

جامعة الامارات

الاجمالي



卷之三



Submittal Of Documents

Date: 10/06/2024

Request no: SOD-MSE-AHE-0000033_REV.00
Project No. & Title: Intersection between Regional Ringroad and HSR @ ST. 32+650

Employer:		Engineer:	Arab House of Engineering	Contractor:	
-----------	--	-----------	---------------------------	-------------	--

1. Document type

- | | | | |
|--|-------------------------------------|---|---|
| <input type="checkbox"/> Material samples | <input type="checkbox"/> Catalogues | <input checked="" type="checkbox"/> Tests | <input type="checkbox"/> Technical sheets |
| <input type="checkbox"/> Manufacturer certificates | <input type="checkbox"/> Schedules | <input type="checkbox"/> Other | |

2. Submittal details

Item no.	Description of items submitted/ quantity	Ref.	Contract doc. Ref & compliances
	Non-working Pile load test result		

These are transmitted for:

- Your information Approval Review & comment Other

Submitted by:

Eng. / Ahmed Mohammed EL-sheikh

Signature:

3. Engineer's Representative comments:

- Approved
 Approved as noted
 Revise & resubmit
 Rejected
 Others

Signature:

Date: 11/7/2024

Approval shall not relieve Contractor of his liabilities under the Contract or constitute authorization of any change to Contract Document



حربية / مشروع القطار الكهربائي السريع من المنيا إلى أبو سمبل / أعمال إنشاء نفق تقاطع مسار القطار السريع مع الطريق الدائري الاقليمي بالكليل (٣٢+٥٠)

بالطن توريد وتربيط ورص حديد تسليح DWR B500 لزيادة المرونة (Ductility) في الحديد المستخدم لمقاومة الاهتزازات الناتجة عن السرعات العالية للتقطير تزوم جميع العناصر الانشائية للتكوبري اطوال حتى ١٢ م بالبر والسرع يشمل التقطيع طبقاً للوحات والرسومات التقنية "As Built" والاختبارات وكل لمعدات اللازمة لنقل الحديد وال الحديد المشكل داخل الموقع والمعدات اللازمة لتوصيب وقطع وتشكيل ورفع الحديد والسرع يشمل كل ما يتلزم لنهو العمل نهوا كاملاً طبقاً لأصول الصناعة وتعليمات المهندسين المشرف

بيان الاعمال:


اسم المجموعة : الحديد يجمع أنواعه

22

رقم الـ

نوع المحور	رقم الخازوقي	النوع	منسوب الأرض الطبيعية	طول الحفر	وزن التسلیح	توقيت الصب
-	TEST PLIE	CONCRETE	101.34	66	14.754	25/04/2024
P-02	2	CONCRETE	100	66	14.089	29/04/2024
P-03	3	CONCRETE	100	66	14.089	26/04/2024
P-04	4	CONCRETE	100	66	14.089	29/04/2024
P-05	5	CONCRETE	100	66	14.089	27/04/2024
P-06	6	CONCRETE	100	66	14.089	30/04/2024
P-07	7	CONCRETE	100	66	14.089	28/04/2024
P-08	8	CONCRETE	100	66	14.089	30/04/2024
P-20	9	CONCRETE	100	66	14.089	12/05/2024
P-21	10	CONCRETE	100	66	14.089	15/05/2024
P-22	11	CONCRETE	100	66	14.089	12/05/2024
P-23	12	CONCRETE	100	66	14.089	17/05/2024
P-24	13	CONCRETE	100	66	14.089	13/05/2024
P-25	14	CONCRETE	100	66	14.089	17/05/2024
P-26	15	CONCRETE	100	66	14.089	14/05/2024

الاجمالي





وزارة النقل
الهيئة العامة للطرق والجسور
الم منطقة السادسة

أعمال إنشاء نفق تقاطع مسار القطار السريع مع طريق الدائرى الأقليمي بالكيلو (٣٢+٦٥٠)



2.0m PILE RFT. DETAILS

Bar No.	Bar Diameter	Shape	Bar Length	No. of Bars	Unit weight kg/m	Total Weight kg	Total weight ton							Notes
							<input type="checkbox"/> 10	<input type="checkbox"/> 12	<input type="checkbox"/> 16	<input type="checkbox"/> 18	<input type="checkbox"/> 22	<input type="checkbox"/> 25	<input type="checkbox"/> 32	
1	32	——— 12.00	12	60	6.313	4545.36	0.000	0.00	0.000	0.00	0.000	0.000	4.55	
2	22	——— 4.00	4	60	2.984	716.16	0.000	0.00	0.000	0.00	0.716	0.000	0.00	
3	25	———	12	60	3.853	2774.16	0.000	0.00	0.000	0.00	0.000	2.774	0.00	
4	22	——— 12.00	12	60	2.984	2148.48	0.000	0.00	0.000	0.00	2.148	0.000	0.00	
5	22	○○	6	10	2.984	179.04	0.000	0.00	0.000	0.00	0.179	0.000	0.00	
6	22	○○	6	10	2.984	179.04	0.000	0.00	0.000	0.00	0.179	0.000	0.00	
7	22	○○○	6	13	2.984	232.75	0.000	0.00	0.000	0.00	0.233	0.000	0.00	
8	16	~~~~~	12	175	1.528	4313.72	0.000	0.00	3.314	0.00	0.000	0.000	0.00	
Total Steel Weight FOR 2.0m PILE							0.000	0.000	3.314	0.000	3.455	0.00	4.545	
											14.088			





Mse
Modern structure & Equipment




وزارة الموارد
المياه العامة للشرق والشمال
المنطقة السادسة


احصل انشاء نفق تقاطع مسار القطار السريع مع طريق الدائرى الاقليمي بالكتيلو (٣٢+٦٥٠)

2.0m Test PILE RFT. DETAILS

Bar No.	Bar Diameter	Shape	Bar Length	No. of Bars	Unit weight kg/m	Total Weight kg	Total weight ton						Notes
							□ 10	□ 12	□ 16	□ 18	□ 22	□ 25	
1	32	12.00	12	60	6.313	4545.36	0.000	0.00	0.000	0.00	0.000	0.000	4.55
2	22	3.34	3.34	60	2.984	597.99	0.000	0.00	0.000	0.00	0.598	0.000	0.00
3	25	12.00	12	60	3.853	2774.16	0.000	0.00	0.000	0.00	0.000	2.774	0.00
4	22	12.00	12	60	2.984	2148.48	0.000	0.00	0.000	0.00	2.148	0.000	0.00
5	22	Ring	6	10	2.984	179.04	0.000	0.00	0.000	0.00	0.179	0.000	0.00
6	22	Ring	6	10	2.984	179.04	0.000	0.00	0.000	0.00	0.179	0.000	0.00
7	22	Ring	6	13	2.984	232.75	0.000	0.00	0.000	0.00	0.233	0.000	0.00
8	16	12.00	12	15	1.578	3313.80	0.000	0.00	3.314	0.00	0.000	0.000	0.00
9	25	1.7	1.7	1.7	3.853	783.07	0.000	0.00	0.000	0.00	0.000	0.000	0.00
Total Steel Weight FOR 2.0 m PILE						14753.69	0.000	0.000	3.314	0.000	3.337	3.357	14.515
											14.754		



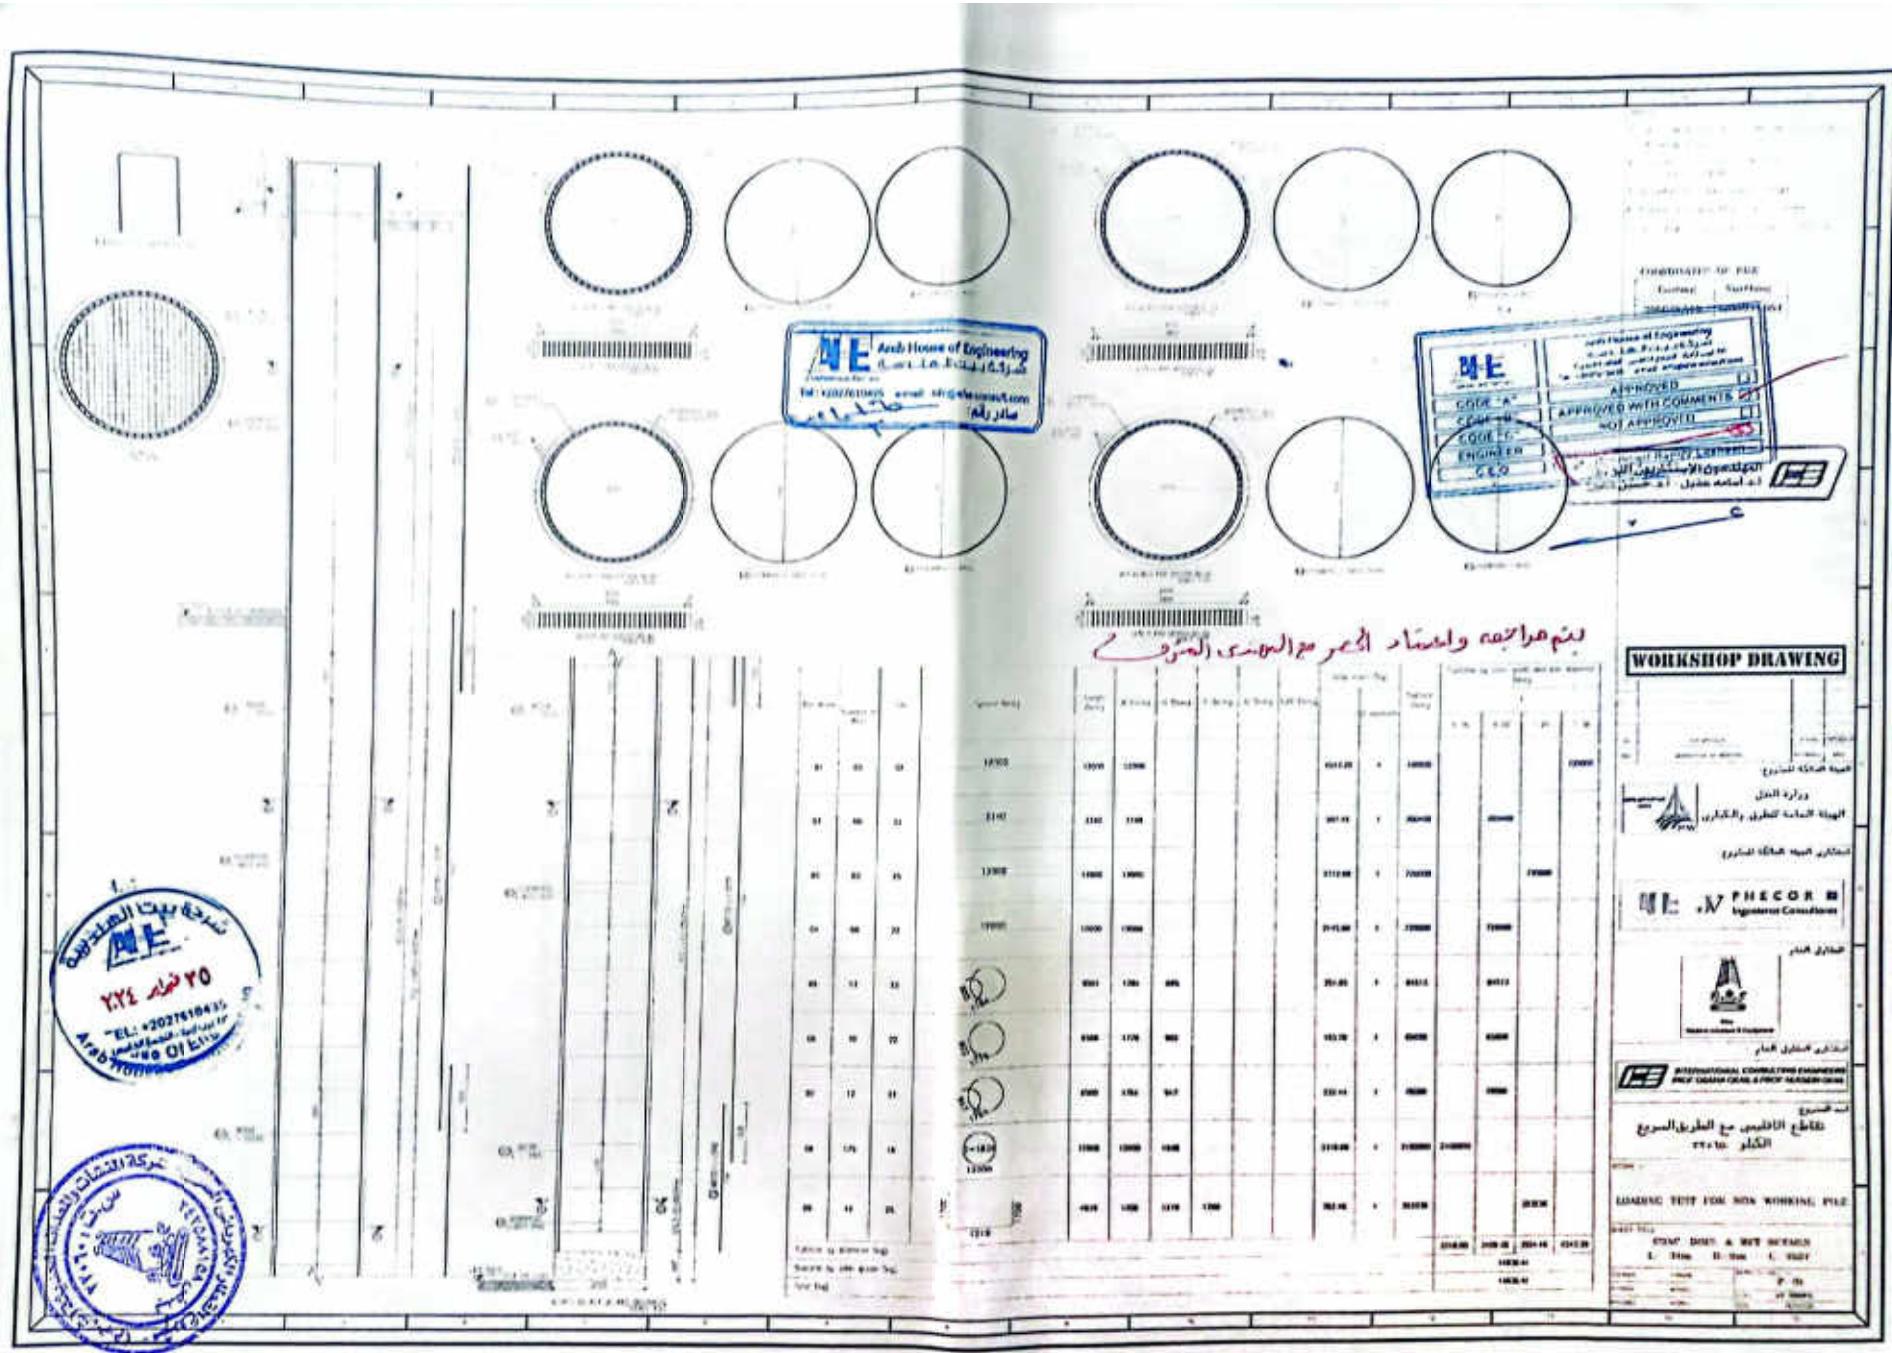

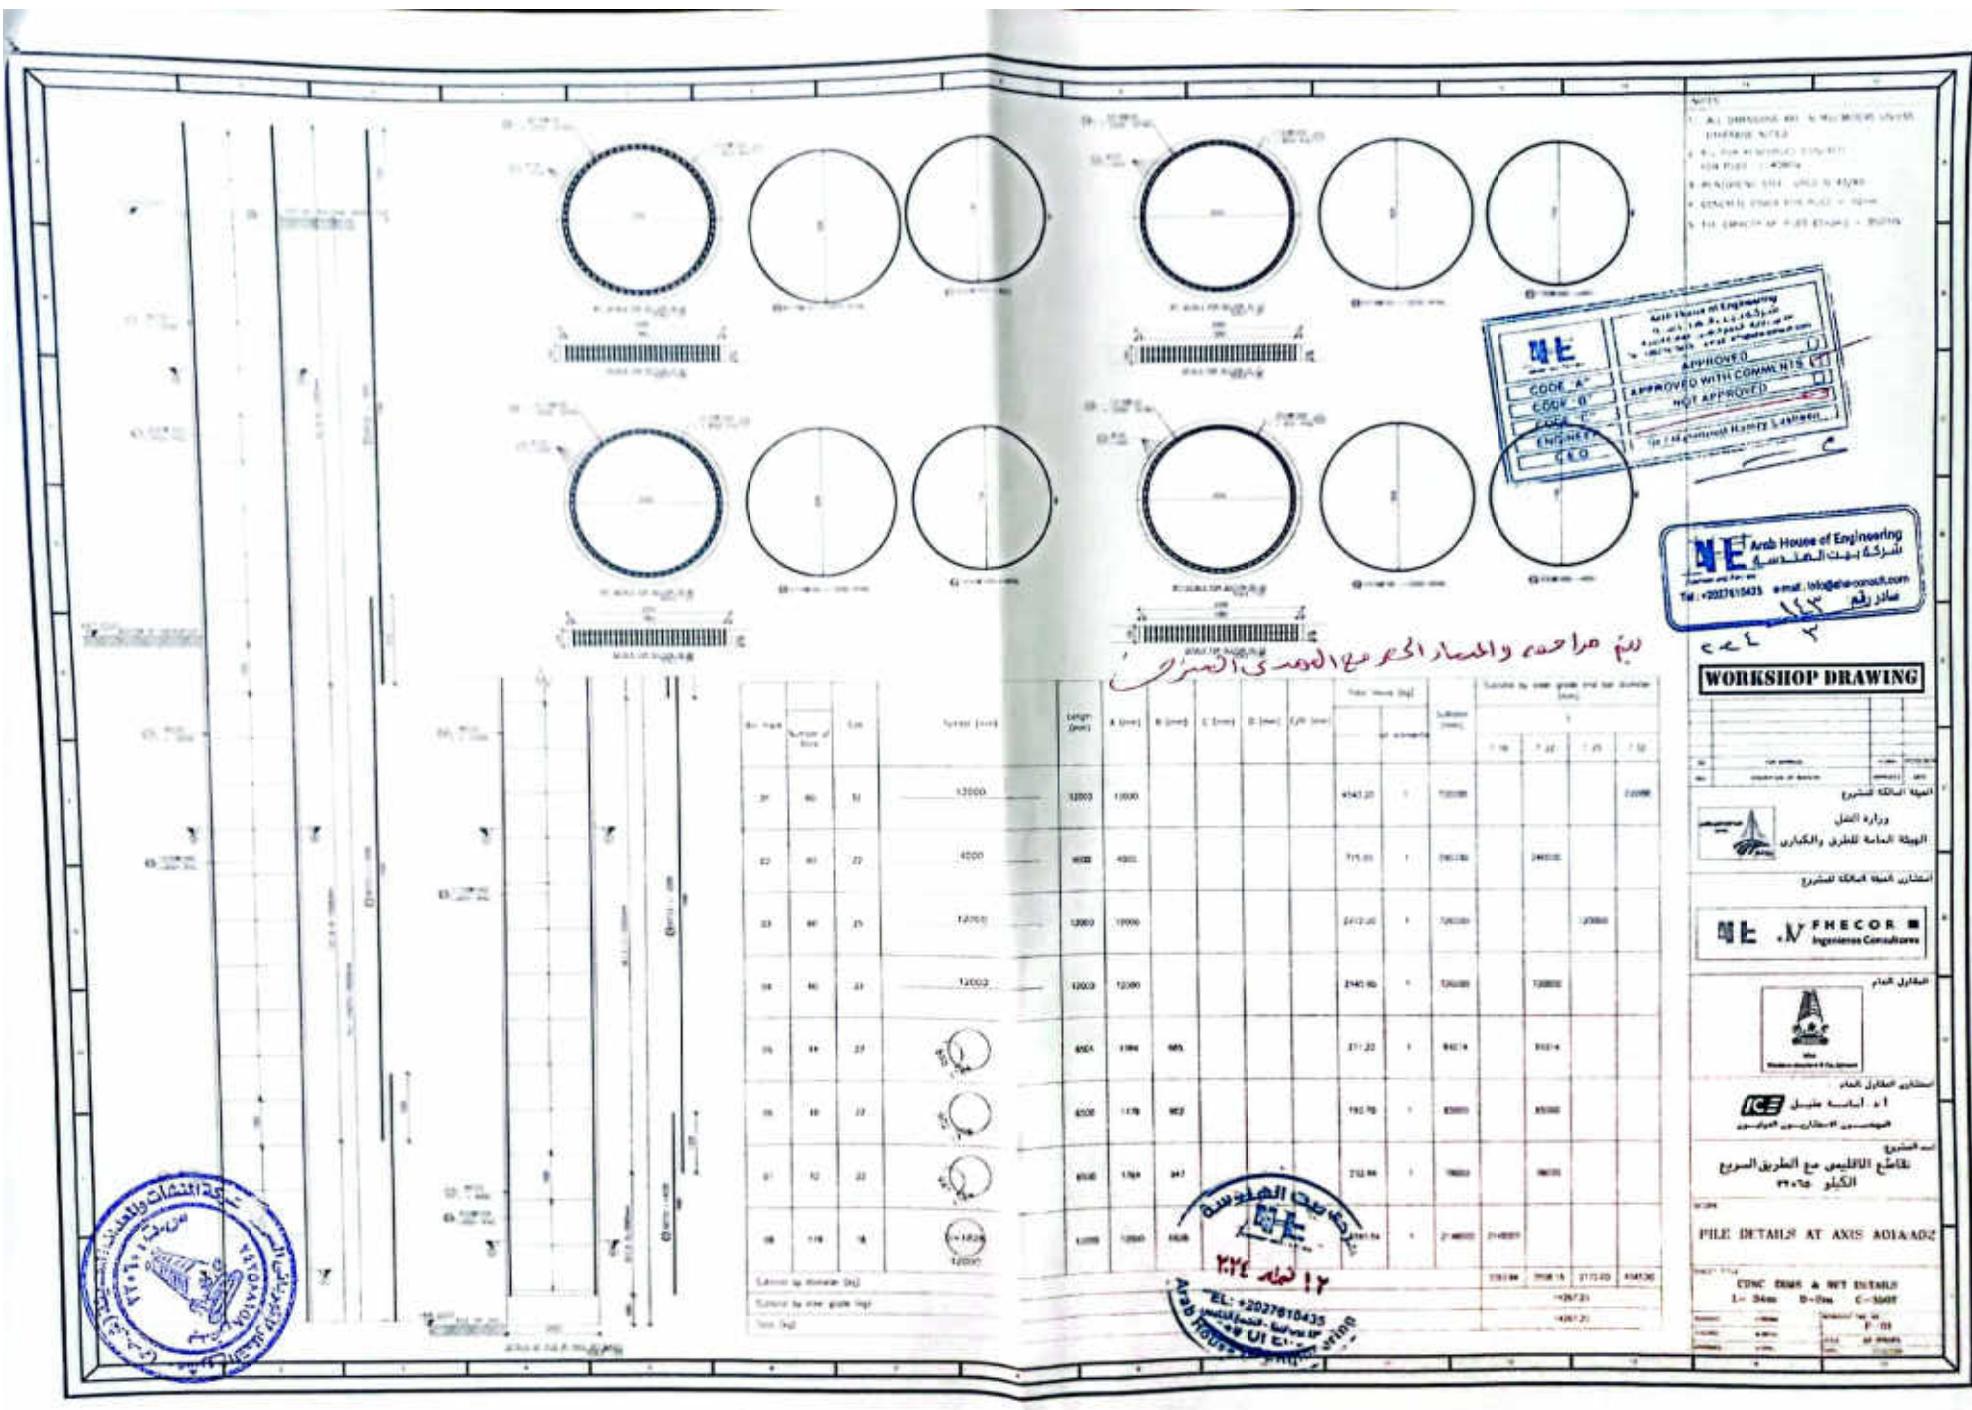



Mse
Modern structure & Equipment



Arab House of Engineering
شركة بيت الهندسة

اللجنة العامة للطرق والجسور
(GARBI)



محضر حصر تشوينات

مشروع نفق تقاطع مسار الخط الثاني للقطار الكهربائي السريع مع الطريق الدائري الإقليمي

عند كم ٣٢+٦٥٠

انه في يوم ١٨ / ١٢ / ٢٠٢٤ الموافق ١٨ / ١٢ / ٢٠٢٤ وبحضور السادة الآتي أسماؤهم :-

- ١- م/ إيهاب محي الدين هلال - مدير المشروع - مكتب الاستشاري - (شركة بيت الهندسة) .
- ٢- م/ أحمد عادل إسماعيل - مدير الموقع - الشركة المنفذة - (شركة المنشآت والمعدات الحديثة) .

تم معاينة كميات حديد التسليح المشوون بموقع المذكور أدناه ، ولا يتم نقل أي كمية من الحديد المشوون إلا بمعروفة مهندس الإستشاري ، والمحافظة على الحديد مسؤولية المقاول

القطر (مم)	#32	#25	#22	#16
الوزن (طن)	٩١٠.٦٦٥	٩٠.٧٥٥	٥٨.٧٠٦	٧٦.٣٦٤
الإجمالي (طن)				٣٢٥.٤٨٤ Ton



التوقيعات :-

١- م/ إيهاب محي الدين هلال

٢- م/ أحمد عادل إسماعيل



Submittal Of Documents

Date: 29/07/2024

Request no: SOD-MSE-AHE-0000041_REV.00

Project No. & Title: Intersection between Regional Ringroad and HSR @ ST. 32+650

Employer:		Engineer:	 Arab House of Engineering شركة هندسة عربية	Contractor:	
-----------	---	-----------	---	-------------	---

Document type					
<input type="checkbox"/> Material samples <input type="checkbox"/> Manufacturer certificates <input type="checkbox"/> Catalogues <input type="checkbox"/> Schedules <input checked="" type="checkbox"/> Tests <input type="checkbox"/> Other <input type="checkbox"/> Technical sheets					
2. Submittal details					
Item no.	Description of items submitted/ quantity	Ref.	Contract doc. Ref. & compliances		
	Compressive Strength Test Result 28 day For Elements Casted From 22/05/2024 To 27/06/2024 & PourCards concrete piles P21 & P23 & P24 & P26				
These are transmitted for:					
<input type="checkbox"/> Your information		<input checked="" type="checkbox"/> Approval	<input checked="" type="checkbox"/> Review & comment	<input type="checkbox"/> Other	
Submitted by: Eng. / Emad Eldeen Abdullah		Signature: 			
3. Engineer's Representative comments:					
<input checked="" type="checkbox"/> Approved <input type="checkbox"/> Approved as noted <input type="checkbox"/> Revise & resubmit <input type="checkbox"/> Rejected <input type="checkbox"/> Others					
Signature: 	Date : 29/7/2024				

Approval shall not relieve Contractor or his facilities under the Contract or constitute authorization of any change to Contract Document



pile ID	Qs-CP				
	Concreting				
	casting				
	from	To	period(hours)	Cast date	Compressive 28 days
MSE-A02-CP-21	26/06/2024 21:25	27/06/2024 01:57	4:32:00	26/6/2024	24/07/2024
MSE-A02-CP-23	27/06/2024 22:37	28/06/2024 01:57	3:20:00	27/6/2024	25/07/2024
MSE-A02-CP-24	10/06/2024 12:16	10/06/2024 16:15	3:59:00	10/6/2024	08/07/2024
MSE-A02-CP-26	12/06/2024 02:13	12/06/2024 05:47	3:34:00	12/6/2024	10/07/2024

COMPRESSIVE STRENGTH OF CONCRETE SPECIMENS EN-12390-3

Date	24-7-2024	Class of Concrete	C400/450 OPC
Client	المنشآت و المعدات الحديثة	Project	تنمية نفق تفاصي مسار الخط الثاني للقطار الكهربائي السريع (6 المتر - الأقصر - أسوان - أبو سليم) مع الطريق الدائري الائتمي عدد كم (650+32) بنظام خوازيق المسنة المتلاصقة
Location	Bani Sweif	Consultant	شركة بيت الهندسة (د/ محمود لاشين)
Form No :		Element	Pile-21 (H)

Cubes No.	Casting Date	Testing Date	Weight gm	Unit Weight Kg/m ³	Load KN	Compressive strength cube (KG/CM ²)	Average (KG/CM ²)	Age(Days)	
1	26-6-2024	24-7-2024	8430	2498	1550	702.7	701.9	28	
2			8460	2507	1624	736.2			
3			8630	2557	1471	666.9			
4			8390	2486	1594	722.6	685.3		
5			8450	2504	1529	693.1			
6			8380	2483	1412	640.1			

Remarks

The Results Test For Compressive Strength After 28 days Comply With The criteria of strength as per BS EN 206.

THE RESULTS IS

COMPLY NOT COMPLY

Tested by :	four technology
Checked by:	Y.A.S
Lab manager	

Approved by Dr Adel Elkordi

CODE Co 008-Modern-Pile-F-37-A



COMPRESSIVE STRENGTH OF CONCRETE SPECIMENS EN-12390-3

Date	25-7-2024	Class of Concrete	C400/450 OPC
Client	المنشآت و المعدات الحديثة	Project	تنمية نفق تقاطع مسار الخط الثاني للطاقة الكهربائية السريع (6) المترور -الإقصر -أسوان -أبو سمبل) مع الطريق الدائري الألبي عدد كم (650+32) بـ نظام خوازيق السندي المتلاصقة
Location	Bani Sweif	Consultant	شركة بيت الهندسة (د / محمود لاشين)
Form No :		Element	Pile-23 (H)

Cubes No.	Casting Date	Testing Date	Weight gm	Unit Weight Kg/m ³	Load KN	Compressive strength cube (KG/CM ²)	Average (KG/CM ²)	Age(Days)	
1	27-6-2024	25-7-2024	8355	2476	1557	705.8	699.5	28	
2			8370	2480	1593	722.2			
3			8395	2487	1479	670.5			
4			8385	2484	1478	670.0	718.1		
5			8500	2519	1652	748.9			
6			8485	2514	1622	735.3			

Remarks

The Results Test For Compressive Strength After 28 days Comply With The criteria of strength as per BS EN 206.

THE RESULTS IS

COMPLY NOT COMPLY

Tested by :	
Checked by:	
Lab manager	

Approved by Dr. Adel Elkordi

CODE Co 008-Modern-Pile-F-38-A



COMPRESSIVE STRENGTH OF CONCRETE SPECIMENS EN-12390-3

Date	10-7-2024	Class of Concrete	C400/450 OPC
Client	المنشآت و المعدات الحديثة	Project	تنفيذ شفاف تقاطع مسار الخط الثاني للقطار الكهربائي السريع (6 اكتوبر - الاقصر - أسوان - ابو سمبل) مع الطريق الدائري الاقليمي عد ٦٣ (650+32) ينظم حوازيق السندي المتلاصقة
Location	Bani Sweif	Consultant	شركة بيت الهندسة (د/ محمود لاشين)
Form No :		Element	Pile-26

Cubes No.	Casting Date	Testing Date	Weight gm	Unit Weight Kg/m ³	Load KN	Compressive strength cube (KG/CM ²)	Average (KG/CM ²)	Age(Days)	
1	12-6-2024	10-7-2024	8370	2480	1543	699.5	670.9	28	
2			8250	2444	1536	696.3			
3			8160	2418	1361	617.0			
4			8212	2433	1556	705.4	674.0		
5			8320	2465	1479	670.5			
6			8285	2455	1425	646.0			

Remarks

The Results Test For Compressive Strength After 28 days Comply With The criteria of strength as per BS EN 206.

THE RESULTS IS

COMPLY NOT COMPLY

Tested by:		Approved by: Dr Adel Elkordi
Checked by:		
Lab manager		
sites No-1		
CODE Co 008-Modern-Pile-F-27-B		



COMPRESSIVE STRENGTH OF CONCRETE SPECIMENS EN-12390-3


Date	8-7-2024	Class of Concrete	C400/450 OPC
Client	المنشآت و المعدات الحديثة	Project	تنفيذ نفق تقاطع مسار الخط الثاني للقطار الكهربائي السريع (6 أكتوبر -القاهرة -اسوان -ابو سمبل) مع الطريق الدائري الاقليمي عد كم (650+32) ينضم خوازيق المسند المتلاصقة
Location	Bani Sweif	Consultant	شركة بيت الهندسة (د/ محمود لاشين)
Form No :		Element	Pile-24 (H)

Cubes No.	Casting Date	Testing Date	Weight gm	Unit Weight Kg/m ³	Load KN	Compressive strength cube (KG/CM ²)	Average (KG/CM ²)	Age(Days)	
1	10-6-2024	8-7-2024	8275	2452	1455	659.6	687.7	28	
2			8365	2479	1515	686.8			
3			8380	2483	1581	716.7			
4			8390	2486	1286	583.0	644.2		
5			8205	2431	1459	661.4			
6			8310	2462	1518	688.2			

Remarks

the results are temporarily accepted in 12days as guidance but is not taken into consideration till results of 28 days

THE RESULTS IS COMPLY NOT COMPLY

Tested by:		Approved by Dr Adel Elkordi
Checked by:		
Lab manager		

sites No-1

CODE Co 008-Modern-Pile-F-28-B



Submittal Of Documents

Date: 29/07/2024

Request no: SOD-MSE-AHE-0000043_REV.00

Project No. & Title: Intersection between Regional Ringroad and HSR @ ST. 32+650

Employer:		Engineer:	Arab House of Engineering	Contractor:	
-----------	--	-----------	---------------------------	-------------	--

Document type					
<input type="checkbox"/> Material samples <input type="checkbox"/> Catalogues <input type="checkbox"/> Manufacturer certificates <input type="checkbox"/> Schedules <input checked="" type="checkbox"/> Tests <input type="checkbox"/> Other <input type="checkbox"/> Technical sheets					
2. Submittal details					
Item no.	Description of items submitted/ quantity نتائج اختبارات معملية بالموقع : 2024 / 06 / 26 (رمل) 2024 / 06 / 26 (سن)	Ref.	Contract doc. Ref. & compliances		
These are transmitted for: <input checked="" type="checkbox"/> Your information <input checked="" type="checkbox"/> Approval <input checked="" type="checkbox"/> Review & comment <input type="checkbox"/> Other					
Submitted by:	Eng. / Emad Eldeen Abdullah	Signature:			
3. Engineer's Representative comments:					
<input type="checkbox"/> Approved <input checked="" type="checkbox"/> Approved as noted <input type="checkbox"/> Revise & resubmit <input type="checkbox"/> Rejected <input type="checkbox"/> Others	<p>تم اعتماد النتائج الخامسة بالرمل . على أن يتم إعداد و إخبار الفوج العمودي مدخل ١٢.٥ (سن)</p>				
Signature:	Date : 29/7/2024				


Approval shall not release Contractor of his liabilities under the Contract or constitute authorization of any change to Contract Document



RESULTS OF SIEVE ANALYSIS OF FINE AGGREGATE
ASTM C 136 &

materials finer than no.200 in aggregate by washing ASTM C 117

Date	16-07-24	Client	المنشآت و المعدات الحديثة
Delivery Date	16-07-24	source	ابو عجوة
Testing Date	26-06-24	FORM NO	2577

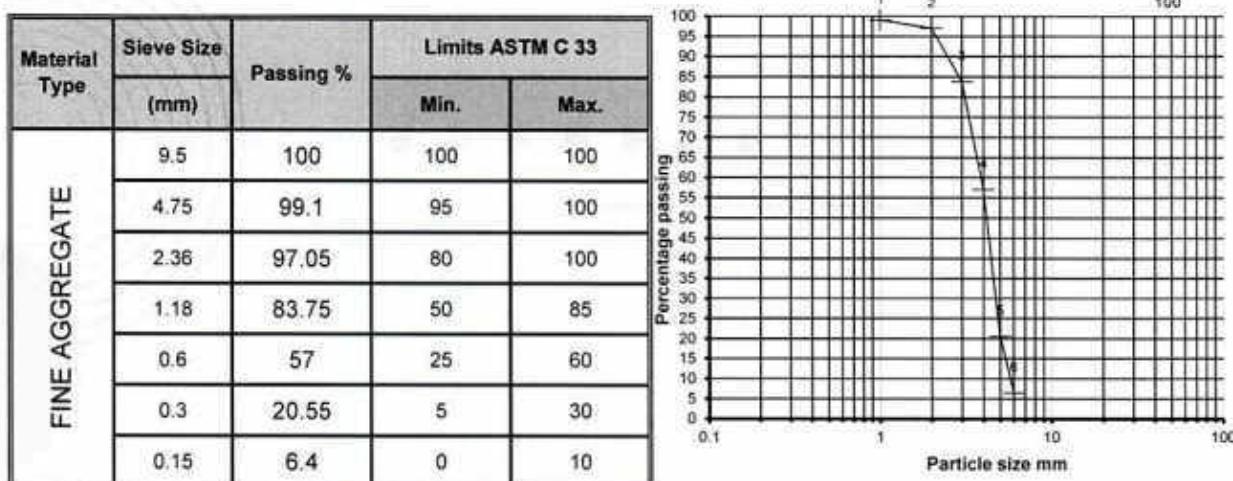

- Fineness modulus: Limits ASTM C 33: (2.3 to 3.1)

materials finer than no.200 in aggregate by washing

Test	Results
Percentage of material finer than Sieve size 75 mm (No.200)	2.1

ASTM C 33 limits:

Shall not exceed 3 % (case of concrete subject to abrasion)

Shall not exceed 5 % (all other concrete)

Note:

The Test Results is (Comp. - Not Comply) with Spec. limits

Tested by :		Approved by Dr. Adel Elkordi
Checked by:		
Lab manager		

CODE Ag 001-F-155

sites No-1




RESULTS OF SIEVE ANALYSIS OF COARSE AGGREGATE
ASTM C 136 &

materials finer than no.200 in aggregate by washing ASTM C 117

Date:	16-07-24	Client:	المنشآت و المعدات الحديثة
Delivery Date	16-07-24	source	عنتا ready rocks
Testing Date	26-06-24	FORM NO.	2577

Material Type	Sieve Size (mm)	Passing %	Limits	
			Min.	Max.
COARSE AGGREGATE (1)	19	100	100	100
	12.5	78.04	90	100
	9.5	42.51	40	70
	4.75	0.55	0	15
	2.36	0.24	0	5

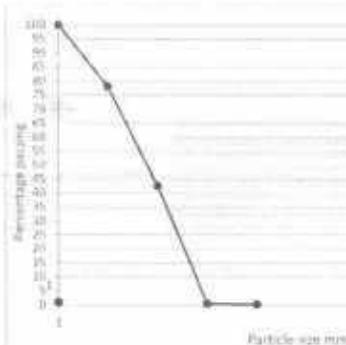

materials finer than no.200 in aggregate by washing

Test	Aggregates
	Size.1
Percentage of material finer than Sieve size 75 mm (No.200)	0.5

ASTM C 33 limits

The amount of percentage of material finer than sieve size 75 µm (No.200)

The Test Results is (Comply) Not Comply) with Spec. limits

Tested by:	
Checked by:	
Lab manager	 sites No-1

CODE: Ag 002-F-157-A

Approved by Dr Adel Elkordi



Submittal Of Documents

Date: 30/07/2024

Request no: SOD-MSE-AHE-0000044_REV.01

Project No. & Title: Intersection between Regional Ringroad and HSR @ ST. 32+650

Employer:		Engineer:		Contractor:	
-----------	--	-----------	--	-------------	--

1. Document type					
<input checked="" type="checkbox"/> Material samples <input checked="" type="checkbox"/> Manufacturer certificates		<input type="checkbox"/> Catalogues <input type="checkbox"/> Schedules		<input checked="" type="checkbox"/> Tests <input type="checkbox"/> Other	<input type="checkbox"/> Technical sheets
2. Submittal details					
Item no.	Description of items submitted/ quantity	Ref.	Contract doc. Ref. & compliances		
	التقارير الشهرية بصلحيات خاملت : (سن ٢٠٢٤ - رمل - اسمنت - مادة - مياه) الخاصة بالخلطة الخرسانية لشهر ٦				

These are transmitted for:

Your information Approval Review & comment Other

Submitted by: Eng. / Emad Eldeen Abdullah Signature:

3. Engineer's Representative comments:	
<input checked="" type="checkbox"/> Approved <input type="checkbox"/> Approved as noted <input type="checkbox"/> Revise & resubmit <input type="checkbox"/> Rejected <input type="checkbox"/> Others	<p>تم إعتماد التقارير الشهرية لأحذية بارات الصلبة (أسمنت ورمل) (اسمنت ماء ورمل)</p> <p></p>
Signature:	Date: 30/7/2024

Approval shall not relieve Contractor of his liabilities under the Contract or constitute authorization of any change to Contract Document.





Contractor

المنشآت و المعدات الحديثة

Project

تنمية قرى فقاطن مسلسل الخط الثاني للطريق الكروبي السريع (6) أكبر الاخضر - سلوان - ابو سمبل مع الطريق الدائري
الخطي عد كم (650+32) بنظام خوارزمي المستند الملاحي



Ref. ITP No

Date

ITP-Ba-01

27-5-2024

Discipline

Concrete Materials

Location

Bani Sweif


NO.	Work Phase (Description of Inspection/Testing)		Codes and Standards	Acceptance Criteria	Frequency	Record (Test Report)	Remarks
	Materials Tests						
1	Fine Aggregate	Fine Aggregate Grading	ASTM C136	Conforms to ASTM C33 requirement	Every 5000 m ³ delivered to site Source change & max Monthly	Material Test Report	
2		Water absorption for fine aggregate	ASTM C 128	Conforms to ASTM C 128 (2.0% maximum)	Every 5000 m ³ delivered to site Source change & max Monthly	Material Test Report	
3		Specific gravity for fine Aggregate	BS 812	Conforms to B.S 812 (Minimum 2.6)	Every 5000 m ³ delivered to site Source change & max Monthly	Material Test Report	
4		Unit Weight of Fine Aggregates	ASTM C 29	-	Every 5000 m ³ delivered to site Source change & max Monthly	Material Test Report	
5		Clay lumps and friable particles / Clay, silt & dust content of Fine Aggregates	ASTM C 142	Conforms to ASTM C33 requirement (5% maximum)	Every 5000 m ³ delivered to site Source change & max Monthly	Material Test Report	
6		Organic impurities in fine aggregate	ASTM C 40	Conforms to ASTM C 40 (Lighter than Standard)	Every 5000 m ³ delivered to site Source change & max Monthly	Material Test Report	
7		Chemical analysis for fine aggregate	BS 812	Conforms to B.S 812	Every 5000 m ³ delivered to site Source change & max Monthly	Material Test Report	
8	Coarse Aggregate	Coarse Aggregate Grading	ASTM C136	Conforms to ASTM C33 requirement	Every 5000 m ³ delivered to site Source change & max Monthly	Material Test Report	
9		Specific gravity for Coarse Aggregate	BS 812	Conforms to B.S 812 (Minimum 2.6)	Every 5000 m ³ delivered to site Source change & max Monthly	Material Test Report	
10		Water absorption for Coarse Aggregate	ASTM C 127	Conforms to ASTM C 127 (2.5% maximum)	Every 5000 m ³ delivered to site Source change & max Monthly	Material Test Report	
11		Unit Weight of Fine Aggregates	ASTM C 29	-	Every 5000 m ³ delivered to site Source change & max Monthly	Material Test Report	
12		Clay lumps and friable particles / Clay, silt & dust content of Fine Aggregates	ASTM C 142	Conforms to ASTM C33 requirement	Every 5000 m ³ delivered to site Source change & max Monthly	Material Test Report	
13		Abrasion by Los Angeles Machine	ASTM C 131	Conforms to ECP (35% maximum)	Every 5000 m ³ delivered to site Source change & max Monthly	Material Test Report	
14		Flakiness Index	BS EN 933-1	Conforms to BS EN 933-1 (25% maximum)	Every 5000 m ³ delivered to site Source change & max Monthly	Material Test Report	
15		Elongation	BS 812	Conforms to B.S 812 (25% maximum)	Every 5000 m ³ delivered to site Source change & max Monthly	Material Test Report	
16		Chemical analysis for coarse aggregate	BS 812	Conforms to B.S 812	Every 5000 m ³ delivered to site Source change & max Monthly	Material Test Report	
17	Cementitious materials	Compressive strength of Hydraulic cement	EN196-1 / ASTM C109	Conforms to ASTM C150 requirement	Every 5000 m ³ delivered to site Source change & max Monthly	Material Test Report	
18		Time of setting	ASTM C 191	Conforms to ASTM C150 requirement	Every 2000 Ton delivered to site Source change & max Monthly	Material Test Report	
19		Fineness of Cement	ASTM C-204	Conforms to ASTM C150 requirement	Every 2000 Ton delivered to site Source change & max Monthly	Material Test Report	
20		Soundness of Cement	ASTM C-114	Conforms to ASTM C150 requirement	Every 2000 Ton delivered to site Source change & max Monthly	Material Test Report	
21		Silica Fume (SF)	ASTM C 1240	Conforms to ASTM C1240	Every 200 Ton delivered to site Source change & max Monthly	Material Test Report	
22	ADMIXTURES	Testing of ADMIXTURES (PH, Density & Solid C.)	ASTM C-494	Conforms to ASTM C494 requirement	Every 200 Ton delivered to site Source change & max Monthly	Material Test Report	
23	Water	Testing of Water (Cl,SO3, PH & T.D.S.)	ASTM C 1602 & ECP 203	Conforms to ASTM D 512 & ASTM D 516	Monthly	Material Test Report	

RESULTS OF SIEVE ANALYSIS OF FINE AGGREGATE
ASTM C 136 &

materials finer than no.200 in aggregate by washing ASTM C 117

Date	13-07-24	Client	المنشآت والمعدات الحديثة
Delivery Date	01-07-24	source	ابو عجود
Testing Date	08-07-24	FORM NO	2482

Material Type	Sieve Size (mm)	Passing %	Limits ASTM C 33	
			Min.	Max.
FINE AGGREGATE	9.5	100	100	100
	4.75	97	95	100
	2.36	94	80	100
	1.18	86.6	50	85
	0.6	61.4	25	60
	0.3	15.7	5	30
	0.15	6.5	0	10

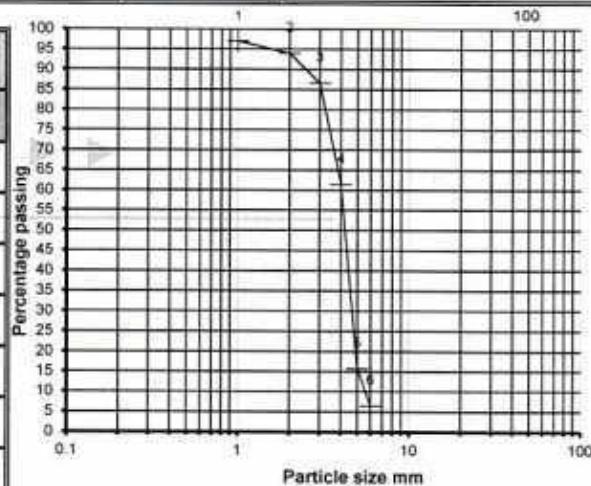

- Fineness modulus: 2.593 Limits ASTM C 33: (2.3 to 3.1)

materials finer than no.200 in aggregate by washing

Test	Results
Percentage of material finer than Sieve size 75 mm (No.200)	2.3

ASTM C 33 limits:

Shall not exceed 3 % (case of concrete subject to abrasion)

Shall not exceed 5 % (all other concrete)

Note:

The Test Results is (Comp. - Not Comply) with Spec. limits

Not Comply) with Spec. limits

Tested by:	
Checked by:	
Lab manager:	

sites No-1

Approved by Dr. Adel Elkordi

CODE:

Ag 001-F-153






RESULTS OF SIEVE ANALYSIS OF COARSE AGGREGATE
ASTM C 136 &

materials finer than no.200 in aggregate by washing ASTM C 117

Date	13-07-24	Client	المنشآت والمعدات الحديثة
Delivery Date	01-07-24	source	علاقه
Testing Date	10-07-24	FORM NO	2482

Material Type	Sieve Size (mm)	Passing %	Limits	
			Min.	Max.
COARSE AGGREGATE (1)	19	100	100	100
	12.5	88.6	90	100
	9.5	55.5	40	70
	4.75	1.8	0	15
	2.36	0.7	0	5

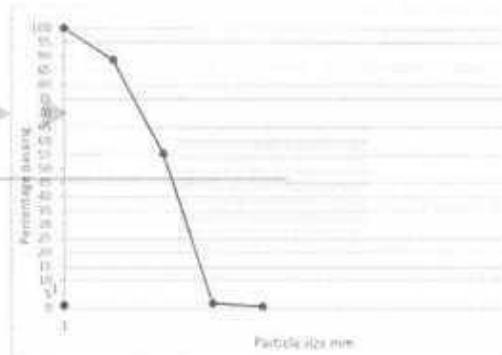

materials finer than no.200 in aggregate by washing

Test	Aggregates Size.1
Percentage of material finer than Sieve size 75 mm (No.200)	0.42

ASTM C 33 limits

The amount of percentage of material finer than sieve size 75 µm (No.200)

The Test Results is (Comply

Not Comply) with Spec. limits

Tested by:		
Checked by:		
Lab manager:		
CODE	Ag 002-F-155-A	
sites No-1		

Approved by Dr Adel Elkordi




RESULTS OF SIEVE ANALYSIS OF COARSE AGGREGATE
ASTM C 136 &

materials finer than no.200 in aggregate by washing ASTM C 117

Date	13-07-24	Client	المنشآت والمعدات الحديثة
Delivery Date	01-07-24	source	عاليه
Testing Date	10-07-24	FORM NO	2482

Material Type	Sieve Size (mm)	Passing %	Limits	
			Min.	Max.
COARSE AGGREGATE (2)	25	100	100	100
	19	84.54	90	100
	12.5	4.61	20	55
	9.5	0.71	0	10
	4.75	0.26	0	5

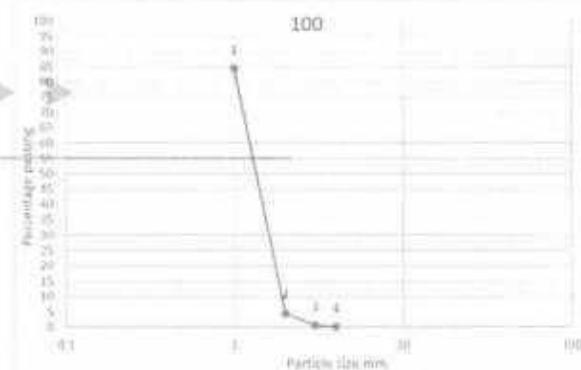

materials finer than no.200 in aggregate by washing

Test	Aggregates Size.2
Percentage of material finer than Sieve size75 mm (No.200)	0.14

ASTM C 33 limits:

The amount of percentage of material finer than sieve size75 µm (No.200)


The Test Results is (Comply)

Not Comply) with Spec. limits

Tested by :	
Checked by:	
Lab manager	

Approved by Dr. Adel Elkordi

CODE Ag 002-F -155-B



**RESULTS OF SPECIFIC GRAVITY AND
ABSORPTION OF FINE AGGREGATE**
ASTM C128

Date	13-07-24	Client	المنشآت والمعادن الخفيفة
Delivery date	01-07-24	source	أبو عجوة
Testing date	08-07-24	FORM NO	2482

Material Type	Test	Results	MIN LIMIT	MAX LIMIT
FINE AGGREGATE	Bulk Specific Gravity Dry	2.50	-	-
	Bulk Specific Gravity (SSD)	2.53	-	-
	Apparent Specific Gravity	2.71	2.50	2.75
	Absorption %	1.20	-	2.00

Note:

- *The Sample was delivered to the Lab by the Client.
- *The Above Data is according to the test results.
- *The Results above apply only to the sample delivered to the lab.
- *According to ASTM C-128 & ASTM C-33 there no limits for Specific gravity
- * OD : Open Dry
- * SSD : Saturated Surface Dry

Tested by :		Approved by :	Dr. Adel Elkordi
Checked by:			
Lab manager:	sites No-1		

CODE Ag 003-F-151



**RESULTS OF SPECIFIC GRAVITY AND ABSORPTION
OF COARSE AGGREGATE
ASTM C127**

Date	13-07-24	Client	المنشآت و المعدات الحديثة
Delivery date	01-07-24	source	عقار
Testing date	08-07-24	FORM NO	2482

Material Type	Test	Aggregates Size # 2	Aggregates Size # 1	LIMIT ECP 203-2017	
				MIN	MAX
COARSE AGGREGATE	Bulk Specific Gravity Dry	2.59	2.49	-	-
	Bulk Specific Gravity (SSD)	2.61	2.52	-	-
	Apparent Specific Gravity	2.63	2.58	2.60	2.70
	Absorption %	1.89	1.78	-	2.50

Note:

- The Sample was delivered to the Lab by the Client.
- The Above Data is according to the information received from the Client.
- The Results above apply only to the sample delivered to the lab.

Tested by :		Approved by	Dr Adel Elkordi
Checked by:			
Lab manager			

CODE Ag 004-F-153



four
technology
labs.

sites No-1



UNIT WEIGHT AND VOIDS IN FINE AGGREGATE
ASTM C 29

Date	13-07-24	Client	المنطقة والمنفذ التجربة
Delivery date	01-07-24	source	ابو عجوة
Testing date	08-07-24	FORM NO	2482

Material Type	Test	Results
FINE AGGREGATE	Unit Weight (Kg/m ³) Rodding	1.730
	Unit Weight (Kg/m ³) loose	1.570

Note:

- The Sample was delivered to the Lab by the Client.
- The Above Data is according to the information received from the Client.
- The Results above apply only to the sample delivered to the lab.

Tested by :		
Checked by :		
Lab manager		
sites No-1		
Approved by		Mr Adel Elkore

CODE Ag 005-F-156



UNIT WEIGHT AND VOIDS IN Coarse AGGREGATE ASTM C 29

Date	13-07-24	Client	المنطقة و المعدات المختبر
Delivery date	01-07-24	source	عنوان
Testing date	08-07-24	FORM NO	2482

Material Type	Test	Aggregates size #1	Aggregates size #2
COARSE AGGREGATE	Unit Weight (Kg/m ³) Rodding	1.540	1.700
	Unit Weight (Kg/m ³) Loose	1.400	1.560

Note:

- According to ASTM C-29 & ASTM C-33 there no limits for unit weight .
- The Sample was delivered to the Lab by the Client .
- The Above Data is according to the information received from the Client .
- The Results above apply only to the sample delivered to the lab .

Tested by :		
Checked by:		
Lab manager		
 four technology labs. sites No-1		
CODE	Ag 006-F-156	
		Approved by : Dr. Adel Elkordi



**RESISTANCE TO DEGRADATION
OF SMALL SIZE AGGREGATE BY ABRASION
AND IMPACT IN LOS ANGELES MACHINE**
ASTM C 131

Date	13-07-24	Client	المنشآت والمعادن الجديدة
Delivery date	01-07-24	source	عنوان
Testing date	08-07-24	FORM NO	2482

Material Type	Test	Aggregates size #1 %	Aggregates size #2 %	LIMIT ECP - 203
COARSE AGGREGATE	Amount of loss by abrasion and impact (%) Coarse Aggregate	16.8	17.2	30%

ASTM C 33 limits:

The amount of loss by abrasion and impact for moderate weathering regions class 4 M

***Gradings of Test Samples (Grade B)**

Note:

- The Sample was delivered to the Lab by the Client.
- The Above Data is according to the information received from the Client.
- The Results above apply only to the sample delivered to the lab.

Tested by :		
Checked by:		
Lab manager		
CODE	Ag 007-F-157	sites No-1



Aggregate Crushing VALUE BS 812 - PART 110

Date	13-07-24	Client	المنشآت و المعدات الحديثة
Delivery date	01-07-24	source	عنقه
Testing date	08-07-24	FORM NO	2482

Material Type	Test	Aggregates size #2 %	Aggregates size #1 %	MAX LIMIT ECP 207
COARSE AGGREGATE	ACV VALUE (KN)	15.23	16.7	30%

Note:

BS 812 - PART 110 limits:

- The Sample was delivered to the Lab by the Client.
- The Above Data is according to the information received from the Client.
- The Results above apply only to the sample delivered to the lab.

Tested by :	Approved by	Dr. Adel Elkordi
Checked by:		
Lab manager		
CODE Ag 008-F-145		
sites No-1		



CLAY LUMPS AND FRIABLE PARTICLES IN FINE AGGREGATE ASTM C 142

Date	13-07-24	Client	المكتب والجهات المختصة
Delivery date	01-07-24	source	ابو عجوة
Testing date	08-07-24	FORM NO	2482

Material Type	Test	Results	limit MAX
FINE AGGREGATE	Percentage of clay lumps and friable Particles %	1.40	3.0%

Note:

ASTM C 33 limits:

- The amount of clay lumps & friable particles Shall not exceed 3 %
- The Sample was delivered to the Lab by the Client.
- The Above Data is according to the information received from the Client.
- The Results above apply only to the sample delivered to the lab.

Tested by :		
Checked by:		
Lab manager	 Ag 010-F-147 sites No-1	
CODE	Approved by	Dr. Adel Elkordi



CLAY LUMPS AND FRIABLE PARTICLES IN COARSE AGGREGATE ASTM C 142

Date	13-07-24	Client	المنشآت والمعادن الحديثة
Delivery date	01-07-24	source	معقلا
Testing date	08-07-24	FORM NO	2482

Material Type	Test	Aggregates size #2 %	Aggregates size #1 %	LIMIT (ECP 203-2017)
COARSE AGGREGATE	Percentage of clay lumps and friable Particles %	0.30	0.78	3%

Note:

ASTM C 33 limits:

- The amount of clay lumps & friable particles for moderate weathering regions class 4 M Shall not exceed 5%
- The Sample was delivered to the Lab by the Client.
- The Above Data is according to the information received from the Client.
- The Results above apply only to the sample delivered to the lab.

Tested by:		Approved by	Dr. Adel Elkordi
Checked by:			
Lab manager			

CODE Ag 011-5-147 sites No-1

four technology labs.



**ELONGATION AND FLAKINESS
OF AGGREGATE**
BS 812 Part 105

Date	13-07-24	Client	المنشآت و المعدات الخديوية
Delivery date	01-07-24	source	علاقه
Testing date	08-07-24	FORM NO	2482

Material Type	Test	Aggregates size # 2 %	Aggregates size # 1 %	LIMIT (ECP 203 - 2017)
COARSE AGGREGATE	Flakiness Index %	18.63	17.9	25%

Note:

- The Sample was delivered to the Lab by the Client.
- The Above Data is according to the information received from the Client.
- The Results above apply only to the sample delivered to the lab.
- BS 812 Part 105 limits
- Shall not exceed 25% (Limits for concrete Aggregate)

Tested by:		Approved by:	Dr Adel Elkordi
Checked by:			
Lab manager:	 four technology labs.		
CODE Ag 013-P-148		sites No-1	



ELONGATION AND FLAKINESS OF AGGREGATE BS 812 Part 105

Date	13-07-24	Client	المنشآت و المعدات الحديثة
Delivery date	01-07-24	source	عنتاقيه
Testing date	08-07-24	FORM NO	2482

Material Type	Test	Aggregates	Aggregates	LIMIT (ECP 203 - 2017)
		size # 2 %	size # 1 %	
COARSE AGGREGATE	Elongation Index %	21	19.8	30%

Note:

- *The Sample was delivered to the Lab by the Client.
- *The Above Data is according to the information received from the Client.
- *The Results above apply only to the sample delivered to the lab.
- * BS 812 Part 105 limits
- Shall not exceed 25% (Limits for concrete Aggregate)

Tested by :			Approved by	Dr. Adel Elkordi
Checked by:				
Lab manager	 sites No-1			

CODE Ag 014-F-145



ORGANIC IMPURITIES IN FINE AGGREGATE ASTM C 40

Date	13-07-24	Client	UNIMIX (محطة سري)
Delivery date	12-09-23	source	ابو عجوة
Testing date	08-07-24	FORM NO	2482

Material Type	Test	Results	Limit
FINE AGGREGATE	organic impurities	Nil	Not Darker Than Light Yellow

Note:

- The Sample was delivered to the Lab by the Client.
- The Above Data is according to the information received from the Client.
- The Results above apply only to the sample delivered to the lab.

ASTM C 33 limits:

- Color should be lighter than the standard

The Test Results is (Comply - Not Comply) with Spec. Limits

Tested by :		Approved by
Checked by:		
Lab manager		
CODE Ag 019-F-145		Dr Adel Elkordi
sites No-1		



RESULTS OF Testing of Aggregate (Fine or Coarse)
(Chlorides & Sulphate)
BS-812 Part117 & Part118

Date	10-07-24	Client	المنشآت والمعدات الحديثة
Delivery date	01-07-24	source	ابو عجوة
Testing date	08-07-24	PROJECT	تنقب نفق تقاطع مسار الخط الناقل للقطار الكهربائي السريع (٦ اكتوبر - الاقصر - سوان - ابو سمبل) مع الطريق الدائري الاقليمي عدكم (650+32) بنظام خوازيق السندي المتلاصقة

Material Type	Test	Results	Limits According to ECP
Sand	Chloride Content	0.05%	0.06%
	Sulfate Content	0.2900	0.40%

Note:

- The Sample was delivered to the Lab by the Client.
- The Above Data is according to the information received from the Client.
- The Results above apply only to the sample delivered to the lab.
- The sample is acceptable, but the sources should be monitored to confirm the quality and prevent any quality issues

Tested by :		Approved by Dr Adel Elkordi
Checked by:		
Lab manager	sites No-1	form no :2482

CODE Ch 006-F-398

CODE Ch 007-F-245



RESULTS OF Testing of Aggregate (Fine or Coarse)
(Chlorides & Sulphate)
BS-812 Part117 & Part118

Date	13-07-24	Client	المنشآت والمعدات الحديبية
Delivery date	01-07-24	source	علاقه
Testing date	08-07-24	PROJECT	تنفيذ تجربة تفاصيل مسار الخط الثاني للقطار الكهربائي السريع (6) الأكتوبر - الإسكندرية - أسوان. أبو سليم) مع الطريق الدائري الاقليمي عد ٩٣ (650+32) بنظام خوازيق السندي المناسبة

Material Type	Test	Results	Limits According to ECP
Aggregate.1	Chloride Content	0.0340	0.04%
	Sulfate Content	0.35	0.40%
Aggregate.2	Chloride Content	0.0280	0.04%
	Sulfate Content	0.34	0.40%

Note:

- The Sample was delivered to the Lab by the Client.
- The Above Data is according to the information received from the Client.
- The Results above apply only to the sample delivered to the lab.

Tested by :		Approved by Dr Adel Elkordi
Checked by :		
Lab manager		form no:2482

CODE Ch 006-F-399

CODE Ch 007-F-246





Testing of Cement (Cement Content determination) ASTM C-114

Date	13-07-24	Source	Bani Sweif
Tasting date	08-07-24	Client	المنشآت و المعدات الحديثة
Delivery date	01-07-24	source	الوطنيه OPC



Material Type	Test	Results	Egption Code 4756 Max Limites
Cement	Insoluble Residue	2.5%	5.0%
	Sulfur Trioxide	2.40%	3.5%
	Loss On Ignition	3.2%	5.0%

Note:

- The Sample was delivered to the Lab by the Client.
- The Above Data is according to the information received from the Client.
- The Results above apply only to the sample delivered to the lab.

The Test Results is (Comply - Not Comply) with Spec. Limits

Tested by :	 sites No-1	Approved by Dr Adel Elkordi
Checked by:		
Lab manager	form no:2482	

CODE Ch 010-F -150



RESULTS OF Testing of ADMIXTURES (PH, Density& Solid C.) ASTM C-494

Date	13-07-24	FORM NO	2482
Delivery date	01-07-24	Client	المنشاءات الحديثة
Testing date	08-07-24	ADD TYPE	اباي FM240



Material Type	Test	Results
ADMIXTURES	PH Value	6.1
	Density	1.180
	Solid Content	39.5%

Note:

- The Sample was delivered to the Lab by the Client.
- The Above Data is according to the information received from the Client.
- The Results above apply only to the sample delivered to the lab.

The Test Results is (Comply - Not Comply) with Spec. Limits

Tested by :	 Dr. Adel Elkordi	Approved by Dr Adel Elkordi
Checked by:		
Lab manager		
sites No-1		
CODE Ch 005-F-172		



RESULTS OF Testing of water (Cl, SO₃, PH & T.D.S.)
AASHTO T-26 & ASTM C-94

Date	13-07-24	SOURCE	Portable Water
Delivery date	01-07-24	CLIENT	المنشآت الحديثة
Testing date	08-07-24	FORM NO	2482

Material Type	Test	Results
Water	PH Value	<u>7.1</u>
	Total Dissolved Salts (T.D.S)	<u>600</u> ppm
	Chloride Content	<u>120</u> ppm
	Sulfate Content	<u>15</u> ppm

Note:

- The Sample was delivered to the Lab by the Client.
- The Above Data is according to the information received from the Client.
- The Results above apply only to the sample delivered to the lab.

The Test Results is (Comply - Not Comply) with Spec. Limits

Tested by :		Approved by Dr Adel Elkordi
Checked by:		
Lab manager		
CODE Ch 003-F-152		
 sites No-1		



**Results of Physical Analysis of Cement
Limits as per
BS EN196 Part-1**

Date	13-07-24	SOURCE	بني سويف
Client	المنشاءات الحديثة	Type	OPC
FORM NO	2482	Delivery Date	01-07-24

Compressive Strength Of Mortar Cubes (BS EN196 Part-1)

Age (days)	Compressive Strength (MPa)			AV.Compressive Strength (MPa)	Limits MIN (MPa)
2	11	10.8	▶	10.2	10
28				10.7	

Note:

Compressive Strength BS EN196 Part-1

CODE Ce 001-F-156

Setting Time By Vicate Apparatus (ASTM C 191)

Test	Setting Time (minute)	(Limits)
Initial Setting Time	140	45 minute (Min.)
Final Setting Time	382	375 minute (Max.)

CODE Ce 002-F-152

Fineness Of Cement By Air Permeability Apparatus (ASTM C 204)

TEST	Fineness (m ² /Kg)	ASTM C 150 limit
Air Permeability Test	3170	2600 Cm ² /Kg (Min.)

CODE Ce 003-F-146

Soundness of Cement

Result (mm)	Limits
2.0	Not More Than 10 mm.

CODE Ce 004-F-126

Note:

- *The Test Results is (Comply - Not Comply) with Spec. Limits
- *The Sample was delivered to the Lab by the Client.
- *The Above Data is according to the information received from the Client.
- *The Results above apply only to the sample delivered to the lab.

Tested by :	four technology labs.
Checked by:	
Lab manager	

sites No-1

Approved by

Dr Adel Elkordi



CERTIFICATE OF ANALYSIS COA

HA-BE-QC-F0103

CERTIFICATE OF ANALYSIS


DELIVERY NOTE No. : EGY/2024/1802 DATE: 04.06.2024
 CHARGE No. : EGY/2024/1108

COSTUMER : Modern Structures
 PLANT : BANI SWEIF
 QUANTITY : 5000 liters

PRODUCT : PANTARHIT® FM240
 ITEM No. : 0808/E
 DESCRIPTION : Super Plasticizer admixture
 ACTIVE SUBSTANCES : Naphthalene sulphonate with additives
 STANDARD COMPLIANCE : BS EN 934-2
 DATE OF TESTING : 15.05.2024

RESULTS:

DESCRIPTION	SPECIFICATION	RESULTS
Steadiness	Homogenous	homogenous
State	Liquid	liquid
Color	Dark brown	Dark brown
Density	$1,22 \pm 0,03$	1.22
pH – value	$7,0 \pm 1,0$	7.4



Mahmoud Eid

(QC In charge)

(Production Manager)

(Technical Department)

Submittal Of Documents

Date: 12/08/2024

Request no: SOD-MSE-AHE-0000048_REV.00

Project No. & Title: Intersection between Regional Ringroad and HSR @ ST. 32+650

Employer:		Engineer:	Arab House of Engineering شركة بيت الهندسة Lahcen and Partners	Contractor:	
-----------	--	-----------	--	-------------	--

1. Document type

- Material samples Catalogues Tests
 Manufacturer certificates Schedules Other Technical sheets

2. Submittal details

Item no.	Description of items submitted/ quantity	Ref.	Contract doc. Ref. & compliances
	التقارير الشهرية بصلاحيات خامات : متابعة تقرير الاسمنت بعد ٢٨ يوم الخاصة بالخلطة الخرسانية لشهر ٦-٢٠٢٤		

These are transmitted for:

- Your information Approval Review & comment Other

Submitted by: Eng. / Emad Eldeen Abdullah

Signature:




3. Engineer's Representative comments:

- Approved
 Approved as noted
 Revise & resubmit
 Rejected
 Others

تم عتاد المعايير المذكورة في التقرير

Signature:



Date: 12/8/2024

Approval shall not relieve Contractor of his liabilities under the Contract or constitute authorization of any change to Contract Document



**Results of Physical Analysis of Cement
Limits as per
BS EN196 Part-1**

Date	13-07-24	SOURCE	بني سويف
Client	المنشآت الحديثة	Type	OPC
FORM NO	2482	Delivery Date	01-07-24

Compressive Strength Of Mortar Cubes (BS EN196 Part-1)

Age (days)	Compressive Strength (MPa)			AV.Compressive Strength (MPa)	Limits MIN (MPa)
2	11	10.8	▶▶▶	10.2	10
28	52.4	52.7	—	53.1	52.5

Note:

Compressive Strength BS EN196 Part-1

CODE Ce01-F-12-8-24-5

Setting Time By Vicate Apparatus (ASTM C 191)

Test	Setting Time (minute)	(Limits)
Initial Setting Time	140	45 minute (Min.)
Final Setting Time	382	375 minute (Max.)

CODE Ce02-F-12-8-24-5

Fineness Of Cement By Air Permeability Apparatus (ASTM C 204)

TEST	Fineness (m ² /Kg)	ASTM C 150 limit
Air Permeability Test	3170	2600 Cm ² /Kg (Min.)

CODE Ce03-F-12-8-24-5

Soundness of Cement

Result (mm)	Limits
2.0	Not More Than 10 mm.

CODE Ce04-F-12-8-24-5


Note:

- The Test Results is Comply - Not Comply) with Spec. Limits.
- The Sample was delivered to the Lab by the Client.
- The Above Data is according to the information received from the Client.
- The Results above apply only to the sample delivered to the lab.

Tested by:

Checked by:

Lab manager



Approved by

Dr Adel Elkordi



Submittal Of Documents

Date: 12/08/2024

Request no: SOD-MSE-AHE-0000049_REV.00

Project No. & Title: Intersection between Regional Ringroad and HSR @ ST. 32+650

Employer:		Engineer:		Contractor:	
-----------	--	-----------	--	-------------	--

1. Document type

- Material samples Catalogues Tests Technical sheets
 Manufacturer certificates Schedules Other

2. Submittal details

Item no.	Description of items submitted/ quantity Compressive Strength Test Result 7 day For Elements Casted 01/08/2024 & PourCards concrete piles P25	Ref.	Contract doc. Ref. & compliances
----------	---	------	----------------------------------

These are transmitted for:

- Your information Approval Review & comment Other

Submitted by:

Eng. / Emad Eldeen Abdullah

Signature:



3. Engineer's Representative comments:

- Approved
 Approved as noted
 Revise & resubmit
 Rejected
 Others


تم عتادتني بالباقي أيام على يوم إيداع النطفي بعد
ستة أيام -

Signature:

Date :

12/18/2024

Approval shall not relieve Contractor of his liabilities under the Contract or constitute authorization of any change to Contract Document



<i>pile ID</i>	Qs-CP				
	Concreting				
	casting				
	from	To	period(hours)	Cast date	Compressive 7 days
	01/08/2024 16:24	01/08/2024 21:05	4:41:00	1/8/2024	8/8/2024

COMPRESSIVE STRENGTH OF CONCRETE SPECIMENS EN-12390-3

Date	8-8-2024	Class of Concrete	C400/450 OPC
Client	المنشآت و المعدات الحديثة	Project	تنفيذ نفق تقاطع مسار الخط الثاني للقطار الكهربائي السريع (٦ اكتوبر -الاقصر -اسوان-ابو سمبل) مع الطريق الدائري الاقليمي عدده كم (650+32) بنظام خوازيق السندي المتلاصقة
Location	Bani Sweif	Consultant	شركة بيت الهندسة (د/ محمود لاشين)
		Element	Pile-25 (H)

Cubes No.	Casting Date	Testing Date	Weight gm	Unit Weight Kg/m3	Load KN	Compressive strength cube (KG/CM2)	Average (KG/CM2)	Age(Days)	
1	1-8-2024	8-8-2024	8499	2518	1336	605.7	614.0	7	
2			8174	2422	1251	567.1			
3			8285	2455	1476	669.1			
4			8382	2484	1487	674.1	661.3		
5			8115	2404	1398	633.8			
6			8410	2492	1491	675.9			

Remarks

the results are temporarily accepted in 7days as guidance but is not taken into consideration till results of 28 days

THE RESULTS IS: COMPLY NOT COMPLY

Tested by:		Approved by Dr. Adel Elkordi
Checked by:		
Lab manager		
CODE Co 008-Modern-Pile-F-39		CODE: CO08-F-12-8-24-8
sites No-1		




Submittal Of Documents

Date: 14/08/2024

Request no: SOD-MSE-AHE-0000050_REV.00

Project No. & Title: Intersection between Regional Ringroad and HSR @ ST. 32+650

Employer:	Engineer:	Contractor:
	AHE Arab House of Engineering شركة بيت المهندس <small>Lahcen and Partners</small>	

1. Document type			
<input type="checkbox"/> Material samples <input type="checkbox"/> Catalogues <input checked="" type="checkbox"/> Tests <input type="checkbox"/> Technical sheets <input type="checkbox"/> Manufacturer certificates <input type="checkbox"/> Schedules <input type="checkbox"/> Other			
2. Submittal details			
Item no.	Description of items submitted/ quantity Compressive Strength Test Result 7 day For Elements Casted From 04/08/2024 To 06/08/2024 & PourCards Bentinite piles P42-P40-P38-P36-P41	Ref.	Contract doc. Ref. & compliances
These are transmitted for: <input type="checkbox"/> Your information <input checked="" type="checkbox"/> Approval <input checked="" type="checkbox"/> Review & comment <input type="checkbox"/> Other			
Submitted by:	Eng. / Ahmed Mohammed EL- sheikh	Signature:	
3. Engineer's Representative comments:			
<input checked="" type="checkbox"/> Approved <input type="checkbox"/> Approved as noted <input type="checkbox"/> Revise & resubmit <input type="checkbox"/> Rejected <input type="checkbox"/> Others			
Signature:	Date : 14/8/2024		

Approval shall not relieve Contractor of his liabilities under the Contract or constitute authorization of any change to Contract Document.



pile ID	Axis	Qs-BP				
		Concreting				
		casting				
		from	To	period(hours)	cast date	Compressive 7 days
B P-36	A01	6/8/2024 12:34 PM	6/8/2024 1:40 PM	1:06:00	06/08/2024	13/08/2024
B P-38	A01	5/8/2024 4:06 PM	5/8/2024 8:53 PM	4:47:00	05/08/2024	12/08/2024
B P-40	A01	5/8/2024 12:15 PM	5/8/2024 2:05 PM	1:50:00	05/08/2024	12/08/2024
B P-41	A01	6/8/2024 5:22 PM	6/8/2024 6:21 PM	0:59:00	06/08/2024	13/08/2024
B P-42	A01	4/8/2024 4:32 PM	4/8/2024 6:21 PM	1:49:00	04/08/2024	11/08/2024



COMPRESSIVE STRENGTH OF CONCRETE SPECIMENS EN-12390-3

Date	11-08-24	Class of Concrete	C15 Kg/Cm ² / 200 Kg OPC
Client	المنشآت و المعدات الحديثة	Project	نقيذ نقى تقاطع مسار الخط الثاني للقطار الكهربائي السريع (6 اكتوبر - الاقصر - اسوان - ابو سمبل) مع الطريق الدائري (الإقليمي عد كم (650+32) بنظام خوازيق السندي المتلاصقة
Location	Bani Sweif	Consultant	شركة بيت الهندسة (د/ محمود لاشين)
Form No :	2771-1	Element	Pile-P42

Cubes No.	Casting Date	Testing Date	Weight gm	Unit Weight Kg/m3	Load KN	Compressive strength cube (KG/CM2)	Average (KG/CM2)	Age(Days)
1			698	2035	38.9	81.0		
2	04-08-24	11-8-2024	700	2041	42.6	88.7	79.9	7
3			722	2105	33.6	69.9		

Remarks

the results are temporarily accepted in 7 days as guidance but is not taken into consideration till results of 28 days

THE RESULTS IS

COMPLY NOT COMPLY

Tested by:	
Checked by:	
Lab manager	
	
sites No-1	
CODE: Co 008-Modern-Pile-F-40	

Approved by Dr Adel Elkordi

CODE: CO08-F-13-8-24-43



COMPRESSIVE STRENGTH OF CONCRETE SPECIMENS EN-12390-3

Date	12-08-24	Class of Concrete	C15 Kg/Cm ² / 200 Kg OPC
Client	المنشآت و المعدات الحديثة	Project	تفيد تلقى تقاطع مسار الخط الثاني للقطار الكهربائي المرربع (٦ اكتوبر - القصر - اسوان - ابو سمبل) مع الطريق الدائري (اثني عد كم (650+32) بنظام خوازيق السندي الملائمة
Location	Bani Sweif	Consultant	شركة بيت الهندسة (د/ محمود لاشين)
Form No :	2771-2	Element	Pile-P40

Cubes No.	Casting Date	Testing Date	Weight gm	Unit Weight Kg/m3	Load KN	Compressive strength cube (KG/CM2)	Average (KG/CM2)	Age(Days)
1	05-08-24	12-8-2024	691	2015	28.9	60.2	58.6	7
2			701	2044	26.9	56.0		
3			683	1991	28.7	59.7		

Remarks

the results are temporarily accepted in 7 days as guidance but is not taken into consideration till results of 28 days

THE RESULTS IS COMPLY NOT COMPLY

Tested by	Checked by
Lab manager	4tl four technology labs.
sites No-1	
CODE Co 008 Modern Pile F-41	

Approved by Dr Adel Elkordi

CODE: CO08-F-13-8-24-44



COMPRESSIVE STRENGTH OF CONCRETE SPECIMENS EN-12390-3

Date	12-08-24	Class of Concrete	C15 Kg/Cm ² / 200 Kg OPC
Client	المنشآت و المعدات الحديثة	Project	نتفہ تلقی تقطیع مسار الخط الثانی للقطار الكهربائی السريع (٦ اکتوبر - الاقصر - اسوان - ابو سمیل) مع الطريق الدائری الانقیمی عد کم (650+32) بنظام خوازینی السنند الملائصۃ
Location	Bani Sweif	Consultant	شركة بيت الهندسة (د/ محمود لاشين)
Form No :	2771-3	Element	Pile-P38

Cubes No.	Casting Date	Testing Date	Weight gm	Unit Weight Kg/m ³	Load KN	Compressive strength cube (KG/CM ²)	Average (KG/CM ²)	Age(Days)
1			696	2029	26.5	55.2		
2	05-08-24	12-8-2024	690	2012	25.6	53.3	54.7	7
3			726	2117	26.7	55.6		

Remarks

the results are temporarily accepted in 7 days as guidance but is not taken into consideration till results of 28 days

THE RESULTS IS

COMPLY

NOT COMPLY

Tested by :		Approved by Dr Adel Elkordi
Checked by:		
Lab manager		
CODE Co 008-Modern-Pile F-42		CODE: CO08-F-13-8-24-45
sites No-1		



COMPRESSIVE STRENGTH OF CONCRETE SPECIMENS EN-12390-3

Date	13-08-24	Class of Concrete	C15 Kg/Cm ² / 200 Kg OPC
Client	المنشات و المعدات الحديثة	Project	تنفيذ نفق تقاطع مسار الخط الثاني للقطار الكهربائي السريع (6 المكتوبر -القصر -اسوان- ابو سمبل) مع الطريق الدائري الاقليمي عد كم (650+32) بنظام خوازيق السندي المتلاصقة
Location	Bani Sweif	Consultant	شركة بيت الهندسة (د/ محمود لاشين)
Form No :	2771-4	Element	Pile-P36

Cubes No.	Casting Date	Testing Date	Weight gm	Unit Weight Kg/m3	Load KN	Compressive strength cube (KG/CM2)	Average (KG/CM2)	Age(Days)
1			681	1985	19.1	39.8		
2	06-08-24	13-8-2024	687	2003	26	54.1	50.7	7
3			688	2006	27.9	58.1		

Remarks

the results are temporarily accepted in 7 days as guidance but is not taken into consideration till results of 28 days

THE RESULTS IS COMPLY NOT COMPLY

Tested by:	Approved by Dr Adel Elkordi
Checked by:	
Lab manager	
	
CODE: CO08-F-13-8-24-46	
sites No-1	
CODE Co 008-Modern-Pile-E-43	



COMPRESSIVE STRENGTH OF CONCRETE SPECIMENS EN-12390-3

Date	13-08-24	Class of Concrete	C15 Kg/Cm ² / 200 Kg OPC
Client	المنشآت و المعدات الحديثة	Project	تفيد نقق تفاصيل مسار الخط الثاني للقطار الكهربائي السريع (٦ اكتوبر - الاقصر - اسوان - ابو سمبل) مع الطريق الدائري الاقليمي عد كم (650+32) بنظام خوازيق السندي المتلاصقة
Location	Bani Sweif	Consultant	شركة بيت الهندسة (د/ محمود لاشين)
Form No :	2771-5	Element	Pile-P41

Cubes No.	Casting Date	Testing Date	Weight gm	Unit Weight Kg/m ³	Load KN	Compressive strength cube (KG/CM ²)	Average (KG/CM ²)	Age(Days)
1	06-08-24	13-8-2024	672	1959	20.3	42.3	44.7	7
2			680	1983	17.3	36.0		
3			673	1962	26.8	55.8		

Remarks

the results are temporarily accepted in 7 days as guidance but is not taken into consideration till results of 28 days

THE RESULTS IS

COMPLY

NOT COMPLY

Tested by :		Approved by Dr. Adel Elkordi
Checked by:		
Lab manager		
CODE: CO08-F-13-8-24-47		
CODE: CO 008-Modern-Pile F-44		



Submittal Of Documents

Date: 15/08/2024

Request no: SOD-MSE-AHE-0000051_REV.00

Project No. & Title: Intersection between Regional Ringroad and HSR @ ST. 32+650

Employer:		Engineer:		Contractor:	
-----------	--	-----------	--	-------------	--

1. Document type

- Material samples Catalogues Tests Technical sheets
 Manufacturer certificates Schedules Other

2. Submittal details

Item no.	Description of items submitted/ quantity	Ref.	Contract doc. Ref. & compliances
	Compressive Strength Test Result 7 day For Elements Casted 07/08/2024 & PourCards Bentinite piles P37-P39		

These are transmitted for:

- Your information Approval Review & comment

Submitted by: Eng. / Emad Eldein Abdullah

Signature:

3. Engineer's Representative comments:

- Approved
 Approved as noted
 Revise & resubmit
 Rejected
 Others

تم اعتماد تفاصيل التحصيلى في اليوم والى عقاد الدهانى لنتائج الكسر
٢٨ آب ٢٠٢٤

Signature:

Date: 15/8/2024

Approval shall not relieve Contractor of his liabilities under the Contract or constitute authorization of any change to Contract Documents.



pile ID	Axis	Qs-BP				
		Concreting				
		casting				
		from	To	period(hours)	cast date	Compressive 7 days
B P-37	A01	7/8/2024 6:00 PM	7/8/2024 6:53 PM	0:53:00	07/08/2024	14/08/2024
B P-39	A01	7/8/2024 12:28 PM	7/8/2024 2:01 PM	1:33:00	07/08/2024	14/08/2024

COMPRESSIVE STRENGTH OF CONCRETE SPECIMENS EN-12390-3

Date	14-08-24	Class of Concrete	C15 Kg/Cm ² / 200 Kg OPC
Client	المنشآت و المعدات الحديثة	Project	تنفيذ نفق تقاطع مسار الخط الثاني للقطار الكهربائي السريع (6 اكتوبر -الأخضر -اسوان -ابو سمبل) مع الطريق الدائري الاقليمي عدم كم (650+32) بنظام خوازيق السندي المتلاصقة
Location	Bani Sweif	Consultant	شركة بيت الهندسة (د/ محمود لاشين)
Form No :	2771-7	Element	Pile-P 37

Cubes No.	Casting Date	Testing Date	Weight gm	Unit Weight Kg/m3	Load KN	Compressive strength cube (KG/CM2)	Average (KG/CM2)	Age(Days)
1	07-08-24	14-8-2024	638	1860	19.9	41.4	42.3	7
2			658	1918	21.1	43.9		
3			658	1918	19.9	41.4		

Remarks

the results are temporarily accepted in 7 days as guidance but is not taken into consideration till results of 28 days

THE RESULTS IS COMPLY NOT COMPLY

Tested by:		Approved by Dr Adel Elkordi
Checked by:		
Lab manager		
sites No-1		CODE: CO08-F-14-8-24-14
CODE Co 008-Modern-Pile-F-46		



COMPRESSIVE STRENGTH OF CONCRETE SPECIMENS EN-12390-3

Date	14-08-24	Class of Concrete	C15 Kg/Cm ² / 200 Kg OPC
Client	المنشآت و المعدات الحديثة	Project	تنفيذ نفق تقاطع مسار الخط الثاني للقطار الكهربائي السريع (٦اكتوبر -الأخضر -اسوان -ابو سمبل) مع الطريق الدائري (الأقليمي عدم كم (650+32) بنظام خوازيق السندي المتلاصقة
Location	Bani Sweif	Consultant	شركة بيت الهندسة (د/ محمود لاشين)
Form No :	2771-6	Element	Pile-P 39


Cubes No.	Casting Date	Testing Date	Weight gm	Unit Weight Kg/m3	Load KN	Compressive strength cube (KG/CM2)	Average (KG/CM2)	Age(Days)
1	07-08-24	14-8-2024	691	2015	15.7	32.7	37.6	7
2			695	2026	12.9	26.9		
3			681	1985	25.6	53.3		

Remarks

the results are temporarily accepted in 7 days as guidance but is not taken into consideration till results of 28 days

THE RESULTS IS

COMPLY NOT COMPLY

Tested by:	
Checked by:	
Lab manager:	

Approved by Dr. Adel Elkordi

CODE: CO08-F-14-8-24-13

CODE Co 008-Modern-Pile-F-45



Submittal Of Documents

Date: 17/08/2024

Request no: SOD-MSE-AHE-0000053_REV.00

Project No. & Title: Intersection between Regional Ringroad and HSR @ ST. 32+650

Employer:		Engineer:		Contractor:	
-----------	--	-----------	--	-------------	--

1. Document type					
<input type="checkbox"/> Material samples <input type="checkbox"/> Manufacturer certificates		<input type="checkbox"/> Catalogues <input type="checkbox"/> Schedules		<input checked="" type="checkbox"/> Tests <input type="checkbox"/> Other	<input type="checkbox"/> Technical sheets
2. Submittal details					
Item no.	Description of items submitted/ quantity Compressive Strength Test Result 7 day For Elements Casted 08/08/2024 & PourCards Bentinite piles P35	Ref.	Contract doc. Ref. & compliances		

These are transmitted for:					
<input type="checkbox"/> Your information		<input checked="" type="checkbox"/> Approval	<input checked="" type="checkbox"/> Review & comment	<input type="checkbox"/> Other	
Submitted by:	Eng. / Emad Eldeen Abdullah		Signature:		

3. Engineer's Representative comments:					
<input checked="" type="checkbox"/> Approved <input type="checkbox"/> Approved as noted <input type="checkbox"/> Revise & resubmit <input type="checkbox"/> Rejected <input type="checkbox"/> Others	<p>تم اعتماد جميع الاختبارات بعد 7 ايام على ان يتم الاعتماد النهائي</p> <p>٢٨ / ٠٨ / ٢٠٢٤</p> 				
Signature:		Date: 17/08/2024			

Approval shall not relieve Contractor of his liabilities under the Contract or constitute authorization of any change to Contract Documents.



<i>pile ID</i>	<i>Axis</i>	Qs-BP				
		Concreting				
		casting				
		from	To	period(hours)	cast date	Compressive 7 days
B P-35	A01	8/8/2024 10:50 AM	8/8/2024 1:03 PM	2:13:00	08/08/2024	15/08/2024

COMPRESSIVE STRENGTH OF CONCRETE SPECIMENS EN-12390-3

Date	15-08-24	Class of Concrete	C15 Kg/Cm ² / 200 Kg OPC
Client	المنشآت و المعدات الحديثة	Project	تنمية نفق تفاصيل الخط الثاني للقطار الكهربائي السريع (٦ اكتوبر - الاقصر - اسوان - ابو سمبل) مع الطريق الدائري الاقليمي عدد كم (650+32) بنظام خوازيق المسند المتلاصقة
Location	Bani Sweif	Consultant	شركة بيت الهندسة (د/ محمود لاشين)
Form No :	2771-8	Element	Pile-P 35

Cubes No.	Casting Date	Testing Date	Weight gm	Unit Weight Kg/m3	Load KN	Compressive strength cube (KG/CM2)	Average (KG/CM2)	Age(Days)
1	08-08-24	15-8-2024	628	1831	29.4	61.2	57.5	7
2			629	1834	28.2	58.7		
3			639	1863	25.3	52.7		

Remarks

the results are temporarily accepted in 7 days as guidance but is not taken into consideration till results of 28 days

THE RESULTS IS COMPLY NOT COMPLY

Tested by:	
Checked by:	✓
Lab manager:	

Approved by Dr. Adel Elkordi

CODE: CO08-F-15-8-24-27

CODE Co 008-Modern-Pile-F47

sites No-1



Submittal Of Documents

Date: 04/09/2024

Request no: SOD-MSE-AHE-0000060 REV.00

Project No. & Title: Intersection between Regional Ringroad and HSR @ ST-32+650

1. Document type

- Material samples Catalogues Tests Technical sheets
 Manufacturer certificates Schedules Other


2. Submittal details

These are transmitted for:

- Your information Approval Review & comment

Submitted by: Eng / Ahmed Mohammed EL-sheikh

Signature:



3 Engineer's Representative comments:

- Approved
 - Approved as noted
 - Revise & resubmit
 - Rejected
 - Others

Signature:



Date: 04-09-2024

Approval shall not relieve Contractor of his liabilities under the Contract or constitute authorization of any change to Contract Document.



pile ID	Axis	Qs-BP				
		Concreting				
		casting				
		from	To	period(hours)	cast date	Compressive 28 days
B P-38	A01	5/8/2024 4:06 PM	5/8/2024 8:53 PM	4:47:00	05/08/2024	02/09/2024
B P-40	A01	5/8/2024 12:15 PM	5/8/2024 2:05 PM	1:50:00	05/08/2024	02/09/2024
B P-42	A01	4/8/2024 4:32 PM	4/8/2024 6:21 PM	1:49:00	04/08/2024	01/09/2024

COMPRESSIVE STRENGTH OF CONCRETE SPECIMENS EN-12390-3

Date	01-09-24	Class of Concrete	C15 Kg/Cm ² / 200 Kg OPC
Client	المنشآت و المعدات الحديثة	Project	النيل للقطط سير الكهربائي السريع (6 الكيلومتر - الاقصى - أسوان - أبو سمبل) مع التغليف الداخلي الألمنيوم عددهم (6,50+32) ينتمون لخوازيق المتن المتلاصقة
Location	Bani Sweif	Consultant	شركة بيت الهندسة (د/ محمود لاشين)
Form No :	2771-1	Element	Pile-P42

Cubes No.	Casting Date	Testing Date	Weight gm	Unit Weight Kg/m3	Load KN	Compressive strength cube (KG/CM2)	Average (KG/CM2)	Age(Days)
1	04-08-24	11-8-2024	698	2035	38.9	81.0	90.9	7
2			700	2041	42.6	88.7		
3			722	2105	33.6	69.9		
4		1-9-2024	663	1933	51	106.2	101.9	28
5			649	1892	48	99.9		
6			680	1983	47.8	99.5		

Remarks

The Results Test For Compressive Strength After 28 days Comply With The criteria of strength as per BS EN 206.

THE RESULTS IS

COMPLY NOT COMPLY

Tested by:	
Checked by:	g.f
Lab manager:	

Approved by: Dr Adel Elkordi

CODE: CO08-F-13-8-24-43 & CO08-F-2-9-24-8

CODE: Co 008-Modern-Pile-F-40



sites No



COMPRESSIVE STRENGTH OF CONCRETE SPECIMENS EN-12390-3

Date	02-09-24	Class of Concrete	C15 Kg/Cm ² / 200 Kg OPC
Client	المنشآت و المعدات الحديثة	Project	الفرز على تقاطع مسار الخط الثاني للناظر الكهربائي أمورع (٦ إكتوبر -القاهرة -اسوان .ابو سمبل) مع الغريق المانعى (الطبىعى عددهم 650+32) بنظام خوازيق المتن المتلاصقة
Location	Bani Sweif	Consultant	شركة بيت الهندسة (د/ محمود لاشين)
Form No :	2771-2	Element	Pile-P40

Cubes No.	Casting Date	Testing Date	Weight gm	Unit Weight Kg/m3	Load KN	Compressive strength cube (KG/CM2)	Average (KG/CM2)	Age(Days)
1	05-08-24	12-8-2024	691	2015	28.9	60.2	68.8	7
2			701	2044	26.9	56.0		
3			683	1991	28.7	59.7		
4		2-9-2024	647	1886	42.9	89.3	78.9	28
5			638	1860	34.8	72.4		
6			628	1831	36	74.9		

Remarks

The Results Test For Compressive Strength After 28 days Comply With The criteria of strength as per BS EN 206.

THE RESULTS IS

COMPLY NOT COMPLY

Tested by:	
Checked by:	Yaf
Lab manager:	

Approved by Dr Adel Elkordi

CODE: CO08-F-13-8-24-44 & CO08-F-2-9-24-9

CODE Co 008-Modern-Pile-F-41



COMPRESSIVE STRENGTH OF CONCRETE SPECIMENS EN-12390-3

Date	02-09-24	Class of Concrete	C15 Kg/Cm ² / 200 Kg OPC
Client	المنشآت والمعدات الحديثة	Project	شعبة تكنولوجيا مياه الشرب والصرف الصحي للإسكندرية (6) الكهرباء والطاقة (النيل والمنطقة الصناعية) بـ ٦٥٠+٣٢ بنظام خوازيق المسند المتلاصقة
Location	Bani Sweif	Consultant	شركة بيت الهندسة (د/ محمود لاشين)
Form No :	2771-3	Element	Pile-P38

Cubes No.	Casting Date	Testing Date	Weight gm	Unit Weight Kg/m3	Load KN	Compressive strength cube (KG/CM2)	Average (KG/CM2)	Age(Days)	
1	05-08-24	12-8-2024	696	2029	26.5	55.2	62.8	7	
2			690	2012	25.6	53.3			
3			726	2117	26.7	55.6			
4	2-9-2024		646	1883	39.3	81.8	71.0	28	
5			669	1950	34.7	72.2			
6			657	1915	28.3	58.9			

Remarks

The Results Test For Compressive Strength After 28 days Comply With The criteria of strength as per BS EN 206.

THE RESULTS IS

COMPLY NOT COMPLY

Tested by:	
Checked by:	
Lab manager:	
four technology labs.	

Approved by Dr. Adel Elkordi

CODE: CO08-F-13-8-24-45 & CO08-F-2-9-24-10

CODE Co 008-Modern-Pile-F-42



Submittal Of Documents

Date: 10/09/2024

Request no: SOD-MSE-AHE-0000064 REV.00

64

Project No. & Title: Intersection between Regional Ringroad and HSR @ ST. 32+650

Employer:	Engineer:	Contractor:
	AH Arab House of Engineering Lashem and Partners	

1. Document type

- Material samples Catalogues Tests Technical sheets
 Manufacturer certificates Schedules Other

2. Submittal details

Item no.	Description of items submitted/ quantity	Ref.	Contract doc. Ref. & compliances
	Compressive Strength Test Results day For Elements Casted From 04/08/2024 To 08/08/2024 & Pour Cards Bentinite piles P35&P36&P37&P38&P39&P40&P41&P42		

These are transmitted for:

- Your information Approval Review & comment
 Other

Submitted by: Eng / Ahmed Mohammed EL-Sheikh

Signature:



3. Engineer's Representative comments:

- Approved
 Approved as noted
 Revise & resubmit
 Rejected
 Others

Signature:



Date: 11 - 9 - 2024

Approval shall not release Contractor of his liabilities under the Contract or constitute authorization of any change to Contract Document



pile ID	Axis	Qs-BP				
		Concreting				
		casting				
		from	To	period(hours)	cast date	Compressive 28 days
B P-35	A01	8/8/2024 10:50 AM	8/8/2024 1:03 PM	2:13:00	08/08/2024	05/09/2024
B P-36	A01	6/8/2024 12:34 PM	6/8/2024 1:40 PM	1:06:00	06/08/2024	03/09/2024
B P-37	A01	7/8/2024 6:00 PM	7/8/2024 6:53 PM	0:53:00	07/08/2024	04/09/2024
B P-38	A01	5/8/2024 4:06 PM	5/8/2024 8:53 PM	4:47:00	05/08/2024	02/09/2024
B P-39	A01	7/8/2024 12:28 PM	7/8/2024 2:01 PM	1:33:00	07/08/2024	04/09/2024
B P-40	A01	5/8/2024 12:15 PM	5/8/2024 2:05 PM	1:50:00	05/08/2024	02/09/2024
B P-41	A01	6/8/2024 5:22 PM	6/8/2024 6:21 PM	0:59:00	06/08/2024	03/09/2024
B P-42	A01	4/8/2024 4:32 PM	4/8/2024 6:21 PM	1:49:00	04/08/2024	01/09/2024

COMPRESSIVE STRENGTH OF CONCRETE SPECIMENS EN-12390-3

Date	05-09-24	Class of Concrete	C15/ 200 Kg OPC
Client	المنشآت و المعدات الحديثة	Project	بنك مصر (6 أكتوبر - الأقصر - لمبوران - بور سعيد) مع الطريق الدائري الألكتروني عددة كم (650+32) ينطلق شوارع السند المتلاصقة
Location	Bani Sweif	Consultant	شركة بيت الهندسة (د/ محمود لاشين)
Form No :	2854	Element	Pile-P 35

Cubes No.	Casting Date	Testing Date	Weight gm	Unit Weight Kg/m ³	Load KN	Compressive strength cube (KG/CM ²)	Average (KG/CM ²)	Age(Days)
4	08-08-24	5-9-2024	638	1860	44.8	93.3	85.3	28
5			643	1875	39.2	81.6		
6			644	1878	38.9	81.0		

Remarks

The Results Test For Compressive Strength After 28 days Comply With The criteria of strength as per BS EN 206.

THE RESULTS IS



COMPLY



NOT COMPLY

Tested by :	
Checked by:	
Lab manager	
sites No-1	
CODE Co 008-Modern-Pile-F-62-B	

Approved by Dr Adel Elkordi

CODE: CO08-F-5-9-24-18



COMPRESSIVE STRENGTH OF CONCRETE SPECIMENS EN-12390-3

Date	03-09-24	Class of Concrete	C15 Kg/Cm ² / 200 Kg OPC
Client	المنشآت و المعدات الحديثة	Project	الجاري تنفيذ مسار الخط الثاني للنيل الكهربائي ال مشروع (٦) الكوبر - القصرين - أسوان - أبو سمبل مع تنفيذ الماء الطلق عدده كم (٦٥٥+٣٢) ينبع خوازيق العدد المتلاصنة
Location	Bani Sweif	Consultant	شركة بيت الهندسة (د/ محمود لاشين)
Form No :	2771-5	Element	Pile-P41

Cubes No.	Casting Date	Testing Date	Weight gm	Unit Weight Kg/m3	Load KN	Compressive strength cube (KG/CM2)	Average (KG/CM2)	Age(Days)
1	06-08-24	3-9-2024	648	1889	31	64.5	56.2	28
2			657	1915	25	52.0		
3			620	1808	25	52.0		

Remarks

The Results Test For Compressive Strength After 28 days Comply With The criteria of strength as per BS EN 206,

THE RESULTS IS

COMPLY NOT COMPLY

Tested by:	
Checked by:	
Lab manager	
	
four technology labs.	
CODE Co 008-Modern-Pile-F-44-B	
sites No-1	

Approved by Dr Adel Elkordi

CODE: C008-F-4-9-24-17



COMPRESSIVE STRENGTH OF CONCRETE SPECIMENS EN-12390-3


Date	04-09-24	Class of Concrete	C15 Kg/Cm ² / 200 Kg OPC
Client	المنشآت و المعدات الحديثة	Project	البنية التحتية لخانع مصر الخط الثاني للطاقة التهرباتي ال مشروع (٦) الكهرباء - الأقصر - أسوان - أبو سمبل (مع الخطين التدريجي والقطبي عبارة عن (650+32) خط خوازيق المسند المتلاصقة)
Location	Bani Sweif	Consultant	شركة بيت الهندسة (د/ محمود لاشين)
Form No :	2771-6	Element	Pile-P 39

Cubes No.	Casting Date	Testing Date	Weight gm	Unit Weight Kg/m3	Load KN	Compressive strength cube (KG/CM2)	Average (KG/CM2)	Age(Days)
1	07-08-24	4-9-2024	637	1857	30	62.4	50.0	28
2			659	1921	23	47.9		
3			640	1866	19	39.6		

Remarks

The Results Test For Compressive Strength After 28 days Comply With The criteria of strength as per BS EN 206.

THE RESULTS IS: COMPLY NOT COMPLY

Tested by:	
Checked by:	
Lab manager	
 four technology CODE Co 008-Modern-Pile-45-B	
sites No-1	

Approved by: Dr. Adel Elkordi

CODE: CO08-F-4-9-24-18



COMPRESSIVE STRENGTH OF CONCRETE SPECIMENS EN-12390-3

Date	04-09-24	Class of Concrete	C15 Kg/Cm ² / 200 Kg OPC
Client	المنشآت و المعدات الحديثة	Project	تحقيق نقل تفاصيل الخط الثاني للخط الكهربائي السرعى (٦) الكوبر - القصرين - أسوان - بور سعيد مع الطرق الدائرية الالتوبيس عبد كر (650+32) بنظام خوازيق المسند المتلاصقة
Location	Bani Sweif	Consultant	شركة بيت الهندسة (د/ محمود لاشين)
Form No :	2771-7	Element	Pile-P 37

Cubes No.	Casting Date	Testing Date	Weight gm	Unit Weight Kg/m3	Load KN	Compressive strength cube (KG/CM2)	Average (KG/CM2)	Age(Days)
1	07-08-24	4-9-2024	647	1886	27	56.2	51.3	28
2			657	1915	28	58.3		
3			637	1857	19	39.6		

Remarks

The Results Test For Compressive Strength After 28 days Comply With The criteria of strength as per BS EN 206.

THE RESULTS IS COMPLY NOT COMPLY

Tested by:	
Checked by:	
Lab manager	four technology labs.
CODE Co 008-Modern-Pile-F-4645 sites No-1	

Approved by Dr Adel Elkordi

CODE: CO08-F-4-9-24-19



COMPRESSIVE STRENGTH OF CONCRETE SPECIMENS EN-12390-3

Date	03-09-24	Class of Concrete	C15 Kg/Cm ² / 200 Kg OPC
Client	المنشآت و المعدات الحديثة	Project	نيلز لاق لقطع مسار الخط الثاني للقطار الكهربائي السريع (٦ الكوبر - القصرين - أسوان - أبو سمبل) مع خطي الماء الرياحيين عدد كم (650+32) بـ ظلم خوازيق استد الملاصقة
Location	Bani Sweif	Consultant	شركة بيت الهندسة (د/ محمود لاشين)
Form No :	2771-4	Element	Pile-P36

Cubes No.	Casting Date	Testing Date	Weight gm	Unit Weight Kg/m ³	Load KN	Compressive strength cube (KG/CM ²)	Average (KG/CM ²)	Age(Days)
1	06-08-24	3-9-2024	658	1918	31	64.5	69.4	28
2			663	1933	33	68.7		
3			658	1918	36	74.9		

Remarks

The Results Test For Compressive Strength After 28 days Comply With The criteria of strength as per BS EN 206.

THE RESULTS IS COMPLY NOT COMPLY

Tested by:	
Checked by:	✓
Lab manager	

4tl
four
technology
labs.

CODE Co 008-Modern-Pile-F-4\$ites No-1

Approved by Dr. Adel Elkordi

CODE: CO08-F-4-9-24-16



COMPRESSIVE STRENGTH OF CONCRETE SPECIMENS EN-12390-3

Date	01-09-24	Class of Concrete	C15 Kg/Cm ² / 200 Kg OPC
Client	المنشآت و المعدات الحديثة	Project	نقدب - على مسافر الخط الثاني للطيران الكهربائي ال مشروع (6) الكوبر - الأقصر - أسوان - بور سعيد) مع الطريق السارى الائتمانى عبد كرم (650+32) يضم خوازق المست المتلاصنة
Location	Bani Sweif	Consultant	شركة بيت الهندسة (د/ محمود لاشين)
Form No :	2771-1	Element	Pile-P42

Cubes No.	Casting Date	Testing Date	Weight gm	Unit Weight Kg/m3	Load KN	Compressive strength cube (KG/CM2)	Average (KG/CM2)	Age(Days)
4	04-08-24	1-9-2024	663	1933	51	106.2	101.9	28
5			649	1892	48	99.9		
6			680	1983	47.8	99.5		

Remarks:

The Results Test For Compressive Strength After 28 days Comply With The criteria of strength as per BS EN 206.

THE RESULTS IS COMPLY NOT COMPLY

Tested by:	
Checked by:	
Lab manager	four technology labs.

Approved by: Dr. Adel Elkordi

CODE: CO08-F-2-9-24-8

CODE Co 008-Modern-Pile-F-40-B	sites No-1
--------------------------------	------------



COMPRESSIVE STRENGTH OF CONCRETE SPECIMENS EN-12390-3

Date	02-09-24	Class of Concrete	C15 Kg/Cm ² / 200 Kg OPC
Client	المنشآت و المعدات الحديثة	Project	نقابة نقلي تفاصيل مسار الخط الثاني للقطار التهريجي المرسني (٦ المطير - المفتر - المطران - بور سعيد) مع الخريطة الدلالة الألبيمي عدد كم (650+32) ينضم خوازيق العصى المتلاصقة
Location	Bani Sweif	Consultant	شركة بيت الهندسة (د/ محمود لاشين)
Form No :	2771-2	Element	Pile-P40

Cubes No.	Casting Date	Testing Date	Weight gm	Unit Weight Kg/m ³	Load KN	Compressive strength cube (KG/CM ²)	Average (KG/CM ²)	Age(Days)
4			647	1886	42.9	89.3		
5	05-08-24	2-9-2024	638	1860	34.8	72.4	78.9	28
6			628	1831	36	74.9		

Remarks

The Results Test For Compressive Strength After 28 days Comply With The criteria of strength as per BS EN 206.

THE RESULTS IS COMPLY NOT COMPLY

Tested by:	
Checked by:	4
Lab manager:	
	
CODE Co 008-Modern-Pile-F-41B No-1	

Approved by Dr. Adel Elkordi

CODE: CO08-F-2-9-24-9



COMPRESSIVE STRENGTH OF CONCRETE SPECIMENS EN-12390-3

Date	02-09-24	Class of Concrete	C15 Kg/Cm ² / 200 Kg OPC
Client	المنشآت و المعدات الحديثة	Project	نقداً لاقى تفاصيل الخطة الثانية للنظام التهريبي الموقع (٦) المكتوبر - الأقصر - أسوان - باب سليم (مع الطريق الدائري الالامي عددهم (650+32) يضم خوازيق العدد المتلاصقة)
Location	Bani Sweif	Consultant	شركة بيت الهندسة (د/ محمود لاشين)
Form No :	2771-3	Element	Pile-P38

Cubes No.	Casting Date	Testing Date	Weight gm	Unit Weight Kg/m3	Load KN	Compressive strength cube (KG/CM2)	Average (KG/CM2)	Age(Days)
4	05-08-24	2-9-2024	646	1883	39.3	81.8	71.0	28
5			669	1950	34.7	72.2		
6			657	1915	28.3	58.9		

Remarks

The Results Test For Compressive Strength After 28 days Comply With The criteria of strength as per BS EN 206.

THE RESULTS IS COMPLY NOT COMPLY

Tested by:	
Checked by:	
Lab manager:	
CODE Co 008-Modern-Pile-F-42-B	
SITES No-1	

Approved by Dr Adel Elkordi

CODE: CO08-F-2-9-24-10

