

أعمال إنشاء الجسر القرائي للقطار الكهربائي السريع (أكتوبر / أوبسبيل)

القطاع الثاني (على مدار / مخطط) من محطة ١٧٦٢٨٠٠ حتى محطة ٣٣٤٨٠٠ بطول ١٥٨ كم (أعمال قطع تقاطع لتنفيذ المسافة من الكمر ٢٠٠+٥٨٥ إلى الكمر ٢٠٢+٣٥٠)

تنفيذ شركة / أبو عبيدة للمقاولات العامة والتوريدات العمومية من محطة ٢٠٠+٨٥٠ إلى ٢٠٢+٣٥٠ بطول ١,٥ كم

رقم بند	بيان الأعمال	الوحدة	سعر الوحدة	الكمية	الإجمالي
١	المواد الأولية والعمالة				
١-١	بأثر المبالغ أمداد تجهيز الموقع من الأثاث والمواد والعمالة التي يستلزم لها استخدام تنفيذ ذات الطبيعة القارية للكمية بحدود ٢٠٠ م. وتغطي بها المبالغ الموضوعة لتجهيز الموقع القاري للكمية بحدود المخرج طبقاً للشروط والمواصفات والمواصفات الهندسية المرفقة بمسألة النقل من ٥٠٠ م. ويتم احتساب عمالة ٢٠٠ م. بحدود ١ كم زائد.	٢٥	٨,٣٥	١	٨,٣٥
١-٢	بالحدود ١٥٨ كم من مسار القطار و التغطية منها على ١٥ م. بطول ١٥٨ كم. ويتم احتساب عمالة ٢٠٠ م. بحدود ١ كم زائد.	العدد	٧٥,٠٠	٢,٥٣٩	١٩٠,٤٢٥,٠٠
٢	العمالة العامة				
٢-١	المحطة إنشاء من ٢٠٢/٢/٢٢				
٢-٢	بأثر المبالغ أمداد تجهيز الموقع من الأثاث والمواد والعمالة التي يستلزم لها استخدام تنفيذ ذات الطبيعة القارية للكمية بحدود ٢٠٠ م. وتغطي بها المبالغ الموضوعة لتجهيز الموقع القاري للكمية بحدود المخرج طبقاً للشروط والمواصفات والمواصفات الهندسية المرفقة بمسألة النقل من ٥٠٠ م. ويتم احتساب عمالة ٢٠٠ م. بحدود ١ كم زائد.	٢٥	٢٩,٣٢	١	٢٩,٣٢
٢-٣	المحطة إنشاء من ٢٠٢/٢/٢٢				
٢-٤	بأثر المبالغ أمداد تجهيز الموقع من الأثاث والمواد والعمالة التي يستلزم لها استخدام تنفيذ ذات الطبيعة القارية للكمية بحدود ٢٠٠ م. وتغطي بها المبالغ الموضوعة لتجهيز الموقع القاري للكمية بحدود المخرج طبقاً للشروط والمواصفات والمواصفات الهندسية المرفقة بمسألة النقل من ٥٠٠ م. ويتم احتساب عمالة ٢٠٠ م. بحدود ١ كم زائد.	٢٥	٣٤,٢٠	٢,٤٩٠,٥٨٠	٨٥,١٦
٢-٥	المحطة إنشاء من ٢٠٢/٢/٢٢				
٢-٦	بأثر المبالغ أمداد تجهيز الموقع من الأثاث والمواد والعمالة التي يستلزم لها استخدام تنفيذ ذات الطبيعة القارية للكمية بحدود ٢٠٠ م. وتغطي بها المبالغ الموضوعة لتجهيز الموقع القاري للكمية بحدود المخرج طبقاً للشروط والمواصفات والمواصفات الهندسية المرفقة بمسألة النقل من ٥٠٠ م. ويتم احتساب عمالة ٢٠٠ م. بحدود ١ كم زائد.	٢٥	٣٨,٣٠	١	٣٨,٣٠
٢-٧	المحطة إنشاء من ٢٠٢/٢/٢٢				
٢-٨	بأثر المبالغ أمداد تجهيز الموقع من الأثاث والمواد والعمالة التي يستلزم لها استخدام تنفيذ ذات الطبيعة القارية للكمية بحدود ٢٠٠ م. وتغطي بها المبالغ الموضوعة لتجهيز الموقع القاري للكمية بحدود المخرج طبقاً للشروط والمواصفات والمواصفات الهندسية المرفقة بمسألة النقل من ٥٠٠ م. ويتم احتساب عمالة ٢٠٠ م. بحدود ١ كم زائد.	٢٥	٩٧,٥٠	٤,١٨٢	٤٠٧,٧٤٥,٠٠
٢-٩	المحطة إنشاء من ٢٠٢/٢/٢٢				
٢-١٠	بأثر المبالغ أمداد تجهيز الموقع من الأثاث والمواد والعمالة التي يستلزم لها استخدام تنفيذ ذات الطبيعة القارية للكمية بحدود ٢٠٠ م. وتغطي بها المبالغ الموضوعة لتجهيز الموقع القاري للكمية بحدود المخرج طبقاً للشروط والمواصفات والمواصفات الهندسية المرفقة بمسألة النقل من ٥٠٠ م. ويتم احتساب عمالة ٢٠٠ م. بحدود ١ كم زائد.	٢٥	١١٢,٧٠	٤,٠٤٠	٤٥٥,٣٠٨,٠٠
٢-١١	المحطة إنشاء من ٢٠٢/٢/٢٢				
٢-١٢	بأثر المبالغ أمداد تجهيز الموقع من الأثاث والمواد والعمالة التي يستلزم لها استخدام تنفيذ ذات الطبيعة القارية للكمية بحدود ٢٠٠ م. وتغطي بها المبالغ الموضوعة لتجهيز الموقع القاري للكمية بحدود المخرج طبقاً للشروط والمواصفات والمواصفات الهندسية المرفقة بمسألة النقل من ٥٠٠ م. ويتم احتساب عمالة ٢٠٠ م. بحدود ١ كم زائد.	٢٥	١٢١,٦٥	٩,٠٠٠	١,٠٩٤,٨٥٠,٠٠
٢-١٣	المحطة إنشاء من ٢٠٢/٢/٢٢				
٢-١٤	بأثر المبالغ أمداد تجهيز الموقع من الأثاث والمواد والعمالة التي يستلزم لها استخدام تنفيذ ذات الطبيعة القارية للكمية بحدود ٢٠٠ م. وتغطي بها المبالغ الموضوعة لتجهيز الموقع القاري للكمية بحدود المخرج طبقاً للشروط والمواصفات والمواصفات الهندسية المرفقة بمسألة النقل من ٥٠٠ م. ويتم احتساب عمالة ٢٠٠ م. بحدود ١ كم زائد.	٢٥	١٣٠,٦٠	١٨,٩٢٠	٢,٤٣١,٧٧٢,٠٠
٢-١٥	المحطة إنشاء من ٢٠٢/٢/٢٢				
٢-١٦	بأثر المبالغ أمداد تجهيز الموقع من الأثاث والمواد والعمالة التي يستلزم لها استخدام تنفيذ ذات الطبيعة القارية للكمية بحدود ٢٠٠ م. وتغطي بها المبالغ الموضوعة لتجهيز الموقع القاري للكمية بحدود المخرج طبقاً للشروط والمواصفات والمواصفات الهندسية المرفقة بمسألة النقل من ٥٠٠ م. ويتم احتساب عمالة ٢٠٠ م. بحدود ١ كم زائد.	٢٥	١٣٩,٥٥	٤,٥٦٠	١,٦٣٦,٣٤٨,٠٠
٢-١٧	المحطة إنشاء من ٢٠٢/٢/٢٢				
٢-١٨	بأثر المبالغ أمداد تجهيز الموقع من الأثاث والمواد والعمالة التي يستلزم لها استخدام تنفيذ ذات الطبيعة القارية للكمية بحدود ٢٠٠ م. وتغطي بها المبالغ الموضوعة لتجهيز الموقع القاري للكمية بحدود المخرج طبقاً للشروط والمواصفات والمواصفات الهندسية المرفقة بمسألة النقل من ٥٠٠ م. ويتم احتساب عمالة ٢٠٠ م. بحدود ١ كم زائد.	٢٥	٨,٩٥	١	٨,٩٥
٢-١٩	المحطة إنشاء من ٢٠٢/٢/٢٢				
٢-٢٠	بأثر المبالغ أمداد تجهيز الموقع من الأثاث والمواد والعمالة التي يستلزم لها استخدام تنفيذ ذات الطبيعة القارية للكمية بحدود ٢٠٠ م. وتغطي بها المبالغ الموضوعة لتجهيز الموقع القاري للكمية بحدود المخرج طبقاً للشروط والمواصفات والمواصفات الهندسية المرفقة بمسألة النقل من ٥٠٠ م. ويتم احتساب عمالة ٢٠٠ م. بحدود ١ كم زائد.	٢٥	٢,٧٥	٤٠,٤٠٤	١١١,١٠٥,٥٠



استشاري أبحاث التربة والاماسات :
أ.د.م. هشام محمد حلمي



مشروع :
قطار اسوان الكهربائي السريع - القطاع الثاني

تقرير بنتائج اختبارات صلاحية تربة للتأسيس

مقدمة : تم إعداد هذا التقرير بناءً على طلب شركة / ابو عجيبة

وذلك لتحديد خصائص ومذي صلاحية عينة تراب للاستخدام في / طبقات الردم لجسر القطار الكهربائي

مصدر العينة : عند المحطة / تشويبة يعين المسار 202+220

- الملتصق : وقد تم توريد العينة بمعرفة 1- م/ محمود الحيلي رقم الهاتف = 01030344342

- تنبيه هام : العينة مسنولة من أحضرها

- تاريخ توريد العينة : 2023/11/21

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفلوط)

وقد تم عمل الاختبارات الآتية :

- 1- التخرج الحبيبي
- 2- حد السيولة واللدونة
- 3- اختبار البرونكتور
- 4- اختبار CBR
- 5- اختبار المواد العضوية

وكانت نتائج الاختبارات كالآتي :

م	نوع الاختبار	النتائج	حدود القبول والرفض طبقاً للمواصفات
1	تصنيف العينة	A-1-a	(A-1-a) - (A-1-b) - (A-2-4)
2	نسبة الماء من مغل 200	9.4%	لا تزيد عن (15 %)
3	مجال اللدونة	NP	(A-1-a or A-1-b = 6 max) (A-2-4 = 10 max)
4	أقصى كثافة جافة (البرونكتور) yd max	2.170 gm/cm3	لا تقل عن 1.88 gm/cm3
5	نسبة المياه الأصلية	5.9%	---
6	قيمة CBR المقصورة	49.1%	لا تقل عن 20%
8	المواد العضوية	لا يوجد	لا تزيد عن 1%

= و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للتأسيس عليها



مهندس المعمل
التوقيع

فني المعمل
التوقيع

Coarse & Fine Aggregate Grading - ASTM C136 & AASHTO T27

202+220	الموقع : تشوين يمين الممرار	25/11/2023	التاريخ :
---------	-----------------------------	------------	-----------

نتائج الاختبار :-

المر %	المحجوز %	وزن المحجوز التراكمي	وزن المحجوز على كل منخل	رقم المنخل (inch)	رقم المنخل (mm)
100%	0%	0	0	5"	127
100.00%	0.00%	0	0	4"	101.6
100.00%	0.00%	0	0	3"	76.2
93.25%	6.75%	790	790	2.5"	63.5
87.67%	12.33%	1443	653	2"	50.8
83.74%	16.26%	1902	459	1.5"	37.5
78.32%	21.68%	2537	635	1"	25
75.21%	24.79%	2900	363	3/4"	19
70.26%	29.74%	3480	580	1/2"	12.7
66.32%	33.68%	3940	460	3/8"	9.5
62.82%	37.18%	4350	410	# 4	4.75
62.82%			7350	المر من منخل # 4	
			11700	وزن العينة الكلي	
			500	وزن عينة القاع	
47.7%	52.3%	120	120	# 10	2.36
25.4%	74.6%	298	178	# 40	0.425
9.4%	90.6%	425	127	# 200	0.075

NP	السيولة و اللدونة
A-1-a	التصنيف

ملاحظات :



Handwritten signature in blue ink.

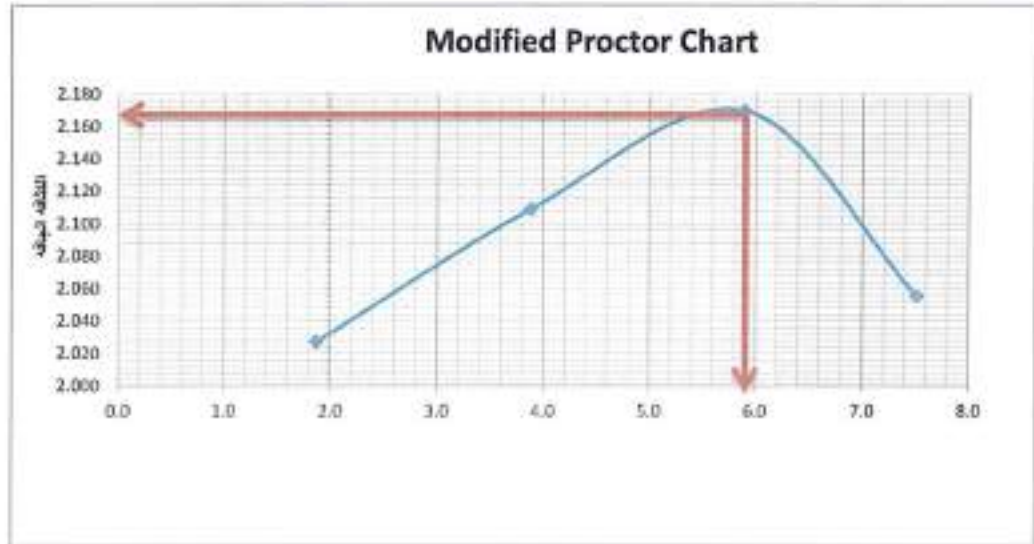
مهندس المعمول
م
التوقيع

Modified Proctor : ASTM D1557

نوع العينة:		عينة محجر	
تصنيف العينة:		A-1-a	
نتائج الاختبار:			
وزن قالب	5731	الكتلة جافة	2.170
حجم قالب	2140	الماء الاسمية	5.9

رقم الاختبار	1	2	3	4
وزن القالب + العينة رطبة	10150.0	10420	10648	10460
وزن قربة الرطبة	4419.0	4689	4917	4729
الكتلة الرطبة	2.065	2.191	2.298	2.210

رقم البطة	1	2	3	4	5	6	7	8
وزن البطة	53.9	55.4	54.5	52.7	55.5	55.8	53.2	53.6
وزن البطة + العينة رطبة	150.0	150.0	150.0	150.0	150.0	150.0	150.0	150.0
وزن البطة + العينة جافة	148	148.5	146	145.8	144.9	144.6	143	143.5
وزن الماء	2.0	1.5	4.0	3.2	5.1	5.4	7.0	6.5
وزن العينة جافة	94.1	93.1	91.5	94.1	89.4	88.8	89.8	89.9
المحتوى المائي %	2.1	1.6	4.4	3.4	5.7	6.1	7.8	7.2
متوسط المحتوى المائي %	1.9	3.9	5.9	7.5				
معدل البطة	2.027	2.109	2.170	2.055				



ملاحظات:



مهندس المعمل
الموقع

فني المعمل
الموقع

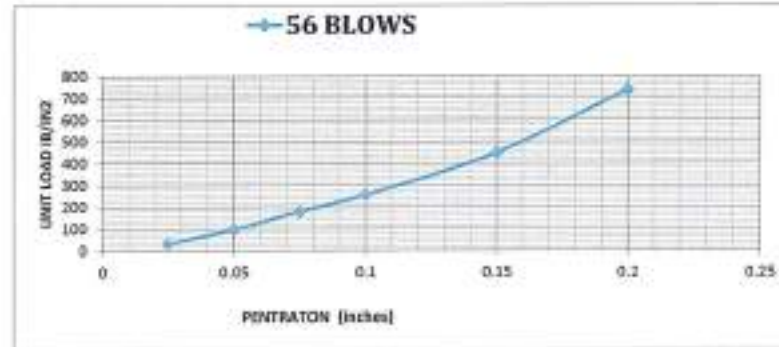
اختبار نسبة تحميل كاليفورنيا (C . B . R) ASTM D1883

A-1-a		تصنيف العينة	
56	عدد الضربات	56	عدد الضربات
10	رقم الجقنة	2131	حجم القالب (سم3)
55.2	وزن الجقنة	5289	وزن القالب (جم)
150	وزن الجقنة +العينة رطبة جم	19120	وزن القالب +وزن العينة رطبة (جم)
144.8	وزن الجقنة +العينة جافة جم	4831	وزن العينة رطبة (جم)
5.2	وزن الماء جم	2.297	كثافة الرطبة (جم/سم3)
89.6	وزن العينة جافة جم	2.143	القيمة كثره جافة (جم/سم3)
5.8%	المحتوى المائي %	2.170	كثافة البرونكتور (جم/سم3)
		95.7%	نسبة الدمك

نسبة الانتفاش	0.20%	غير قابلة للانتفاش
---------------	-------	--------------------

حساب نسبة تحميل كاليفورنيا

7.62	5.08	3.81	2.54	1.9%	1.27	0.635	الاختراق في بالسم
0.3	0.2	0.15	0.1	0.075	0.05	0.025	الاختراق في بالبووصه
1403	1001	610	349	245	132	44	القراءة kg
3092.327	2207.01128	1343.671	769.1576	539.98	291.966	97.32197674	القراءة بالباوند
1031.243	736.004215	448.0936	256.5022	180.075	97.3661	32.45537791	الحمل lb/in2



49.1%	قيمة C . B . R
-------	----------------

ملاحظات : تم حفر القالب في الماء لمدة 96 ساعة خلفا لمواسفة المشروع



مهندس المعمل
د. م. م. م.
التوقيع

م. م. م.
التوقيع

استشاري أبحاث التربة والاساسات :
أ.د.م. هشام محمد حلمي



مشروع :
قطار اسوان الكهربائي السريع - القطاع الثاني

تقرير نتائج اختبارات صلاحية اُتربة للتأسيس

مقدمة : تم إعداد هذا التقرير بناءا على طلب شركة / ابو عجيبة

وذلك لتحديد خصائص ومدي صلاحية عينة تراب للإستخدام في / طبقات الردم لجسر القطار الكهربائي

مصدر العينة : عند المحطة / تشوينة بمين المسار ٢٠٢+٢٢٠

- المنسوب: وقد تم توريد العينة بمعرفة ١- م/ محمود الحيتي رقم الهاتف = ٠١٠٣٠٣٤٤٣٤٢

- تنبيه هام : العينة مسنولية من أحضرها

- تاريخ توريد العينة : ٢٠٢٣/١٢/٢

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفوط)

وقد تم عمل الاختبارات الآتية :

١- التدرج الحبيبي

٢- حد السيولة واللدونة

٣- اختبار البرونكتور

٤- اختبار CBR

٥- اختبار المواد العضوية

وكانت نتائج الاختبارات كالآتي :

م	نوع الاختبار	النتائج	حدود القبول والرفض طبقا للمواصفات
1	تصنيف العينة	A-1-a	(A-1-a) - (A-1-b) - (A-2-4)
2	نسبة الماء من منخل 200	١١.٨%	لا تزيد عن (15 %)
3	مجال اللدونة	NP	(A-1-a or A-1-b = 6 max) (A-2-4 = 10 max)
4	أقصى كثافة جافة (البرونكتور) yd max	2.171 gm/cm3	لا تقل عن 1.88 gm/cm3
5	نسبة العيية الأصولية	6.1%	--
6	قيمة CBR المغمورة	51.1%	لا تقل عن 20%
8	المواد العضوية	لا يوجد	لا تزيد عن 1%

• و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للتأسيس عليها

مهندس المعمل

التوقيع

فني المعمل

التوقيع



Coarse & Fine Aggregate Grading - ASTM C136 & AASHTO T27

الموقع : تشوين يمين المسار 202+220

التاريخ : 12/06/2023

نتائج الاختبار :-

رقم المنخل (mm)	رقم المنخل (inch)	وزن المحجوز على كل منخل	وزن المحجوز التراكمي	المحجوز %	المر %
127	5"	0	0	0%	100%
101.6	4"	0	0	0.00%	100.00%
76.2	3"	0	0	0.00%	100.00%
63.5	2.5"	0	0	0.00%	100.00%
50.8	2"	1425	1425	12.12%	87.88%
37.5	1.5"	475	1900	16.16%	83.84%
25	1"	625	2525	21.47%	78.53%
19	3/4"	475	3000	25.51%	74.49%
12.7	1/2"	485	3485	29.63%	70.37%
9.5	3/8"	475	3960	33.67%	66.33%
4.75	# 4	410	4370	37.16%	62.84%
	المر من منخل # 4	7390		62.84%	
	وزن العينة الكلى	11760			
	وزن عينة التاعم	500			
2.36	# 10	118	118	52.0%	48.0%
0.425	# 40	168	286	73.1%	26.9%
0.075	# 200	120	406	88.2%	11.8%

المسئولة و اللدونة	NP
التصنيف	A-1-a

ملاحظات :



Handwritten signature in blue ink.

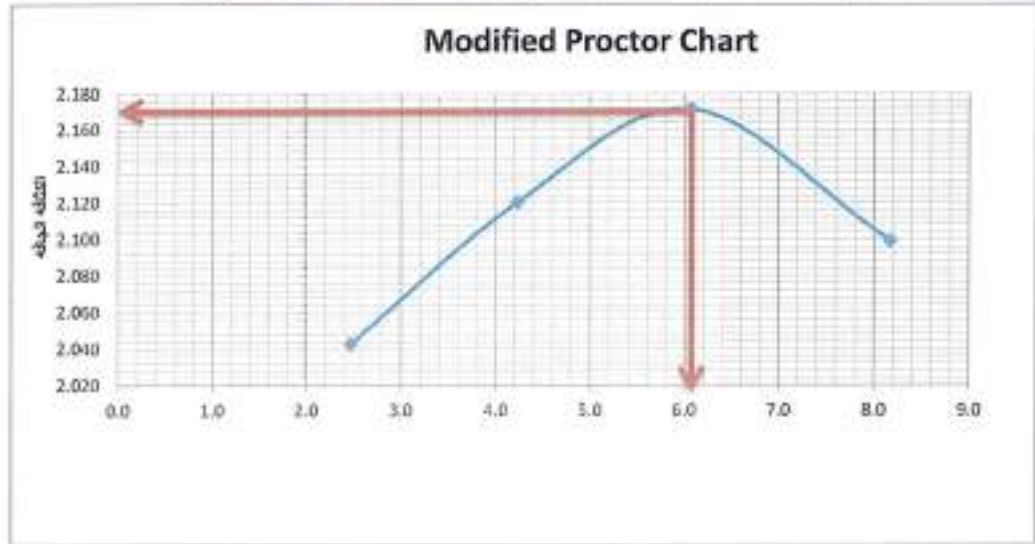
مهندس المعمل
التوقيع

Modified Proctor : ASTM D1557

نوع العينة:		عينة مجهر	
تصنيف العينة:		A-1-a	
نتائج الاختبار :-			
وزن القالب	5731	المسي 805 جافه	2.171
حجم القالب	2140	المياه الاسريه	6.1

رقم الاختبار	1	2	3	4
وزن القالب + العينة رطبه	10210.0	10460	10660	10590
وزن التربه الرطبه	4479.0	4729	4929	4859
الكثافه الرطبه	2.093	2.210	2.303	2.271

رقم الجفنه	1	2	3	4	5	6	7	8
وزن الجفنه	53.9	55.4	54.5	52.7	55.5	55.8	53.2	53.8
وزن الجفنه + العينه رطبه	150.0	150.0	150.0	150.0	150.0	150.0	150.0	150.0
وزن الجفنه + العينه جافه	147.5	147.9	145.5	146.7	144.3	144.9	142.5	142.9
وزن المياه	2.5	2.1	4.5	3.3	5.7	5.1	7.5	7.1
وزن العينه جافه	93.6	92.5	91	94	88.8	89.1	89.3	89.3
المحتوى المائى %	2.7	2.3	4.9	3.5	6.4	5.7	8.4	8.0
متوسط المحتوى المائى %	2.5	4.2	6.1	8.2				
الكثافه الجافه	2.043	2.120	2.171	2.099				



ملاحظات :



مهندس المعمل
التوقيع

فني المعمل
التوقيع

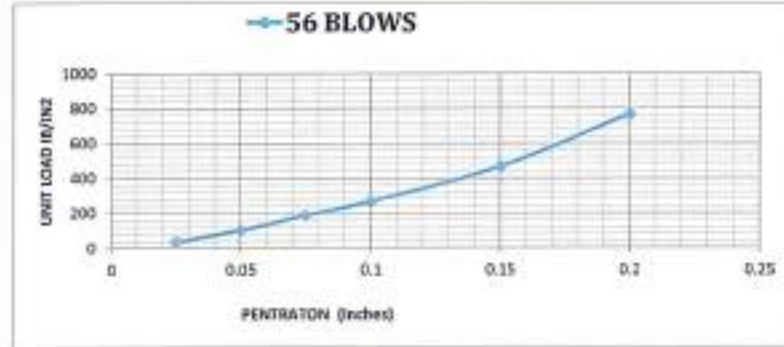
اختبار نسبة تحميل كاليفورنيا (C . B . R) ASTM D1883

A-1-a		تصنيف العينة	
56	عدد الضربات	56	عدد الضربات
30	رقم الجقنة	2131	حجم القالب (سم3)
45.6	وزن الجقنة	5289	وزن القالب (جم)
150	وزن الجقنة + العينة رطبة جم	10115	وزن القالب + وزن العينة رطبة (جم)
144	وزن الجقنة + العينة جافة جم	4826	وزن العينة رطبة (جم)
6	وزن الماء جم	2.265	كثافة الرطبة (جم/سم3)
96.4	وزن العينة جافة جم	2.136	القياس كثافة جافة (جم/سم3)
6.1%	المحتوى المائي %	2.171	كثافة البرونكتور (جم/سم3)
		98.3%	نسبة الدمك

نسبة الانتفاش	0.20%	غير قابلة للانتفاش
---------------	-------	--------------------

حساب نسبة تحمل كاليفورنيا

7.62	5.08	3.81	2.54	1.95	1.27	0.635	الاختراق بالملم
0.3	0.2	0.15	0.1	0.075	0.05	0.025	الاختراق بالبوليمر
1460	1042	635	363	255	138	46	القياس kg
3218.545	2297.09337	1398.515	800.5517	562.02	303.883	101.2943023	بعد المعالجة بالبوليمر
1073.335	766.045203	466.3831	266.9717	187.425	101.34	33.78008721	الحمل lb/in2



51.1%	قيمة C . B . R
-------	----------------

ملاحظات: تم نشر القالب في الماء لمدة 96 ساعة طبقاً لمواصفة المشروع



مهندس العمل
م. م. م. م.
توقيع

المسؤول
م. م. م. م.
توقيع

تقرير بنتائج إختبارات صلاحية أترية للتأسيس

مقدمة : تم إعداد هذا التقرير بناءا علي طلب شركة / ابو عجيبة

وذلك لتحديد خصائص ومذي صلاحية عينة تراب للإستخدام في / طبقات الردم لجسر القطار الكهربائي

مصدر العينة : عند المحطة / تشوينة يمين المسار 202+220

المنسوب : وقد تم توريد العينة بمعرفة 1- م / محمود الحيني رقم الهاتف =01030344342

تنبيه هام : العينة مسنولة من أحضرها

تاريخ توريد العينة : 2023/12/21

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بنى مزار - منفلووط)

وقد تم عمل الإختبارات الآتية :

- 1-التدرج الحبيبي
- 2-حد السيولة واللدونة
- 3-إختبار البروكتور
- 4-إختبار CBR
- 5-إختبار المواد العضوية

وكانت نتائج الإختبارات كالآتي :

م	نوع الإختبار	النتائج	حدود القبول والرفض طبقا للمواصفات
1	تصنيف العينة	A-1-a	(A-1-a) - (A-1-b) - (A-2-4)
2	نسبة المار من ملخل 200	9.4%	لا تزيد عن (15 %)
3	مجال اللدونة	NP	(A-1-a or A-1-b = 6 max) (A-2-4 = 10 max)
4	أقصى كثافة جافة (البروكتور) γ_d max	2.171 gm/cm3	لا تقل عن 1.88 gm/cm3
5	نسبة المياه الأصولية	6.3%	--
6	قيمة CBR المغمورة	49.1%	لا تقل عن 20%
8	المواد العضوية	لا يوجد	لا تزيد عن 1%

• و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للتأسيس عليها



مهندس المعمل
م/أ
التوقيع

فني المعمل
أ/أ
التوقيع

Coarse & Fine Aggregate Grading - ASTM C136 & AASHTO T27

202+220	الموقع : تشوين يمين المسار	25/12/2023	التاريخ :
---------	----------------------------	------------	-----------

لنتائج الاختبار :-

المر %	المحجوز %	وزن المحجوز الترافمي	وزن المحجوز على كل منخل	رقم المنخل (inch)	رقم المنخل (mm)
100%	0%	0	0	5"	127
100.00%	0.00%	0	0	4"	101.6
89.34%	10.66%	1135	1135	3"	76.2
79.44%	20.56%	2190	1055	2.5"	63.5
78.97%	21.03%	2240	50	2"	50.8
74.55%	25.45%	2710	470	1.5"	37.5
71.64%	28.36%	3020	310	1"	25
68.45%	31.55%	3360	340	3/4"	19
64.51%	35.49%	3780	420	1/2"	12.7
56.06%	43.94%	4680	900	3/8"	9.5
47.65%	52.35%	5575	895	# 4	4.75
47.65%			5075	المر من منخل # 4	
			10650	وزن العينة الكلية	
			500	وزن عينة الناعم	
40.5%	59.5%	75	75	# 10	2.36
19.3%	80.7%	298	223	# 40	0.425
9.4%	90.6%	401	103	# 200	0.075

NP	السيولة و اللدونة
A-1-a	التصنيف

ملاحظات :



مهندس

مهندس المعم
التوقيع

Modified Proctor : ASTM D1557

نوع العينة:	عينة محضر
تصنيف العينة:	A-1-a

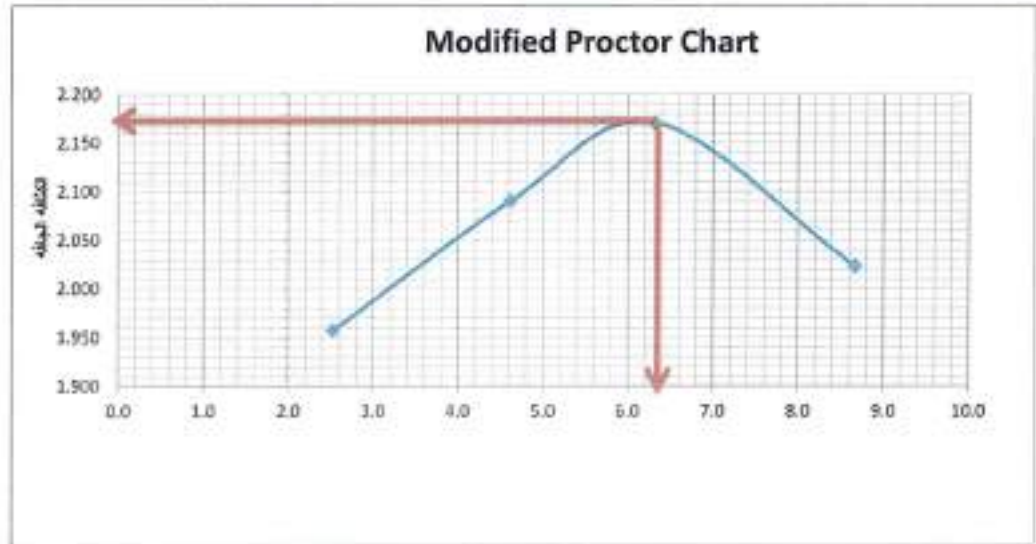
نتائج الاختبار:-

الحد الأقصى لوزن الحبله	2.171
الحد الأدنى لوزن الحبله	6.3

وزن القالب	5731
حجم القالب	2140

رقم الاختبار	1	2	3	4
وزن القالب + العينة رطبه	10025.0	10410	10670	10436
وزن القالب الجاف	4294.0	4679	4939	4705
الكثافه الرطبه	2.007	2.186	2.308	2.199

رقم الحبله	1	2	3	4	5	6	7	8
وزن الحبله	53.9	55.4	54.5	52.7	55.5	55.8	53.2	53.6
وزن الحبله + العينة رطبه	150.0	150.0	150.0	150.0	150.0	150.0	150.0	150.0
وزن الحبله + العينة جافه	147.3	148	145.6	145.9	144.8	144	142.8	142
وزن الحبله	2.7	2.0	4.4	4.1	5.2	8.0	7.4	8.0
وزن الحبله جافه	93.4	92.6	91.1	93.2	89.3	88.2	89.4	88.4
المستوى المائي %	2.9	2.2	4.8	4.4	5.8	8.8	8.3	9.0
متوسط المستوى المائي %	2.5	4.6	6.3	8.7				
الكثافه الجافه	1.957	2.090	2.171	2.023				



ملاحظات:



مختبر

مهندس المعمل
توقيع

فني المعمل
التوقيع

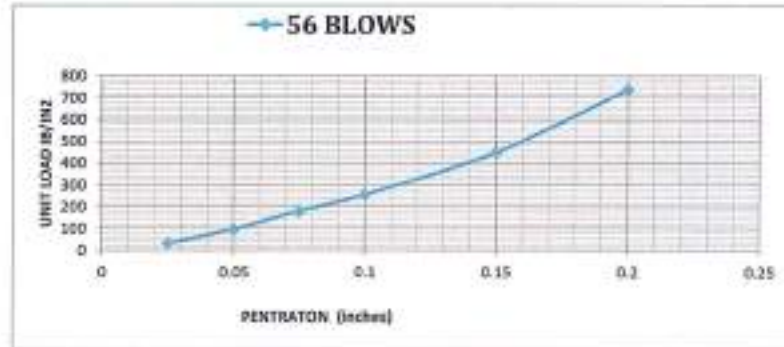
اختبار نسبة تحميل كاليفورنيا (C . B . R) ASTM D1883

A-1-a		تصنيف العينة	
66	عدد الضربات	66	عدد الضربات
f	رقم البقعة	2131	حجم القالب (سم3)
33.7	وزن البقعة	6269	وزن القالب (جم)
150	وزن البقعة + العينة رطبة جم	10136	وزن القالب + وزن العينة رطبة (جم)
143.1	وزن البقعة + العينة جافة جم	4847	وزن العينة رطبة (جم)
6.9	وزن الماء جم	2.275	الكثافة الرطبة (جم/سم3)
109.4	وزن العينة جافة جم	2.140	الكتلة الجافة (جم/سم3)
6.3%	المحتوى المائي %	2.171	كثافة البروكور (جم/سم3)
		98.6%	نسبة الدمك

نسبة الانتفاش	0.20%	غير قابلة للانتفاش
---------------	-------	--------------------

حساب نسبة تحمل كاليفورنيا

7.62	5.08	3.81	2.54	1.95	1.27	0.635	الاختراق بالملم
0.3	0.2	0.15	0.1	0.075	0.05	0.025	الاختراق بالملليمتر
1403	1001	610	349	245	132	44	الترادف kg
3092.327	2207.01128	1343.671	769.1576	539.98	291.966	97.32197674	الترادف بالباوند
1031.243	736.004215	448.0936	256.5022	180.075	97.3661	32.45537791	المعدل lb/in2



49.1%	قيمة " C . B . R "
-------	--------------------

ملاحظات : تم اختبار القالب في الماء لمدة 96 ساعة طبقاً لوصفية المشروع



مهندس العمل
التوقيع

لمشي العمل
التوقيع



التاريخ : 2024-9-22

اسم المشروع : مشروع القطار الكهربائي السريع قطاع (أكتوبر - أبو سمبل)
الموضوع : اعتماد الهيئة العامة للطرق والكبارى لطلبات استلام الأعمال الخاصة بالمشروع
الشركة المنفذة : ابوعجيلة للمقاولات العامة والتوريدات العمومية في المسافة
من (200+876) الى (202+376) بطول 1.5 كم.

عقد رقم : - (2023-2022-1968) بتاريخ 2023-5-17

- (2023-2023-142) بتاريخ 2023-8-3

- (2023-2023-143) بتاريخ 2023-8-3

- (2023-2023-499) بتاريخ 2023-10-12

- (2023-2023-1021) بتاريخ 2024-1-18

- (2023-2023-1229) بتاريخ 2024-2-26

- (2024-2024-209) بتاريخ 2024-8-21

تم الإطلاع ظاهريا على طلبات الفحص الخاصة بالمشروع المذكور عاليه والمرفقة بمستخلصات
المذكورة عالية لعدد (77) طلبات فحص وذلك بعد مراجعتها وتوقيعها من استشارى المساحة (XYZ)
واستشارى ضبط الجودة (مكتب أ.د حسن مهدي) وعليه تم اعتمادها

وتنقسم الى :

- (53) طلبات فحص لأعمال الردم .
- (14) طلبات فحص لأعمال الحفر .
- (4) طلبات فحص لأعمال التطهير .

عن الاستشاري (أ.د حسن مهدي)
مشاريع القطار السريع

مهندس الاستشاري
أ.د حسن مهدي

يعتمد،،،

مهندس الهيئة العامة للطرق والكبارى

مهندس الهيئة العامة للطرق والكبارى

أعمال الجسر الترابي لمسار القطار الكهربائي السريع الخط الثاني (الفيوم / بني سويف - أبو سمبل) (مرحلة الجسور والتأسيس والأساس) القطاع الثاني (بني مزار / منفلووط) أعمال قطع للقطاع لتنفيذ المسافة من ٢٠٠+٨٥٠ إلى ٢٠٢+٣٥٠

البرنامج الزمني

تاريخ نهو الاعمال ٢٠٢٥/٤/٢٥

مدة تنفيذ العمل ٨ شهور

تاريخ استلام الموقع ٢٠٢٤/٨/٢٦

رقم البند	بيان الاعمال	الوحدة	الكمية	أغسطس-٢٠٢٤	سبتمبر-٢٠٢٤	أكتوبر-٢٠٢٤	نوفمبر-٢٠٢٤	ديسمبر-٢٠٢٤	يناير-٢٠٢٥	فبراير-٢٠٢٥	مارس-٢٠٢٥	أبريل-٢٠٢٥
١	أعمال تطهير											
٢-١	بالعدد إزالة لشجار من مسار الطريق و التخلص منها على الا يقل قطر الشجرة عن ٣٠ سم وإزالة الجنوز بالكامل و نقلها خارج الموقع طبقا لتعليمات المهندس المشرف	بالعدد	٢,٥٣٩,٠	٨٤٦,٣٣	٨٤٦,٣٣	٨٤٦,٣٣						
٢	أعمال الحفر											
٤-٢	بالمتر المكعب اعمال حفر بالمعدات الميكانيكية في تربة صخرية ومحمل على البند الاتي ١- تحميل ونقل ناتج الحفر لمسافة لا تقل عن ٥٠٠ متر ٢ - ارنكة العيول الجاتية باستخدام المعدات الميكانيكية ٣- توريد اترية مطابقة للمواصفات وتشغيلها باستخدام الات السوية بسمك لا يزيد عن ٢٥ سم لاستكمال المنسوب التصميمي لتشكيل الجسر والاكتاف (نسبة تحمل كاليفورنيا حتى ١٠ %) ورشها بالمياه الاصولية للوصول الى نسبة الرطوبة المطلوبة والدمك الجيد بالهراسات للوصول الى أقصى كثافة جافة (95% من الكثافة الجافة القصوى). ويتم التنفيذ طبقاً للمناسيب التصميمية والقطاعات العرضية النموذجية والرسومات التفصيلية المعتمدة والبند بجمع مستملات طبقاً لاصول الصناعة ومواصفات الهيئة العامة للطرق والكباري وتعليمات المهندس المشرف. - علاوة ١ جنيه/كم لمسافة نقل ناتج الحفر وتصحيح ١,١ جنيه/كم ابتداء من ٢٠٢٢/٥/٤.	م³										
١-٤-٢	ذات اجهاد (٢٠٠-٢٠٠) كجم/سم² لمسافة نقل حتى ٥٠٠ متر ابتداء من ٢٠٢٤/٣/٢٢	م³	٤,١٨٢,٠	١,٣٩٤,٠٠	١,٣٩٤,٠٠	١,٣٩٤,٠٠						
٢-٤-٢	ذات اجهاد (٤٠٠-٤٠٠) كجم/سم² لمسافة نقل حتى ٥٠٠ متر ابتداء من ٢٠٢٤/٣/٢٢	م³	٤,٠٤٠,٠	١,٣٤٦,٦٧	١,٣٤٦,٦٧	١,٣٤٦,٦٧						
٣-٤-٢	ذات اجهاد (٥٠٠-٥٠٠) كجم/سم² لمسافة نقل حتى ٥٠٠ متر ابتداء من ٢٠٢٤/٣/٢٢	م³	٩,٠٠٠,٠	٣,٠٠٠,٠٠	٣,٠٠٠,٠٠	٣,٠٠٠,٠٠						
٤-٤-٢	ذات اجهاد (٦٠٠-٦٠٠) كجم/سم² لمسافة نقل حتى ٥٠٠ متر ابتداء من ٢٠٢٤/٣/٢٢	م³	١٨,٦٢٠,٠	٦,٢٠٦,٦٧	٦,٢٠٦,٦٧	٦,٢٠٦,٦٧						
٥-٤-٢	ذات اجهاد (٧٠٠-٧٠٠) كجم/سم² لمسافة نقل حتى ٥٠٠ متر ابتداء من ٢٠٢٤/٣/٢٢	م³	٤,٥٦٠,٠	١,٥٢٠,٠٠	١,٥٢٠,٠٠	١,٥٢٠,٠٠						

مهندس الشركة المنفذة



م / احمد فتح

التوقيع /

عن الاستشاري أ.د حسن مهدي

م / محمد مغرب
التوقيع

م / احمد عزب

التوقيع

يعتمد؟؟؟

مهندس الهيئة العامة للطرق والكباري

التوقيع



البرنامج الزمني

أعمال الجسر الترابي لمسار القطار الكهربائي السريع الخط الثاني (الفيوم / بني سويف - أبو سمبل) (مرحلة الجسور والتأسيس والأساس) القطاع الثاني (بني مزار / متفوط) أعمال قطع للقطاع لتنفيذ المسافة من ٢٠٠+٨٥٠ إلى ٢٠٢+٣٥٠

من المحطة ٢٠٠+٨٥٠ إلى المحطة ٢٠٢+٣٥٠ بطول ١,٥ كم رقم العقد (٢٠٢٥/٢٠٢٤/٢٠٩)

تاريخ استلام الموقع ٢٠٢٤/٨/٢٦

مدة تنفيذ العملية ٨ شهور

تاريخ نهو الاعمال ٢٠٢٥/٤/٢٥

رقم البند	بيان الاعمال	الوحدة	الكمية	أغسطس-٢٠٢٤	سبتمبر-٢٠٢٤	أكتوبر-٢٠٢٤	نوفمبر-٢٠٢٤	ديسمبر-٢٠٢٤	يناير-٢٠٢٥	فبراير-٢٠٢٥	مارس-٢٠٢٥	أبريل-٢٠٢٥
١	٢	٣	٤	٥	٦	٧	٨	٩	١٠	١١	١٢	١٣
٥-٢	بالمتر المكعب اعمال حفر باستخدام المعدات الميكانيكية في السفو وتسوية السطح بالآلات التسوية والرش بالمياه الاصلية للوصول الى نسبة الرطوبة المطلوبة والدمك الجيد بالهراسات للوصول الى أقصى كثافة جافة (٩٥% من الكثافة الجافة القصوى) ومحمل على البند تحميل ونقل الأتربة الزائدة لمسافة ١,٥ كم من محور الطريق والقناة تشمل استخدام المياه في تثبيت السفو واعداد مدقات على السفو لحركة المعدات ويتم التنفيذ طبقاً للمناسيب التصميمية والقطاعات العرضية النموذجية والرسومات التفصيلية المعتمدة والبند بجميع مشتملاته طبقاً لأصول الصناعة ومواصفات الهيئة العامة للطرق والكباري وتعليمات المهندس المشرف علاوة ١ جنية / كم لمسافة نقل ناتج الحفر وتصبح ١,١ جنية / كم ابتداءً من ٢٠٢٣/٥/٤.	م٣	٧٣,١٣١,٠								١٢,١٨٨,٥٠	
٣	أعمال الردم											
١-٣	أعمال تحميل وتوريد ونقل أتربة مطابقة للمواصفات ولشغلها باستخدام آلات التسوية بسبك لا يزيد عن ٥٠ سم حتى مسوب (2- متر) أسفل مسوب الفرمة و بسبك لا يزيد عن ٢٥ سم اعلي من مسوب (2- متر) من مسوب الفرمة لاستكمال المنسوب التصميمي لتشكيل الجسر والاكتاف (نسبة تحمل كاليفورنيا لا تقل عن ١٥%) ورشها بالمياه الاصلية للوصول الى نسبة الرطوبة المطلوبة والدمك الجيد بالهراسات للوصول الى أقصى كثافة جافة (95% من الكثافة الجافة القصوى) ويتم التنفيذ طبقاً للمناسيب التصميمية والقطاعات العرضية النموذجية والرسومات التفصيلية المعتمدة والبند بجميع مشتملاته طبقاً لأصول الصناعة ومواصفات الهيئة العامة للطرق والكباري وتعليمات المهندس المشرف. - في حالة طلب جهاز الإشراف زيادة نسبة الدمك عن ٩٥% بحسب زيادة ١ جنية على زيادة نسبة الدمك لكل ١%. - مسافة النقل حتى ٢ كم ويتم احتساب علاوة ١,٤ جنية لكل كم بالزيادة او التقصان وتصبح ١,٥ جنية لكل كم اعتباراً من ٢٠٢٣/٥/٤. -السعر يشمل عمل تشوينات و تخليط واختبارات و نقل لموقع العمل حتي مسافة ٢ كم. - والبند لا يشمل القيمة المحجرة.	م٣										
١-٣-١	نفس بند رقم (١-٣) في شهر سبتمبر ٢٠٢٣	م٣	٥,٤٤١,٠								١,٨١٣,٦٧	
١-٣-٤	نفس بند رقم (١-٣) ابتداء من ٢٠٢٤/٣/٢٢	م٣	٩,٦٦٩,٠								٣,٢٢٣,٠٠	

مهندس الشركة المنقذة

م / احمد فتحي

التوقيع /



عن الاستشاري أ.د حسن مهدي

م / محمود غريب
التوقيع

م / احمد عزب

التوقيع

يعتمد

مهندس الهيئة العامة للطرق والكباري

بيان المعدات

التاريخ : ٢٠٢٤-٩-٢٢

اسم المشروع : مشروع القطار السريع (أكتوبر-أوسمبل)
المسافة من كم ٢٠٠+٨٥٠ وحتى كم ٢٠٢+٣٥٠ بطول ١,٥ كم

بالإشارة الى العقد المبرم بين الهيئة العامة للطرق والكباري وشركة أبوعحيلة للمقاولات العامة
رقم (٢٠٢٥/٢٠٢٤/٢٠٩) بتاريخ ٢٠٢٤-٨-٢١
لتنفيذ المشروع عاليه بالمعدات الآتية :

المعدة	العدد	تاريخ الصنع
حفار	3	2009
		2005
لودر	4	2010
		2001
عربية قلاب	4	2015
	5	2008
	2	2005
بلدوزر	1	2000
تانك مياة	1	2015
جريد	1	2003
هراس	2	2002

عن الاستشاري أ.د حسن مهدي

م/محمود عريب

م/ احمد عزب

التوقيع

يعتمد!!!
مهندس الهيئة العامة للطرق والكباري

لدى الشركة المتفذة

احمد فتوح

يوقع / المصنف





هيكل تنظيمي للعاملين بمشروع القطار السريع شركة أبوعجيلة للمقاولات العامة

التاريخ : ٢٠٢٢-٩-٢٤

اسم المشروع : مشروع القطار السريع (أكتوبر-أوسمبل)

رقم العقد: (٢٠٢٥/٢٠٢٤/٢٠٩)

مستسل	الاسم	الوظيفة	عدد سنوات الخبرة	رقم التليفون
1	محمد حامد يحي	مدير المشروع	10	01009742637
2	احمد احمد محمود	مدير المكتب الفني	5	01017199596
3	نادي عادل	مدير ضبط الجودة	5	01019930593
4	ربيع نوحيد	مدير السلامة الوقائية	10	01114562154
5	وليد محمود محمد	مهندس التنفيذ	5	01090254469
6	محمد عماد الدين محمد	مهندس صيانة (ميكانيكا وكهرباء)	5	01559856322
7	احمد قاسم	مهندس التخطيط والبرمجة الزمنية	5	01223691236
8	احمد السيد احمد	مراقب تنفيذ (فني مواد)	5	01002612002
	محمد نادي			01063768307
9	عبدالعال رجب	حساب كميات	5	01029734478
10	حسين محمد جبريل	مساح	7	01064950832
	محمد جمال		7	01033806848
11	محمد ابوغنيمه	فني سلامة مرورية	5	01092355765
	محمد حسين		5	01022245866

مهندس الشركة المنفذة

م / احمد فتوح

التوقيع /

عن الاستشاري أ.د حسن مهدي

م / احمد عزب

م / محمود عزب

التوقيع /

التوقيع /

يعتمد!!!

مهندس الهيئة العامة للطرق والكباري



مهندس الشركة المنفذة
وليد محمود محمد

0024-5541-5135

مهندس الشركة المنفذة
وليد محمد محمد

أحمد هادي

محضر استلام موقع

مشروع إنشاء خط القطار الكهربائي السريع (أكتوبر - أبو سمبل) من الكم 200+850 حتى الكم 202+350 بطول 1.5 كم
تنفيذ شركة أبو عجيبة للمقاولات العامة والتوريدات العمومية.

انه في يوم الاثنين الموافق 26 / 8 / 2024 وبناء على عقد العملية رقم 209 / 2024 / 2025

اجتمعت اللجنة المشكلة من السادة الاتي اسماؤهم بعد وهم :-

عن الهيئة العامة للطرق والكباري (طرف اول)

مدير عام المشروعات
مهندس الإشراف بالمنطقة السادسة
مدير المشروع
ممثل الاستشاري (مكتب أ.د/حسن مهدي)
استشاري المساحة (XYZ)

- 1- السيد المهندس / مصطفى شعبان البدري
 - 2- السيد المهندس / محمود حسين
 - 3- السيد المهندس / محمود غريب
 - 4- السيد المهندس / احمد عزب
 - 5- السيد المهندس / محمد عبدالرحمن
- عن الشركة المنفذة (طرف ثاني)


مهندس عن الشركة المنفذة

1- السيد المهندس / احمد قتيح

وقد قامت اللجنة بالانتقال علي الطبيعة للموقع عالية بالمعاينة الظاهرية علي المبيعة قام الطرف الاول بتسليم الطرف الثاني الموقع خاليا من العوائق الظاهرية ولا مانع من استلام الموقع والبدء في الاعمال ويحضر تاريخ 26 / 8 / 2024 هو تاريخ استلام الموقع .

وقفل المحضر علي ذلك .

اللجنة من الهيئة (طرف اول)

- 5- 
- 4- 
- 3- 
- 2- 
- 1- 

مشروع القطار السريع
السيد / محمد شعبان البدري

الشركة المنفذة (طرف ثاني)

1- 

19788 م ت

ABUAGLA

بجس 199-161-009

رئيس الإدارة المركزية للمنطقة
السادسة بني سويف
مهندس / طارق الجزار

محضر معاينة مسافة نقل توريد تربة صالحة من محجر (أبو هشيمة)

مشروع القطار السريع (6 أكتوبر / أبو سمبل)
القطاع الثاني بطول 158 كم من 176+700 كم إلى 334+800
تنفيذ شركة : أبو عجيلة للمقاولات العامة بطول 1.5 كم
من 200+876 إلى 202+376

بالإشارة إلى التكاليف الصادر من الهيئة العامة للطرق والكباري لصالح شركة أبو عجيلة
للمقاولات العامة و التوريدات العمومية بشأن تنفيذ الجسر الترابي والأعمال الصناعية
بمشروع القطار الكهربائي السريع (أكتوبر - أسوان) في المسافة الكيلومترية 200+876
إلى العلامة الكيلومترية 202+ 376

بناءً على تعليمات السيد المهندس / رئيس قطاع التنفيذ والمناطق بالتوريد من محاجر
خارجية مرخصة بصفة مؤقتة لحين اعتماد وترخيص محاجر أخرى أقرب للقطاع

فقد اجتمعت اللجنة يوم الاثنين الموافق 2023/8/28 قامت اللجنة المشكلة من :-

- مهندس الإشراف بالهيئة
مدير المشروع
مهندس المكتب الاستشاري (X,Y,Z)
مدير المشروع شركة أبو عجيلة للمقاولات المتكاملة والتوريدات
- (1) السيد المهندس / محمد السيد شعبان
(2) السيد المهندس / حاتم مهران
(3) السيد المهندس / محمد عبدالرحمن سالم
(4) السيد المهندس / محمد حامد أبو عجيلة
- وقامت اللجنة بالذهاب إلى مكان محجر (أبو هشيمة) حيث وجد أن المسافة من القطاع (من محطة 200+876 حتى
202+376) حتى مكان المحجر (49 كم) وذلك بسبب تعذر وجود محجر قريب على أن يتم التوريد بعد عمل اختبارات
الصلاحية اللازمة والتأكد من صلاحية مواد المحجر للتوريد .

Easting	Northing	Longitude (E)	Latitude (N)	Station	الشركة	من
260126.0446	3137487.7094	30° 33' 10.74 "	28° 20' 30.11 "	200+876	أبو عجيلة	البداية
260129.6907	3135991.0284	30° 33' 11.98 "	28° 19' 41.52 "	202+376	أبو عجيلة	النهاية
270048.623	3178136.045	30° 38' 45.6 "	28° 42' 36.3 "	-	محجر	أبو هشيمة

هذا المحضر اعتماد مؤقت لحين اعتماد محجر بجوار القطاع ، ولا يعد إثبات لتوريد أية كميات من المحجر المذكور ، ويجب
على استشاري ضبط الجودة متابعة وحصر أي كميات يتم توريدها من المحجر المذكور ومتابعة صلاحية المحجر بصفة دورية
مستمرة ومقارنتها بصلاحية المواد المثبوتة لتوريدها على القطاع .

واقفل المحضر على ذلك ؟؟؟

مدير المشروع
د.م/حاتم مهران

استشاري المساحة (X,Y,Z)
م/محمد عبدالرحمن سالم

عن الشركة المنفذة

م/محمد حامد أبو عجيلة

يعتمد...
مهندس الهيئة العامة للطرق والكباري

نسخة ختم أكتوبر 2023

أبو عجيلة للتوريدات والمقاولات العامة
409-141-199



مكتب أ.د/حسن مهدي
للإستشارات الهندسية

SYSTRA



مشروع القطار السريع (6 أكتوبر / أبو سمبل)
القطاع الثاني بطول 158 كم من 176+700 كم الى 334+800
تنفيذ شركة : أبو عجيبة للمقاولات العامة بطول 1.5 كم
من كم 200+876 الى كم 202+376

محضر إجمال

اسم الشركة : أبو عجيبة للمقاولات العامة والتوريدات العمومية

القطاع: (201+920) الى (202+376)

أنه في يوم الثلاثاء الموافق 26 / 9 / 2023 قامت اللجنة المكونة من السادة :-

- 1- السيد المهندس/ حاتم مهران
 - 2- السيد المهندس/ محمود عبدالرحيم الحيني
 - 3- السيد المهندس/ محمد حامد أبو عجيبة
- مدير المشروع مكتب أ.د / حسن مهدي شركة أبو عجيبة للمقاولات العامة

قامت اللجنة بالمعاينة الظاهرية وأخذ عينات وإجراء اختبارات صلاحية للقطاع من (201+920) احداثي (260168.4582E, 3136445.233N) الى (202+376) احداثي (260129.6912E, 3135991.0324N) وطبقاً لنتيجة العينة المرفقة تبين أن التربة غير صالحة

للتأسيس (سفو) ويلزم إزالتها وذلك حسب توصيات استشاري التربة وتوصيات سيفكون جروب .

ملحوظات : ...
التوقيع :
التوقيعات :-

لجنة
مجلس
مجلس

عن مكتب أ.د حسن مهدي
مدير المشروع
م. محمود عيسى
م. محمد عبد الله

عن الشركة المنفذة
م. محمد عبد الله
م. محمد عبد الله

استشاري أبحاث التربة والاساسات :
أ.د.م. هشام محمد حلمي



مشروع :
قطار اسوان الكهربائي السريع - القطاع الثاني

تقرير بنتائج اختبارات صلاحية اترية للتأسيس

مقدمة : تم إعداد هذا التقرير بناءا على طلب شركة / ابو عجيله

وذلك لتحديد خصائص ومدي صلاحية عينة تراب للإستخدام في / طبقات الردم لجسر القطار الكهربائي

مصدر العينة : عند المحطة / 202+280 عينة ارض طبيعيه

- المنذوبين: وقد تم توريد العينة بمعرفة م/ محمود الحيني . بتاريخ : 2023/8/21

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفلوط)

- التوصيف الظاهري للعينة : كتبان رملية ناعمة (ملو)

- تنبيه العينة مستوية من احضرها

وقد تم عمل الاختبارات الآتية :

- 1-التدرج الحبيبي
- 2-حد السيولة واللدونة
- 3-إختبار البروكتور
- 4-إختبار CBR
- 5-إختبار المواد العضوية

وكانت نتائج الاختبارات كالآتي :

م	نوع الإختبار	النتائج
1	تصنيف العينة	A-3
2	نسبة العار من منخل 200	2.6 %
3	مجال اللدونة	عديمة اللدونة
4	أقصى كثافة جافة (البروكتور) $\gamma_d \max$	1.871 gm/cm3
5	نسبة للماء الأمولية	9.7%
6	قيمة CBR المغمورة	8.4%
8	المواد العضوية	لا يوجد

• و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي غير صالحة للتأسيس عليها



احمد حسن هاشم
مهندس

مهندس المعجل
م/ محمد البنا
التوقيع

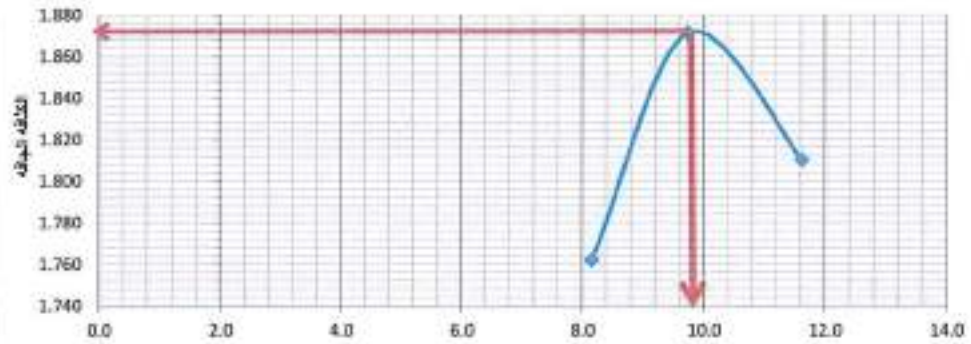
Modified Proctor : ASTM D1557

نوع العينة:	عينة كاشان رملية
تصنيف العينة:	A-3
نتائج الاختبار:	
وزن القالب:	5731
حجم القالب:	2140
القيمة الجافة جافه:	1.871
البيانات الاصوليه:	9.7

رقم الاختبار	1	2	3
وزن القالب + العينة رطبه	9810.0	10126	10055
وزن القالب + العينة جافه	4079.0	4396	4324
الوزن الجافه	1.906	2.054	2.021

رقم الجفنه	1	2	3	4	5	6
وزن الجفنه	53.85	55.31	54.35	54.15	55.14	53.4
وزن الجفنه + العينة رطبه	150.0	150.0	150.0	150.0	150.0	150.0
وزن الجفنه + العينة جافه	142.5	143.1	141.6	141.4	140.2	139.87
وزن العياد	7.5	6.9	8.4	8.6	9.8	10.1
وزن العينة جافه	88.65	87.79	87.25	87.25	85.06	86.47
المحتوى المائى %	8.5	7.9	9.6	9.9	11.5	11.7
متوسط المحتوى المائى %	8.2	9.7	11.6			
الوزن الجافه	1.762	1.871	1.810			

Modified Proctor Chart



ملاحظات :



احمد محمد هادي
مهندس

مهندس المعمول
د. محمد هادي محمد البنا
التوقيع /
- د. محمد هادي محمد البنا -

Coarse & Fine Aggregate Grading - ASTM C136 & AASHTO T27

التاريخ :	25-08-23	الموقع : St 202+280	ارض طبيعيه
-----------	----------	---------------------	------------

نتائج الاختبار :-

رقم المنخل (mm)	رقم المنخل (inch)	وزن المحجوز على كل منخل	وزن المحجوز التراكمي	المحجوز %	المر %
127	5"	0	0	0%	100%
101.6	4"	0	0	0.00%	100.00%
76.2	3"	0	0	0.00%	100.00%
63.5	2.5"	0	0	0.00%	100.00%
50.8	2"	0	0	0.00%	100.00%
37.5	1.5"	0	0	0.00%	100.00%
25	1"	0	0	0.00%	100.00%
19	3/4"	0	0	0.00%	100.00%
12.7	1/2"	0	0	0.00%	100.00%
9.5	3/8"	0	0	0.00%	100.00%
4.75	# 4	0	0	0.00%	100.00%
	المر من منخل # 4	500			100.00%
	وزن العينة الكلي	500			
	وزن عينة الناعم	500			
2.36	# 10	0	0	0.0%	100.0%
0.425	# 40	51	51	10.2%	89.8%
0.075	# 200	436	487	97.4%	2.6%
السيولة و اللدونة		N.P			
التصنيف		A-3			

ملاحظات : توصيف العينة : كثبان رملية ناعمة (Sand Dunes)



المهندس
المختبر

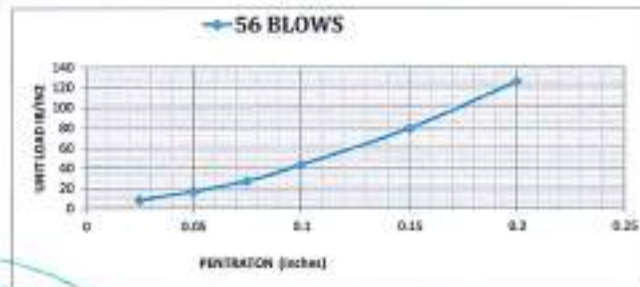
مهندس العمل
المختبر
التوقيع

اختبار نسبة تحميل كاتيلورتيا (C . B . R) ASTM D1883

A-3		تصنيف العينة	
56	عدد الضربات	56	عدد الضربات
2	رقم البقعة	2131	مجم الغالب (سم)
54.3	وزن البقعة	5289	وزن البقعة (جم)
150	وزن البقعة +العينة رطبة جم	9682	وزن الغالب +وزن العينة رطبة (جم)
141.3	وزن البقعة +العينة جافة جم	4313	وزن البقعة رطبة (جم)
8.5	وزن الماء جم	2.024	الترسيب (متر) (سم)
87.8	وزن العينة جافة جم	1.044	نسبة الماء جافة (جم/سم)
9.7%	المحتوى المائي %	1.071	ثقله الجزيئي (جم/سم)
		86.6%	نسبة التماسك
	غير قابلة للتفتت	0.08%	نسبة التفتت

حساب نسبة تحميل كاتيلورتيا

7.62	5.08	3.81	2.54	1.95	1.27	0.635	الأحجار الخشنة
0.3	0.2	0.15	0.1	0.075	0.05	0.025	الأحجار الخشنة
258.0	171	108.0	59.0	37.0	23.0	11.0	الترسيب (سم)
568.632	376.884	238.032	130.036	81.548	50.692	24.244	الترسيب بالمتر
189.63	125.685	79.38	43.365	27.195	16.905	8.085	الترسيب (سم)



8.4%

قيمة C . B . R

ملاحظات : تم إجراء اختبار في الماء لمدة 96 ساعة طبقاً للمواصفة المعمول بها



احمد مصطفى

مهندس المحسن
مهندس محمد البنا

مشروع :
قطار اسوان الكهربائي السريع - القطاع الثاني

استشاري أبحاث التربة والاساسات :
أ.د.م. هشام محمد حلمي



تقرير بنتائج اختبارات صلاحية أترية للتأسيس

مقدمة : تم إعداد هذا التقرير بناءً على طلب شركة / ابو عجيله

وذلك لتحديد خصائص ومدى صلاحية عينة تراب للإستخدام في / طبقات الردم لجسر القطار الكهربائي

مصدر العينة : عند المحطة / 202+020 عينه ارض طبيعيه

- المندوب : وقد تم توريد العينة بمعرفة م/ محمود الحيني . بتاريخ : 2023/9/21

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفلووط)

- التوصيف الظاهري للعينة : كتبان رملية ناعمة (مغو)

- تبييه العينة مسئولية من احضرها

وقد تم عمل الاختبارات الآتية :

- 1-النترج الحبيبي
- 2-حد السيولة واللونة
- 3-إختبار البروكتور
- 4-إختبار CBR
- 5-إختبار المواد العضوية

وكانت نتائج الاختبارات كالآتي :

م	نوع الإختبار	النتائج
1	تصنيف العينة	A-3
2	نسبة الماء من مخلل 200	4 %
3	مجال اللدونة	عديمة اللدونة
4	أقصى كثافة جافة (البروكتور) $\gamma_d \max$	1.863 gm/cm3
5	نسبة المياه الأصولية	10 %
6	قيمة CBR المغمورة	7.7%
8	المواد العضوية	لا يوجد

• و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي غير صالحة للتأسيس عليها



أ.د.م. هشام محمد حلمي

مهندس المعمول
أ.م.م. محمد البنا
التوقيع

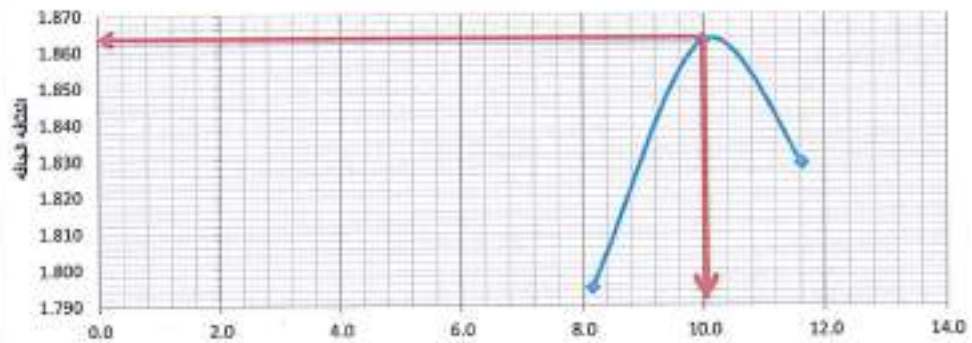
Modified Proctor : ASTM D1557

نوع العينة:	عينة كتيان رملية
تصنيف العينة:	A-3
تاريخ الاختبار:	
وزن القالب:	5731
حجم القالب:	2140
المسح ككثافة جافة:	1.883
البيانات الاسمية:	10.0

رقم الاختبار	1	2	3
وزن القالب + العينة رطبة	9886.0	10116	10100
وزن التربة الرطبة	4155.0	4385	4369
كثافة الرطبة	1.942	2.049	2.042

رقم الحقل	1	2	3	4	5	6
وزن الحقل	53.85	55.31	54.35	54.15	55.14	53.4
وزن الحقل + العينة رطبة	150.0	150.0	150.0	150.0	150.0	150.0
وزن الحقل + العينة جافة	142.5	143.1	141.4	141.2	140.2	139.87
وزن المياه	7.5	8.9	8.6	8.8	9.8	10.1
وزن العينة جافة	88.65	87.79	87.05	87.05	85.06	86.47
المحتوى المائي %	8.5	7.9	9.9	10.1	11.5	11.7
متوسط المحتوى المائي %	8.2	10.0	11.6			
كثافة الحقل	1.795	1.863	1.829			

Modified Proctor Chart



ملاحظات:



أحمد مصطفى
مهندس

مهندس المعمل
أحمد مصطفى
التوقيع
مهندس

Coarse & Fine Aggregate Grading - ASTM C136 & AASHTO T27

التاريخ :	25-09-23	الموقع : St= 202+020	ارض طبيعية
-----------	----------	----------------------	------------

نتائج الاختبار :-

رقم المنخل (mm)	رقم المنخل (inch)	وزن المحجوز على كل منخل	وزن المحجوز التراكمي	المحجوز %	العار %
127	5"	0	0	0%	100%
101.6	4"	0	0	0.00%	100.00%
76.2	3"	0	0	0.00%	100.00%
63.5	2.5"	0	0	0.00%	100.00%
50.8	2"	0	0	0.00%	100.00%
37.5	1.5"	0	0	0.00%	100.00%
25	1"	0	0	0.00%	100.00%
19	3/4"	0	0	0.00%	100.00%
12.7	1/2"	0	0	0.00%	100.00%
9.5	3/8"	0	0	0.00%	100.00%
4.75	# 4	0	0	0.00%	100.00%
	العار من منخل # 4	500			100.00%
	وزن العينة الكلي	500			
	وزن عينة التام	500			
2.36	# 10	10	10	2.0%	98.0%
0.425	# 40	51	61	12.2%	87.8%
0.075	# 200	419	480	96.0%	4.0%
المسبولة و اللدونة		N.P			
التصنيف		A-3			

ملاحظات : توصيف العينة : كتيان رملية ناعمة (Sand Dunes)



احمد محمد علي
مهندس

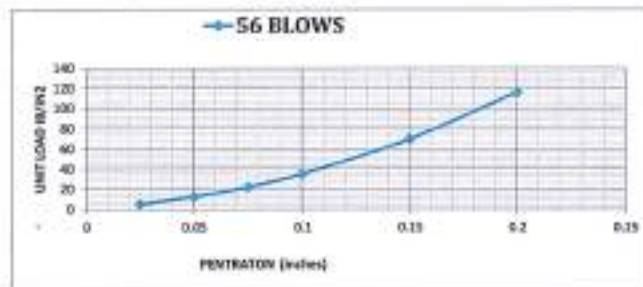
مهندس المعماري محمد البنا
التوقيع

اختبار نسبة تحميل كاتيلورنيا (C . B . R) ASTM D1883

A-3		تصنيف العينة	
56	عدد الضربات	56	عدد الضربات
2	رقم البقعة	2131	ختم القالب (سم)
21.6	وزن البقعة	5289	وزن القالب (جم)
193	وزن البقعة + العينة رطبة (جم)	5590	وزن القالب + وزن العينة رطبة (جم)
198.3	وزن البقعة + العينة جافة (جم)	4391	وزن العينة رطبة (جم)
11.7	وزن الماء (جم)	2.018	كثافة الرطبة (جم / سم ³)
116.7	وزن العينة جافة (جم)	1.834	القيمة كاتيلورنيا (جم / سم ²)
10.0%	المستوى المائي %	1.863	كثافة البرونز (جم / سم ³)
		98.5%	نسبة الماء
	غير قابلة للتشبع	0.00%	نسبة الفراغ

خصائص نسبة تحميل كاتيلورنيا

7.62	5.08	3.81	2.54	1.95	1.27	0.635	الأختبار لباريتم
0.3	0.2	0.15	0.1	0.075	0.05	0.025	الأختبار لباريتم
240.0	158	95.0	48.0	30.0	17.0	7.0	الفرادة kg
528.96	348.232	209.38	105.792	66.12	37.468	15.428	الفرادة والبرونز
176.4	116.13	69.825	35.28	22.05	12.495	5.145	المعدل 8/IN2



7.7%	قيمة C . B . R
------	----------------

ملاحظات : تم عمل القالب في الماء لمدة 96 ساعة قبل الاختبار



احمد محمد عيسى
مهندس

مهندس محمد البنا
مهندس

	مشروع القطار الكهربائي السريع	 مكتب أ.د/حسن مهدي للإستشارات الهندسية
	إستكمال إسناد أعمال الجسر الترابي والأعمال الصناعية بقطاعات مشروع إنشاء القطار الكهربائي السريع (أكتوبر-أبوسمبل)	
	تنفيذ شركة أبو عجيبة للمقاولات العامة والتوريدات العمومية مستخلص (١) جارى	

الحصر الإجمالي لكميات القطاع حتى تاريخ ٢٠٢٤/٤/١

Station	Total Cut Area(m2)	Cum. Cut Vol(m3)	As Built vol.cut		
				CUT VOL(m3)	Total.Qty
200+876.01	580.84	0	cut	0	529753.21
200+880.00	586.05	2,325.62		2,325.62	
200+900.00	630.8	14,494.09		12,168.47	
200+920.00	667.79	27,479.99		12,985.90	
200+940.00	665.5	40,812.95		13,332.96	
200+960.00	635.92	53,827.17		13,014.23	
200+980.00	655.55	66,741.85		12,914.68	
201+000.00	650.46	79,801.90		13,060.05	
201+020.00	610.45	92,410.94		12,609.04	
201+040.00	622.17	104,737.11		12,326.16	
201+060.00	621.82	117,176.99		12,439.89	
201+080.00	624.05	129,635.71		12,458.71	
201+100.00	616.97	142,045.96		12,410.26	
201+120.00	615.77	154,373.38		12,327.42	
201+140.00	617.82	166,709.30		12,335.92	
201+160.00	623.52	179,122.78		12,413.48	
201+180.00	614.79	191,505.94		12,383.16	
201+200.00	633.1	203,984.90		12,478.96	
201+220.00	599.85	216,314.49		12,329.59	
201+240.00	499.13	227,304.33		10,989.84	
201+260.00	445.74	236,753.04		9,448.72	
201+280.00	450.78	245,718.30		8,965.26	
201+285.93	449.56	248,387.80		2669.5	
201+300.00	460.6	254,790.75		6,402.95	
201+320.00	478.13	264,178.05		9,387.30	
201+340.00	476.54	273,724.79		9,546.74	
201+360.00	473.02	283,220.47		9,495.68	
201+380.00	467.7	292,627.66		9,407.19	
201+400.00	480.96	302,114.23		9,486.57	
201+420.00	473.9	311,662.81		9,548.58	
201+440.00	516.53	321,567.07		9,904.26	
201+460.00	579.3	332,525.35		10,958.28	
201+465.93	585.45	335,978.82		3453.48	
201+480.00	583.85	344,204.87		8,226.04	
201+500.00	576.27	355,806.07		11,601.20	
201+520.00	563.45	367,203.19		11,397.13	
201+540.00	521.62	378,053.86		10,850.67	
201+560.00	446.24	387,732.49		9,678.63	
201+580.00	417	396,364.88		8,632.38	
201+600.00	431.82	404,853.04		8,488.16	
201+620.00	454.9	413,720.28		8,867.24	
201+640.00	461.11	422,880.41		9,160.14	

عن الاستشاري أ.د حسن مهدي

م/ عبد الحميد علاء الدين م/ احمد عزب

عن استشاري المساحة

م/ محمد عبدالرحمن م/ محمد عبد الله

عن الشركة

م/ محمد حامد أبو عجيبة م/ محمد عبد الله

أ.د حسن مهدي



	مشروع القطار الكهربائي السريع	 الهيئة القومية للإشراق مكتب أ.د/حسن مهدي للإستشارات الهندسية
	إستكمال إسناد أعمال الجسر الترابي والأعمال الصناعية بقطاعات مشروع إنشاء القطار الكهربائي السريع (أكتوبر-أبوسمبل)	
	تنفيذ شركة أبوعجيبة للمقاولات العامة والتوريدات العمومية مستخلص (١) جارى	

الحصر الإجمالي لكميات القطاع حتى تاريخ ٢٠٢٤/٤/١

Station	Total Cut Area(m2)	Cum. Cut Vol(m3)	As Built vol.cut		
				CUT VOL(m3)	Total.Qty
201+660.00	464.24	432,133.91	cut	9,253.50	529753.21
201+680.00	279.68	439,573.14		7,439.23	
201+700.00	169.23	444,062.22		4,489.08	
201+720.00	182.97	447,584.18		3,521.96	
201+740.00	231.09	451,724.78		4,140.60	
201+760.00	469.19	458,727.54		7,002.77	
201+780.00	474.56	468,164.96		9,437.42	
201+800.00	429.35	477,204.06		9,039.10	
201+820.00	392.13	485,418.87		8,214.81	
201+840.00	217.75	491,517.65		6,098.78	
201+860.00	0	493,695.16		2,177.51	
201+880.00	0	493,695.16		0.00	
201+900.00	0	493,695.16		0.00	
201+920.00	172.54	495,420.53		1,725.37	
201+940.00	117.37	498,319.63		2,899.09	
201+960.00	121.91	500,712.41		2,392.78	
201+980.00	141.36	503,345.11		2,632.70	
202+000.00	131.55	506,074.23		2,729.12	
202+020.00	123.82	508,627.92		2,553.69	
202+040.00	93.18	510,797.88		2,169.96	
202+060.00	50.98	512,239.45		1,441.57	
202+080.00	49.6	513,245.30		1,005.85	
202+100.00	43	514,171.38		926.08	
202+120.00	38.08	514,982.21		810.83	
202+140.00	0	515,362.98		380.78	
202+160.00	0	515,362.98		0.00	
202+180.00	0	515,362.98		0.00	
202+200.00	0	515,362.98		0.00	
202+220.00	73.22	516,095.23		732.24	
202+240.00	80.7	517,634.50		1,539.28	
202+260.00	97.19	519,413.44		1,778.93	
202+280.00	119.49	521,580.25		2,166.81	
202+300.00	140.13	524,176.43		2,596.18	
202+320.00	63.81	526,215.81		2,039.38	
202+340.00	66.23	527,516.19		1,300.37	
202+360.00	64.12	528,819.69		1,303.50	
202+376.01	52.46	529,753.19		933.50	

يعتمد
مهندس الإشراف للهيئة
م/محمود حسين
/م

عن الاستشاري أ.د حسن مهدي
م/عبد الحميد علاء الدين
م/أحمد عزب
م/أحمد عزب

عن الشركة
م/محمد حامد أبوعجيبة
م/محمد عبد الرحمن



	مشروع القطار الكهربائي السريع	 الهيئة القومية للإسكاف مكتب أد/حسن مهدي للإستشارات الهندسية
	إستكمال إسناد أعمال الجسر الترابي والأعمال الصناعية بقطاعات مشروع إنشاء القطار الكهربائي	
	السريع (أكتوبر - أبوسمبل) تنفيذ شركة أبو عجيله للمقاولات العامة والتوريدات العمومية	

حصر كمية الاحلال في السفو ابتداء من شهر سبتمبر ٢٠٢٢

Station	Total Cut Area(m2)	Cum. Cut Vol(m3)	As Built vol.cut		
				CUT VOL(m3)	Total.Qty
201+920.00	172.54	495,420.53	CUT	1,725.37	36058.01
201+940.00	117.37	498,319.63		2,899.09	
201+960.00	121.91	500,712.41		2,392.78	
201+980.00	141.36	503,345.11		2,632.70	
202+000.00	131.55	506,074.23		2,729.12	
202+020.00	123.82	508,627.92		2,553.69	
202+040.00	93.18	510,797.88		2,169.96	
202+060.00	50.98	512,239.45		1,441.57	
202+080.00	49.6	513,245.30		1,005.85	
202+100.00	43	514,171.38		926.08	
202+120.00	38.08	514,982.21		810.83	
202+140.00	0	515,362.98		380.78	
202+160.00	0	515,362.98		0.00	
202+180.00	0	515,362.98		0.00	
202+200.00	0	515,362.98		0.00	
202+220.00	73.22	516,095.23		732.24	
202+240.00	80.7	517,634.50		1,539.28	
202+260.00	97.19	519,413.44		1,778.93	
202+280.00	119.49	521,580.25		2,166.81	
202+300.00	140.13	524,176.43		2,596.18	
202+320.00	63.81	526,215.81		2,039.38	
202+340.00	66.23	527,516.19		1,300.37	
202+360.00	64.12	528,819.69		1,303.50	
202+376.01	52.46	529,753.19		933.50	

عن الاستشاري أد حسن مهدي

م/ احمد عزب
م/ محمود غرابي

عن استشاري المساحة

م/ محمد عبدالرحمن

م/ محمد عبدالرحمن
م/ محمد عبدالرحمن

عن الشركة

م/ احمد فتحي

م/ احمد فتحي
م/ احمد فتحي
ABUAGLA
إستشارات الهندسية - القاهرة
١٩٩-١٦١-٦٠٩

	مشروع القطار الكهربائي السريع	 مكتب المهندس مهدي للاستشارات الهندسية
	إستكمال أعمال الجسر الترابي لمسار القطار الكهربائي السريع الخط الثاني (الفيوم / بني سويف - أيا سمبل) (مرحلة الجسور والأساس والأبواب) القطاع الثاني (بني مزار / منقلاوط)	
	تنفيذ شركة أبو عجيله للمقاولات العامة والتوريدات العمومية كميات حتي مستخلص جاري (١) جاري لعقد رقم (٢٠٢٥/٢٠٢٤/٢٠٩) بتاريخ 2024/4/1 ASBUILT	

بند رقم (١-٣) : أعمال تحميل وتوريد ونقل أتربة مطابقة للمواصفات وتشغيلها باستخدام آلات التسوية بسمك لا يزيد عن ٥٠ سم حتى منسوب (2- متر) أسفل منسوب الفرمة و بسمك لا يزيد عن ٢٥ سم اعلي من منسوب (2- متر) من منسوب الفرمة لاستكمال المنسوب التصميمي الخ

Station	Total Fill Area(m2)	Cum. Fill Vol(m3)	As Built vol.Fill				اجمالي الكميات ابتداء من ٢٠٢٤/٢/٢٢
			FILL	Fill VOL(m3)	Total.Qty	Fill VOL(m3) ابتداء من ٢٠٢٤/٢/٢٢	
201+920.00	202.61	2026.07	FILL	2026.07	100122.28	582.22	9669.67
201+940.00	227.66	6,328.78		4,302.71		1,170.55	
201+960.00	248.2	11,087.40		4,758.61		1,162.28	
201+980.00	274.47	16,314.06		5,226.57		1,140.36	
202+000.00	262.01	21,578.88		5,364.82		1,142.87	
202+020.00	243.79	26,736.89		5,058.01		1,149.44	
202+040.00	194.01	31,114.85		4,377.95		1,134.32	
202+060.00	362.48	36,679.73		5,564.88		561.35	
202+080.00	341.72	43,721.80		7,042.07		0.00	
202+100.00	314.56	50,284.61		6,562.81		0.00	
202+120.00	301.56	56,445.77		6,161.16		0.00	
202+140.00	0	59,461.36		3,015.59		0.00	
202+160.00	0	59,461.36		0.00		0.00	
202+180.00	0	59,461.36		0.00		0.00	
202+200.00	0	59,461.36		0.00		0.00	
202+220.00	317.97	62,641.01		3,179.66		162.54	
202+240.00	312.67	68,947.36		6,306.35		325.06	
202+260.00	320.6	75,280.03		6,332.66		321.62	
202+280.00	330.13	81,787.33		6,507.30		322.02	
202+300.00	335.88	88,447.44		6,660.11		328.98	
202+320.00	141.42	93,220.38		4,772.95		166.06	
202+340.00	132.47	95,959.23		2,738.85		0.00	
202+360.00	116.74	98,451.35		2492.11		0	
202+376.01	91.94	100,122.29		1,670.94		0.00	

عن الاستشاري أد حسن مهدي
مدير المشروع
م / محمود هريز
م / احمد عزب

المساحة
م/ محمد عبدالرحمن
١٨/١٢

عن الشركة
م / احمد فتح
م / احمد
١٢
١٩٧٨
ABUAGLA
ب ض ١٠٩ - ١٥١ - ٦٠٩

	مشروع القطار الكهربائي السريع	 الهيئة القومية للإتقان مكتب أ.د/حسن مهدي للإستشارات الهندسية
	إستكمال أعمال الجسر الترابي لمسار القطار الكهربائي السريع الخط الثاني (الفيوم / بني سويف - أبو سمبل) (مرحلة الجسور والتأسيس والأساس) القطاع الثاني (بني مزار / متفلوط)	
	تنفيذ شركة أبو عجيبة للمقاولات العامة والتوريدات العمومية حصر اجمالي لكميات الردم	

بند رقم (١-٣) : أعمال تحميل وتوريد ونقل أتربة مطابقة للمواصفات وتشغيلها باستخدام آلات التسوية بسمك لا يزيد عن ٥٠ سم حتى منسوب (-2 متر) أسفل منسوب القرمه و بسمك لايزيد عن ٢٥سم اعلي من منسوب (-2 متر) من منسوب القرمه لاستكمال المنسوب التصميميالخ

Station	Total Fill Area(m2)	Cum. Fill Vol(m3)	Fill	As Built vol.Fill	
				Fill VOL(m3)	Total.Qty
201+920.00	202.61	2026.07	Fill	2026.07	100122.28
201+940.00	227.66	6,328.78		4,302.71	
201+960.00	248.2	11,087.40		4,758.61	
201+980.00	274.47	16,314.06		5,226.67	
202+000.00	262.01	21,678.88		5,364.82	
202+020.00	243.79	26,736.89		5,058.01	
202+040.00	194.01	31,114.85		4,377.95	
202+060.00	362.48	36,679.73		5,564.88	
202+080.00	341.72	43,721.80		7,042.07	
202+100.00	314.56	50,284.61		6,562.81	
202+120.00	301.56	56,445.77		6,161.16	
202+140.00	0	59,461.36		3,015.59	
202+160.00	0	59,461.36		0.00	
202+180.00	0	59,461.36		0.00	
202+200.00	0	59,461.36		0.00	
202+220.00	317.97	62,641.01		3,179.66	
202+240.00	312.67	68,947.36		6,306.35	
202+260.00	320.6	75,280.03		6,332.66	
202+280.00	330.13	81,787.33		6,507.30	
202+300.00	335.88	88,447.44		6,660.11	
202+320.00	141.42	93,220.38		4,772.95	
202+340.00	132.47	95,959.23		2,738.85	
202+360.00	116.74	98,451.35		2492.11	
202+376.01	91.94	100,122.29		1,670.94	

اجمالي كميات الردم المصروفه سابقا	0
اجمالي كميات الردم الفعلية الحالية بعد خصم سمك خرسانه الميول	100122.28
كمية خصم سمك خرسانه الميول	911

عن الاستشاري المساحة
 م/محمد عبد الرحمن
 م/احمد عزب
 م/محمود غريب
 عن الاستشاري أ.د/حسن مهدي
 م/احمد عزب
 م/محمود غريب



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name [Signature]	Sign [Signature]	Date 15-8-2022																
Received by Employers Representative		UIR	Time 2																
			<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>EW</td> <td>OT</td> <td>15</td> <td>8</td> <td>22</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	EW	OT	15	8	22		
C1	C2	C3	DD	MM	YY	HH	MM												
KP	EW	OT	15	8	22														
CODE-1	CODE-2	CODE-3	CODE-4																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 202+376	
	E=260126.0446 N=3137487.7094	E=260129.6912 N=3135991.0324
Inspection description[Disinfection Of Trees Cutting From st (200+876) to st (202+376)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))

[Signature]

Comments by: General consultant (systra)

- Trees No. was checked only by xyz and under their own responsibility
- you must follow specs and design dr

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	[Signature]	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	[Signature]	15-8-2022		A	
	H.M.C	[Signature]	15-8-2022		A	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024		AWC	

* Designer

** Alignment: Bridges: Culvert Only

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name [Signature]	Sign [Signature]	Date 15-8-2022																
Received by Employers Representative		UIR	Time 2																
			<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>EW</td> <td>OT</td> <td>15</td> <td>8</td> <td>22</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	EW	OT	15	8	22		
C1	C2	C3	DD	MM	YY	HH	MM												
KP	EW	OT	15	8	22														
CODE-1	CODE-2	CODE-3	CODE-4																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 202+376	
	E=260126.0446 N=3137487.7094	E=260129.6912 N=3135991.0324
Inspection description[Disinfection Of Trees Cutting From st (200+876) to st (202+376)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

[Signature]

Comments by: General consultant (systra)

- Trees No. was checked only by xyz and under their own responsibility
- you must follow specs and design dr

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	[Signature]	[Signature]			A-AWC-R	
Contractor QA\QC*	XYZ	[Signature]	15-8-2022		A	
	H.M.C	[Signature]	15-8-2022		A	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024		AWC	

* Designer

** Alignment: Bridges: Culvert Only

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيل للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
	20-10-2022	3								
Received by Employers Representative			C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	20	10	22		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5						

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+686 E=260126.0446 E=260172.2356 N=3137487.7094 N=3136679.1711	
Inspection description/ تطهير بعد قطع الاشجار Disinfection of crops and trees cutting from st (200+876) to st (201+686)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
---	--

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA/QC*	XYZ		20-10-2022	14:30	A	
	H.M.C		20/10/2022	15:00	A	
GARB**						
Employers Representative						

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
	20-10-2022	4								
Received by Employers Representative			C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	20	10	28		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5						

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+686 TO 201+846	
	E=260172.2356 N=3136679.1711	E=260170.8362 N=3136519.1841
Inspection description/		
Disinfection of crops and trees cutting from st (201+686) to st (201+846) تم تعقيم بعد قطع الأشجار		

منطقة قطع

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. (xyz))	Comments by: General consultant (systra)

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA/QC*	XYZ		20-10-2022	16:00	A	
	H.M.C		20/10/2022	16:30		
GARB**						
Employers Representative						

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
	محمد بن محمد	[Signature]	20-10-2022	5						
Received by Employers Representative		[Stamp]	C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	20	10	22		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+966 TO 202+376	
	E=260166.4277	E=260129.6912
	N=3136399.268	N=3135991.0324
<u>Inspection description/</u> Disinfection of crops and trees cutting from st (201+966) to st (202+376)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT: (xyz))

Comments by: General consultant (systra)

[Signature]

- Levels and coordinater were checked only by xyz and under their own responsibility
 - you must follow specs, design dng and geo-technical report.
 - this work was inspected only by xyz and

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	محمد بن محمد	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	[Signature]	20-10-2022	14:30		
	H.M.C	[Signature]	20/10/2022	14:30		
GARB**						
Employers Representative	Khaled alr	[Signature]	23/9/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR. Hassan Mahdy (H.M.C)					
Issued by Contractor	Name	Sign	Date					
			25-10-2022					
Received by Employers Representative	Name	Sign	Time					
			6					
C1		C2	C3	DD	MM	YY	HH	MM
KP		EW	OT	25	10	22		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+466 TO 201+666	
	E=260165.8013	E=260172.0505
	N=3136899.0593	N=3136699.1703
Inspection description/ As-Built for rock surface from st (201+466) to st (201+666) الرفع المسام + معاينة السطح الصخري (المسحوب الأول)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

اعمل قطع جانبي الهيئة العامة للمقاولات العامة	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C - you must follow spec and geo-technical report
---	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer					A-AWC-R	
Contractor QA/QC*	XYZ		25-10-2022	13:00	A	
	H.M.C		25/10/2022	13:00	A	
GARB**						
Employers Representative	Khaled ali		23/9/2024			



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)			
Issued by Contractor	Name	Sign	Date	Time			
	29-10-2022	7					
Received by Employers Representative	C1	C2	C3	DD	MM	YY	HH
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	200+876 TO 201+466		
	E=260126.0446	E=260165.8013	
	N=3137487.7094	N=3136899.0593	
Inspection description[الرفع المساحي + المعاينة للطرح المرفوض (المسوح الأول) As-Built for rock surface from st (200+876) to st (201+466)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

As-built	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C. - you must follow specs and design drawings.
----------	--

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	محمد عبد الحليم	محمد عبد الحليم	29-10-2022	12:00	A	
Contractor QA/QC*	XYZ	محمد عبد الحليم	29/10/2022		A	
GARB**						
Employers Representative	Khaled ali	كhaled ali	23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة زينة حيلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
	أحمد محمد	[Signature]	2-11-2022	8						
Received by Employers Representative	[Signature]	[Signature]	C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	2	11	22		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+036 TO 201+086	
	E=260137.1186 N=3137328.0971	E=260140.5793 N=3137278.217
<u>Inspection description/</u> As-Built for rock surface from st (201+036) to st (201+086)		

الرفع المسامى + معاينة السطح المجرى (المستوى المظن) الثالث

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
2/11/2022	

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))	Comments by: General consultant (systra)
	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C - you must follow spec and geo-technical report

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	أحمد محمد	[Signature]					
Contractor QA/QC*	XYZ	[Signature]	2-11-2022	17:30	A		
	H.M.C	[Signature]	2/11/2022	13:30	A		
GARB**							
Employers Representative	Khaled ali	[Signature]	23/9/2024				

مكتبة A / مكتبة A
التصديق الكبريات / التصديق الكبريات
حاصل في عمليات التفتيش

Page 1 of 1

شیریں

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عبيدة المقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	محمد أبو بكر	Date	6-11-2022						
	Sign		Time	10						
Received by Employers Representative	UIR		C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	6	11	2022		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+156 TO 201+246	
	E=260145.4242 N=3137208.3848	E=260151.6535 N=3137118.6007
<u>Inspection description:</u> As-Built for rock surface from st (201+156) to st (201+246)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate:

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))

Comments by: General consultant (systra)

 مستشار استشارات المقاولات العامة - الخرج	- Levels and Coordinates were checked only by xyz and under their own responsibility. - This work was inspected only by xyz and H.M.C. you must follow specs and geo-technical report
--	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	محمد أبو بكر				A-AWC-R	
Contractor QA\QC*	XYZ		6-11-2022	14:00	A	
	H.M.C		6/11/2022	14:30	A	
GARB**						
Employers Representative	Khaled ali		23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أ.إ.ص.م العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
	24-11-2022	12								
Received by Employers Representative	UIR		C1	C2	C3	DO	MM	YY	HH	MM
			KP	EW	OT	24	11	22		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5						

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+076 TO 201+156		
	E=260139.8871	E=260145.4242	
	N=3137288.193	N=3137208.3848	
Inspection description:			
As-Built for rock surface from st (201+076) to st (201+156)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. xyz)

التحقيق الهندسي
مكتب أ.إ.ص.م
للإشراف الهندسي

Comments by: General consultant (systra)

- Levels and Coordinates were checked only by xyz and under their own responsibility
- This work was inspected only by xyz and you must follow specs and geo-technical report

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	أ.إ.ص.م العامة					
Contractor QA/QC*	XYZ		24-11-2022	12:00	A	
	H.M.C		24/11/2022	12:30	A	
GARB**						
Employers Representative	Khaled di		23/9/2014			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name أبو عجلة	Sign أبو عجلة	Date 7-12-2022																
Received by Employers Representative			Time 13																
		UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>EW</td> <td>OT</td> <td>7</td> <td>12</td> <td>23</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	EW	OT	7	12	23		
C1	C2	C3	DD	MM	YY	HH	MM												
KP	EW	OT	7	12	23														
CODE-1	CODE-2	CODE-3	CODE-4																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+286 TO 201+386	
	E=260154.422 N=3137078.6966	E=260161.1582 N=3136978.9239
<u>Inspection description/</u> As-Built for rock surface from st (201+286) to st (201+386)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT: (xyz))

Comments by: General consultant (systra)



- Levels and coordinates were checked only by xyz and under their own responsibility
- This work was inspected only by xyz and H.M.C.
- you must follow specs and geo-technical report

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	أبو عجلة	أبو عجلة			A-AWC-R	
Contractor QA/QC*	XYZ	أبو عجلة	7-12-2022	14:00	A	
	H.M.C	أبو عجلة	7/12/2022	14:30	A	
GARB**						
Employers Representative	Khaled ali	أبو عجلة	23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name Sign	Date	Time
Received by Employers Representative	Sign	13-12-2022	14
UIR		C1 KP	C2 EW
		C3 OT	DD 13
		MM 12	YY 22
		HH	MM
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+386 TO 201+426	
	E=260161.1582 N=3136978.9239	E=260163.6041 N=3136938.9988
Inspection description/		
الرفع المساحي + معاينة سطح صخره (المنسوب الثالث) As-Built for rock surface from st {201+386} to st {201+426}		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

	- Levels and coordinates were checked only by systra and under their own responsibility - This work was inspected only by systra and H.M.C - you must follow specs and geo-technical report
---	--

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer					A-AWC-R	
Contractor QA/QC*	XYZ		13-12-2022	12:10	A	
	H.M.C		13/12/2022	12:10	A	
GARB**						
Employers Representative	Khaled al.		23/12/2022			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)			
Issued by Contractor	Name	Sign	Date	Time			
	13-12-2022	16					
Received by Employers Representative	C1	C2	C3	DD	MM	YY	HH
	KP	EW	OT	13	12	23	
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5			

EXPLANATION OF WORK TO BE INSPECTED


Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+036	
	E=260126.0446 N=3137487.7094	E=260137.1186 N=3137328.0971
Inspection description/ الرفع المساحي + معاينة السطح المهيض (المسوح الكاف) - بحسب As-Built for rock surface from st (200+876) to st (201+036)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C - you must follow spec and geo-technical rep.

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer						
Contractor QA/QC*	XYZ		13-12-2022	13:30	A	
	H.M.C		13/12/2022	14:00	A	
GARB**						
Employers Representative	Phaked ali		23/12/2022		A	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR ,Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
			2023-1-3	17						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	3	1	23		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	200+876 TO 201+666		
	E=260126.0446	E=260172.0505	
	N=3137487.7094	N=3136699.1703	
Inspection description/			
As-Built for cut from st (200+876) to st (201+666)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
2023/1/3	

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

مستوى المقاولات العامة - الخطة المرسومة

- Levels and coordinates were checked only by XYZ and under their own responsibility
- you must follow specs and design drawings

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor	XYZ		3-1-2023	14:00	A	
QA/QC*	H.M.C		3/1/2023	19:00		
GARB**						
Employers Representative	Khaled Ali		23/9/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name 1575 Sign 	Date	13-6-2023
Received by Employers Representative	Time 18	Time	18
Received by Employers Representative	UIR	C1 KP	C2 EW
		C3 OT	DD 13
		MM 6	YY 23
		HH	MM
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+660	
	E=260126.0446 N=3137487.7094	E=260171.9793 N=3136705.1798
Inspection description		
As-Built for cut from st (200+876) to st (201+660)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
12/6/2023	

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

as built for cut from st (200+876) to st (201+660)

- levels and coordinates were checked only by xyz and under their own responsibility
- you must follow spec and design dwg.

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA/QC*	XYZ		13-6-2023	9:00	A	
	H.M.C		13/6/2023			
GARB**						
Employers Representative	Khaled Ali		23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله والمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name Sign 24-8-2023	Date	Time 19
Received by Employers Representative	Sign 23	Time	

CODE -1	CODE -2	CODE -3	CODE -4	CODE -5
---------	---------	---------	---------	---------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+840 E=260126.0446 N=3137487.7094	E=260170.9813 N=3136525.1923
Inspection description/ As-Built for cut from st (200+876) to st (201+840)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
24/8/2023	

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

asbuilt قطاع الضلع الخلد لاري	- Levels and coordinates were checked only by xyz and under their own responsibility - you must follow specs and design drrg
-------------------------------------	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer					A-AWC-R	
Contractor	XYZ		26-8-2023	10:00	A	
QA/QC*	H.M.C		26/8/2023	10:15	A	
GARB**						
Employers Representative	Khaled ali		23/8/2023			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name وليد فهد محمد	Date	9-11-2023
Received by Employers Representative	Sign وليد فهد محمد	REQ.NUM	20
Received by Employers Representative	UIR	C1 KP	C2 SU
		C3 OT	DD 9
		MM 11	YY 23
		HH	MM
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description/ تشييد قاع إحلل from st (202+220) to st (202+300)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))

Comments by: General consultant (systra)

 	- levels and coordinates were checked only by xyz and under their own responsibility - No objection according to the attached reports and lab. results.
---	--

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد فهد محمد	وليد فهد محمد	19-11-2023	10:00	(A)	
Contractor QA/QC*	XYZ	محمد علي محمد	9/11/2023	11:00	A	
Employers Representative	Khaled ali		23/11/2023			

* Designer

** Alignment: Bridges: Culvert Only

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عبيدة للمقاولات 2023	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name [Signature] [Stamp: ABU ABIDA]	Date	REQ. NUM 22															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>21</td> <td>11</td> <td>23</td> <td>2</td> <td>30</td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	21	11	23	2	30
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT	21	11	23	2	30											
CODE-1	CODE-2	CODE-3	CODE-4															
CODE-5																		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+000 TO 202+120	
	E=260164.6561 N=3136365.3242	E=260156.5571 N=3136245.6007
Inspection description/ تنشغيل قاع إحلال from st (202+000) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
[Signature] [Stamp: GARB SURVEY CONSATANT]	- Levels and coordinates were checked only by XYZ and under their own responsibility - This work was checked only by XYZ and H.M.C. - you must follow speed and design drawing and geo-technical report

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time			
Contractor Engineer	[Signature]	[Signature]					
Contractor QA/QC*	XYZ	[Signature]	21-11-2023	3:15	(A)		
	H.M.C	[Signature]	21/11/2023	3:00	A		
GARB**							
Employers Representative	Khaled ali	[Signature]	23/11/2024		Any		

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown:

Contractor Company	أبو عجمية للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name:  Sign:  Date: 21-11-2023	REQ. NUM	23															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>22</td> <td>11</td> <td>23</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	22	11	23		
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT	22	11	23													
CODE-1	CODE-2	CODE-3	CODE-4															

EXPLANATION OF WORK TO BE INSPECTED


Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300 E=260147.6147 E=260139.0278 N=3136146.003 N=3136066.4661	
<u>Inspection description/</u> طبقة ردم منسوب (-9.5) متر from st (202+220) to st (202+300)		


INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))	Comments by: General consultant (systra)
	- No objection, according to the attached reports and Lab. results. - you must follow specs and design drawings

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time			
Contractor Engineer	وليد عوريجي						
Contractor QA/QC*	XYZ		22-11-2023	3:45	(A)		
	H.M.C		22/11/2023	11:00	A		
GARB**							
Employers Representative	Fhaled ali		23/10/2024				

RECEIPT of NOTIFICATION Minimum Notice Period not less than 24 Hours
The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة المقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name	Sign	Date
	[Signature]		25-11-2023
Received by Employers Representative	[Signature]		REQ.NUM
		24	

C1	C2	C3	D0	MM	YY	HH	MM
AP	SU	OT	25	11	23		

CODE-1
CODE-2
CODE-3
CODE-4
CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+000 TO 202+020	
	E=260164.6561	E=260163.5058
	N=3136365.3242	N=3136345.3573

Inspection description:

منطقة ردم منسوب (13) متر from st (202+000) to st (202+020)

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (systa)) 	Comments by: General consultant (systa) - No objection, according to the attached reports and lab. results. - you must follow specs and design drawings
---	--

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	[Signature]	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	[Signature]	25-11-2023	12:30	(A)	
	H.M.C	[Signature]	25/11/2023	11:00	A	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024			



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)					
Issued by Contractor	Name [Signature]	Date	28-11-2023					
Received by Employers Representative	Sign [Signature]	REQ NUM	25					
UIR	C1 KP	C2 SU	C3 OT	DD 28	MM 11	YY 23	HH 11	MM 00

CODE-1

CODE-2-109

CODE-3

CODE-4

CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300 E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description منسوب (9-متر) from st (202+220) to st (202+300)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

تم استلام استبيان المعاينة
والتأكد من أن العمل جاهز للمعاينة

- No objection, according to the attached reports and lab. results
- you must follow specs and design dng.

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمود	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	[Signature]	28/11/2023	3:30	A	
	H.M.C	[Signature]	28/11/2023	11:00	A	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company			Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name	Sign	Date	REQ.NUM																
			29-11-2023	26																
Received by Employers Representative			UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DO</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>29</td> <td>11</td> <td>23</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DO	MM	YY	HH	MM	KP	SU	OT	29	11	23		
C1	C2	C3	DO	MM	YY	HH	MM													
KP	SU	OT	29	11	23															

CODE-1

CODE-2

CODE-3

CODE-4

CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+060 TO 202+080		
	E=260160.9658	E=260159.576	
	N=3136305.4382	N=3136285.4865	
Inspection description: from st (202+060) to st (202+080) طبقة ردم منسوب (-11) متر			



INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))	Comments by: General consultant (systra)
	- No objection, according to the attached reports and lab. results. - you must follow specs and design draw

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد فريد					
Contractor QA/QC*	XYZ		29-11-2023	1:15	(A)	
	H.M.C		29-11-2023	12:45	A	
GARB**						
Employers Representative	Khaled ali		29/11/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name وليد محمد	Date	29-11-2023															
Received by Employers Representative	Sign [Signature]	REQ.NUM	27															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>29</td> <td>11</td> <td>23</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	29	11	23		
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT	29	11	23													
CODE-1	CODE-2	CODE-3	CODE-4															
CODE-5																		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+080 TO 202+120	
	E=260159.576 N=3136285.4865	E=260156.5571 N=3136245.6007
Inspection description/		
منطقة ردم منسوب (10.5-) متر from st (202+080) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSANTANT.(xyz))	Comments by: General consultant (systra)
	-No objection, according to the attached reports and lab. results -you must follow specs and design dwg

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمد	[Signature]	29-11-2023	11:30	(A)	
Contractor QA/QC*	XYZ	[Signature]	29-11-2023	12:30	A11	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	157137 أبو عجلة للتقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name وليد محمد Sign [Signature] Date 30-11-2023	REQ. NUM	28
Received by Employers Representative	UIR	C1 KP	C2 SU
		C3 OT	DD 30
			MM 11
			YY 23
			HH MM

CODE-1

CODE-2

CODE-3

CODE-4

CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+000 TO 202+020 E=260164.6561 N=3136365.3242	E=260163.5058 N=3136345.3573
Inspection description: ردم طبقة ردم منسوب (-12.5) متر from st (202+000) to st (202+020)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (XYZ)) [Signature] [Stamp]	Comments by: General consultant (systra) - No objection, according to the attached reports and lab. results. - you must follow spec and design draw
---	---

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمد	[Signature]				
Contractor QA/QC*	XYZ	[Signature]	30-11-2023	13:00	A	
	H.M.C	[Signature]	30/11/2023	12:30 pm	A	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name 157537	Sign	Date 3-12-2023
Received by Employers Representative		UIR	REQ.NUM 30
		C1 KP	C2 SU
		C3 OT	DD
		MM	YY 23
		HH	MM
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+100 E=260160.9658 N=3136305.4382	E=260158.1064 N=3136265.5406
Inspection description منطقة ردم مسوب (-10.5) متر from st (202+060) to st (202+100)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz)) مستشاري المساحة (xyz)	Comments by: General consultant (systra) - No objection, according to the attached reports and lab. results. - you must follow specs and design d.
--	--

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA/QC*	XYZ		3-12-2023	4:15	(A)	
	H.M.C		3/12/2023	2:30pm	AWC	
GARB**						
Employers Representative	Khaled ali		28/9/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للمشاورات الهندسية



شركة السيترا للتصميم والدراسات



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ. NUM						
	وليد عيسى	وليد عيسى	7-12-2023	32						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT				23	
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5						

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+060 TO 202+120		
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007	
Inspection description/			
من طرقة ردم ملمسوب (-10) متر from st (202+060) to st (202+120)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as Indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
لا يوجد اعتراض على النتائج	-No objection, according to the attached reports and lab. results. -you must follow specs and design drug

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد عيسى	وليد عيسى					
Contractor QA/QC*	XYZ	محمد علي	7-12-2023	1:30	(A)		
	H.M.C	خالد علي	7/12/2023	12:15	A		
GARB**							
Employers Representative	Khaled ali	خالد علي	23/12/2024		AWC		



UNIVERSAL INSPECTION REQUEST



مكتب أمان مهاب
للإشراف الهندسية



الهيئة العامة للإشراف



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR. Hassan Mahdy (H.M.C)
Issued by Contractor	Name	Sign	Date	REQ. NUM
	وليد محمود	وليد	9-12-2023	33
Received by Employers Representative	UIR		C1 C2 C3 DO MM YY HH MM	
			KP SU OT	23
CODE-1		CODE-2	CODE-3	CODE-4
				CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+220 TO 202+300		
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661	
Inspection description/ من تسليم طبقة ردم منسوب (-7.5) متر from st (202+220) to st (202+300)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT,xyz)

Comments by: General consultant (systra)

م.م. وليد محمود

- No objection, according to the attached reports and lab. results.
- you must follow specs and design

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمود				A-AWC-R	
Contractor QA/QC*	XYZ	وليد محمود	9-12-2023	3:30	(A)	
	H.M.C	وليد محمود	9/12/2023	3:10	A	
GARB**						
Employers Representative	Khaled ali		23/9/2024		AWC	



UNIVERSAL INSPECTION REQUEST



مكتب أ.أ.أ. م.أ.أ.
للإشراف الهندسية



الهيئة العامة للإشراف الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR. Hassan Mahdy (H.M.C)					
Issued by Contractor	Name	Sign	Date	REQ. NUM					
	أ.أ.أ. م.أ.أ.	أ.أ.أ. م.أ.أ.	13-12-2023	35					
Received by Employers Representative	UIR	G1	C2	C3	DD	MM	YY	HH	MM
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5	

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+060 TO 202+120		
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007	
Inspection description/ منطقة ردم طلبة (9- متر from st (202+060) to st (202+120)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. (xyz))	Comments by: General consultant (systra)
أ.أ.أ. م.أ.أ.	- No objection, according to the attached reports and lab. results. - you must follow specs and design drawings.

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	أ.أ.أ. م.أ.أ.	أ.أ.أ. م.أ.أ.	13-12-2023	4:00	(A)		
Contractor QA/QC*	XYZ	أ.أ.أ. م.أ.أ.	13-12-2023	3:00	Awc		
GARB**							
Employers Representative	Khaled ali	أ.أ.أ. م.أ.أ.	23/9/2024		Awc		

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



المهندسة العامة
للإستشارات الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)					
Issued by Contractor	Name	Sign	Date	REQ.NUM					
	16-12-2023	36							
Received by Employers Representative	UIR	G1 KP	G2 SU	G3 OT	DD	MM	YY 23	HH	MM
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description: تسليم طبقة ردم مسلوب (7-متر) from st (202+220) to st (202+300)		

INSPECTION DETAILS The following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT: (xyz))

مهندس القطار الكهربائي السريع - الخط الثاني

Comments by: General consultant (systra)

- No objection, according to the attached reports and lab. results.
- you must follow specs and design dirg.

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	د. محمد د. محمد				A-AWC-R	
Contractor QA/QC*	XYZ	عبد الرحمن العاصمي	16-12-2023	3:15	A	
	H.M.C	م. محمد علي	16/12/2023	3:00	A	
GARB**						
Employers Representative	Khaled ali		28/12/2024		Awc	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للطرق
والبنية التحتية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)					
Issued by Contractor	Name	Sign	Date	REQ.NUM					
	وليد فلاح	وليد فلاح	17-12-2023	37					
Received by Employers Representative	UIR	C1	C2	C3	DD	MM	YY	HH	MM

EXPLANATION OF WORK TO BE INSPECTED			
Area	Element		Item
From 200+876 To 202+376	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007	
Inspection description:			
منطقة ردم ملسوب (-8.5) متر from st (202+060) to st (202+120)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by (GARB SURVEY CONSULTANT xyz)	Comments by: General consultant (systra)
استاذ المهندس مستوى التفتيش الكفائي الى الحد - 8.5	- No objection, according to the attached reports and lab. results. - you must follow specs and design dwg

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد فلاح	وليد فلاح				تزامنا مع العمل
Contractor QA/QC*	XYZ	وليد فلاح	17-12-2023	13:00	A	OK
	H.M.C	كhaled ali	17-12-2023	11:00	Awc	OK
GARB**						
Employers Representative	Khaled ali	Khaled ali	20/12/2024		Awc	



UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإشراف الهندسية



المشاور الهندسي الدكتور
أدريس مهدي



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown:

Contractor Company	البنية التحتية للطرق والبنية التحتية	Designer Company*	DR. Hassan Mahdy (H.M.C)						
Issued by Contractor	Name: <u>أدريس مهدي</u> Sign: <u>[Signature]</u>	Date	19-12-2023						
Received by Employers Representative	UIR	REQ.NUM	38						
		C1	C2	C3	DD	MM	YY	HH	MM
		AP	SU	OT			YY		
CODE-1	CODE-2: 203-161-199	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+576	202+220 TO 202+300	
	E=260147.5147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description (		
from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (7,0-)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	M5 Reference	

Comments by: (GARB SURVEY CONSULTANT: XYZ)

تم فحص القطاع ووجدنا
مستوى تسطير أكثر من المطلوب - الخط الذي

Comments by: General consultant (systra)

- No objection, according to the attached reports and lab. results.
- you must follow specs and design drug

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	أدريس مهدي	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	[Signature]	19-12-2023	3:30	A	
	H.M.C	[Signature]	19-12-2023	11:30	A	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)				
Issued by Contractor	Name	Sign	Date				
	وليد محمود محمد		20-12-2023				
Received by Employers Representative		REQ.NUM	39				
C1	C2	C3	DD	MM	YY	HH	MM
	KP	SU	OT			23	

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description/		
من (8-) متر from st (202+060) to st (202+120) طبقة ردم منسوب		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

تمت المعاينة وفقاً للمواصفات
والمواصفات الفنية
والمواصفات الهندسية
والمواصفات الإدارية

- No objection, according to the attached reports and lab. results.
- You must follow specs and design draw

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمود محمد				A-AWC-R	
Contractor QA/QC*	XYZ		20-12-2023	3:40	A	
	H.M.C		20-12-2023	1:45	A	
GARB**						
Employers Representative	Khaled ali		23/9/2024		A	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للإستثمار



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name Sign 21-12-2023	Date	REQ.NUM 40															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>21</td> <td>12</td> <td>23</td> <td>11</td> <td>30</td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	21	12	23	11	30
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT	21	12	23	11	30											
CODE-1	CODE-2	CODE-3	CODE-4															
CODE-5	CODE-6	CODE-7	CODE-8															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description: منسوب (6-متر) تسليم طبقة ردم منسوب (202+220) إلى (202+300)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT: xyz)	Comments by: General consultant (systra)
	- No objection, according to the attached reports and lab. results. - you must follow specs and design d.

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمد	وليد محمد				
Contractor QA/QC*	XYZ	عبد الرحمن العرابي	21-12-2023	11:00	A	
	H.M.C	محمد بن عبد الله العرابي	21/12/23	11:30	A	
GARB**						
Employers Representative	Khaled ali		23/12/2023		AWC	

Page 1 of 1

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للمستشارات الهندسية



الهيئة العامة للإعانة



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name وليد محمود	Date	23-12-2023																
Received by Employers Representative	Sign [Signature]	REQ.NUM	43																
		<table border="1"> <tr> <td>G1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>23</td> <td>12</td> <td>23</td> <td></td> <td></td> </tr> </table>	G1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	23	12	23			
G1	C2	C3	DD	MM	YY	HH	MM												
KP	SU	OT	23	12	23														
CODE-1	CODE-2	CODE-3	CODE-4																
			CODE-5																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description/ منسوب (7.5-) متر from st (202+060) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT. (xyz))	Comments by: General consultant (systra)
[Signature]	- No objection, according to the attached reports and lab. results. - you must follow specs and design data

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمود	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	[Signature]	23-12-2023	4:30	A	
	H.M.C	[Signature]	23/12/23	4:00	AWC	
GARB**						
Employers Representative	Khaled Ali	[Signature]	23/12/2023		AWC	


RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours												
The Work described below will be complete and ready for inspection at planned time shown												
Contractor Company	المشاورين العامة				Designer Company*	DR. Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ. NUM								
	ولي محمد محمد		25-12-2023	44								
Received by Employers Representative					C1	C2	C3	DO	MM	YY	HH	MM
					KP	SU	OT			23		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5				

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
<u>Inspection description:</u> من st (202+060) to st (202+120) طبقة ردم مملووب (-7) متر		

INSPECTION DETAILS The following will be ready at the Planned inspection Time	
Planned inspection Date	Planned inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.: xyz) المشاورين العامة ولي محمد محمد	Comments by: General consultant (systra) - No objection, according to the attached reports and lab. results. - you must follow specs and design data
--	--

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	ولي محمد محمد	ولي محمد محمد					
Contractor QA/QC*	XYZ	عبد الرحمن العلي	25-12-2023	4:13	A		
	H.M.C	محمد محمد	25-12-2023	4:10	AWC		
GARB**							
Employers Representative	Khaled ali	Khaled ali	23/9/2024		AWC		

UNIVERSAL INSPECTION REQUEST



مكتب أديسن مهندسي
الاستشارات الهندسية



الهيئة العامة للإستثمار



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أيم جلوبل للمشاريع العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	وليد محمود	[Signature]	28-12-2023	46						
Received by Employers Representative		[Signature]	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT				23	
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5						

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+980	
	E=260165.727 N=3136385.3	
Inspection description: منطقة ردم منسوب (-14) متر from st (201+980)		

INSPECTION DETAILS The Following will be ready at the Planned inspection Time

Planned inspection Date	Planned inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))	Comments by: General consultant (systra)
[Signature]	- No objection, according to the attached reports and lab. results. - you must follow spec and design drawings

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود	[Signature]				
Contractor QA/QC*	XYZ	[Signature]	28-12-2023	12:00	A	[Signature]
	H.M.C	[Signature]	28-12-2023	11:00		
GARB**						
Employers Representative	Khaled Ali	[Signature]	23/9/2024		ANC	

Page 1 of 1

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	157537 مكتب المهندس مهدي للإستشارات الهندسية	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name وليد محجور محمد	Sign 	Date 2-1-2024																
Received by Employers Representative			REQ.NUM 48																
		<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>IP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	IP	SU	OT			24			
C1	C2	C3	DD	MM	YY	HH	MM												
IP	SU	OT			24														

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description/ من تسليم طبقة ردم منسوب (4.5) متر from st (202+220) to st (202+300)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))

Comments by: General consultant (systra)

مستوفى القياسات للكميات التسليم - الفتح الذري

-No objection, according to the attached reports and lab. results.

-you must follow specs and design draw

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محجور محمد					
Contractor QA/QC*	XYZ H.M.C		2-1-2024	10:40	A	
GARB**						
Employers Representative	Khaled ali		23/1/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	137517 الهيئة العامة للغذاء والدواء	Designer Company*	DR. Hassan Mahdy (H.M.C)															
Issued by Contractor	Name Sign 2-1-2024	Date	REQ. NUM 49															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			24		
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT			24													
CODE-1	CODE-2	CODE-3	CODE-4															
CODE-5																		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120 E=260160.9658 E=260156.5571 N=3136305.4382 N=3136245.6007	
Inspection description منطقة ردم منسوب (6-) متر from st (202+060) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))	Comments by: General consultant (systra)
	- No objection, according to the attached reports and lab. results - you must follow specs and design drawings

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد بن وليد بن محمد						
Contractor QA/QC*	XYZ	عبدالله بن محمد	2-1-2024	11:40	A		
	H.M.C	محمد بن محمد	2-1-2024	11:50	AWC		
GARB**							
Employers Representative	Khaleel ali		23/1/2024		AWC		

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة المهندسين مهدي للإستشارات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name وليد محمور	Sign 	Date 2-1-2024																
Received by Employers Representative	UIR	REQ NUM 50																	
		<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			24			
C1	C2	C3	DD	MM	YY	HH	MM												
KP	SU	OT			24														
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+960 TO 202+000	
	E=260166.717 N=3136405.271	E=260164.6561 N=3136365.1247
<u>Inspection description</u> from st (201+960) to st (202+000) طبقة ردم منسوب (-13.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. (xyz)) 	Comments by: General consultant (systra) -No objection, according to the attached reports and lab. results. -you must follow specs and design dr
---	--

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمور					
Contractor QA\QC*	XYZ	عبد الرحمن الشراي	2-1-2024	11:15	A	
	H.M.C	محمود محمد	2-1-2024	11:00	AUC	
GARB**						
Employers Representative	Khaled ali		23/9/2024		AUC	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



المهنة العامة الإستشارية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	REQ.NUM							
	[Signature]		6-1-2024	51							
Received by Employers Representative	[Signature]	[Signature]	UIR	C1	C2	C3	DD	MM	YY	HH	MM
				KP	SU	OT				20	
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+960 TO 202+000		
	E=260166.717 N=3136405.271	E=260164.6561 N=3136365.3242	
<u>Inspection description</u> from st (201+960) to st (202+000) طبقه ردم منسوب (-13) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. xyz)	Comments by: General consultant (systra)
[Signature]	- No objection, according to the attached reports and Lab. results. - you must follow specs and design drag

INSPECTION RESULT

					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمدي	[Signature]				
Contractor QA/QC*	XYZ	عبد الرحمن الفراوان	6-1-2024	4:20	A	يرجى إعادة المعاينة قبل العمل [Signature]
	H.M.C	محمود عولمة	6/1/2023	4:15	AWC	
GARB**						
Employers Representative	Khaled ali	[Signature]	29/9/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
			6-1-2024	52						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT				24	
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5						

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+060 TO 202+120		
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007	
Inspection description/			
from st (202+060) to st (202+120) طبقة ردم منسوب (5.5) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
	- No objection, according to the attached reports and lab results. - you must follow spec and design

INSPECTION RESULT

					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA/QC*	XYZ		6-1-2024	5:00	A	
	H.M.C		6/1/2024	4:40	Awc	
GARB**						
Employers Representative	Khaled ali		23/9/2024		Anrc	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	إي. عجيبة للمقاولات العامة 57577	Designer Company*	DR. Hassan Mahdy (H.M.C)						
Issued by Contractor	Name: Sign:	Date	10-1-2024						
Received by Employers Representative	UIR	REQ.NUM	53						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT			28		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description: من (202+060) to st (202+120) طبقة ردم متسوب (-5) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate



Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSALTANT. xyz)	Comments by: General consultant (systra)
تم استلام القسط من رصف ومناسبات تسوية القسط الكهربائي السريع - القسط الذي	-No objection, according to the attached reports and lab. results. -you must follow specs and design dwg

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد الجورجي	وليد ج				
Contractor QA/QC*	XYZ	عبد الرحمن العرياني	10-1-2024	12:30	A	
	H.M.C	صمودي	10-1-2024	12:00	A	
GARB**						
Employers Representative	Khaled chi		23/9/2024		Awc	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157337	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name:  Sign: 	Date	REQ.NUM
Received by Employers Representative	UIR	10-1-2024	54
		C1 C2 C3 DD MM YY HH MM	
		KP SU OT	23
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+300 TO 202+376	
	E=260139.0278 N=3136066.4661	E=260129.6912 N=3135991.0324
Inspection description/		
from st (202+300) to st (202+376)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time


Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))

Comments by: General consultant (systra)





- levels and coordinates were checked only by xyz and under their own responsibility

- you must follow specs and design dwg. and geo-technical report.

- This work was inspected only by xyz and H.M.C

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمود				A-AWC-R	
Contractor QA/QC*	XYZ		10-1-2024	10:30	A	
	H.M.C		10-1-2024	10:30	AWC	
GARB**						
Employers Representative	Khaled ali		23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name	Sign	Date
	15-1-2024		REQ. NUM
Received by Employers Representative	UIR	C1	C2
		C3	DD
		MM	YY
		HH	MM

CODE-3

CODE-2

CODE-3

CODE-4

CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+300 TO 202+340	
	E=260139.0278 N=3136066.4661	E=260134.2574 N=3136026.7517
Inspection description/		
from st (202+300) to st (202+340) ردم منسوب (8.5-) متر		

INSPECTION DETAILS The following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT - (xyz))	Comments by: General consultant (systra)
تم استلام المخطط من مهندس محمد صالح مهندس محمد صالح - المهندس العام	-you must follow specs and design drug- -you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	علي محمد	علي محمد	16-1-2024	8:30	A	
Contractor QA/QC*	XYZ	علي محمد	15/1/2024	4:30pm	A	
GARB**						
Employers Representative	Khaled ali	علي محمد	26/1/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أ.إ.ص.ن مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
SYSTRA



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name:  Sign: 	Date	REQ. NUM						
Received by Employers Representative	UIR	15-1-2024	56						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT			24		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description:		
تسليم طبقة ردم منسوب (4) متر from st (202+220) to st (202+300)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	


Comments by: (GARB SURVEY CONSANTANT.(xyz))

Comments by: General consultant (systra)



-you must follow specs and design by
-you must do leveling and lining
the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود محمد		15-1-2024			
Contractor QA/QC*	XYZ	عبد الرحمن الزينادي	16-1-2024	9:18	A	
	H.M.C	محمد علي	15/1/2024	5:10	A	
GARB**						
Employers Representative	Khaled ali		15/1/2024		AWC	



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name [Signature] Sign [Signature]	Date	REQ. NUM
Received by Employers Representative	UIR	16-1-2024	57
		C1 C2 C3 DD MM YY HH MM	
		KP SU OT	24
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description/		
منطقة ردم منسوب (-4.5) متر from st (202+060) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT-xyz)	Comments by: General consultant (systra)
 مشروع القمم الكبريتات السريع - القمم الثاني	- you must follow specs and design durg. - you must do landing and lining the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد عمار	[Signature]				
Contractor QA\QC*	XYZ	[Signature]	16-1-2024	3:30	A	
	H.M.C	[Signature]	16/1/24	3:00	Awc	
GARB**						
Employers Representative	Khaled ali	[Signature]	16/1/2024		Awc	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name 157537 Sign وليد خلافة	Date 17-1-2024	REQ.NUM 58															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>17</td> <td>1</td> <td>24</td> <td>4</td> <td>00</td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	17	1	24	4	00
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT	17	1	24	4	00											
CODE-1	CODE-2	CODE-3	CODE-4															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300 E=260147.6147 E=260139.0278 N=3136146.003 N=3136066.4661	
Inspection description/		
from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (3.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: GARB SURVEY CONSATANT (xyz)	Comments by: General consultant (systra)
	-you must follow specs and design dng -you must do leveling and lining the compacted side slope & filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد خلافة					
Contractor QA/QC*	XYZ	عبد الرحمن العرابي	17-1-2024	5:10	A	
	H.M.C	عبد الرحمن العرابي	17/1/2024	4:00	A	
GARB**						
Employers Representative	Khaled Ali		17/1/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أديان مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)					
Issued by Contractor	Name	137537	Sign	Date	REQ.NUM				
	وليد محمد		20-1-2024		59				
Received by Employers Representative	UIR	C1	C2	C3	DO	MM	YY	HH	MM
		KP	SU	OT				24	
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5	

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+300 TO 202+360		
	E=260139.0278 N=3136066.4661	E=260131.7531 N=3136006.9091	
Inspection description			
منسوب (8-متر) from st (202+300) to st (202+360) تسليم طبقة ردم منسوب (8-متر)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: GARB SURVEY CONSATANT. (xyz)	Comments by: General consultant (systra)
ملاحظات المهندس الاستشاري	- you must follow specs and design dng. - you must do leveling and Cinning the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمد					
Contractor QA/QC*	XYZ	عبد الرحمن الزباري	20+2024	10:00	A	
	H.M.C	محمود علي	20/1/2024	9:00	A	
GARB**						
Employers Representative	Khaled ali		20/1/2024		Amr	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name:  Sign: 	Date	REQ.NUM
Received by Employers Representative	UIR	18-1-2024	60
		C1 C2 C3 DD MM YY HH MM	
		KP SU OT	24
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+920 TO 202+000	
	E=260168.4582 N=3136445.233	E=260164.6561 N=3136365.3242
Inspection description:		
منسوب (12.5-) متر from st (201+920) to st (202+000)		


INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
	- you must follow specs and design dng - you must do leveling and lining - the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	أبو عجلة للمقاولات العامة					
Contractor QA/QC*	XYZ	عبد الرحمن الفرحاني	20-1-2024	11:15	A	
	H.M.C	محمد أحمد محمد	20-1-2024	3:45	A	
GARB**						
Employers Representative	Khaled ali		20/1/2024		Amrc	

UNIVERSAL INSPECTION REQUEST



مكتب أ.د/حسن مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR. Hassan Mahdy (H.M.C)
Issued by Contractor	Name: Sign:	Date	REQ.NUM
Received by Employers Representative	UIR	18-1-2024	61
		C1 C2 C3 DO MM YY HH MM	
		KP SU OT	234
CODE-1	CODE-2	CODE-3	CODE-4
CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+020 TO 202+060	
	E=260163.5058 N=3136345.3573	E=260160.9658 N=3136305.4382
Inspection description/		
منسوب (12.5-) متر from st (202+020) to st (202+060)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT: xyz)	Comments by: General consultant (systra)
تم استكمال العمل كالمواصفات مشروع تقسيم الكمبرياش السريع - الحد الثاني	- you must follow specs and design dw - you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	ر.ب. محمور					
Contractor QA/QC*	XYZ		21-1-2024	5:15	A	
	H.M.C		21-1-2024	5:00	A	
GARB**						
Employers Representative	Ali K		20/1/2024		Awc	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name: Sign:	Date	REQ. NUM
Received by Employers Representative	UIR	21-1-2024	62
		C1 C2 C3 DD MM YY HH MM	
		KP SU OT	24

CODE-1

CODE-2

CODE-3

CODE-4

CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+300 TO 202+376 E=260139.0278 E=260129.6912 N=3136066.4661 N=3135991.0324	
Inspection description/ منسوب (7.5) متر from st (202+300) to st (202+376) تسليم طبقة ردم منسوب (7.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

	-you must follow specs and design dng -you must do leveling and lining the compacted side slope + filling layer
--	---

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود	وليد محمود				
Contractor QA/QC*	XYZ	عبد الرحمن الابرار	21-1-2024	5:13	A	
	H.M.C	شودا شادي	21-1-2024	5:28	A	
GARB**						
Employers Representative	Khaled ali	كhaled ali	21/1/2024		A	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name 	Date	22-1-2024															
Received by Employers Representative	Sign 	REQ.NUM	63															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>20</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			20		
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT			20													
CODE-1	CODE-2	CODE-3	CODE-4															
CODE-5																		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+920 TO 202+040	
	E=260168.4582 N=3136445.233	E=260162.2757 N=3136325.3952
Inspection description[طبقة ردم منسوب (12-) متر from st (201+920) to st (202+040)		


INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. (xyz))	Comments by: General consultant (systra)
	-you must follow specs and design dw -you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمد					
Contractor QA/QC*	XYZ	عبد الرحمن الخياط	23-1-2024	9:00	A	
	H.M.C	محمود السيد	22-1-2024	5:15	AWC	
GARB**						
Employers Representative	Khaled Ali		23/1/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	وليد محمود	وليد علاف	27-1-2024	65						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT				23	
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+920 TO 202+060		
	E=260168.4582	E=260160.9658	
	N=3136445.233	N=3136305.4382	
Inspection description/			
من 200+876 إلى 202+376 من طبقة ردم منسوب (11.5-) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))

Comments by: General consultant (systra)



-you must follow specs and design drawing
-you must do leveling and lining the compacted sideslope of filling layer

INSPECTION RESULT

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد علاف	وليد علاف					
Contractor QA/QC*	XYZ	أحمد محمد	27-1-24	5:00	A		
	H.M.C	محمد أحمد	27-1-24	4:15	A		
GARB**							
Employers Representative	Khaled ali	كhaled ali	27/1/2024				

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	REQ.NUM							
	رئيس محورد	رئيس خلاف	30-1-2024	66							
Received by Employers Representative			UIR	C1	C2	C3	DD	MM	YY	HH	MM
				KP	SU	OT			24		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+300 TO 202+376		
	E=260139.0278	E=260129.6912	
	N=3136066.4661	N=3135991.0324	
<u>Inspection description:</u> from st (202+300) to st (202+376) تسليم طبقة ردم منسوب (6.5-) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
	-you must follow specs and design drug -you must do leveling and lining the compacted sube slp & filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محورد	وليد طلائع				يتم صيانة القطر قبل التورب
Contractor QA/QC*	XYZ	عبد الرحمن	30-1-2024	4:00	(A)	
	H.M.C	محمد منتصر فوزي	30-1-24	12:30	AWC	
GARB**						
Employers Representative	Khated ali		30/1/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ. NUM						
			12-2-2024	67						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT			27		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+920 TO 202+060		
	E=260168.4582	E=260160.9658	
	N=3136445.233	N=3136305.4382	
Inspection description(			
from st (201+920) to st (202+060) طبقة ردم ملسوب (11-0) متر			

INSPECTION DETAILS The Following will be ready at the Planned inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))	Comments by: General consultant (systra)
	- you must follow specs and design - you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer							
Contractor QA/QC*	XYZ		12-2-2024	3:30	A		
	H.M.C		12/2/24	3:20	A		
GARB**							
Employers Representative	Khaleel ali		12/2/2024				

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



شركة أديس مهدي
للإستشارات الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	وليد محمود	وليد عارف	18-2-2024	68						
Received by Employers Representative	[Stamp]	UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT			24		
CODE-3		CODE-2	CODE-3	CODE-4		CODE-5				

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+300 TO 202+376		
	E=260139.0278	E=260129.6912	
	N=3136066.4661	N=3135991.0324	
<u>Inspection description:</u>			
من تسليم طبقة ردم منسوب (6-) متر from st (202+300) to st (202+376)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT - xyz)	Comments by: General consultant (systra)
	- you must follow specs and design durg - you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد عارف	وليد محمود					
Contractor QA/QC*	XYZ	عبد الرحمن الطراوي	19-2-2024	11:30	A		
	H.M.C	محمد منعم فوزي	19-2-2024	12:00	A		
GARB**							
Employers Representative	rehaled ale		19/2/2024		Arre		

UNIVERSAL INSPECTION REQUEST



مكتب أديان مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	REQ.NUM							
	وليد محمود	وليد محمود	22-2-2024	69							
Received by Employers Representative	[Signature]	[Signature]	UIR	C1	C2	C3	DD	MM	YY	HH	MM
				KP	SU	OT			24		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+920 TO 202+060		
	E=260168.4582 N=3136445.233	E=260160.9658 N=3136305.4382	
Inspection description/			
منطقة ردم منسوب (10.5-) متر from st (201+920) to st (202+060)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time:

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))

مستشار الاستشارات العامة
مستشار الاستشارات العامة
مستشار الاستشارات العامة

Comments by: General consultant (systra)

-you must follow specs and design
-you must do leveling and lining
the compacted side slope & filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود	وليد محمود				
Contractor QA/QC*	XYZ	عبد الرحمن الوائلي	24-2-2024	3:30	A	
	H.M.C	محمد منعم فوزي	24-2-2024	11:00	A	
GARB**						
Employers Representative	Khaled ali	[Signature]	24/2/2024		Amr	

UNIVERSAL INSPECTION REQUEST



مكتب أ.د. حسن مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والمصممات الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أ.د. حسن مهدي للإستشارات الهندسية		Designer Company*	DR .Hassan Mahdy (H.M.C)	
Issued by Contractor	Name و. ل. م. ه. د.	Sign [Signature]	Date	23-3-2024	
Received by Employers Representative	[Signature]		REQ.NUM	74	
UIR			C1 KP	C2 SU	C3 OT
			DO	MM 24	YY 24
			HH	MM	

EXPLANATION OF WORK TO BE INSPECTED			
Area	Element		Item
From 200+876 To 202+376	201+920 TO 202+060		
	E=260168.4582 N=3136445.233	E=260160.9658 N=3136305.4382	
Inspection description/ منطقة ردم منسوب (10- متر) from st (201+920) to st (202+060)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz)) [Signature]	Comments by: General consultant (systra) - you must follow specs and design drawings - you must do leveling and lining the compacted side slope of filling layer
---	--

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	و. ل. م. ه. د.	[Signature]				
Contractor QA/QC*	XYZ	[Signature]	23-3-2024	12:15	A	
	H.M.C	[Signature]	23/3/2024	12:00	A	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/3/2024		AWS	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للإعانة
SHARER



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name: Sign:	Date	31-3-2024						
Received by Employers Representative	UIR	REQ. NUM	75						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT			24		
CODE -1	CODE -2	CODE -3	CODE -4	CODE -5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	E=260168.4582 N=3136445.233	E=260160.9658 N=3136305.4382	
Inspection description:			
منطقة ردم منسوب (9.5) متر from st (201+920) to st (202+060)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (systra))

Comments by: General consultant (systra)

تم فحص الموقع ووجدت أن العمل مطابق للمواصفات
نموذج شتر الكونسلانج - الهندس أدريس مهدي

-you must follow specs and design draw
-you must do leveling and lining
the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود محمد					
Contractor QA/QC*	XYZ عبد الرحمن الطرطوسي		1-4-2024	12:00	A	
	H.M.C	محمود علي	31-3-2024	11:00	A	
GARB**						
Employers Representative	Khakdali		1/4/2024		Done	

UNIVERSAL INSPECTION REQUEST



مكتب أ.د. حسن مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name:  Sign: 	Date	REQ.NUM						
Received by Employers Representative	UIR	1-4-2024	76						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT			24		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description(		
منسوب (3-متر) from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (3-متر)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	



Comments by: (GARB SURVEY CONSATANT (xyz))

Comments by: General consultant (systra)

تأكد من أن العمل يتم وفقاً للمواصفات والمواصفات المطلوبة - التفت إلى

- you must follow specs and design dra
- you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	أبو عجلة					
Contractor QA/QC*	XYZ		1-4-2024	11:30	A	
	H.M.C		1-4-2024	11:00	A	
GARB**						
Employers Representative	Khaled ali		1/4/2024		AWC	

