

المنطقة السادسة - بيني سوف

مذكرة

للعرض على السيد المهندس / رئيس قطاع التنفيذ و المناطق

بخصوص: طلب شركة ابو عجيبة للمقاولات العامة اضافة مدة لعملية "انشاء الجسر الترابي لمشروع القطار الكهربائي السريع
من كم 200+850 الى كم 202+350 " بطول 1.5 كم (اتجاه ملوي) .

- اسندت الهيئة المشروع عالية الى الشركة المنفذة بالعقد رقم (2024/2023/499) المؤرخ في 2023/10/12 بقيمة اجمالية قدرها 57000000 جنيها ولمدة (8) شهور .
- بتاريخ 2023/10/19 تم تسليم الموقع للشركة المنفذة ليكون تاريخ النهو طبقا للعقد الاصيلي في 2024/06/18 .
- وردنا كتاب الشركة المنفذة تطلب فيه اضافة مدة ستة شهور للعملية لوجود بعض المعوقات التي تسببت في تاخر نهو الاعمال (مرفق) .

الرأي

- التفضل بالإحاطة.
- التكرم بالموافقة على اضافة مدة قدرها (6) شهور من تاريخ إنتهاء العقد في 2024/06/18 ليصبح تاريخ النهو 2024/12/18 وذلك للمبررات الاتية :-

- 1- بناءا على قرار مجلس الوزراء بجلسته رقم (254) المنعقدة بتاريخ 2023/08/30 .
- 2- بناءا على المذكرة المعروضة على السيد اللواء مهندس رئيس مجلس الادارة بخصوص الموافقة على مد مدة عقود المشروعات (6 اشهر) في ضوء كتاب الوزارة رقم (13793) والمرفق به كتاب دوري السيد اللواء / امين عام مجلس الوزراء رقم (3-27815) بذات الخصوص (مرفق) .
- 3- تاخر التنفيذ بسبب تحرير سعر الصرف وزيادة تكلفة أسعار المواد الخام وارتفاع اسعار نقلها .
- 4- نقص الدعم الدولارى بالاسواق .
- 5- ارتفاع اسعار قطع الغيار وندرة توافرها بالاسواق .

والأمر مفوض

وتفضلوا سيادتكم بقبول فائق الاحترام

وتفضلوا سيادتكم بقبول فائق الاحترام

تحرير في: 2024/ /

رئيس الإدارة المركزية

المنطقة السادسة - بيني سوف

مهندس /

طارق يوسف الجزار



مختص

مختص

استشاري أبحاث التربة والاساسات :
أ.د. هشام محمد حلمي



مشروع :
قطار اسوان الكهربائي السريع - القطاع الثاني

تقرير بنتائج اختبارات صلاحية تربة للتأسيس

مقدمة : تم إعداد هذا التقرير بناءا على طلب شركة / ابو عجيبة
ولذلك لتحديد خصائص ومدى صلاحية عينة تراب كثر من طينية تصلح للتأسيس

مصدر العينة : عند المحطة / (٢٠١+٨٠٠) أرض طينية

- المندوب: وقد تم توريد العينة بمعرفة ١- م/ محمود عبد الرحيم الحيني (مهندس الإشراف مكتب د/ حسن مهدي) رقم الهاتف = ٠١١٥٩٤٠٠١٠٨

- تاريخ توريد العينة : ٢٠٢٣/٨/١٦

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفوط)

- التوضيف الظاهري للعينة : كثبان رملية ناعمة (سفو)

وقد تم عمل الاختبارات الآتية :

- ١- التدرج الحبيبي
- ٢- حد السيولة واللدونة
- ٣- اختبار البروكتور
- ٤- اختبار CBR
- ٥- اختبار المواد العضوية

وكالت نتائج الاختبارات كالتالي :

م	نوع الاختبار	النتائج	ملاحظات
١	تصنيف العينة	A-3	
٢	مجال اللدونة	--	
٣	أقصى كثافة جافة (البروكتور) $\gamma_d \max$	1.902 gm/cm ³	
٤	نسبة للماء الأساسية	9.10%	
٥	رقعة CBR المغمورة	9.30%	
6	المواد العضوية	لا يوجد	

• و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي غير صالحة للتأسيس عليها .



مهندس المعمل
م/ محمد إسماعيل
التوقيع / محمد إسماعيل

فني المعمل
أ/ أحمد حسن عبيد
التوقيع / أحمد حسن عبيد

Coarse & Fine Aggregate Grading - ASTM C136 & AASHTO T27

أرض طبيعية

الموقع: ST = 201+800

21/08/2023

التاريخ:

نتائج الاختبار :-

رقم المنخل (mm)	رقم المنخل (inch)	وزن المحجوز على كل منخل	وزن المحجوز الفرغس	المحجوز %	الباق %
125	5"	0	0	0%	100%
101.6	4"	0	0	0.00%	100.00%
76.2	3"	0	0	0.00%	100.00%
63.5	2.5"	0	0	0.00%	100.00%
50.8	2"	0	0	0.00%	100.00%
37.5	1.5"	0	0	0.00%	100.00%
25	1"	0	0	0.00%	100.00%
19	3/4"	0	0	0.00%	100.00%
12.7	1/2"	0	0	0.00%	100.00%
9.5	3/8"	0	0	0.00%	100.00%
4.75	# 4	0	0	0.00%	100.00%
	المر من منخل # 4	500			100.00%
	وزن العينة الكلي	500			
	وزن عينة الناعم	500			
2.36	# 10	0	0	0.0%	100.0%
0.425	# 40	80	80	16.0%	84.0%
0.075	# 200	392	472	94.4%	5.6%
السيولة و اللدونة		N.P			
التصنيف		A-3			

ملاحظات : توصيف العينة : غثيان رملية ناعمة (Sand Dunes)



مهندس المعمل
د. محمد بن عبد الله
التوقيع: محمد بن عبد الله

في المعمل
أحمد حسن عيسى
التوقيع: أحمد حسن عيسى

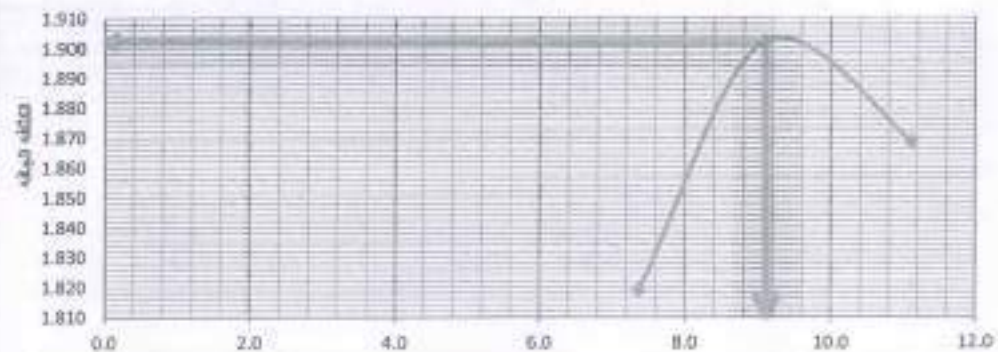
Modified Proctor : ASTM D1557

نوع العين:	عينة كابل رملية
تصنيف العين:	A-3
نتائج الاختبار:	
وزن القالب:	5731
حجم القالب:	2140
الغسالة جافة:	1.902
الغسالة الرطبة:	9.10

رقم الاختبار:	1	2	3
وزن القالب + العينة رطبة:	9910.0	10172	10174
وزن القرينة الرطبة:	4179.0	4441	4443
وزن القرينة الجافة:	1.953	2.075	2.076

رقم الحقل:	1	2	3	4	5	6
وزن الحقل:	25.2	25.33	52.2	54.11	53.11	52.31
وزن الحقل + العينة رطبة:	150.0	150.0	150.0	150.0	150.0	150.0
وزن الحقل + العينة جافة:	141.22	141.66	141.8	142.05	140.31	140.21
وزن الغسالة:	8.8	8.3	8.2	7.9	9.7	9.8
وزن العينة جافة:	116.02	116.33	89.6	87.94	87.2	87.9
المستوى المائي %:	7.6	7.2	9.2	9.0	11.1	11.1
متوسط المستوى المائي %:	7.4	9.1	11.1			
المتانة الجافة:	1.819	1.902	1.868			

Modified Proctor Chart



ملاحظات:



مهندس المعمل
د. محمد بن عبد الله
الرياض / المملكة العربية السعودية

في المعمل
أحمد حسن عتيق
تقريباً / المملكة العربية السعودية

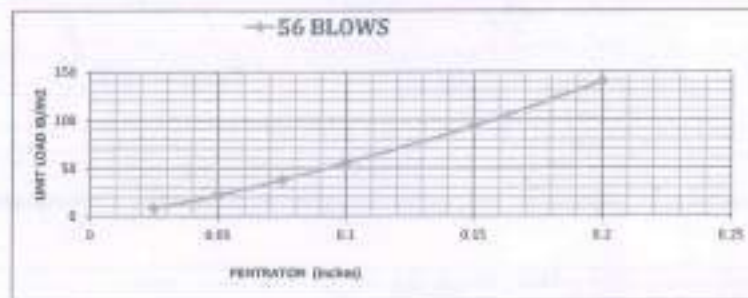
المعيار نسبة تحمل كاليفورنيا (ASTM D1883) (C, B, R)

A-3		تصنيف العينة	
56	عدد الضربات	56	عدد الضربات
2	رقم القالب	3131	حجم القالب (سم ³)
83.68	وزن القالب	5286	وزن القالب (كجم)
150	وزن القالب والحلقة رملية دم	9545	وزن القالب وحلقة رملية (دم)
149	وزن القالب والحلقة رملية دم	4255	وزن القالب رملية (دم)
8	وزن الماء دم	1.997	مقدار مائية (دم) (سم ³)
88.3	وزن القالب رملية دم	1.831	نسبة رطوبته (دم) (سم ³)
9.1%	المحتوى المائي %	1.900	مقدار الهواء (دم) (سم ³)
		96.3%	نسبة التشبع

نسبة الانكماش	0.00%	غير قابلة للانكماش
---------------	-------	--------------------

حساب نسبة تحمل كاليفورنيا

7.62	5.08	3.81	2.54	1.95	1.27	0.635	الأحمر في بالم
0.3	0.2	0.15	0.1	0.075	0.05	0.025	الأحمر في بالم حبه
329.0	190	127.0	75.0	51.0	29.0	11.0	الوزن kg
722.912	418.78	279.908	185.3	112.404	63.916	24.244	الوزن بالبرونز
241.08	139.65	93.345	55.125	37.485	21.315	8.085	الحمل lb/in ²



9.3%	قيمة C.B.R
------	------------

ملاحظات: تم نشر القالب في الماء لمدة 24 ساعة قبل إجراء الاختبار.

مهندس العمل
د. محمد عبد الله
قوله: احمد عبد الله

في العمل
احمد حسن عيسى
عبدالله محمد



استشاري أبحاث التربة والاساسات :
أ.د.م. هشام محمد حلمي



مشروع :
قطار اسوان الكهربائي السريع - القطاع الثاني

تقرير بنتائج اختبارات صلاحية تربة للتأسيس

مقدمة : تم إعداد هذا التقرير بناءا على طلب شركة / ابو عجيلة

وذلك لتحديد خصائص ومدى صلاحية عينة تراب كل من طينية تصلح للتأسيس

مصدر العينة : عند المحطة / (٢٠١٠٧٠٠) أرض طينية

- المندوب : وقد تم توريد العينة بمعرفة ١- م/محمود عبدالرحيم الحيني (مهندس الإشراف مكتب د/ حسن مهدي) رقم الهاتف = ٠١١٥٩٤٠٠١٠٨

تاريخ توريد العينة : ٢٠٢٣ / ٨ / ١٦

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفلوط)

- التوصيف الظاهري للعينة : كتبان رمالية ناعمة (سقا)

وقد تم عمل الاختبارات الآتية :

- ١- اختبار الحبيبي
- ٢- حد السيولة واللدونة
- ٣- اختبار البرونكتور
- ٤- اختبار CBR
- ٥- اختبار المواد العضوية

وكلفت نتائج الاختبارات كالآتي :

ملاحظات	النتائج	نوع الاختبار	م
	A-3	تصنيف العينة	١
	--	مجال اللدونة	٢
	1.910 gm/cm3	أقصى كثافة جافة (البرونكتور) $\gamma_d \max$	٣
	9.6%	نسبة المياه الأموية	٤
	8.50%	قيمة CBR المغورة	٥
	لا يوجد	المواد العضوية	٦

• و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي غير صالحة للتأسيس عليها .



مهندس المعمل
م/م احمد حليم
التوقيع / احمد حليم

فني المعمل
أ/ احمد حسني
التوقيع / احمد حسني

Coarse & Fine Aggregate Grading - ASTM C136 & AASHTO T27

الشارخ :	21/06/2023	الموقع : ST = 201+700	أرض طبيعية
----------	------------	-----------------------	------------

نتائج الاختبار :-

رقم مخل (mm)	رقم المخل (inch)	وزن المجهز على كل مخل	وزن المجهز الفراسي	المجهز %	المز %
127	5"	0	0	0%	100%
101.6	4"	0	0	0.00%	100.00%
76.2	3"	0	0	0.00%	100.00%
63.5	2.5"	0	0	0.00%	100.00%
50.8	2"	0	0	0.00%	100.00%
37.5	1.5"	0	0	0.00%	100.00%
25	1"	0	0	0.00%	100.00%
19	3/4"	0	0	0.00%	100.00%
12.7	1/2"	0	0	0.00%	100.00%
9.5	3/8"	0	0	0.00%	100.00%
4.75	# 4	0	0	0.00%	100.00%
	المز من مخل # 4	500			100.00%
	وزن العينة الكلي	500			
	وزن عينة الناعم	500			
2.36	# 10	10	10	2.0%	98.0%
0.425	# 40	77	87	17.4%	82.6%
0.075	# 200	379	466	93.2%	6.8%
المسبوبة و الدونة		N.P			
التصنيف		A-3			

ملاحظات : توصيف العينة : تليان رملية ناعمة (Sand Dunes)



مهندس العمل
أحمد حسن عتيق
التوقيع

أحمد حسن عتيق
مهندس العمل

Modified Proctor : ASTM D1557

نوع العينة:	عينة بثلاث رملية
تصنيف العينة:	A-3

نتائج الاختبار :-

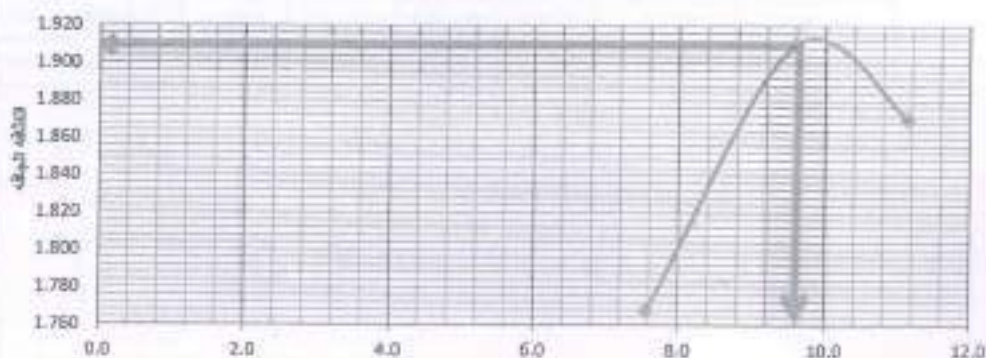
1.910	القيمة الكلية جافه
9.59	المراد الاسويه

5731	وزن القالب
2140	حجم القالب

رقم الاختبار	1	2	3
وزن القالب + العينة رطبه	9799.0	10210	10179
وزن التربه الرطبه	4068.0	4479	4648
الكثافه الرطبه	1.901	2.093	2.079

رقم الجفده	1	2	3	4	5	6
وزن الجفده	52.31	54.32	52.12	53.66	54.21	52.32
وزن الجفده + العينة رطبه	150.0	150.0	150.0	150.0	150.0	150.0
وزن الجفده + العينة جافه	143.21	143.2	141.4	141.61	140.5	140.1
وزن العياد	6.8	6.8	8.6	8.4	9.5	9.9
وزن العينة جافه	90.9	88.86	89.28	87.95	86.29	87.78
المحتوى المائى %	7.5	7.7	9.6	9.5	11.0	11.3
متوسط المحتوى المائى %	7.6	9.6	11.1			
الكثافه الجافه	1.767	1.910	1.870			

Modified Proctor Chart



ملاحظات :



مهندس العمل
د. أحمد سليمان
التوقيع: أحمد سليمان

قن العمل
أحمد سليمان عليه
التوقيع: أحمد سليمان

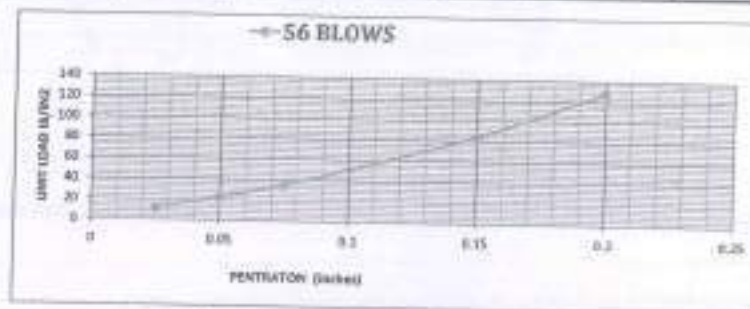
اختبار نسبة تحميل كاليفورنيا (C . B . R) ASTM D1683

تصنيف العينة		A-3	
عدد الطرقات	36	عدد الطرقات	56
حجم القالب (سم ³)	2131	زمن التوقف	5
وزن القالب (جم)	5288	وزن القالب	93.88
وزن القالب بدون العينة رطبه (جم)	9039	وزن القالب بالعينة رطبه (جم)	150
وزن العينة رطبه (جم)	4941	وزن القالب بالعينة رطبه (جم)	141.8
تغطية قرحية (جم/سم ²)	2.037	وزن الماء (جم)	8.4
المسحوق (جم/سم ²)	1.859	وزن العينة رطبه (جم)	37.9
كثافة التربة (جم/سم ³)	1.910	الامتصاص المائي %	9.8%
نسبة الماء	97.4%		

نسبة الانتفاش	0.08%	غير قابلة للتحميل
---------------	-------	-------------------

حساب نسبة تحميل كاليفورنيا

7.62	5.08	3.81	2.54	1.95	1.27	0.635	الاختبار في الماء
0.3	0.2	0.15	0.1	0.075	0.05	0.025	الاختبار في الماء
234.0	174	115.0	69.0	48.0	31.0	15.0	التراب kg
515.736	383.496	253.46	152.076	105.792	68.324	33.06	التراب بالتراب
171.99	127.89	84.525	50.715	35.28	22.785	11.025	التراب 1B/1N2



9.8%	قيمة C . B . R
------	----------------

ملاحظة: تم إجراء الاختبار في الماء لمدة 96 ساعة قبل إجراء الاختبار



مجلس البحث العلمي
مجلس البحث العلمي
مجلس البحث العلمي

مجلس البحث العلمي
مجلس البحث العلمي
مجلس البحث العلمي



التاريخ : 2024-9-22

اسم المشروع : مشروع القطار الكهربائي السريع قطاع (أكتوبر - أبو سمبل)
الموضوع : اعتماد الهيئة العامة للطرق والكبارى لطلبات استلام الأعمال الخاصة بالمشروع
الشركة المنفذة : ابوعجيلة للمقاولات العامة والتوريدات العمومية في المسافة
من (200+876) الى (202+376) بطول 1.5 كم.

عقد رقم : - (2023-2022-1968) بتاريخ 2023-5-17

- (2023-2023-142) بتاريخ 2023-8-3

- (2023-2023-143) بتاريخ 2023-8-3

- (2023-2023-499) بتاريخ 2023-10-12

- (2023-2023-1021) بتاريخ 2024-1-18

- (2023-2023-1229) بتاريخ 2024-2-26

- (2024-2024-209) بتاريخ 2024-8-21

تم الإطلاع ظاهريا على طلبات الفحص الخاصة بالمشروع المذكور عاليه والمرفقة بمستخلصات
المذكورة عالية لعدد (77) طلبات فحص وذلك بعد مراجعتها وتوقيعها من استشارى المساحة (XYZ)
واستشارى ضبط الجودة (مكتب أ.د حسن مهدي) وعليه تم اعتمادها

وتنقسم الى :

- (53) طلبات فحص لأعمال الردم .
- (14) طلبات فحص لأعمال الحفر .
- (4) طلبات فحص لأعمال التطهير .

عن الاستشاري (أ.د حسن مهدي)
مشاريع القطار السريع

مهندس الاستشاري
أ.د حسن مهدي

يعتمد،،،

مهندس الهيئة العامة للطرق والكبارى

مهندس الهيئة العامة للطرق والكبارى

اتجاه ملوي

من المحطة ٨٥٠+٢٠٠ الى المحطة ٢٠٢+٣٥٠ بطول ١,٥ كم رقم العقد (٢٠٢٤/٢٠٢٣/٤٩٩)

البرنامج الزمني

أعمال الجسر الترابي لمسار القطار الكهربائي السريع الخط الثاني (اليوم / بني سويف - أبوسمبل) القطاع الثاني (بني مزار / منفلووط)

تاريخ استلام الموقع ٢٠٢٣/١٠/١٩

مدة تنفيذ العمل ٨ شهور

تاريخ نهو الاعمال ٢٠٢٤/٦/١٨

رقم البند	بيان الاعمال	الوحدة	الكمية	أكتوبر-٢٠٢٣	نوفمبر-٢٠٢٣	ديسمبر-٢٠٢٣	يناير-٢٠٢٤	فبراير-٢٠٢٤	مارس-٢٠٢٤	أبريل-٢٠٢٤	مايو-٢٠٢٤	يونيو-٢٠٢٤
٥-٢	التراب المكعب أعمال حفر باستخدام المعدات الميكانيكية في السفو وتسوية السطح بألات التسوية والريش بالمياه الاسطوانية للوصول إلى نسبة الرطوبة المطلوبة والتمك الجيد بالهراسات للوصول إلى أقصى كثافة جافة (95 % من الكثافة الجافة القصوى) ومحمل على البند تحميل ونقل الأتربة الزائدة لمسافة ١,٥ كم من محور الطريق مع تغطية ناتج الحفر بالمقلب بطبقة أتربة بسمك متوسط ٢٠ سم و الفنة تشمل استخدام المياه في تثبيت السفو و اعداد مدقات على السفو لحركة المعدات و ويتم التنفيذ طبقاً للمناسيب التصميمية والقطاعات العرضية النموذجية والرسومات التفصيلية المعتمدة والبند بجميع مشتملاته طبقاً لأصول الصناعة ومواصفات الهيئة العامة للطرق والكباري وتعليمات المهندس المشرف.	م³										
	نفس البند رقم ٥-٢ في شهر سبتمبر ٢٠٢٣	م³	٣٤٠٣٥								٨,٥٠٨,٧٥	
٤-٢	بالتراب المكعب اعمال حفر بالمعدات الميكانيكية في تربة صخرية ومحمل على البند الاتي ١- تحميل ونقل ناتج الحفر لمسافة لا تقل عن ٥٠٠ متر ٢- اربكة الميول الجانبية باستخدام المعدات الميكانيكية ٣- توريد التربة مطابقة للمواصفات ولشغلها باستخدام الات التسوية بسمك لا يزيد عن ٢٥ سم لاستكمال المنسوب التصميمي لتشكل الجسر والاكتاف (نسبة تحمل كالفورنيا لا تقل عن ١٠ %) ورشها بالمياه الاسطوانية للوصول إلى نسبة الرطوبة المطلوبة والتمك الجيد بالهراسات للوصول إلى أقصى كثافة جافة (95% من الكثافة الجافة القصوى). ويتم التنفيذ طبقاً للمناسيب التصميمية والقطاعات العرضية النموذجية والرسومات التفصيلية المعتمدة والبند بجميع مشتملاته طبقاً لأصول الصناعة ومواصفات الهيئة العامة للطرق والكباري وتعليمات المهندس المشرف.	م³	توزيع الكميات									
	المنفذ في أغسطس ٢٠٢٣											
١-٤-٢	ذات اجهاد (٢٠٠-٣٠٠) كجم/سم² لمسافة نقل حتي ٥٠٠ متر في اغسطس ٢٠٢٣	م³	٣١								١٠,٣٣	١٠,٣٣
٢-٤-٢	ذات اجهاد (٣٠٠-٤٠٠) كجم/سم² لمسافة نقل حتي ٥٠٠ متر في اغسطس ٢٠٢٣	م³	٤١٦٨								١,٣٨٩,٣٣	١,٣٨٩,٣٣
٣-٤-٢	ذات اجهاد (٤٠٠-٥٠٠) كجم/سم² لمسافة نقل حتي ٥٠٠ متر في اغسطس ٢٠٢٣	م³	٩٧٥٨								٣,٢٥٢,٦٧	٣,٢٥٢,٦٧
٤-٤-٢	ذات اجهاد (٥٠٠-٦٠٠) كجم/سم² لمسافة نقل حتي ٥٠٠ متر في اغسطس ٢٠٢٣	م³	١٣١٣٠								٤,٣٧٦,٦٧	٤,٣٧٦,٦٧

عن الاستشاري أ.د حسن مهدي

مهندس الشركة المنفذة

يعتمد

مهندس الهيئة العامة للطرق والكباري

م/احمد عزب
التوقيع

م/محمود غريب
التوقيع

م/احمد فتوح
التوقيع

م/احمد فتوح
التوقيع



البرنامج الزمني

أعمال الجسر الترابي لمسار القطار الكهربائي السريع الخط الثاني (الفيوم / بني سويف - أبوسمبل) القطاع الثاني (بني مزار / منفلووط)

من المحطة ٨٥٠+٢٠٠ الي المحطة ٢٠٥٠+٢٠٢

بطول ١,٥ كم رقم العقد (٢٠٢٤/٢٠٢٣/٤٩٩)

اتجاه ملوي

تاريخ استلام الموقع ٢٠٢٣/١٠/١٩

مدة تنفيذ العمليه ٨ شهور

تاريخ نهو الاعمال ٢٠٢٤/٦/١٨

رقم البند	بيان الاعمال	الوحدة	الكمية	أكتوبر-٢٠٢٣				نوفمبر-٢٠٢٣				ديسمبر-٢٠٢٣				يناير-٢٠٢٤				فبراير-٢٠٢٤				مارس-٢٠٢٤				أبريل-٢٠٢٤				مايو-٢٠٢٤				يونيو-٢٠٢٤																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
				من ٧-١	من ١٥-٨	من ٢٢-١٦	من ٣٠-٢٣	من ٧-١	من ١٥-٨	من ٢٢-١٦	من ٣٠-٢٣	من ٧-١	من ١٥-٨	من ٢٢-١٦	من ٣٠-٢٣	من ٧-١	من ١٥-٨	من ٢٢-١٦	من ٣٠-٢٣	من ٧-١	من ١٥-٨	من ٢٢-١٦	من ٣٠-٢٣	من ٧-١	من ١٥-٨	من ٢٢-١٦	من ٣٠-٢٣	من ٧-١	من ١٥-٨	من ٢٢-١٦	من ٣٠-٢٣																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				
٢	أعمال الحفر																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		</

عن الاستشاري أ.د حسن مهدي

مهندس الشركة المنفذة

يعتمد؟؟؟

مهندس الهيئة العامة للطرق والكباري

م/احمد عزب

م/محمود عزب

التوقيع

التوقيع

م/احمد فتوح
التوقيع /





هيكل تنظيمي للعاملين بمشروع القطار السريع شركة أبوعجيلة للمقاولات العامة

التاريخ : ٢٠٢٢-٩-٢٤

اسم المشروع : مشروع القطار السريع (أكتوبر-أوسمبل)

رقم العقد : (٢٠٢٤/٢٠٢٣/٤٩٩)

رقم التليفون	عدد سنوات الخبرة	الوظيفة	الاسم	مستسل
01009742637	10	مدير المشروع	محمد حامد يحي	1
01017199596	5	مدير المكتب الفني	احمد احمد محمود	2
01019930593	5	مدير ضبط الجودة	نادي عادل	3
01114562154	10	مدير السلامة الوقائية	زبيح توحيد	4
01090254469	5	مهندس التنفيذ	وليد محمود محمد	5
01559856322	5	مهندس صيانة (ميكانيكا وكهرباء)	محمد عماد الدين محمد	6
01223691236	5	مهندس التخطيط والبرمجة الزمنية	احمد قاسم	7
01002612002	5	مراقب تنفيذ (فني مواد)	احمد السيد احمد	8
01063768307			محمد نادي	
01029734478	5	حساب كميات	عبدالعال رجب	9
01064950832	7	مساح	حسين محمد جبريل	10
01033806848	7		محمد جمال	
01092355765	5	فني سلامة مرورية	محمد ابوغنيمه	11
0102245866	5		محمد حسين	

مهندس الشركة المنفذة

م / احمد فنيح

التوقيع /

عن الاستشاري أ.د حسن مهدي
م / احمد عزب
م / محمود عزب
التوقيع /

يعتمد:؟؟؟

مهندس الهيئة العامة للطرق والكباري



بيان المعدات

التاريخ : ٢٠٢٢-٩-٢٤

اسم المشروع : مشروع القطار السريع (أكتوبر-أوسمبل)
المسافة من كم ٢٠٠+٨٥٠ وحتى كم ٢٠٢+٣٥٠ بطول ١,٥ كم

بالإشارة الى العقد المبرم بين الهيئة العامة للطرق والكباري وشركة أبوعحيلة للمقاولات العامة
رقم (٢٠٢٤/٢٠٢٣/٤٩٩) بتاريخ ٢٠٢٣-١٠-١٢
لتنفيذ المشروع عاليه بالمعدات الآتية :

المعدة	العدد	تاريخ الصنع
حفار	3	2009
		2005
لودر	4	2010
		2001
عربية قلاب	4	2015
	5	2008
	2	2005
بلدوزر	1	2000
تانك مياة	1	2015
جريد	1	2003
هراس	2	2002

عن الاستشاري أد حسن مهدي

م/محمود غريب
التوقيع

م/ احمد عزب
التوقيع

مهندس الهيئة العامة للطرق والكباري

يعتمد!!!

ندس الشركة المنفذة

احمد فتوح

يفع / احمد فتوح



جدول توزيع اجهادات الصخر للقطاع من ٢٠٠+٨٧٦ الى ٢٠١+٦٤٠
تنفيذ شركة ابو عجيله للمقاولات العامة القطاع من المحطة ٢٠٠+٨٧٦ كم الي المحطة ٢٠٢+٨٧٦ كم

حتى تاريخ ٢٠٢٢/١١/١٤

الاجهاده بالمقاييس ٢٠٠+٨٧٦ (كجم / سم)	الاجهاده بالمقاييس ٢٠١+٦٤٠ (كجم / سم)	الاجهاده بالمقاييس ٢٠٢+٨٧٦ (كجم / سم)	الاجهاده بالمقاييس ٢٠٣+٥٠٠ (كجم / سم)	الاجهاده بالمقاييس ٢٠٤+٢٠٠ (كجم / سم)	المسبوق (م)	الاجهاده (كجم / سم)	المحطة	مبنة
0.00			0.00		89.12	590.0	200+876.01	1
2,451.68			2,451.68		89.08	560.0	200+880.00	2
9,893.34			9,893.34		88.88	600.0	200+900.00	3
9,701.29	9,701.29				88.67	250.0	200+920.00	4
9,197.66			9,197.66		88.46	500.0	200+940.00	5
8,834.38				8,834.38	88.26	630.0	200+960.00	6
9,215.85	9,215.85				88.05	400.0	200+980.00	7
9,804.14	9,804.14				87.85	390.0	201+000.00	8
9,977.50				9,977.50	87.64	610.0	201+020.00	9
10,398.13			10,398.13		87.43	550.0	201+040.00	10
10,812.59			10,812.59		87.23	500.0	201+060.00	11
10,695.49			10,695.49		87.02	570.0	201+080.00	12
10,067.13	10,067.13				86.82	267.0	201+100.00	13
10,011.24				10,011.24	86.61	620.0	201+120.00	14
9,758.73			9,758.73		85.76	500.0	201+140.00	15
10,318.80		10,318.80			85.55	450.0	201+160.00	16
11,130.49		11,130.49			85.35	440.0	201+180.00	17
11,103.67	11,103.67				85.14	260.0	201+200.00	18
11,234.40		11,234.40			84.93	390.0	201+220.00	19
10,299.42				10,299.42	84.73	650.0	201+240.00	20
8,039.35				8,039.35	84.52	630.0	201+260.00	21

الشركة المنفذة

حمد فتيح

١٩٧٨

عن الاستشاري ا.د حسن مهدي
مدير المشروع
م/محمود غريب
المكتب الفني
م/احمد عزب





الترتيب	الاجزاء والمقاييس ٢٠٠٠-٢٠٠٠ (كجم / سم ^٢)	الاجزاء والمقاييس ٢٠٠٠-٢٠٠٠ (كجم / سم ^٢)	الاجزاء والمقاييس ٢٠٠٠-٢٠٠٠ (كجم / سم ^٢)	الاجزاء والمقاييس ٢٠٠٠-٢٠٠٠ (كجم / سم ^٢)	الاجزاء والمقاييس ٢٠٠٠-٢٠٠٠ (كجم / سم ^٢)	المسبوق (م)	الاجزاء (كجم / سم ^٢)	المسافة	ملاحظة
22	6,829.61			6,829.61		84.32	510.0	201+280.00	
23	10,218.98			10,218.98		84.11	550.0	201+300.00	
24	8,466.06			8,466.06		83.90	600.0	201+320.00	
25	8,693.69				8,693.69	83.70	640.0	201+340.00	
26	8,567.94			8,567.94		83.49	590.0	201+360.00	
27	8,251.06			8,251.06		83.28	520.0	201+380.00	
28	8,252.44			8,252.44		83.08	500.0	201+400.00	
29	8,500.81			8,500.81		82.87	570.0	201+420.00	
30	9,470.53			9,470.53		83.27	510.0	201+440.00	
31	12,967.51			12,967.51		83.07	550.0	201+460.00	
32	10,951.35		10,951.35			82.86	490.0	201+480.00	
33	9,199.31	9,199.31				82.65	280.0	201+500.00	
34	8,710.47		8,710.47			82.45	350.0	201+520.00	
35	8,379.96			8,379.96		82.24	570.0	201+540.00	
36	8,372.24		8,372.24			82.03	460.0	201+560.00	
37	8,799.80		8,799.80			81.83	500.0	201+580.00	
38	9,068.39		9,068.39			81.62	500.0	201+600.00	
39	9,165.69			9,165.69		81.42	580.0	201+620.00	
40	4,621.06			4,621.06		81.21	540.0	201+640.00	
360,432.18	40,071.40	38,964.86	58,641.07	166,899.27	55,855.58	اجمالي الكمية (م)			
25,963.20	2,942.32	2,167.28	4,722.32	12,924.63	3,206.65	الكمية المنفذة من شهر سبتمبر حتى شهر يناير			

يعتمد
مهندس الهيئة العامة للطرق والكباري

عن الاستشاري ا.د. حسن مهدي
مدير المشروع
م/محمود حبيب
المكتب الفني
م/احمد عزب
١٤
١٤

الشركة المنفذة

حمد فتح

١٩٧٩





جدول توزيع اجهادات الصخر للقطاع من ٢٠٠+٨٧٦ الى ٢٠١+٦٤٠
تنفيذ شركة ابوعجيلة للمقاولات العامة القطاع من المحطة ٢٠٠+٨٧٦ الى المحطة ٢٠٢+٨٧٦ كم

حتى تاريخ ٢٠٢٣/٨/٢٤

الاجهادات بالمقاييسه ٢٠٠٠-٢٠٠٠ (كجم / سم)	الاجهادات بالمقاييسه ٤٠٠٠-٢٠٠٠ (كجم / سم)	الاجهادات بالمقاييسه ٨٠٠٠-٤٠٠٠ (كجم / سم)	الاجهادات بالمقاييسه ٦٠٠٠-٤٠٠٠ (كجم / سم)	الاجهادات بالمقاييسه ٧٠٠٠-٦٠٠٠ (كجم / سم)	المشوب (م)	الاجهات (كجم / سم)	المحطة	متر
0.00			0.00		89.12	590.0	200+876.01	1
2,382.75			2,382.75		89.08	560.0	200+880.00	2
9,672.89			9,672.89		88.88	600.0	200+900.00	3
9,397.29	9,397.29				88.67	250.0	200+920.00	4
8,828.23			8,828.23		88.46	500.0	200+940.00	5
8,622.69				8,622.69	88.26	630.0	200+960.00	6
9,056.30	9,056.30				88.05	400.0	200+980.00	7
9,633.59	9,633.59				87.85	390.0	201+000.00	8
9,816.77				9,816.77	87.64	610.0	201+020.00	9
10,161.19			10,161.19		87.43	550.0	201+040.00	10
10,316.01			10,316.01		87.23	500.0	201+060.00	11
10,106.96			10,106.96		87.02	570.0	201+080.00	12
9,326.54	9,326.54				86.82	267.0	201+100.00	13
9,085.07				9,085.07	86.61	620.0	201+120.00	14
8,723.87			8,723.87		85.76	500.0	201+140.00	15
9,427.85		9,427.85			85.55	450.0	201+160.00	16
10,627.76		10,627.76			85.35	440.0	201+180.00	17
10,619.76	10,619.76				85.14	260.0	201+200.00	18
10,688.55	10,688.55				84.93	390.0	201+220.00	19
9,805.55				9,805.55	84.73	650.0	201+240.00	20
7,513.81				7,513.81	84.52	630.0	201+260.00	21

عن الاستشاري أد حسن مهدي

مدير المشروع

م/محمود غريب

المكتب الفني

م/أحمد عزب

الشركة المنفذة

حمد فتح

بيع/





جدول توزيع اجهادات الصخر للقطاع من ٢٠٠+٨٧٦ إلى ٢٠١+٦٤٠
تنفيذ شركة ابوعجيلة للمقاولات العامة القطاع من المحطة ٢٠٠+٨٧٦ كم إلى المحطة ٢٠٢+٨٧٦ كم

حتى تاريخ ٢٠٢٢/٨/٢٤

مرتبة	المحطة	الاجهاد (كجم / سم ^٢)	المسبوب (م)	الاجهاد بالمقاييسه ٧٠٠-٦٠٠ (كجم / سم ^٢)	الاجهاد بالمقاييسه ٦٠٠-٥٠٠ (كجم / سم ^٢)	الاجهاد بالمقاييسه ٥٠٠-٤٠٠ (كجم / سم ^٢)	الاجهاد بالمقاييسه ٤٠٠-٣٠٠ (كجم / سم ^٢)	الاجهاد بالمقاييسه ٣٠٠-٢٠٠ (كجم / سم ^٢)	الإجمالي
22	201+280.00	510.0	84.32		6,493.55				6,493.55
23	201+300.00	550.0	84.11		8,857.74				8,857.74
24	201+320.00	600.0	83.90		7,644.47				7,644.47
25	201+340.00	640.0	83.70	7,805.04					7,805.04
26	201+360.00	590.0	83.49		7,599.15				7,599.15
27	201+380.00	520.0	83.28		7,628.19				7,628.19
28	201+400.00	500.0	83.08		7,945.26				7,945.26
29	201+420.00	570.0	82.87		8,261.94				8,261.94
30	201+440.00	510.0	83.27		8,539.07				8,539.07
31	201+460.00	550.0	83.07		11,153.78				11,153.78
32	201+480.00	490.0	82.86			9,333.44			9,333.44
33	201+500.00	280.0	82.65					7,785.49	7,785.49
34	201+520.00	350.0	82.45				7,419.14		7,419.14
35	201+540.00	570.0	82.24		7,686.87				7,686.87
36	201+560.00	460.0	82.03			7,940.71			7,940.71
37	201+580.00	500.0	81.83			8,284.23			8,284.23
38	201+600.00	500.0	81.62			8,304.76			8,304.76
39	201+620.00	580.0	81.42		8,030.34				8,030.34
40	201+640.00	540.0	81.21		3,942.38				3,942.38
اجمالي الكمية (م ^٣)									334,468.98
الكمية المنفذ من شهر يوليو حتى شهر أغسطس									78,885.62
المنفذ في يوليو ٢٠٢٢									39,442.81
المنفذ في أغسطس ٢٠٢٢									39,442.81

يعتمد !!!
مهندس الهيئة العامة للطرق والكباري

عن الاستشاري أ.د حسن مهدي
مدير المشروع
م/محمود شريب
المكتب الفني
م/أحمد عزب
م/

الشركة المنفذة
حمد فتيح
فريق /





جدول توزيع اجهادات الصخر للقطاع من ٢٠٠٨٧٦ الى ٢٠١٦٤٠
تنفيذ شركة ابو عجيله للمقاولات العامة للقطاع من المحطة ٢٠٠٨٧٦ كم الي المحطة ٢٠٢٨٧٦ كم

حتى asbuilt بتاريخ ٢٠٢٢/٦/١٣

الاجمالي	الاجهات بالمقاييس ٢٠٠٨٧٦ - ٢٠١٦٤٠ (كجم / سم)	الاجهات بالمقاييس ٢٠٠٨٧٦ - ٢٠١٦٤٠ (كجم / سم)	الاجهات بالمقاييس ٢٠٠٨٧٦ - ٢٠١٦٤٠ (كجم / سم)	الاجهات بالمقاييس ٢٠٠٨٧٦ - ٢٠١٦٤٠ (كجم / سم)	الاجهات بالمقاييس ٢٠٠٨٧٦ - ٢٠١٦٤٠ (كجم / سم)	المسحوب (م)	الاجهات (كجم / سم)	المحطة	العمود
0.00				0.00		89.12	590.0	200+876.01	1
112.38				112.38		89.08	560.0	200+880.00	2
2,663.76				2,663.76		88.88	600.0	200+900.00	3
1,435.54	1,435.54					88.67	250.0	200+920.00	4
1,064.63				1,064.63		88.46	500.0	200+940.00	5
1,920.04					1,920.04	88.26	630.0	200+960.00	6
2,125.51		2,125.51				88.05	400.0	200+980.00	7
1,834.39		1,834.39				87.85	390.0	201+000.00	8
1,879.09					1,879.09	87.64	610.0	201+020.00	9
2,578.06				2,578.06		87.43	550.0	201+040.00	10
3,143.58				3,143.58		87.23	500.0	201+060.00	11
2,954.06				2,954.06		87.02	570.0	201+080.00	12
2,223.81	2,223.81					86.82	267.0	201+100.00	13
2,473.07					2,473.07	86.61	620.0	201+120.00	14
1,698.26				1,698.26		85.76	500.0	201+140.00	15
1,254.30			1,254.30			85.55	450.0	201+160.00	16
1,565.36			1,565.36			85.35	440.0	201+180.00	17
1,349.70	1,349.70					85.14	260.0	201+200.00	18
1,103.95		1,103.95				84.93	390.0	201+220.00	19
1,023.98					1,023.98	84.73	650.0	201+240.00	20
783.13					783.13	84.52	630.0	201+260.00	21

عن الاستشاري ا.د حسن مهدي
مدير المشروع
م/محمود غريب

المكتب الفني
م/احمد عرب

عن الشركة المنفذة
م/احمد فتح
التوقيع





جدول توزيع اجهادات الصخر للقطاع من ٨٧٦+٢٠٠ الى ٦٤٠+٢٠١
تنفيذ شركة ابروجبل للمقاولات العامة القطاع من المحطة ٨٧٦+٢٠٠ كم الى المحطة ٢٠٢+٨٧٦ كم

حتى التكلفة بتاريخ ٢٠٢٢/٦/١٢

الاجمالي	الاجمالي بالمقاييس ٢٠٠٠٠٠ (كجم / سم)	الاجمالي بالمقاييس ١٠٠٠٠٠ (كجم / سم)	الاجمالي بالمقاييس ٥٠٠٠٠٠ (كجم / سم)	الاجمالي بالمقاييس ٢٠٠٠٠٠ (كجم / سم)	المسبوق (م)	الاجمالي (كجم / سم)	المنطقة	العمق
626.38			626.38		84.32	510.0	201+280.00	22
729.41			729.41		84.11	550.0	201+300.00	23
1,458.37			1,458.37		83.90	600.0	201+320.00	24
2,205.69				2,205.69	83.70	640.0	201+340.00	25
2,709.16			2,709.16		83.49	590.0	201+360.00	26
3,092.92			3,092.92		83.28	520.0	201+380.00	27
2,936.12			2,936.12		83.08	500.0	201+400.00	28
2,322.45			2,322.45		82.87	570.0	201+420.00	29
773.02			773.02		83.27	510.0	201+440.00	30
236.87			236.87		83.07	550.0	201+460.00	31
236.87		236.87			82.86	490.0	201+480.00	32
236.87	236.87				82.65	280.0	201+500.00	33
236.87		236.87			82.45	350.0	201+520.00	34
236.87			236.87		82.24	570.0	201+540.00	35
236.87		236.87			82.03	460.0	201+560.00	36
236.87		236.87			81.83	500.0	201+580.00	37
236.87		236.87			81.62	500.0	201+600.00	38
236.87			236.87		81.42	580.0	201+620.00	39
236.87			236.87		81.21	540.0	201+640.00	40
54,408.78	5,245.92	5,300.72	3,767.13	29,810.02	10,285.00	الجمالي الكلية (م)		
9,068.13	874.32	883.45	627.85	4,968.34	1,714.17	المنفذ في يناير ٢٠٢٢		
9,068.13	874.32	883.45	627.85	4,968.34	1,714.17	المنفذ في فبراير ٢٠٢٢		
9,068.13	874.32	883.45	627.85	4,968.34	1,714.17	المنفذ في مارس ٢٠٢٢		
9,068.13	874.32	883.45	627.85	4,968.34	1,714.17	المنفذ في ابريل ٢٠٢٢		
9,068.13	874.32	883.45	627.85	4,968.34	1,714.17	المنفذ في مايو ٢٠٢٢		
9,068.13	874.32	883.45	627.85	4,968.34	1,714.17	المنفذ في يونيو ٢٠٢٢		

يعتمد !!!
مهندس الهيئة العامة للطرق والكباري

المكتب الفني
م/أحمد عزب
م/أحمد عزب
م/أحمد عزب
م/أحمد عزب

عن الشركة المنفذة
م/أحمد فتوح
التوقيع





جدول توزيع اجهادات الصخر للقطاع من ٨٧٦+٢٠٠ الى ٨٧٦+٢٠١
تنفيذ شركة ابو عجيله للمقاولات العامة القطاع من المحطة ٨٧٦+٢٠٠ الى المحطة ٨٧٦+٢٠٢ كم

حتى asbuilt بتاريخ ٢٠٢٢/١/٣

الاجمالي	الاجهاده بالمقاييس ٢٠٠-٢٠١ (كم / سم)	الاجهاده بالمقاييس ٢٠١-٢٠٢ (كم / سم)	الاجهاده بالمقاييس ٢٠٢-٢٠٣ (كم / سم)	الاجهاده بالمقاييس ٢٠٣-٢٠٤ (كم / سم)	الاجهاده بالمقاييس ٢٠٤-٢٠٥ (كم / سم)	النسب (م)	الاجهاده (كم / سم)	المحطة	هيكلة
0.00				0.00		89.12	590.0	200+876.01	1
2,184.54				2,184.54		89.08	560.0	200+880.00	2
6,343.73				6,343.73		88.88	600.0	200+900.00	3
6,968.18	6,968.18					88.67	250.0	200+920.00	4
6,513.96				6,513.96		88.46	500.0	200+940.00	5
5,620.74					5,620.74	88.26	630.0	200+960.00	6
5,904.97		5,904.97				88.05	400.0	200+980.00	7
6,487.94		6,487.94				87.85	390.0	201+000.00	8
6,468.92					6,468.92	87.64	610.0	201+020.00	9
6,183.40				6,183.40		87.43	550.0	201+040.00	10
5,642.90				5,642.90		87.23	500.0	201+060.00	11
5,417.11				5,417.11		87.02	570.0	201+080.00	12
5,413.19	5,413.19					86.82	267.0	201+100.00	13
4,925.54					4,925.54	86.61	620.0	201+120.00	14
5,300.81				5,300.81		85.76	500.0	201+140.00	15
5,929.39			5,929.39			85.55	450.0	201+160.00	16
6,154.93			6,154.93			85.35	440.0	201+180.00	17
6,044.32	6,044.32					85.14	260.0	201+200.00	18
6,073.37		6,073.37				84.93	390.0	201+220.00	19
5,341.24					5,341.24	84.73	650.0	201+240.00	20
3,477.38					3,477.38	84.52	630.0	201+260.00	21

عن الاستشاري ا.د حسن مهدي

مدير المشروع

م/محمود العريب

المكتب الفني

م/احمد عزب

الشركة المنفذة

شركة ابو عجيله للمقاولات العامة

تاريخ: ١٩٧٨٨





جدول توزيع اجهادات الصخر للقطاع من ٨٧٦+٢٠٠ الى ٦٤٠+٢٠١
تنفيذ شركة ابروجيلا للمقاولات العامة القطاع من المحطة ٨٧٦+٢٠٠ الى المحطة ٨٧٦+٢٠٢ كم

حتى asbuilt بتاريخ ٢٠٢٢/١/٢

محطة	المحطة	الاجمالي (كجم / سم ٢)	الاجمالي (م)	الاجمالي بالمقاييس ٢٠٠-٢٠١ (كجم / سم ٢)	الاجمالي بالمقاييس ٢٠٠-٢٠٢ (كجم / سم ٢)	الاجمالي بالمقاييس ٢٠٠-٢٠٣ (كجم / سم ٢)	الاجمالي بالمقاييس ٢٠٠-٢٠٤ (كجم / سم ٢)	الاجمالي
22	201+280.00	510.0	84.32	2,510.82				2,510.82
23	201+300.00	550.0	84.11	5,380.56				5,380.56
24	201+320.00	600.0	83.90	4,293.43				4,293.43
25	201+340.00	640.0	83.70	4,641.79				4,641.79
26	201+360.00	590.0	83.49	4,380.66				4,380.66
27	201+380.00	520.0	83.28	3,951.10				3,951.10
28	201+400.00	500.0	83.08	3,792.97				3,792.97
29	201+420.00	570.0	82.87	5,054.19				5,054.19
30	201+440.00	510.0	83.27	7,939.23				7,939.23
31	201+460.00	550.0	83.07	8,491.55				8,491.55
32	201+480.00	490.0	82.86	5,674.33		5,674.33		5,674.33
33	201+500.00	280.0	82.65	4,498.55	4,498.55			4,498.55
34	201+520.00	350.0	82.45	4,693.60	4,693.60			4,693.60
35	201+540.00	570.0	82.24	4,346.00				4,346.00
36	201+560.00	460.0	82.03	4,378.58		4,378.58		4,378.58
37	201+580.00	500.0	81.83	4,401.76		4,401.76		4,401.76
38	201+600.00	500.0	81.62	4,095.15		4,095.15		4,095.15
39	201+620.00	580.0	81.42	4,076.95			4,076.95	4,076.95
40	201+640.00	540.0	81.21	2,176.80			2,176.80	2,176.80
اجمالي الكمية (م)			30,475.61	93,980.71	30,634.14	23,159.88	22,924.24	201,174.58

يعتمد !!!
مهندس الهيئة العامة للطرق والكباري

عن الاستشاري ا.د حسن مهدي
المكتب الفني
م/ احمد عزب
م/ محمود غريب
مدير المشروع

الشركة المنفذة
احمد فتوح
وقفا





مركز الاستشارات الهندسية
Engineering Consultation Center

معمل الخرسانة
Concrete plant



رؤية الكلية : تسعى الكلية إلى أن تكون مؤسسة تعليمية وبحثية عالية الجودة متميزة بتقديم خدمات مجتمعية لتنمية البيئة وتعسيها

نتائج اختبارات عينات من مكعبات الحجر		
خاص بعملية : القطار السريع (أكتوبر - أسوان) القطاع الثاني بطول ١٥٨ كم المسافة من ١٧٦ + ٨٠٠ : ٢٣٤ + ٨٠٠		
مقاول : شركة أبو عجيلة للمقاولات - القطاع ٨٥٠ + ٢٠٠ : ٢٠٢ + ٢٥٠ بطول ١,٥ كم		
توريد : ٨٣٦٨٨٨٦٤١٥	بتاريخ : ٢٣ / ٥ / ٢٠٢٣	رقم القيد : ١

نتائج الاختبارات

القطاع من ٢٠١ + ٦٤٠ : ٢٠١ + ٤٤٠

م	الأبعاد / سم	المحطة	منسوب	حمل الكسر / طن	إجهاد الكسر / كجم/سم ^٢
١	١٠ × ١٠ × ١٠	٢٠١ + ٤٤٠	٨٣,٢٧١	٥١	٥١٠
٢	١٠ × ١٠ × ١٠	٢٠١ + ٤٦٠	٨٣,٠٦٥	٥٥	٥٥٠
٣	١٠ × ١٠ × ١٠	٢٠١ + ٤٨٠	٨٢,٨٥٨	٤٩	٤٩٠
٤	١٠ × ١٠ × ١٠	٢٠١ + ٥٠٠	٨٢,٦٥٢	٢٨	٢٨٠
٥	١٠ × ١٠ × ١٠	٢٠١ + ٥٢٠	٨٢,٤٤٦	٣٥	٣٥٠
٦	١٠ × ١٠ × ١٠	٢٠١ + ٥٤٠	٨٢,٢٤	٥٧	٥٧٠
٧	١٠ × ١٠ × ١٠	٢٠١ + ٥٦٠	٨٢,٠٣٤	٤٦	٤٦٠
٨	١٠ × ١٠ × ١٠	٢٠١ + ٥٨٠	٨١,٨٢٨	٥٠	٥٠٠
٩	١٠ × ١٠ × ١٠	٢٠١ + ٦٠٠	٨١,٦٢٢	٥٠	٥٠٠
١٠	١٠ × ١٠ × ١٠	٢٠١ + ٦٢٠	٨١,٤١٥	٥٨	٥٨٠
١١	١٠ × ١٠ × ١٠	٢٠١ + ٦٤٠	٨١,٢٠٩	٥٤	٥٤٠

* تم توريد العينات بمعرفة م / محمود الحيني دون أدنى مسئولية على المعمل

يعتمد ،
الرأي الاستشاري على مسئولية اللجنة
مركز الاستشارات الهندسية



المشرف على المعمل

أ. د. / أسامة

التوقيع : /

فنى المعمل

١ / /

التوقيع : /

التوقيع : /

رسالة الكلية : تتلزم كلية الهندسة جامعة المنيا بتقديم برامج تعليمية وفقاً للمعايير القومية لإعداد خريج متميز وقادر على المنافسة في أسواق العمل محلياً وإقليمياً وعالمياً، كما تتلزم بالتشجيع والتطوير في البحث العلمي بما يخدم البيئة والتطور التكنولوجي .



مركز الاستشارات الهندسية
Engineering Consultation Center

معمل الخرسانة
Concrete plant



رؤية الكلية : تسعى الكلية إلى أن تكون مؤسسة تعليمية وبحثية عالية الجودة متميزة بتقديم خدمات مجتمعية لتنمية البيئة وتعويضها

نتائج اختبارات عينات من مكعبات الحجر		
خاص بعملية : القطار السريع (أكتوبر - أسوان) القطاع الثاني بطول ١٥٨ كم المسافة من ٨٠٠ + ١٧٦ : ٨٠٠ + ٣٣٤		
مقاول : شركة أبو عجيلة للمقاولات - القطاع ٨٥٠ + ٢٠٠ : ٢٠٢ + ٣٥٠ بطول ١,٥ كم		
توريد : ٨٣٦٨٨٨٦٤١٥	بتاريخ : ٢٣ / ٥ / ٢٠٢٣	رقم القيد : ٢

نتائج الاختبارات

القطاع من ٨٧٦ + ٢٠٠ : ١٢٠ + ٢٠١

م	الأبعاد / سم	المحطة	منسوب	حمل الكسر / طن	إجهاد الكسر / كجم/سم ^٢
١	١٠ × ١٠ × ١٠	٢٠٠ + ٨٧٦,٠١	٨٩,١٢٤	٥٩	٥٩٠
٢	١٠ × ١٠ × ١٠	٢٠٠ + ٨٨٠	٨٩,٠٨٣	٥٦	٥٦٠
٣	١٠ × ١٠ × ١٠	٢٠٠ + ٩٠٠	٨٨,٨٧٧	٦٠	٦٠٠
٤	١٠ × ١٠ × ١٠	٢٠٠ + ٩٢٠	٨٨,٦٧	٢٥	٢٥٠
٥	١٠ × ١٠ × ١٠	٢٠٠ + ٩٤٠	٨٨,٤٦٤	٥٠	٥٠٠
٦	١٠ × ١٠ × ١٠	٢٠٠ + ٩٦٠	٨٨,٢٥٨	٦٣	٦٣٠
٧	١٠ × ١٠ × ١٠	٢٠٠ + ٩٨٠	٨٨,٠٥٢	٤٠	٤٠٠
٨	١٠ × ١٠ × ١٠	٢٠١ + ٠٠٠	٨٧,٨٤٦	٣٩	٣٩٠
٩	١٠ × ١٠ × ١٠	٢٠١ + ٠٢٠	٨٧,٦٤	٦١	٦١٠
١٠	١٠ × ١٠ × ١٠	٢٠١ + ٠٤٠	٨٧,٤٣٤	٥٥	٥٥٠
١١	١٠ × ١٠ × ١٠	٢٠١ + ٠٦٠	٨٧,٢٢٧	٥٠	٥٠٠
١٢	١٠ × ١٠ × ١٠	٢٠١ + ٠٨٠	٨٧,٠٢١	٥٧	٥٧٠
١٣	١٠ × ١٠ × ١٠	٢٠١ + ١٠٠	٨٦,٨١٥	٦٠	٢٦٧
١٤	١٠ × ١٠ × ١٠	٢٠١ + ١٢٠	٨٦,٦٠٩	٦٢	٦٢٠

* تم توريد العينات بمعرفه م / محمود الحيني دون أدنى مسئولية علي المعمل

بمعد ،
الرأي الاستشاري علي مسئولية اللجنة
مركز الاستشارات الهندسية

المشرف علي المعمل

فني المعمل

أ. د. / /

/ /

التوقيع :

التوقيع :

رسالة الكلية : تلتزم كلية الهندسة جامعة المنيا بتقديم برامج تعليمية وفقاً للمعايير القومية لإعداد خريج متميز وقادر على المنافسة في اسواق العمل محلياً وإقليمياً وعالمياً، كما تلتزم بالتنشجيع والتطوير في البحث العلمي بما يخدم البيئة والتطور التكنولوجي .



مركز الاستشارات الهندسية
Engineering Consultation Center

معمل الخرسانة
Concrete plant



رؤية الكلية : تسعى الكلية إلى أن تكون مؤسسة تعليمية وبحثة عالية الجودة متميزة بتقديم خدمات مجتمعية لتنمية البيئة وتعميرها

نتائج اختبارات عينات من مكعبات الحجر		
خاص بعملية : القطار السريع (أكتوبر - أسوان) القطاع الثاني بطول ١٥٨ كم المسافة من ٨٠٠ + ١٧٦ : ٨٠٠ + ٣٣٤		
مقاوله : شركة أبو عجيلة للمقاولات - القطاع ٨٥٠ + ٢٠٠ : ٢٠٢ + ٣٥٠ بطول ١,٥ كم		
توريد : ٨٢٤٩١١٤٩٨٤	بتاريخ : ٢٧ / ٤ / ٢٠٢٣	رقم القيد : ١

نتائج الاختبارات

القطاع من ١٤٠ + ٢٠٠ : ٢٠١ + ٤٢٠

م	الأبعاد / سم	المحطة	متسوب	حمل الكسر / طن	إجهاد الكسر / كجم/سم ^٢
١	١٠ × ١٠ × ١٠	٢٠١ + ١٤٠	٨٥,٧٥٨	٥٠	٥٠٠
٢	١٠ × ١٠ × ١٠	٢٠١ + ١٦٠	٨٥,٥٥٢	٤٥	٤٥٠
٣	١٠ × ١٠ × ١٠	٢٠١ + ١٨٠	٨٥,٣٥٤	٤٤	٤٤٠
٤	١٠ × ١٠ × ١٠	٢٠١ + ٢٠٠	٨٥,١٣٩	٢٦	٢٦٠
٥	١٠ × ١٠ × ١٠	٢٠١ + ٢٢٠	٨٤,٩٣٣	٢٩	٢٩٠
٦	١٠ × ١٠ × ١٠	٢٠١ + ٢٤٠	٨٤,٧٢٧	٦٥	٦٥٠
٧	١٠ × ١٠ × ١٠	٢٠١ + ٢٦٠	٨٤,٥٢١	٦٣	٦٣٠
٨	١٠ × ١٠ × ١٠	٢٠١ + ٢٨٠	٨٤,٣١٥	٥١	٥١٠
٩	١٠ × ١٠ × ١٠	٢٠١ + ٣٠٠	٨٤,١٠٩	٥٥	٥٥٠
١٠	١٠ × ١٠ × ١٠	٢٠١ + ٣٢٠	٨٣,٩٠٢	٦٠	٦٠٠
١١	١٠ × ١٠ × ١٠	٢٠١ + ٣٤٠	٨٣,٦٩٦	٦٤	٦٤٠
١٢	١٠ × ١٠ × ١٠	٢٠١ + ٣٦٠	٨٣,٤٩٠	٥٩	٥٩٠
١٣	١٠ × ١٠ × ١٠	٢٠١ + ٣٨٠	٨٣,٢٨٢	٥٢	٥٢٠
١٤	١٠ × ١٠ × ١٠	٢٠١ + ٤٠٠	٨٣,٠٧٨	٥٠	٥٠٠
١٥	١٠ × ١٠ × ١٠	٢٠١ + ٤٢٠	٨٢,٨٧٢	٥٧	٥٧٠

* تم توريد العينات بمعرفه م / محمود الحيني دون أدنى مسئولية على المعمل

يعتمد ،
الرأي الاستشاري على مسئولية اللجنة
مركز الاستشارات الهندسية

المشرف على المعمل

أ. د. / محمد /

التوقيع : محمد /

فنى المعمل

أ. د. / محمد /

التوقيع : محمد /

رسالة الكلية : تلزم كلية الهندسة جامعه المنيا بتقديم برامج تعليمية وفقاً للمعايير القومية لإعداد خريج متميز وقادر على المنافسة في اسواق العمل محلياً وإقليمياً وعالمياً، كما تلزم بالتنظيم بالتشجيع والتطوير في البحث العلمي بما يخدم البيئة والتطور التكنولوجي.

محضر استلام موقع

مشروع إنشاء خط القطار الكهربائي السريع (أكتوبر - أبو سمبل) من الكم 200+850 حتي الكم 202+350 بطول 1.5 كم تنفيذ شركة أبو عجيلة للمقاولات العامة والتوريدات العمومية.

انه في يوم الخميس الموافق 19 / 10 / 2023 وبناء على عقد العملية رقم 499 / 2023 / 2024 اتجاه ملوي

اجتمعت اللجنة المشكلة من السادة الاتي اسماؤهم بعد وهم :-

عن الهيئة العامة للطرق والكباري (طرف اول)

مدير عام المشروعات

1- السيد المهندس / مصطفى شعبان البدري

مهندس الإشراف بالمنطقة السادسة

2- السيد المهندس / محمود حسين

مدير المشروع الاستشاري (مكتب أ.د/حسن مهدي)

3- السيد المهندس / حاتم مهران

استشاري المساحة (XYZ)

4- السيد المهندس / محمد عبدالرحمن سالم

عن الشركة المنفذه (طرف ثاني)

مهندس عن الشركة المنفذه

1- السيد المهندس / محمد حامد ابو عجيلة

وقد قامت اللجنة بالانتقال علي الطبيعة للموقع عالية بالمعاينة الظاهرية علي الطبيعة قام الطرف الاول بتسليم الطرف الثاني الموقع خاليا من العوائق الظاهرية ولا مانع من استلام الموقع والبدء في الاعمال ويعتبر تاريخ 19 / 10 / 2023 هو تاريخ استلام الموقع .

وقفل المحضر علي ذلك .

اللجنة من الهيئة (طرف اول)



4- السيد المهندس / محمد حامد ابو عجيلة

3- السيد المهندس / حاتم مهران

2- السيد المهندس / مصطفى شعبان البدري

1- السيد المهندس / محمد حامد ابو عجيلة

الشركة المنفذه (طرف ثاني)

1- السيد المهندس / محمد حامد ابو عجيلة

رئيس الادارة المركزية للمنطقة

السادسة ببني سويف

مهندس / طارق الجزار





الهيئة العامة للطرق والكباري والبنية التحتية

2022/ 8 / 21

مكتبه
الإستشارية الهندسية



الهيئة العامة للطرق والكباري والبنية التحتية



محضر معاينة تربة (ملاو)

المشروع القطار الكهربائي السريع (الكويت - العراق) القطاع الثاني

بطول 158 كم المسافة من (176+800 إلى 334+800)

تنفيذ شركة أبو عبيدة للمقاولات القطاع من 200+850 إلى 202+850 وقر 1.5 كم

السيد / **يوسف الأحمد** الموافق ٨ / ٨ / 2022 قسم الإستشارات الهندسية العامة للطرق والكباري
مكتبه الإستشاري العامة بمعاينة القطاع من 200+850 إلى 202+850 المسافة 202+350
بطول 1.5 كم

الهيئة العامة للطرق والكباري

السيد / **يوسف الأحمد** الموافق ٨ / ٨ / 2022 قسم الإستشارات الهندسية العامة للطرق والكباري

مكتبه الإستشاري العامة

السيد / **يوسف الأحمد** الموافق ٨ / ٨ / 2022 قسم الإستشارات الهندسية العامة للطرق والكباري

شركة أبو عبيدة للمقاولات العامة وقر 1.5 كم

السيد / **يوسف الأحمد** الموافق ٨ / ٨ / 2022 قسم الإستشارات الهندسية العامة للطرق والكباري

السيد / **يوسف الأحمد** الموافق ٨ / ٨ / 2022 قسم الإستشارات الهندسية العامة للطرق والكباري

السيد / **يوسف الأحمد** الموافق ٨ / ٨ / 2022 قسم الإستشارات الهندسية العامة للطرق والكباري
مكتبه الإستشاري العامة بمعاينة القطاع من 200+850 إلى 202+850 المسافة 202+350
بطول 1.5 كم
السيد / **يوسف الأحمد** الموافق ٨ / ٨ / 2022 قسم الإستشارات الهندسية العامة للطرق والكباري



السيد / **يوسف الأحمد** الموافق ٨ / ٨ / 2022 قسم الإستشارات الهندسية العامة للطرق والكباري

محضر مسابقة نقل

مشروع القطار الكهربائي السريع (6 أكتوبر-اسوان) القطاع الثاني

انه في يوم الاثنين الموافق 2022/9/5 قامت اللجنة المديكة من :-

(1) السيد المهندس / مصطفى محمد عبدالحمد مهندس المشروع الهيئة العامة للطرق والكباري

(2) السيد المهندس / محمد عبدالرحمن سالم مهندس المكتب الاستشاري (X,Y,Z)

(3) السيد المهندس / محمد حامد أبو عجيبة مدير المشروع شركة اورعجلة للمقاولات المتكاملة والتوريدات

وقد تم اللجوء بالذهاب الى مكان المقاب حيث وجد ان المسافة من قطاع (من محطة 200+800 حتى 202+300)

على مكان المقاب 3 كم وذلك بسبب تعذر وجود مدال بسبب وجود مزارع حول القطاع

وهذا محضر منا بذلك

التوقيع



م / مصطفى محمد عبدالحمد

م / محمد عبدالرحمن سالم

م / محمد حامد أبو عجيبة

الإدارة المركزية بالمنطقة السادسة بنى سويف

اعتماد

م / طارق يوسف الجزان



	مشروع القطار الكهربائي السريع	 الهيئة العامة للغمر مكتب أ.د/حسن مهدي للإستشارات الهندسية
	إستكمال إسناد أعمال الجسر الترابي والأعمال الصناعية بقطاعات مشروع إنشاء القطار الكهربائي السريع (أكتوبر-أبوسمبل)	
	تنفيذ شركة أبو عجيبة للمقاولات العامة والتوريدات العمومية مستخلص (١) جارى	

الحصر الإجمالي لكميات القطاع حتى تاريخ ٢٠٢٤/٤/١

Station	Total Cut Area(m2)	Cum. Cut Vol(m3)	As Built vol.cut		
				CUT VOL(m3)	Total.Qty
200+876.01	580.84	0	cut	0	529753.21
200+880.00	586.05	2,325.62		2,325.62	
200+900.00	630.8	14,494.09		12,168.47	
200+920.00	667.79	27,479.99		12,985.90	
200+940.00	665.5	40,812.95		13,332.96	
200+960.00	635.92	53,827.17		13,014.23	
200+980.00	655.55	66,741.85		12,914.68	
201+000.00	650.46	79,801.90		13,060.05	
201+020.00	610.45	92,410.94		12,609.04	
201+040.00	622.17	104,737.11		12,326.16	
201+060.00	621.82	117,176.99		12,439.89	
201+080.00	624.05	129,635.71		12,458.71	
201+100.00	616.97	142,045.96		12,410.26	
201+120.00	615.77	154,373.38		12,327.42	
201+140.00	617.82	166,709.30		12,335.92	
201+160.00	623.52	179,122.78		12,413.48	
201+180.00	614.79	191,505.94		12,383.16	
201+200.00	633.1	203,984.90		12,478.96	
201+220.00	599.85	216,314.49		12,329.59	
201+240.00	499.13	227,304.33		10,989.84	
201+260.00	445.74	236,753.04		9,448.72	
201+280.00	450.78	245,718.30		8,965.26	
201+285.93	449.56	248,387.80		2669.5	
201+300.00	460.6	254,790.75		6,402.95	
201+320.00	478.13	264,178.05		9,387.30	
201+340.00	476.54	273,724.79		9,546.74	
201+360.00	473.02	283,220.47		9,495.68	
201+380.00	467.7	292,627.66		9,407.19	
201+400.00	480.96	302,114.23		9,486.57	
201+420.00	473.9	311,662.81		9,548.58	
201+440.00	516.53	321,567.07		9,904.26	
201+460.00	579.3	332,525.35		10,958.28	
201+465.93	585.45	335,978.82		3453.48	
201+480.00	583.85	344,204.87		8,226.04	
201+500.00	576.27	355,806.07		11,601.20	
201+520.00	563.45	367,203.19		11,397.13	
201+540.00	521.62	378,053.86		10,850.67	
201+560.00	446.24	387,732.49		9,678.63	
201+580.00	417	396,364.88		8,632.38	
201+600.00	431.82	404,853.04		8,488.16	
201+620.00	454.9	413,720.28		8,867.24	
201+640.00	461.11	422,880.41		9,160.14	

عن الاستشاري أ.د حسن مهدي

م/ عبد الحميد علاء الدين م/ احمد عزب

عن استشاري المساحة

م/ محمد عبدالرحمن م/ محمد

عن الشركة

م/ محمد حامد أبو عجيبة م/ محمد

9/11



	مشروع القطار الكهربائي السريع	 الهيئة العامة للنقل مكتب أ.د/حسن مهدي للإستشارات الهندسية
	إستكمال إسناد أعمال الجسر الترابي والأعمال الصناعية بقطاعات مشروع إنشاء القطار الكهربائي	
	السريع (أكتوبر - أبوسمبل) تنفيذ شركة أبو عجيله للمقاولات العامة والتوريدات العمومية	

حصر كمية الاحلال في السفو ابتداء من شهر سبتمبر ٢٠٢٢

Station	Total Cut Area(m2)	Cum. Cut Vol(m3)	As Built vol.cut		
				CUT VOL(m3)	Total.Qty
201+920.00	172.54	495,420.53	CUT	1,725.37	36058.01
201+940.00	117.37	498,319.63		2,899.09	
201+960.00	121.91	500,712.41		2,392.78	
201+980.00	141.36	503,345.11		2,632.70	
202+000.00	131.55	506,074.23		2,729.12	
202+020.00	123.82	508,627.92		2,553.69	
202+040.00	93.18	510,797.88		2,169.96	
202+060.00	50.98	512,239.45		1,441.57	
202+080.00	49.6	513,245.30		1,005.85	
202+100.00	43	514,171.38		926.08	
202+120.00	38.08	514,982.21		810.83	
202+140.00	0	515,362.98		380.78	
202+160.00	0	515,362.98		0.00	
202+180.00	0	515,362.98		0.00	
202+200.00	0	515,362.98		0.00	
202+220.00	73.22	516,095.23		732.24	
202+240.00	80.7	517,634.50		1,539.28	
202+260.00	97.19	519,413.44		1,778.93	
202+280.00	119.49	521,580.25		2,166.81	
202+300.00	140.13	524,176.43		2,596.18	
202+320.00	63.81	526,215.81		2,039.38	
202+340.00	66.23	527,516.19		1,300.37	
202+360.00	64.12	528,819.69		1,303.50	
202+376.01	52.46	529,753.19		933.50	

عن الاستشاري أ.د حسن مهدي

م/ احمد عزب
م/ محمود غرابي

عن استشاري المساحة

م/ محمد عبدالرحمن

م/ محمد عبدالرحمن
م/ محمد عبدالرحمن

عن الشركة

م/ احمد فتيح

م/ احمد فتيح
م/ احمد فتيح
ABUAGLA
إستشارات الهندسية - المقاولات العامة
١٩٩-١٦١-٦٠٩

	مشروع القطار الكهربائي السريع	 مكتب المهندسين للإستشارات الهندسية
	إستكمال أعمال الجسر الترابي لمسار القطار الكهربائي السريع الخط الثاني (الفيوم / بني سويف - أبو سمبل) (مرحلة الجسور والأساس والأسيس والقطاع الثاني (بني مزار / منقلاوط)	
	تنفيذ شركة أبو عجيبة للمقاولات العامة والتوريدات العمومية كميات حتي مستخلص جاري (١) جاري لعقد رقم (٢٠٢٥/٢٠٢٤/٢٠٩) بتاريخ 2024/4/1 ASBUILT	

بند رقم (١-٣) : أعمال تحميل وتوريد ونقل أتربة مطابقة للمواصفات وتشغيلها باستخدام آلات التسوية بسمك لا يزيد عن ٥٠ سم حتى منسوب (-2 متر) أسفل منسوب الفرمة و بسمك لايزيد عن ٢٥ سم اعلي من منسوب (-2 متر) من منسوب الفرمة لإستكمال المنسوب التصميمي الخ

Station	Total Fill Area(m2)	Cum. Fill Vol(m3)	As Built vol.Fill			
			Fill VOL(m3)	Total.Qty	Fill VOL(m3) ابتداء من ٢٠٢٤/٢/٢٢	اجمالي الكميات ابتداء من ٢٠٢٤/٢/٢٢
201+920.00	202.61	2026.07	2026.07	100122.28	582.22	9669.67
201+940.00	227.66	6,328.78	4,302.71		1,170.55	
201+960.00	248.2	11,087.40	4,758.61		1,162.28	
201+980.00	274.47	16,314.06	5,226.57		1,140.36	
202+000.00	262.01	21,578.88	5,364.82		1,142.87	
202+020.00	243.79	26,736.89	5,058.01		1,149.44	
202+040.00	194.01	31,114.85	4,377.95		1,134.32	
202+060.00	362.48	36,679.73	5,564.88		561.35	
202+080.00	341.72	43,721.80	7,042.07		0.00	
202+100.00	314.56	50,284.61	6,562.81		0.00	
202+120.00	301.56	56,445.77	6,161.16		0.00	
202+140.00	0	59,461.36	3,015.59		0.00	
202+160.00	0	59,461.36	0.00		0.00	
202+180.00	0	59,461.36	0.00		0.00	
202+200.00	0	59,461.36	0.00		0.00	
202+220.00	317.97	62,641.01	3,179.66		162.54	
202+240.00	312.67	68,947.36	6,306.35		325.06	
202+260.00	320.6	75,280.03	6,332.66		321.62	
202+280.00	330.13	81,787.33	6,507.30		322.02	
202+300.00	335.88	88,447.44	6,660.11		328.98	
202+320.00	141.42	93,220.38	4,772.95		166.06	
202+340.00	132.47	95,959.23	2,738.85		0.00	
202+360.00	116.74	98,451.35	2492.11		0	
202+376.01	91.94	100,122.29	1,670.94		0.00	

عن الإستشاري أد حسن مهدي
مدير المشروع
م / محمود هريش
م / أحمد عزب

المساحة
م/ محمد عبدالرحمن
١٨/٤

عن الشركة
م / احمد فتح
م / أحمد
١٢
١٩٧٨
ABUAGLA
ب ض ١٠٩ - ١٥١ - ٦٠٩

	مشروع القطار الكهربائي السريع إستكمال أعمال الجسر الترابي لمسار القطار الكهربائي السريع الخط الثاني (الفيوم / بني سويف - أبو سمبل) (مرحلة الجسور والتأسيس والأساس) القطاع الثاني (بني مزار / متفلوط) تنفيذ شركة أبو عجيبة للمقاولات العامة والتوريدات العمومية حصر اجمالي لكميات الردم	الهيئة القومية للإتفاق مكتب أ.د/حسن مهدي للإستشارات الهندسية
--	--	--

بند رقم (١-٣) : أعمال تحميل وتوريد ونقل أتربة مطابقة للمواصفات وتشغيلها باستخدام آلات التسوية بسمك لا يزيد عن ٥٠ سم حتى منسوب (-2 متر) أسفل منسوب القرمه و بسمك لايزيد عن ٢٥سم اعلي من منسوب (-2٠ متر) من منسوب القرمه لاستكمال المنسوب التصميميالخ

Station	Total Fill Area(m2)	Cum. Fill Vol(m3)	As Built vol.Fill	
			Fill VOL(m3)	Total.Qty
201+920.00	202.61	2026.07	2026.07	100122.28
201+940.00	227.66	6,328.78	4,302.71	
201+960.00	248.2	11,087.40	4,758.61	
201+980.00	274.47	16,314.06	5,226.67	
202+000.00	262.01	21,678.88	5,364.82	
202+020.00	243.79	26,736.89	5,058.01	
202+040.00	194.01	31,114.85	4,377.95	
202+060.00	362.48	36,679.73	5,564.88	
202+080.00	341.72	43,721.80	7,042.07	
202+100.00	314.56	50,284.61	6,562.81	
202+120.00	301.56	56,445.77	6,161.16	
202+140.00	0	59,461.36	3,015.59	
202+160.00	0	59,461.36	0.00	
202+180.00	0	59,461.36	0.00	
202+200.00	0	59,461.36	0.00	
202+220.00	317.97	62,641.01	3,179.66	
202+240.00	312.67	68,947.36	6,306.35	
202+260.00	320.6	75,280.03	6,332.66	
202+280.00	330.13	81,787.33	6,507.30	
202+300.00	335.88	88,447.44	6,660.11	
202+320.00	141.42	93,220.38	4,772.95	
202+340.00	132.47	95,959.23	2,738.85	
202+360.00	116.74	98,451.35	2492.11	
202+376.01	91.94	100,122.29	1,670.94	
اجمالي كميات الردم المصروفة سابقا				0
اجمالي كميات الردم الفعلية الحالية بعد خصم سمك خرسانه الميول				100122.28
كمية خصم سمك خرسانه الميول				911

عن الاستشاري المساحة
م/محمد عبد الرحمن
م/احمد عزب
م/محمود غريب
عن الاستشاري أ.د/حسن مهدي
م/احمد عزب
م/محمود غريب



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name [Signature]	Date	Time
Received by Employers Representative	Sign [Signature]	15-8-2022	2
UIR	C1 KP	C2 EW	C3 OT
	DD 15	MM 8	YY 22
	HH	MM	

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
From 200+876 To 202+376	200+876 TO 202+376	
	E=260126.0446 N=3137487.7094	E=260129.6912 N=3135991.0324
Inspection description[Disinfection Of Trees Cutting From st (200+876) to st (202+376)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
[Signature]	- Trees No. was checked only by xyz and under their own responsibility - you must follow specs and design dr

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	[Signature]	[Signature]				
Contractor QA/QC*	XYZ	[Signature]	15-8-2022		A	
	H.M.C	[Signature]	15-8-2022		A	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024		AWC	

* Designer

** Alignment: Bridges: Culvert Only

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name [Signature]	Date	Time
Received by Employers Representative	Sign [Signature]	15-8-2022	2
UIR	C1 KP	C2 EW	C3 OT
	DD 15	MM 8	YY 22
	HH	MM	

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
From 200+876 To 202+376	200+876 TO 202+376	
	E=260126.0446 N=3137487.7094	E=260129.6912 N=3135991.0324
Inspection description[Disinfection Of Trees Cutting From st (200+876) to st (202+376)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
[Signature]	- Trees No. was checked only by xyz and under their own responsibility - you must follow specs and design dr

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	[Signature]	[Signature]				
Contractor QA/QC*	XYZ	[Signature]	15-8-2022		A	
	H.M.C	[Signature]	15-8-2022		A	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024		AWC	

* Designer

** Alignment: Bridges: Culvert Only

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيل للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
	20-10-2022	3								
Received by Employers Representative			C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	20	10	22		

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+686 E=260126.0446 E=260172.2356 N=3137487.7094 N=3136679.1711	
Inspection description/ تطهير بعد قطع الاشجار Disinfection of crops and trees cutting from st (200+876) to st (201+686)		

مقطع مقص

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
---	--

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA/QC*	XYZ		20-10-2022	14:30	A	
	H.M.C		20/10/2022	15:00	A	
GARB**						
Employers Representative						

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
	أديسن مهدي	أديسن مهدي	20-10-2022	4						
Received by Employers Representative			C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	20	10	22		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5						

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+686 TO 201+846	
	E=260172.2356 N=3136679.1711	E=260170.8362 N=3136519.1841
Inspection description/		
Disinfection of crops and trees cutting from st (201+686) to st (201+846) / تم تعقيم بعد قطع الأشجار		

منطقة قطع

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
أديسن مهدي	أديسن مهدي

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	أديسن مهدي	أديسن مهدي				
Contractor QA/QC*	XYZ	أديسن مهدي	20-10-2022	16:00	A	
	H.M.C	أديسن مهدي	20/10/2022	16:30		
GARB**						
Employers Representative						

UNIVERSAL INSPECTION REQUEST



المملكة العربية السعودية
الجمهورية العربية السورية



الجمهورية العربية السورية
الجمهورية العربية السورية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours
The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	Name	Sign	Date	Designer Company*	Time	CODE-1				CODE-2				CODE-3				CODE-4				CODE-5							
						Received by	Employers Representative	C1	C2	C3	OT	DD	MM	YY	HH	MM	CP	EW	OT	DD	MM	YY	HH	MM					
Issued by						20-10-2022						5																	

EXPLANATION OF WORK TO BE INSPECTED			
Area	Element	Item	Inspection description
From 200+876 To 202+376	E=260166.4277 N=3136399.268 E=260129.6912 N=3135991.0324	201+966 TO 202+376	Disinfection of crops and trees cutting from st (201+966) to st (202+376), المكافحة للحشرات والتقليم من (201+966) إلى (202+376)

INSPECTION DETAILS	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as Indicated ☐
Must be included as appropriate			
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBB SURVEY CONSULTANT (XYZ))	Comments by: General consultant (systa)
--	---

INSPECTION RESULT			
Approval	Status	Not Attend	Please Tick if

Organisation				Contractor Engineer				Contractor				QA/QC*				GARBB**				Employers Representative			
Name	Sign	Date	Time	A-AWC-R	XYZ	H.M.C	Khaled alr	23/10/2024	AWC														

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name <i>أبو عجلة</i>	Sign <i>أبو عجلة</i>	Date 25-10-2022
Received by Employers Representative		Time 6	
		UIR	
		C1 KP	C2 EW
		C3 OT	DD 25
		MM 10	YY 22
		HH 00	MM 00
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+466 TO 201+666	
	E=260165.8013 N=3136899.0593	E=260172.0505 N=3136699.1703
Inspection description/ As-Built for rock surface from st (201+466) to st (201+666)		

الرفع المسام + معاينة السطح المصق (المسحوب الأول)

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C - you must follow spec and geo-technical report
---	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	<i>أبو عجلة</i>	<i>أبو عجلة</i>			A-AWC-R	
Contractor QA/QC*	XYZ	<i>أبو عجلة</i>	25-10-2022	13:00	A	
	H.M.C	<i>أبو عجلة</i>	25/10/2022	13:00	A	
GARB**						
Employers Representative	Khaled ali	<i>أبو عجلة</i>	23/9/2024			



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
			29-10-2022	7						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	29	10	28		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	200+876 TO 201+466		
	E=260126.0446	E=260165.8013	
	N=3137487.7094	N=3136899.0593	
Inspection description[الرفع المساحي + المعاينة للطرح المقصود (المسوح الأول) As-Built for rock surface from st (200+876) to st (201+466)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

(as built) [Signature] [Stamp]	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C. - you must follow specs and design drawings.
--------------------------------------	--

INSPECTION RESULT

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time			
Contractor Engineer							
Contractor QA/QC*	XYZ		29-10-2022	12:00	A		
	H.M.C		29/10/22		A		
GARB**							
Employers Representative	Khaleed ali		23/9/2024				

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة زينة حيلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
	أحمد أبو بكر		2-11-2022	8						
Received by Employers Representative			C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	2	11	22		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+036 TO 201+086	
	E=260137.1186	E=260140.5793
	N=3137328.0971	N=3137278.217
<u>Inspection description/</u> As-Built for rock surface from st (201+036) to st (201+086)		

الرفع المسامى + معاينة السطح المجرى (المنسوب المظن) الثالث

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
2/11/2022	

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C - you must follow spec and geo-technical report

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	أحمد أبو بكر						
Contractor QA/QC*	XYZ	محمد عبد الرحمن	2-11-2022	17:30	A		
	H.M.C	محمد عبد الرحمن	2/11/2022	13:30	A		
GARB**							
Employers Representative	Khaled Ali		23/9/2024				

مكتبة A / مكتبة B / مكتبة C / مكتبة D / مكتبة E / مكتبة F / مكتبة G / مكتبة H / مكتبة I / مكتبة J / مكتبة K / مكتبة L / مكتبة M / مكتبة N / مكتبة O / مكتبة P / مكتبة Q / مكتبة R / مكتبة S / مكتبة T / مكتبة U / مكتبة V / مكتبة W / مكتبة X / مكتبة Y / مكتبة Z

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عبيدة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
	محمد أبو بكر	[Signature]	6-11-2022	10						
Received by Employers Representative	[Signature]	[Signature]	C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	6	11	2022		
CODE-1		CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+156 TO 201+246	
	E=260145.4242	E=260151.6535
	N=3137208.3848	N=3137118.6007
<u>Inspection description:</u> As-Built for rock surface from st (201+156) to st (201+246)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. (xyz))	Comments by: General consultant (systra)
[Signature]	- Levels and Coordinates were checked only by xyz and under their own responsibility. - This work was inspected only by xyz and H.M.C. you must follow specs and geo-technical report

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	محمد أبو بكر	[Signature]					
Contractor QA\QC*	XYZ	[Signature]	6-11-2022	14:00	A		
	H.M.C	[Signature]	6/11/2022	14:30	A		
GARB**							
Employers Representative	Khaled Ali	[Signature]	23/9/2024				

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name أبو عجلة	Sign أبو عجلة	Date 7-12-2022																
Received by Employers Representative			Time 13																
		UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>EW</td> <td>OT</td> <td>7</td> <td>12</td> <td>23</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	EW	OT	7	12	23		
C1	C2	C3	DD	MM	YY	HH	MM												
KP	EW	OT	7	12	23														
CODE-1	CODE-2	CODE-3	CODE-4																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+286 TO 201+386	
	E=260154.422 N=3137078.6966	E=260161.1582 N=3136978.9239
<u>Inspection description</u> As-Built for rock surface from st (201+286) to st (201+386)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT: xyz)	Comments by: General consultant (systra)
	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C. - you must follow specs and geo-technical report

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	XYZ	أبو عجلة	7-12-2022	14:00	A		
Contractor QA/QC*	H.M.C	أبو عجلة	7/12/2022	14:30	A		
GARB**							
Employers Representative	Khaled ali	أبو عجلة	23/9/2024				

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR ,Hassan Mahdy (H.M.C)					
Issued by Contractor	Name Sign	Date	Time					
Received by Employers Representative	Sign	13-12-2022	14					
UIR	C1 KP	C2 EW	C3 OT	DD 13	MM 12	YY 22	HH	MM
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5				

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+386 TO 201+426	
	E=260161.1582 N=3136978.9239	E=260163.6041 N=3136938.9988
Inspection description: الرفع المساحي + معاينة سطح صخره (المستوي الثالث) As-Built for rock surface from st (201+386) to st (201+426)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)



- Levels and coordinates were checked only by systra and under their own responsibility
- This work was inspected only by systra and H.M.C
- you must follow specs and geo-technical report

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer					A-AWC-R	
Contractor QA/QC*	XYZ		13-12-2022	12:16	A	
	H.M.C		13/12/2022	12:17	A	
GARB**						
Employers Representative	Khaled al.		23/12/2022			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR ,Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
			2023-1-3	17						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	3	1	23		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	200+876 TO 201+666		
	E=260126.0446	E=260172.0505	
	N=3137487.7094	N=3136699.1703	
Inspection description/			
As-Built for cut from st (200+876) to st (201+666)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
2023/1/3	

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

مستشار
للإستشارات الهندسية
أدامن مهدي

Comments by: General consultant (systra)

- Levels and coordinates were checked only by XYZ and under their own responsibility
- you must follow specs and design drawings

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor	XYZ		3-1-2023	19:00	A	
QA/QC*	H.M.C		3/1/2023	19:00		
GARB**						
Employers Representative	Khaled ali		23/9/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name 1375 Sign 	Date	13-6-2023																
Received by Employers Representative	Time 18	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>EW</td> <td>OT</td> <td>13</td> <td>6</td> <td>23</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	EW	OT	13	6	23		
C1	C2	C3	DD	MM	YY	HH	MM												
KP	EW	OT	13	6	23														
CODE-1	CODE-2	CODE-3	CODE-4																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+660	
	E=260126.0446 N=3137487.7094	E=260171.9793 N=3136705.1798
Inspection description		
As-Built for cut from st (200+876) to st (201+660)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
12/6/2023	

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

as built for cut from st (200+876) to st (201+660)

- Levels and coordinates were checked only by xyz and under their own responsibility
- you must follow spec and design dwg.

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA/QC*	XYZ		13-6-2023	9:00	A	
	H.M.C		13/6/2023			
GARB**						
Employers Representative	Khaled ali		23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله والمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name Sign 24-8-2023	Date	Time 19
Received by Employers Representative	Sign 23	Time	

CODE -1	CODE -2	CODE -3	CODE -4	CODE -5
---------	---------	---------	---------	---------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+840 E=260126.0446 N=3137487.7094	E=260170.9813 N=3136525.1923
Inspection description: As-Built for cut from st (200+876) to st (201+840)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
24/8/2023	

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

as built
قطاع الضلع

- Levels and coordinates were checked only by xyz and under their own responsibility
- you must follow specs and design dwg.

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer					A-AWC-R	
Contractor QA/QC*	XYZ		26-8-2023	10:00	A	
	H.M.C		26/8/2023	10:15	A	
GARB**						
Employers Representative	Khaled ali		23/8/2023			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name وليد فهد محمد	Date	9-11-2023
Received by Employers Representative	Sign وليد فهد محمد	REQ.NUM	20
Received by Employers Representative	UIR	C1 KP	C2 SU
		C3 OT	DD 9
		MM 11	YY 23
		HH	MM
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description/ تشييد قاع إحلل from st (202+220) to st (202+300)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))	Comments by: General consultant (systra)
	- levels and coordinates were checked only by xyz and under their own responsibility - No objection according to the attached reports and lab. results.

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد فهد محمد	وليد فهد محمد	19-11-2023	10:00	(A)	
Contractor QA/QC*	XYZ	محمد عبد الرحمن	9/11/2023	11:00	A	
GARB**						
Employers Representative	Khaled ali		23/9/2024			

* Designer

** Alignment: Bridges; Culvert Only

UNIVERSAL INSPECTION REQUEST



مكتب أد/حسن مهدي
للإستشارات الهندسية



الهيئة القومية للإستشارات
الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عبيدة للمقاولات 2023		Designer Company*	DR ,Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ. NUM						
			20-11-2023	22						
Received by Employers Representative	UIR		C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT	21	11	23	2	30
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+000 TO 202+120		
	E=260164.6561	E=260156.5571	
	N=3136365.3242	N=3136245.6007	
Inspection description/			
تشييد قاع إحلال from st (202+000) to st (202+120)			

INSPECTION DETAILS The Following will be ready at the Planned inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was checked only by xyz and H.M.C. - you must follow speed and design drawing and geo-technical report

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمد				A-AWC-R	
Contractor QA/QC*	XYZ		21-11-2023	3:15	(A)	
	H.M.C	عبدالله محمد	21/11/2023	3:00	A	
GARB**						
Employers Representative	Khaled ali		23/11/2024		Any	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown:

Contractor Company	أبو عجمية للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name:  Sign: 	Date	REQ. NUM																
Received by Employers Representative	UIR	21-11-2023	23																
		<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>22</td> <td>11</td> <td>23</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	22	11	23			
C1	C2	C3	DD	MM	YY	HH	MM												
KP	SU	OT	22	11	23														
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5															

EXPLANATION OF WORK TO BE INSPECTED



Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
<u>Inspection description/</u> from st (202+220) to st (202+300) طبقة ردم منسوب (-9.5) متر		


INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time


COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
 	- No objection, according to the attached reports and Lab. results. - you must follow specs and design drawings

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time			
Contractor Engineer	وليد عوريجي						
Contractor QA/QC*	XYZ		22-11-2023	3:45	(A)		
	H.M.C		22/11/2023	11:00	A		
GARB**							
Employers Representative	Fhaled ali		23/11/2023				

RECEIPT of NOTIFICATION Minimum Notice Period not less than 24 Hours
The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة المقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name	Sign	Date
			25-11-2023
Received by Employers Representative	شركة سايسترا		REQ.NUM
		24	
		UIR	
		C1 KP C2 SU C3 OT DD 25 MM 11 YY 23 HH MM	
CODE-1		CODE-2	CODE-3
		CODE-4	CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+000 TO 202+020	
	E=260164.6561	E=260163.5058
	N=3136365.3242	N=3136345.3573
<u>Inspection description:</u> منطقة ردم منسوب (13) متر from st (202+000) to st (202+020)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (systa)) 	Comments by: General consultant (systa) - No objection, according to the attached reports and lab. results. - you must follow specs and design drawings
--	--

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمد	وليد محمد			A-AWC-R	
Contractor QA/QC*	XYZ	محمد ابراهيم	25-11-2023	12:30	(A)	
	H.M.C	محمد علي	25/11/23	11:00	A	
GARB**						
Employers Representative	Khaled ali	كhaled ali	23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name 	Sign 	Date 28-11-2023																
Received by Employers Representative	UIR	REQ NUM 25																	
		<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>28</td> <td>11</td> <td>23</td> <td>11</td> <td>00</td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	28	11	23	11	00	
C1	C2	C3	DD	MM	YY	HH	MM												
KP	SU	OT	28	11	23	11	00												
CODE-1	CODE-2-109	CODE-3	CODE-4	CODE-5															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300 E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description منسوب (9-متر) from st (202+220) to st (202+300)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)



- No objection, according to the attached reports and lab. results
- you must follow specs and design dng.

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمد					
Contractor QA/QC*	XYZ	عبد الله الدلاوي	28/11/2023	3:30	A	
	H.M.C	عبد الله الدلاوي	28/11/2023	11:00	A	
GARB**						
Employers Representative	Khaled ali		23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	Name		Sign	Designer Company*	DR .Hassan Mahdy (H.M.C)				
Issued by Contractor	29-11-2023		REQ.NUM		26				
Received by Employers Representative	C1		C2	C3	DO	MM	YY	HH	MM
	KP		SU	OT	29	11	23		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5	

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+060 TO 202+080		
	E=260160.9658 N=3136305.4382	E=260159.576 N=3136285.4865	
Inspection description[from st (202+060) to st (202+080) طبقة ردم منسوب (-11) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))	Comments by: General consultant (systra)
 المهندس خالد علي - الهندس	- No objection, according to the attached reports and lab. results. - you must follow specs and design draw

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد فريد	وليد فريد				
Contractor QA/QC*	XYZ	خالد علي	29-11-2023	11:15	(A)	
	H.M.C	محمد احمد	29-11-2023	12:45	A	
GARB**						
Employers Representative	Khaled ali	كhaled علي	29/11/2023		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)					
Issued by Contractor	Name وليد محمود محمد	Date	29-11-2023					
Received by Employers Representative	Sign [Signature]	REQ.NUM	27					
UIR	C1 KP	C2 SU	C3 OT	DD 29	MM 11	YY 23	HH	MM
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5				

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+080 TO 202+120 E=260159.576 N=3136285.4865	E=260156.5571 N=3136245.6007
Inspection description: منطقة ردم منسوب (-10.5) متر from st (202+080) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSANTANT.(xyz))

Comments by: General consultant (systra)

-No objection, according to the attached reports and lab. results
-you must follow specs and design dwg

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمود محمد	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	[Signature]	29-11-2023	11:30	(A)	
	H.M.C	[Signature]	29-11-2023	12:30	A11	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	157137 أبو عزة للتقانات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)					
Issued by Contractor	Name م.د/حسن مهدي	Date	30-11-2023					
Received by Employers Representative	Sign م.د/حسن مهدي	REQ. NUM	28					
UIR	C1 KP	C2 SU	C3 OT	DD 30	MM 11	YY 23	HH	MM

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+000 TO 202+020 E=260164.6561 N=3136365.3242	E=260163.5058 N=3136345.3573
Inspection description: ردم طبقة ردم منسوب (-12.5) متر from st (202+000) to st (202+020)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (XYZ)) م.د/حسن مهدي	Comments by: General consultant (systra) -No objection, according to the attached reports and lab. results. -you must follow spec and design draw
---	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	م.د/حسن مهدي	م.د/حسن مهدي	30-11-2023	13:00	A	
Contractor QA/QC*	XYZ	م.د/حسن مهدي	30-11-2023	12:30pm	A	
GARB**						
Employers Representative	Khaled Ali	م.د/حسن مهدي	23/9/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 57537	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name [Signature]	Date	2-12-2023																
Received by Employers Representative	Sign [Signature]	REQ.NUM	29																
UIR		<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>2</td> <td>12</td> <td>23</td> <td></td> <td></td> </tr> </table>		C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	2	12	23		
C1	C2	C3	DD	MM	YY	HH	MM												
KP	SU	OT	2	12	23														
CODE-1	CODE-2	CODE-3	CODE-4																
CODE-5	CODE-6	CODE-7	CODE-8																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description[from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (-8.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (sysra)
[Signature]	- No objection, according to the attached reports and lab. results. - you must follow specs and design dr

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	علي محمد	[Signature]				
Contractor QA/QC*	XYZ	عبد الرحمن الوالد	21/12/2023	3:15	A	
	H.M.C	أحمد مصطفى	21/12/23	3:00	AWC	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/12/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
			3-12-2023	30						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT				23	
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5						

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+060 TO 202+100		
	E=260160.9658	E=260158.1064	
	N=3136305.4382	N=3136265.5406	
Inspection description			
from st (202+060) to st (202+100) طبقة ردم مسسوب (-10.5) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))	Comments by: General consultant (systra)
	- No objection, according to the attached reports and lab. results.
	- you must follow specs and design d.

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA\QC*	XYZ		3-12-2023	4:15	(A)	
	H.M.C		3/12/2023	2:30 PM	AWC	
GARB**						
Employers Representative	Khaled ali		28/9/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown.

Contractor Company	شركة البترول العالمية		Designer Company*	DR. Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	REQ. NUM							
	[Signature]		5-12-2023	31							
Received by Employers Representative	[Signature]	[Signature]	UIR	C1	C2	C3	DD	MM	YY	HH	MM
				KP	SU	OT				23	
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+220 TO 202+300		
	E=260147.6147	E=260139.0278	
	N=3136146.003	N=3136066.4661	
Inspection description/			
من تسليم طبقة ردم منسوب (8-متر) from st (202+220) to st (202+300)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT (-xyz))

Comments by: General consultant (systra)

[Signature] مهندس إسماعيل أحمد السريج - الخطة 10	- No objection, according to the attached reports and lab. results. - you must follow specs and design dwg.
--	---

INSPECTION RESULT

					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد صوري	[Signature]	6-12-2023	10:30	(A)	
Contractor QA/QC*	XYZ	[Signature]	6-12-2023	10:30	(A)	
	H.M.C	[Signature]	5/12/2023	4:15Pm	AWC	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024		Awc	



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours
 The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name	Sign	Date															
	وليد عيسى	وليد عيسى	7-12-2023															
Received by Employers Representative		UIR	REQ. NUM															
			32															
		<table border="1" style="width: 100%; border-collapse: collapse;"> <tr> <td>C1</td><td>C2</td><td>C3</td><td>DD</td><td>MM</td><td>YY</td><td>HH</td><td>MM</td> </tr> <tr> <td>KP</td><td>SU</td><td>OT</td><td></td><td></td><td>23</td><td></td><td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			23		
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT			23													
CODE-1	CODE-2	CODE-3	CODE-4															

EXPLANATION OF WORK TO BE INSPECTED


Area	Element	Item
From 200+876 To 202+376	200+876 TO 202+120	
	E=260160.9658	E=260156.5571
	N=3136305.4382	N=3136245.6007
<u>Inspection description/</u> من طرقة ردم ملمسوب (10-) متر from st (202+060) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as Indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz)) 	Comments by: General consultant (systra) -No objection, according to the attached reports and lab. results. -you must follow specs and design drug
--	--

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد عيسى	وليد عيسى	7-12-2023	1:30	(A)	
Contractor QA/QC*	XYZ	محمد علي	7/12/2023	12:15	A	
GARB**						
Employers Representative	Khaled ali		23/12/2024		AWC	



UNIVERSAL INSPECTION REQUEST



مكتب أ.أ.أ.أ.أ.أ.
للإشراف الهندسية



الهيئة العامة للإشراف
على الطرق



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR. Hassan Mahdy (H.M.C)					
Issued by Contractor	Name	Sign	Date	REQ. NUM					
	13-12-2023	35							
Received by Employers Representative	UIR	G1 KP	C2 SU	C3 OT	DD 13	MM 12	YY 23	HH 3	MM 00
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description/ منطقة ردم منسوب (9- متر from st (202+060) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. (xyz))	Comments by: General consultant (systra)
	- No objection, according to the attached reports and lab. results. - you must follow specs and design drawings.

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	أ.أ.أ.أ.أ.أ.	أ.أ.أ.أ.أ.أ.	13-12-2023	4:00	(A)		
Contractor QA/QC*	XYZ	أ.أ.أ.أ.أ.أ.	13-12-2023	3:00	Awc		
GARB**							
Employers Representative	Khaled ali	أ.أ.أ.أ.أ.أ.	23/9/2024		Awc		

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



شركة أديس مهدي
للإستشارات الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة			Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM							
	أبو عجلة	أبو عجلة	16-12-2023	36							
Received by Employers Representative	Signature	Signature	UIR	G1	G2	G3	DD	MM	YY	HH	MM
				XP	SU	OT			23		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	200+220 TO 202+300		
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661	
Inspection description:			
من تسليم طبقة ردم مسلوب (7-متر) from st (202+220) to st (202+300)			

INSPECTION DETAILS The following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT: (xyz))

أبو عجلة
أبو عجلة
أبو عجلة

Comments by: General consultant (systra)

- No objection, according to the attached reports and lab. results.
- you must follow specs and design dwg.

INSPECTION RESULT

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	أبو عجلة	أبو عجلة					
Contractor QA/QC*	XYZ	أبو عجلة	16-12-2023	3:15	A		
	H.M.C	أبو عجلة	16/12/2023	3:00	A		
GARB**							
Employers Representative	Khaled ali	أبو عجلة	29/12/24		Awc		



UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للطرق
والبنية التحتية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	وليد فلاح	وليد فلاح	17-12-2023	37						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT				23	
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007	
Inspection description:			
من (202+060) إلى (202+120) طبقة ردم ملسوب (8.5) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by (GARB SURVEY CONSULTANT xyz)	Comments by: General consultant (systra)
استاذ المهندس مستوى التفتيش الكفائي	- No objection, according to the attached reports and lab. results. - you must follow specs and design dwg

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد فلاح	وليد فلاح				تم العمل
Contractor QA/QC*	XYZ		17-12-2023	13:00	A	OK
	H.M.C		17-12-2023	11:00	Amc	OK
GARB**						
Employers Representative	Khaled ali		20/12/24		Amc	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإشراف الهندسية



المشاور الهندسي الدكتور
أدريس مهدي



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown:

Contractor Company	DR. Hassan Mahdy (H.M.C)	Designer Company*	DR. Hassan Mahdy (H.M.C)
Issued by Contractor	Name: <u>أدريس مهدي</u> Sign: <u>[Signature]</u>	Date	19-12-2023
Received by Employers Representative	REQ. NUM	38	
	C1 C2 C3 C4 C5 C6 C7 C8 C9 C10 C11 C12 C13 C14 C15 C16 C17 C18 C19 C20 C21 C22 C23 C24 C25 C26 C27 C28 C29 C30 C31 C32 C33 C34 C35 C36 C37 C38 C39 C40 C41 C42 C43 C44 C45 C46 C47 C48 C49 C50 C51 C52 C53 C54 C55 C56 C57 C58 C59 C60 C61 C62 C63 C64 C65 C66 C67 C68 C69 C70 C71 C72 C73 C74 C75 C76 C77 C78 C79 C80 C81 C82 C83 C84 C85 C86 C87 C88 C89 C90 C91 C92 C93 C94 C95 C96 C97 C98 C99 C100		
	AP SU OT		
	YY		
	HH		
	MM		
	DD		
	CODE-1	CODE-2	CODE-3

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+576	202+220 TO 202+300	
	E=260147.5147 E=260139.0278	
	N=3136146.003 N=3136066.4661	
Inspection description (		
from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (7,0-)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	M5 Reference	

Comments by: (GARB SURVEY CONSULTANT: XYZ)

Comments by: General consultant (systra)

تم فحص المخطط ووافق عليه المهندس أدريس مهدي مستوى تشتت الكثبان للسرعة - الخط الذي	- No objection, according to the attached reports and lab. results. - you must follow specs and design drawings
---	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	أدريس مهدي	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	[Signature]	19-12-2023	3:30	A	
	H.M.C	[Signature]	19-12-2023	11:30	A	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date						
	وليد محمود محمد		20-12-2023						
Received by Employers Representative		REQ.NUM	39						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT			23		

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description/		
من (8-) متر from st (202+060) to st (202+120) طبقة ردم منسوب		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

- No objection, according to the attached reports and Lab. results.
- You must follow specs and design draw

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمود محمد				A-AWC-R	
Contractor QA/QC*	XYZ		20-12-2023	3:40	A	
	H.M.C		20-12-2023	1:45	A	
GARB**						
Employers Representative	Khaled ali		23/9/2024		A	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والخدمات الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name Sign 21-12-2023	Date	REQ.NUM 40															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>21</td> <td>12</td> <td>23</td> <td>11</td> <td>30</td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	21	12	23	11	30
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT	21	12	23	11	30											
CODE-1	CODE-2	CODE-3	CODE-4															
CODE-5	CODE-6	CODE-7	CODE-8															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300 E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description: from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (6-متر)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT: xyz)	Comments by: General consultant (systra)
	- No objection, according to the attached reports and lab. results. - you must follow specs and design d.

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمد	وليد محمد				
Contractor QA/QC*	XYZ	عبد الرحمن العرابي	21-12-2023	11:00	A	
	H.M.C	محمد بن عبد الله العرابي	21/12/23	11:30	A	
GARB**						
Employers Representative	Khaled ali		23/12/2023		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب المهندس مهدي
للإشراف الهندسية



الهيئة العامة للطرق
والمواصلات



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name وليد محمود محمد	Sign 	Date 23-12-2023	REQ.NUM 41																
Received by Employers Representative			<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>23</td> <td></td> <td></td> </tr> </table>		C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			23		
C1	C2	C3	DD	MM	YY	HH	MM													
KP	SU	OT			23															
CODE-1		CODE-2	CODE-3	CODE-4	CODE-5															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description: from st (202+220) to st (202+300) تسليم طبقة ردم ملسوب (-5.5) متر		

INSPECTION DETAILS The following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz)) 	Comments by: General consultant (systra) - No objection, according to the attached reports and lab. results. - you must follow specs and design dr.
---	---

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود محمد	وليد فهد				
Contractor QA/QC*	XYZ	عبدالله بن علي	23/12/2023	1:00	A	
	H.M.C	محمد علي بن علي	23/12/2023	12:00	A	
GARB**						
Employers Representative	Khaled ali		23/12/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للمشاورات الهندسية



الهيئة العامة للإسكان
General Housing Authority



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name: <u>وليد محمود</u> Sign: <u>[Signature]</u>	Date	REQ.NUM																
Received by Employers Representative		23-12-2023	43																
		<table border="1"> <tr> <td>G1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>23</td> <td>12</td> <td>23</td> <td></td> <td></td> </tr> </table>	G1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	23	12	23			
G1	C2	C3	DD	MM	YY	HH	MM												
KP	SU	OT	23	12	23														
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description/ from st (202+060) to st (202+120) طبقة ردم منسوب (-7.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT. (xyz))

[Signature]
مهندس التخطيط
م. خالد النور

Comments by: General consultant (systra)

- No objection, according to the attached reports and lab. results.
- you must follow specs and design draw

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمود	وليد خلاف			A-AWC-R	
Contractor QA/QC*	XYZ	م. خالد النور	23-12-2023	4:15	A	
	H.M.C	احمد سمير	23/12/23	4:00	AWC	
GARB**						
Employers Representative	Khaled n	[Signature]	23/12/2023		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أراضين مهدي
للإستشارات الهندسية



الهيئة العامة للإعتماد
والتقنين



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	المشروعات العامة		Designer Company*	DR. Hassan Mahdy (H.M.C)																
Issued by Contractor	Name وليد محمود	Sign [Signature]	Date 25-12-2023	REQ. NUM 44																
Received by Employers Representative	[Signature]		<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DO</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>23</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DO	MM	YY	HH	MM	KP	SU	OT			23			
C1	C2	C3	DO	MM	YY	HH	MM													
KP	SU	OT			23															
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description: من 202+060 to 202+120 طبقه ردم منسوب (-7) متر		

INSPECTION DETAILS The following will be ready at the Planned inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT. xyz)

Comments by: General consultant (systra)

[Signature]

- No objection, according to the attached reports and lab. results.
- you must follow specs and design data

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود	[Signature]				
Contractor QA/QC*	XYZ	[Signature]	25-12-2023	4:13	A	
	H.M.C	[Signature]	25-12-2023	4:10	AWC	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أديسن مهندسي
الاستشارات الهندسية



الهيئة العامة للإستثمار



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أيم جلوبل للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	وليد محمود محمد		28-12-2023	46						
Received by Employers Representative		VIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT				23	

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
From 200+876 To 202+376	201+980	
	E=260165.727 N=3136385.3	
Inspection description: منطقة ردم منسوب (-14) متر from st (201+980)		

INSPECTION DETAILS The Following will be ready at the Planned inspection Time	
Planned inspection Date	Planned inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))	Comments by: General consultant (systra)
 - No objection, according to the attached reports and lab. results.	you must follow specs and design drawings

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود محمد	وليد محمود محمد				
Contractor QA/QC*	XYZ	عبد الرحمن العبدان	28-12-2023	13:00	A	
	H.M.C	محمود بشير محمد	28-12-2023	11:00		
GARB**						
Employers Representative	Khaled ali		23/9/2024		ANC	

UNIVERSAL
INSPECTION
REQUEST








RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours
The Work described below will be complete and ready for inspection at planned time shown

Contractor Company

Name

Designer Company*

Date

DR .Hassan Mahdy
(H.M.C)

28-12-2023

Issued by Contractor

Sign

REQ.NUM

47

Received by Employers Representative

Sign

C1 C2 C3 DO MM YY HH MM

KP SU OT 23

EXPLANATION OF WORK TO BE INSPECTED

Area

Element

Item

From 200+876 To 202+376

202+060 TO 202+120
E=260160.9658
N=3136305.4382

E=260156.5571
N=3136245.6007

Inspection description/

from st (202+060) to st (202+120) طبقة ردم منسوب (-6.5) متر

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date

Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐

Test Results Attached ☐

Calibration Attached ☐

Other as indicated ☐

Drawing Reference

ITP Reference

MS Reference

Comments by: (GARB SURVEY CONSATANT-xyz)

Comments by: General consultant (systra)

No objection, according to the attached reports and lab. results.

you must follow specs and design dng.

INSPECTION RESULT

Approval Status

Please Tick if Not Attend

Organisation

Name

Sign

Date

Time

A-AWC-R

Contractor Engineer

XYZ

28-12-2023

11:00

A

Contractor QA/QC*

H.M.C

28-12-2023

18:00

A

GARB**

Employers Representative

23/12/2023

Ame



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company			Designer Company*	DR. Hassan Mahdy (H.M.C)																
Issued by Contractor	Name	Sign	Date	REQ. NUM																
			2-1-2024	49																
Received by Employers Representative			<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			24			
C1	C2	C3	DD	MM	YY	HH	MM													
KP	SU	OT			24															
CODE-1		CODE-2		CODE-3	CODE-4	CODE-5														

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+060 TO 202+120		
	E=260160.9658	E=260156.5571	
	N=3136305.4382	N=3136245.6007	
<u>Inspection description</u> from st (202+060) to st (202+120) طبقة ردم منسوب (-6) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))	Comments by: General consultant (systra)
	- No objection, according to the attached reports and lab. results - you must follow specs and design drawings

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer							
Contractor QA/QC*	XYZ		2-1-2024	11:40	A		
	H.M.C		2-1-2024	11:50	AWC		
GARB**							
Employers Representative	Khaleed ali		23/1/2024		AWC		

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة المهندسين مهدي للإستشارات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name وليد محمور	Sign 	Date 2-1-2024																
Received by Employers Representative	UIR	REQ NUM 50																	
		<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			24			
C1	C2	C3	DD	MM	YY	HH	MM												
KP	SU	OT			24														
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+960 TO 202+000 E=260166.717 E=260164.6561 N=3136405.271 N=3136365.1247	
<u>Inspection description</u> from st (201+960) to st (202+000) طبقة ردم منسوب (-13.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. (xyz)) 	Comments by: General consultant (systra) -No objection, according to the attached reports and lab. results. -you must follow specs and design dr
---	--

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمور					
Contractor QA\QC*	XYZ	عبد الرحمن الشراي	2-1-2024	11:15	A	
	H.M.C	عبد الرحمن الشراي	2-1-2024	11:00	AUC	
GARB**						
Employers Representative	Khaled ali		23/9/2024		AUC	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



المهنة العامة الإستشارية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	REQ.NUM							
	[Signature]		6-1-2024	51							
Received by Employers Representative	[Signature]	[Signature]	UIR	C1	C2	C3	DD	MM	YY	HH	MM
				KP	SU	OT				20	

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+960 TO 202+000		
	E=260166.717	E=260164.6561	
	N=3136405.271	N=3136365.3242	
<u>Inspection description</u> from st (201+960) to st (202+000) طبقه ردم منسوب (-13) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. xyz)	Comments by: General consultant (systra)
[Signature]	- No objection, according to the attached reports and lab. results. - you must follow specs and design drag

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمدي	[Signature]				
Contractor QA/QC*	XYZ	عبد الرحمن العرابي	6-1-2024	4:20	A	
	H.M.C	محمود عولمة	6/1/2023	4:15	AWC	
GARB**						
Employers Representative	Khaled ali	[Signature]	29/9/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أمان مهدي
للإستشارات الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	[Signature]		6-1-2024	52						
Received by Employers Representative	[Stamp]	UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT				24	

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+060 TO 202+120		
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007	
Inspection description/			
from st (202+060) to st (202+120) طبقة ردم منسوب (5.5) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))

تم الاستعراض وفقاً للمواصفات
المشار إليها في التقرير - انظر المرفق

Comments by: General consultant (systra)

- No objection, according to the attached reports and lab results.
- you must follow spec and design

INSPECTION RESULT

					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	علي محمد	[Signature]				
Contractor QA/QC*	XYZ	علي محمد	6-1-2024	5:00	A	
	H.M.C	علي محمد	6/1/2024	4:40	Awc	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024		Anrc	

UNIVERSAL INSPECTION REQUEST



مكتب أ.أ.أ. من مهاي
للإشراف الهندسية



الهيئة العامة للإشراف
على الطرق



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أ.أ.أ. من مهاي للإشراف الهندسية	Designer Company*	DR. Hassan Mahdy (H.M.C)						
Issued by Contractor	Name: Sign:	Date	10-1-2024						
Received by Employers Representative	UIR	REQ.NUM	53						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT			28		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description:		
من (5- متر from st (202+060) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate



Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSALTANT. (xyz))	Comments by: General consultant (systra)
ملاحظات المهندس الاستشاري (xyz)	-No objection, according to the attached reports and lab. results. -you must follow specs and design dwg

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد الحويهد					
Contractor QA/QC*	XYZ	عبد الرحمن العرياني	10-1-2024	12:30	A	
	H.M.C	محمد العرياني	10-1-2024	12:00	A	
GARB**						
Employers Representative	Khaled chi		23/9/2024		Awc	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name:  Sign: 	Date	REQ.NUM
Received by Employers Representative	UIR	10-1-2024	54
		C1 C2 C3 DD MM YY HH MM	
		KP SU OT	23
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+300 TO 202+376	
	E=260139.0278 N=3136066.4661	E=260129.6912 N=3135991.0324
Inspection description/		
from st (202+300) to st (202+376)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time


Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))

Comments by: General consultant (systra)





- levels and coordinates were checked only by xyz and under their own responsibility

- you must follow specs and designing and geo-technical report.


- This work was inspected only by xyz and H.M.C

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمود				A-AWC-R	
Contractor QA/QC*	XYZ		10-1-2024	10:30	A	
	H.M.C		10-1-2024	10:30	AWC	
GARB**						
Employers Representative	Khaled ali		23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name:  Sign: 	Date	REQ. NUM
Received by Employers Representative	UIR	15-1-2024	55
		C1 C2 C3 DD MM YY HH MM	
		KP SU OT	20
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED


Area	Element	Item
From 200+876 To 202+376	202+300 TO 202+340 E=260139.0278 E=260134.2574 N=3136066.4661 N=3136026.7517	
Inspection description/ منسوب (8.5-) متر from st (202+300) to st (202+340)		


INSPECTION DETAILS The following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT - (xyz))	Comments by: General consultant (systra)
	-you must follow specs and design drug- -you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	علي محمد					
Contractor QA/QC*	XYZ	عبد الرحمن العزاد	16-1-2024	8:30	A	
	H.M.C	محمود علي	15/1/2024	4:30pm	A	
GARB**						
Employers Representative	Khaled ali		26/1/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 1075377	Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name: Sign:	Date	15-1-2024						
Received by Employers Representative	UIR	REQ. NUM	56						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT			24		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+220 TO 202+300		
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661	
Inspection description/			
تسليم طبقة ردم منسوب (4) متر from st (202+220) to st (202+300)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

-you must follow specs and design by
 -you must do leveling and lining
 the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود محمد		16-1-2024			
Contractor QA/QC*	XYZ	عبد الرحمن الزقراوي	16-1-2024	9:18	A	
	H.M.C	محمد علي	15/1/2024	5:10	A	
GARB**						
Employers Representative	Khaled ali		16/1/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name: Sign:	Date	REQ. NUM
Received by Employers Representative	UIR	16-1-2024	57
		C1 C2 C3 DD MM YY HH MM	
		KP SU OT	21
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description/		
منطقة ردم منسوب (4.5) متر from st (202+060) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT-xyz)	Comments by: General consultant (systra)
	-you must follow specs and design durg. -you must do landing and lining the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد عمار					
Contractor QA\QC*	XYZ		16-1-2024	3:30	A	
	H.M.C		16/1/2024	3:00	AWC	
GARB**						
Employers Representative	Khaled ali		16/1/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name 157537 Sign وليد خلافة	Date 17-1-2024	REQ.NUM 58															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>17</td> <td>1</td> <td>24</td> <td>4</td> <td>00</td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	17	1	24	4	00
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT	17	1	24	4	00											
CODE-1	CODE-2	CODE-3	CODE-4															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300 E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description/ منسوب (3.5-) متر from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (3.5-) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: GARB SURVEY CONSATANT (xyz)	Comments by: General consultant (systra)
تم فحص الموقع ووجدنا ان العمل مطابق للمواصفات - الفحص النهائي	-you must follow specs and design dng -you must do leveling and lining the compacted side slope & filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	علي محمد علي	علي محمد علي	17-1-2024	5:10	A	
Contractor QA/QC*	XYZ	علي محمد علي	17-1-2024	5:10	A	
	H.M.C	علي محمد علي	17-1-2024	4:00	A	
GARB**						
Employers Representative	Khaled Ali	Khaled Ali	17/1/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أديان مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR. Hassan Mahdy (H.M.C)					
Issued by Contractor	Name	137537	Sign	Date	REQ. NUM				
	وليد محمد		20-1-2024		59				
Received by Employers Representative	UIR	C1	C2	C3	DO	MM	YY	HH	MM
		KP	SU	OT				24	
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5	

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+300 TO 202+360		
	E=260139.0278 N=3136066.4661	E=260131.7531 N=3136006.9091	
Inspection description			
منسوب (8-متر) from st (202+300) to st (202+360) تسليم طبقة ردم منسوب (8-متر)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: GARB SURVEY CONSATANT. (xyz)	Comments by: General consultant (systra)
مستشار المساحة م. خالد علي	- you must follow specs and design dwg. - you must do leveling and Cinning the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمد					
Contractor QA/QC*	XYZ	عبد الرحمن الزباري	20/1/2024	10:00	A	
	H.M.C	محمود علي	20/1/2024	09:00	A	
GARB**						
Employers Representative	Khaled ali		20/1/2024		Amr	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name: <u>علي محمد</u> Sign: <u>علي محمد</u>	Date	REQ.NUM
Received by Employers Representative	UIR	18-1-2024	60
		C1 C2 C3 DD MM YY HH MM	
		KP SU OT	24
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+920 TO 202+000	
	E=260168.4582 N=3136445.233	E=260164.6561 N=3136365.3242
Inspection description:		
منسوب (12.5) متر from st (201+920) to st (202+000)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
تم العمل على الحفر والردم في المنطقة المذكورة في المخطط	- you must follow specs and design drawing - you must do leveling and lining - the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	علي محمد	علي محمد				
Contractor QA/QC*	XYZ	علي محمد	20-1-2024	11:15	A	
	H.M.C	علي محمد	20-1-2024	3:45	A	
GARB**						
Employers Representative	Khaled ali	علي محمد	20/1/2024	Amrc		

UNIVERSAL INSPECTION REQUEST



مكتب أ.د. حسن مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR. Hassan Mahdy (H.M.C)
Issued by Contractor	Name: Sign:	Date	18-1-2024
Received by Employers Representative	UIR	C1 KP	C2 SU
		C3 OT	DD MM YY HH MM
			234
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+020 TO 202+060 E=260163.5058 N=3136345.3573	E=260160.9658 N=3136305.4382
Inspection description/ منسوب (12.5-) متر from st (202+020) to st (202+060)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT: xyz)	Comments by: General consultant (systra)
	- you must follow specs and design dw - you must do leveling and lining - the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	ر.م.ح. محمد		21-1-2024	5:15	A	
Contractor QA/QC*	XYZ		21-1-2024	5:00	A	
GARB**						
Employers Representative	Ali		20/1/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name: Sign:	Date	REQ. NUM
Received by Employers Representative	UIR	21-1-2024	62
		C1 C2 C3 DD MM YY HH MM	
		KP SU OT	24

CODE-1

CODE-2

CODE-3

CODE-4

CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+300 TO 202+376	
	E=260139.0278 E=260129.6912	
	N=3136066.4661 N=3135991.0324	
Inspection description(		
منسوب (7.5) متر from st (202+300) to st (202+376) تسليم طبقة ردم منسوب (7.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

	-you must follow specs and design dng -you must do leveling and lining the compacted side slope & filling layer
--	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمود				A-AWC-R	
Contractor QA/QC*	XYZ	عبد الرحمن الابرار	21-1-2024	5:10	A	
	H.M.C	شودا شادي	21-1-2024	5:28	A	
GARB**						
Employers Representative	Khaled ali		21/1/2024		A	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجمية للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name [Signature]	Date	22-1-2024															
Received by Employers Representative	Sign [Signature]	REQ.NUM	63															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>20</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			20		
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT			20													
CODE-1	CODE-2	CODE-3	CODE-4															
CODE-5																		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+920 TO 202+040	
	E=260168.4582 N=3136445.233	E=260162.2757 N=3136325.3952
Inspection description:		
منسوب (12-) متر from st (201+920) to st (202+040)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. (xyz))	Comments by: General consultant (systra)
	-you must follow specs and design dw -you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمد	[Signature]				
Contractor QA/QC*	XYZ	عبد الرحمن الخياط	23-1-2024	9:00	A	
	H.M.C	محمود العبدى	22-1-2024	5:15	AWC	
GARB**						
Employers Representative	Khaled	[Signature]	23/1/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	REQ. NUM							
	وليد محمود	وليد علاف	27-1-2024	65							
Received by Employers Representative			UIR	C1	C2	C3	DD	MM	YY	HH	MM
				KP	SU	OT			23		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+875 To 202+376	201+920 TO 202+060		
	E=260168.4582	E=260160.9658	
	N=3136445.233	N=3136305.4382	
Inspection description/			
من 200+875 إلى 202+376 من st (201+920) إلى st (202+060) طبقة ردم منسوب (-11.5) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))

Comments by: General consultant (systra)




-you must follow specs and design drawing
-you must do leveling and lining the compacted sideslope of filling layer

INSPECTION RESULT

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد علاف	وليد محمود					
Contractor QA/QC*	XYZ	أحمد محمد	27-1-24	5:00	A		
	H.M.C	محمود محمد	27-1-24	4:15	A		
GARB**							
Employers Representative	Khaled ali		27/1/2024				

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	REQ. NUM							
	رئيس محوّر	رئيس ملاف	30-1-2024	66							
Received by Employers Representative			UIR	C1	C2	C3	DD	MM	YY	HH	MM
				KP	SU	OT			24		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED


Area	Element		Item
From 200+876 To 202+376	202+300 TO 202+376		
	E=260139.0278	E=260129.6912	
	N=3136066.4661	N=3135991.0324	
<u>Inspection description:</u> from st (202+300) to st (202+376) تسليم طبقة ردم منسوب (6.5-) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
	-you must follow specs and design drug -you must do leveling and lining the compacted sube slp & filling layer

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد محوّر	وليد ملاف					يتم صيانة القطار في التور
Contractor QA/QC*	XYZ	محمد رافع	30-1-2024	4:00	(A)		
	H.M.C	محمد منتصر فوزي	30-1-24	12:30	AWC		
GARB**							
Employers Representative	Khated ali		30/1/2024				

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



شركة أديس مهدي
للإستشارات الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	وليد محمود	وليد محمود	18-2-2024	68						
Received by Employers Representative	[Stamp]	UIR	C1	C2	C3	DD	MM	YY	HH	MM
			ICP	SU	OT				24	
CODE-3		CODE-2	CODE-3	CODE-4		CODE-5				

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+300 TO 202+376		
	E=260139.0278	E=260129.6912	
	N=3136066.4661	N=3135991.0324	
<u>Inspection description:</u>			
منسوب (6-) متر from st (202+300) to st (202+376)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT - xyz)	Comments by: General consultant (systra)
تم استلام العمل (الطريق) من قبل فريق العمل في 18/2/2024	- you must follow specs and design durg - you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد محمود	وليد محمود					
Contractor QA/QC*	XYZ	عبد الرحمن الزهراني	19-2-2024	11:30	A		
	H.M.C	محمد منعم فوزي	19-2-2024	12:00	A		
GARB**							
Employers Representative	rehaled ale	[Signature]	19/2/2024		Arre		

UNIVERSAL INSPECTION REQUEST



مكتب أديان مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	REQ.NUM							
	وليد محمود	وليد محمود	22-2-2024	69							
Received by Employers Representative	[Signature]	[Signature]	UIR	C1	C2	C3	DD	MM	YY	HH	MM
				KP	SU	OT			24		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+920 TO 202+060		
	E=260168.4582 N=3136445.233	E=260160.9658 N=3136305.4382	
Inspection description/			
منطقة ردم منسوب (10.5-) متر from st (201+920) to st (202+060)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))

مستشار الاستشارات العامة
للمقاولات العامة

Comments by: General consultant (systra)

-you must follow specs and design
-you must do leveling and lining
the compacted side slope & filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود	وليد محمود				
Contractor QA/QC*	XYZ	عبد الرحمن الوائلي	24-2-2024	3:30	A	
	H.M.C	محمد منعم فوزي	24-2-2024	11:00	A	
GARB**						
Employers Representative	Khaled ali	[Signature]	24/2/2024		Amr	

UNIVERSAL INSPECTION REQUEST



مكتب أديسن مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أديسن مهدي للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	و. ليه. م. م. م.		23-3-2024	74						
Received by Employers Representative	UIR		C1	C2	C3	DO	MM	YY	HH	MM
			KP	SU	OT			24		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+920 TO 202+060		
	E=260168.4582 N=3136445.233	E=260160.9658 N=3136305.4382	
Inspection description/			
منطقة ردم منسوب (10- متر) from st (201+920) to st (202+060)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT - xyz)	Comments by: General consultant (systra)
تم اتمام العمل في المنطقة (الطريق) - الخبير الفني - الخبير الفني	- you must follow specs and design drawings - you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	و. ليه. م. م. م.						
Contractor QA/QC*	XYZ	محمد مشهور فوزي	23-3-2024	12:15	A		
	H.M.C	محمد مشهور فوزي	23/3/2024	12:00	A		
GARB**							
Employers Representative	Khaled ali		23/3/2024		Amir		

UNIVERSAL INSPECTION REQUEST



مكتب أ.أ.حسن مهدي
للإستشارات الهندسية



الهيئة العامة للإعانة
SHARER



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name: Sign:	Date	REQ. NUM						
Received by Employers Representative	UIR	31-3-2024	75						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT			24		
CODE -1	CODE -2	CODE -3	CODE -4	CODE -5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+920 TO 202+060 E=260168.4582 N=3136445.233	E=260160.9658 N=3136305.4382
Inspection description منطقة ردم منسوب (9.5-) متر from st (201+920) to st (202+060)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))

Comments by: General consultant (systra)

تم التأكد من أن العمل جاهز للتحقق من قبل المهندس الاستشاري (xyz) في تاريخ 31-3-2024.

-you must follow specs and design data
-you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود محمد					
Contractor QA/QC*	XYZ عبد الرحمن الطرطوسي		1-4-2024	12:00	A	
	H.M.C	محمود علي	31-3-2024	11:00	A	
GARB**						
Employers Representative	Khakdali		1/4/2024		Done	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name:  Sign:  Date: 1-4-2024	REQ.NUM	76															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			24		
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT			24													
CODE-1	CODE-2	CODE-3	CODE-4															
CODE-5																		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description(		
منسوب (3-متر) from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (3-متر)		



INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))	Comments by: General consultant (systra)
	- you must follow specs and design details - you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	أبو عجلة					
Contractor QA/QC*	XYZ		1-4-2024	11:30	A	
	H.M.C		1-4-2024	11:00	A	
GARB**						
Employers Representative	Khaled ali		1/4/2024		AWC	

