



مكتب أدريس مهدي
للإستشارات الهندسية

مقاييس معدلة (١)



الهيئة العامة للإستثمار
General Investment Authority



أعمال إنشاء الجسر الترابي للقطار الكهربائي السريع (أكتوبر / أوسمبل)

القطاع الثاني (بني دار / مظلوط) من محطة ١٧٦+٢٠٠ حتى محطة ٣٣١+٨٠٠ بطول ١٥٨ كم (تعداد ابرق قراقرص)

تأخذ شركة / أبو عجلة للمقاولات العامة والتوريدات العمومية من محطة ٢٠٠+٨٥٠ الي ٢٠٢+٣٥٠ بطول ١,٥ كم

رقم البند	بيان الأعمال	الوحدة	سعر الوحدة	الكمية	الإجمالي
١	أعمال الإنشاء والتطوير				
١-١	باعتار المصنوع أعمال تطوير الموقع من الأبنية والمباني والمنشآت والتي يستخدم لها استخدام التربة ذات الطبيعة الزراعية الكثيفة بمعدل حتى ٢٠ سم وتطهير منها بالمطبخ العمومية نتيجة لأعمال الرقعة المباشرة الكامل حدود المشروع طبقاً للشروط والقرارات والتعليمات الهندسية المشرفة مسافة النقل حتى ٥٠٠ متر ويتم الحساب بخلافه ٢٠٠ جنيه لكل ١ كم زيادة	٢٤	٦,٠٠٠	١	٦,٠٠٠
١-١	بالاعتبار إزالة الأبنية وتحويلها إلى مزارع لا يقل عن ١ متر والعطش لا يقل عن ٣٠ سم وإزالة الحطب والكامل وإزالة خارج الموقع طبقاً لقرارات المهندس المشرف	العدد	٤٠٠,٠٠٠	١,٥٠٠	٦٠٠,٠٠٠,٠٠٠
٢	تكملة الجسر				
٢-٢٢	المطلة في المسطبي				
٢-٢	باعتار المكعب اتصال حفر واستعداد المكدسات الميكانيكية لجميع أنواع التربة عند التربة المدخلة ونسبة المطلة ١:١:١ السوية والريش بالماء الأموية للوصول إلى نسبة الرطوبة المطلوبة والمكعب الجيد بالهريس للوصول إلى نفس كلفة جاده ١٩١٩ من الكلفة الجادة القصوى ومعدل على اليد التحصيل ونقل التربة الزائدة المسافة ١٠٠ متر من محور الطريق ويتم التكلفة طبقاً لمشتريات التصميمية والمطالقات العرضية والمواضع والرسومات التنفيذية المتعددة واليد يصنع مشغلة طبقاً لأصول الصيانة ومواصفات الهيئة العامة للقرى والتعليمات الهندسية المشرفة	٢٤	٢٨,١٠	١	٢٨,١٠
٢-٢٢	المطلة في المسطبي				
٢-٢	باعتار المكعب اتصال حفر واستعداد المكدسات الميكانيكية في التربة المدخلة عند التربة المدخلة (إستعداد المكدسات) ونسبة المطلة ١:١:١ السوية والريش بالماء الأموية والريش بالماء الأموية للوصول إلى نسبة الرطوبة المطلوبة والمكعب الجيد بالهريس للوصول إلى نفس كلفة جاده ١٩١٩ من الكلفة الجادة القصوى ومعدل على اليد التحصيل ونقل التربة الزائدة المسافة ١٠٠ متر من محور الطريق ويتم التكلفة طبقاً لمشتريات التصميمية والمطالقات العرضية والمواضع والرسومات التنفيذية المتعددة واليد يصنع مشغلة طبقاً لأصول الصيانة ومواصفات الهيئة العامة للقرى والتعليمات الهندسية المشرفة	٢٤	٣٢,٨٠	١	٣٢,٨٠
٢-٢٢	المطلة في المسطبي				
٢-٢	باعتار المكعب اتصال حفر واستعداد المكدسات الميكانيكية في التربة المدخلة عند التربة المدخلة (إستعداد المكدسات) ونسبة المطلة ١:١:١ السوية والريش بالماء الأموية والريش بالماء الأموية للوصول إلى نسبة الرطوبة المطلوبة والمكعب الجيد بالهريس للوصول إلى نفس كلفة جاده ١٩١٩ من الكلفة الجادة القصوى ومعدل على اليد التحصيل ونقل التربة الزائدة المسافة ١٠٠ متر من محور الطريق ويتم التكلفة طبقاً لمشتريات التصميمية والمطالقات العرضية والمواضع والرسومات التنفيذية المتعددة واليد يصنع مشغلة طبقاً لأصول الصيانة ومواصفات الهيئة العامة للقرى والتعليمات الهندسية المشرفة	٢٤	٣٦,٩٠	١	٣٦,٩٠
٤-٢	باعتار المكعب اتصال حفر واستعداد المكدسات الميكانيكية في تربة صخرية ومعدل على البند الآتي ١- تحصيل ونقل التربة المسافة لا تقل عن ٥٠٠ متر ٢- إزالة التربة الصخرية باستعداد المكدسات الميكانيكية ٣- توريد تربة مطلة بالمواضع وتنشيطها واستعداد الكلفة السوية يسكن لا يزيد عن ١٥ سم لاستكمال المكدسات المكدسات المكدسات الجيد ٤- الجسر (الكلفة) (نسبة التحصيل ١:١:١) حتى ١٠٠ متر منها بالماء الأموية للوصول إلى نسبة الرطوبة المطلوبة والمكعب الجيد بالهريس للوصول إلى نفس كلفة جاده ١٩١٩ من الكلفة الجادة القصوى ومعدل على اليد التحصيل ونقل التربة الزائدة المسافة ١٠٠ متر من محور الطريق ويتم التكلفة طبقاً لمشتريات التصميمية والمطالقات العرضية والمواضع والرسومات التنفيذية المتعددة واليد يصنع مشغلة طبقاً لأصول الصيانة ومواصفات الهيئة العامة للقرى والتعليمات الهندسية المشرفة	٢٤			
٢-٢٢	المطلة في المسطبي				
١-٤-٢	زاد اجهاد (٢٠٠-٠-٠) (كجم/سم) مسافة نقل حتى ٥٠٠ متر في مارس ٢٠٢٢	٢٤	٨٦,١٠	١	٨٦,١٠
٢-٤-٢	زاد اجهاد (١٠٠-٠-٠) (كجم/سم) مسافة نقل حتى ٥٠٠ متر في مارس ٢٠٢٢	٢٤	١١٥,٧٠	٢,٢١٩	٣٧٢,٤٣٨,٣٠
٣-٤-٢	زاد اجهاد (٢٠٠-٠-٠) (كجم/سم) مسافة نقل حتى ٥٠٠ متر في مارس ٢٠٢٢	٢٤	١٢٣,٦٠	١,٧١٤	٢١١,٨٥٠,٤٠
٤-٤-٢	مطلة زيادة اجهاد ١٠٠ (كجم/سم) في مارس ٢٠٢٢	٢٤	٧,٩٠	١	٧,٩٠
٥-٤-٢	مطلة ١ جنيه لكل ١ كم مسافة النقل المتعددة ٥.٣ - ١.٢ كم	٢٤	٢,٥٠	٤,٩٣٣	١٢,٣٣٢,٥٠
٢-٢٢	المطلة في أبريل				
٦-٤-٢	زاد اجهاد (٢٠٠-٠-٠) (كجم/سم) مسافة نقل حتى ٥٠٠ متر في أبريل ٢٠٢٢	٢٤	٨٦,٣٠	٨٧٤	٧٥,٤٢٦,٢٠
٧-٤-٢	زاد اجهاد (١٠٠-٠-٠) (كجم/سم) مسافة نقل حتى ٥٠٠ متر في أبريل ٢٠٢٢	٢٤	١٠٠,١٠	٨٨٣	٨٨,٣٨٨,٣٠
٨-٤-٢	زاد اجهاد (٢٠٠-٠-٠) (كجم/سم) مسافة نقل حتى ٥٠٠ متر في أبريل ٢٠٢٢	٢٤	١٠٨,٠٠	٦٢٧	١١٧,٧١٦,٠٠
٩-٤-٢	زاد اجهاد (١٠٠-٠-٠) (كجم/سم) مسافة نقل حتى ٥٠٠ متر في أبريل ٢٠٢٢	٢٤	١١٥,٩٠	٤,٩٦٨	٥٧٥,٧٩١,٢٠
١٠-٤-٢	زاد اجهاد (٢٠٠-٠-٠) (كجم/سم) مسافة نقل حتى ٥٠٠ متر في أبريل ٢٠٢٢	٢٤	١٢٣,٨٠	١,٧١٤	٢١٢,١٩٣,٢٠
١١-٤-٢	مطلة زيادة اجهاد ١٠٠ (كجم/سم) في أبريل ٢٠٢٢	٢٤	٧,٩٠	١	٧,٩٠
١٢-٤-٢	مطلة ١ جنيه لكل ١ كم مسافة النقل المتعددة ٥.٣ - ١.٢ كم	٢٤	٢,٥٠	٩,٠٦٦	٢٢,٦٦٥,٠٠



مهندس الهيئة
التوقيع

مدير المشروع (الإستشاري)
التوقيع

مهندس شركة الصفاة
التوقيع



النقل شركة / أو محطة للمقاولات العامة والتوريدات العمومية من محطة ٢٠٠+٨٥٠ إلى ٢٠٢+٣٥٠ بطول ١,٥ كم

مدير عام المشروع
 المهندس / مصطفى سليمان
 (التوقيع)

مدير المشروع (الإستشاري)
 المهندس /
 (التوقيع)

مدير شركة المصفاة
 المهندس /
 (التوقيع)

م.ت 19788

أبو غزالة
 ABUAGLA
 أبو غزالة للتجارة العامة والمزاد العامة
 ب.م 199-161-609

مذكرة

للعرض على السيد المهندس / رئيس قطاع التنفيذ و المناطق

بخصوص: طلب شركة ابو عجيبة للمقاولات العامة اضافة مدة لعملية "انشاء الجسر الترابي لمشروع القطار الكهربائي السريع
من كم 200+850 الى كم 202+350 بطول 1.5 كم (اتجاه ابوقرقاص) .

- استندت الهيئة المشروع عالية الى الشركة المنفذة بالعقد رقم (2024/2023/142) المورخ في 2023/08/3 بقيمة اجمالية قدرها 5700000 جنيها ولمدة (8) شهور .
- بتاريخ 2023/08/10 تم تسليم الموقع للشركة المنفذة ليكون تاريخ النهو طبقا للعقد الاصلى في 2024/04/09.
- وردنا كتاب الشركة المنفذة تطلب فيه اضافة مدة ستة شهور للعملية لوجود بعض المعوقات التي تسببت في تاخر نهو الاعمال (مرفق) .

الرأي

- التفضل بالإحاطة.
- التكرم بالموافقة على اضافة مدة قدرها (6) شهور من تاريخ انتهاء العقد في 2024/04/09 ليصبح تاريخ النهو 2024/10/09 وذلك للمبررات الاتية :-
- 1- بناءا على قرار مجلس الوزراء بجلسته رقم (254) المنعقدة بتاريخ 2023/08/30 .
- 2- بناءا على المذكرة المعروضة على السيد اللواء مهندس رئيس مجلس الادارة بخصوص الموافقة على مد مدة عقود المشروعات (6 أشهر) في ضوء كتاب الوزارة رقم (13793) والمرفق به كتاب دورى السيد اللواء / أمين عام مجلس الوزراء رقم (3-27815) بذات الخصوص (مرفق) .
- 3- تأخر التنفيذ بسبب تحرير سعر الصرف وزيادة تكلفة أسعار المواد الخام وارتفاع اسعار نقلها .
- 4- نقص الدعم الدولارى بالاسواق .
- 5- ارتفاع اسعار قطع الغيار وندرة توافرها بالاسواق .

والأمر مقوض

وتفضلوا سيادتكم بقبول فائق الاحترام

وتفضلوا سيادتكم بقبول فائق الاحترام

تحرير في: 2024/ /



طارق يوسف الجزار

استشاري أبحاث التربة والاماسات :
أ.د.م. هشام محمد حلمي



مشروع :
قطار اسوان الكهربائي السريع - القطاع الثاني

تقرير بنتائج اختبارات صلاحية تربة للتأسيس

مقدمة : تم إعداد هذا التقرير بناءً على طلب شركة / ابو عجيبة

وذلك لتحديد خصائص ومذي صلاحية عينة تراب للاستخدام في / طبقات الردم لجسر القطار الكهربائي

مصدر العينة : عند المحطة / تشويطة بعين المسار 202+220

- الملتصق : وقد تم توريد العينة بمعرفة 1- م/ محمود الحيلي رقم الهاتف = 01030344342

- تنبيه هام : العينة مسنولة من أعضائها

- تاريخ توريد العينة : 2023/11/21

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفلوط)

وقد تم عمل الاختبارات الآتية :

- 1- التخرج الحبيبي
- 2- حد السيولة واللدونة
- 3- اختبار البرونكتور
- 4- اختبار CBR
- 5- اختبار المواد العضوية

وكانت نتائج الاختبارات كالآتي :

م	نوع الاختبار	النتائج	حدود القبول والرفض طبقاً للمواصفات
1	تصنيف العينة	A-1-a	(A-1-a) - (A-1-b) - (A-2-4)
2	نسبة الماء من مغل 200	9.4%	لا تزيد عن (15 %)
3	مجال اللدونة	NP	(A-1-a or A-1-b = 6 max) (A-2-4 = 10 max)
4	أقصى كثافة جافة (البرونكتور) yd max	2.170 gm/cm3	لا تقل عن 1.88 gm/cm3
5	نسبة المياه الأمولية	5.9%	---
6	قيمة CBR المقصورة	49.1%	لا تقل عن 20%
8	المواد العضوية	لا يوجد	لا تزيد عن 1%

= و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للتأسيس عليها



مهندس المصل
التوقيع

قني المصل
التوقيع

Coarse & Fine Aggregate Grading - ASTM C136 & AASHTO T27

202+220	الموقع : تشوين يمين الممرار	25/11/2023	التاريخ :
---------	-----------------------------	------------	-----------

نتائج الاختبار :-

المر %	المحجوز %	وزن المحجوز التراكمي	وزن المحجوز على كل متخل	رقم المتخل (inch)	رقم المتخل (mm)
100%	0%	0	0	5"	127
100.00%	0.00%	0	0	4"	101.6
100.00%	0.00%	0	0	3"	76.2
93.25%	6.75%	790	790	2.5"	63.5
87.67%	12.33%	1443	653	2"	50.8
83.74%	16.26%	1902	459	1.5"	37.5
78.32%	21.68%	2537	635	1"	25
75.21%	24.79%	2900	363	3/4"	19
70.26%	29.74%	3480	580	1/2"	12.7
66.32%	33.68%	3940	460	3/8"	9.5
62.82%	37.18%	4350	410	# 4	4.75
62.82%			7350	المر من متخل # 4	
			11700	وزن العينة الكلي	
			500	وزن عينة القاع	
47.7%	52.3%	120	120	# 10	2.36
25.4%	74.6%	298	178	# 40	0.425
9.4%	90.6%	425	127	# 200	0.075

NP	السيولة و اللدونة
A-1-a	التصنيف

ملاحظات :



م. م. م. م.

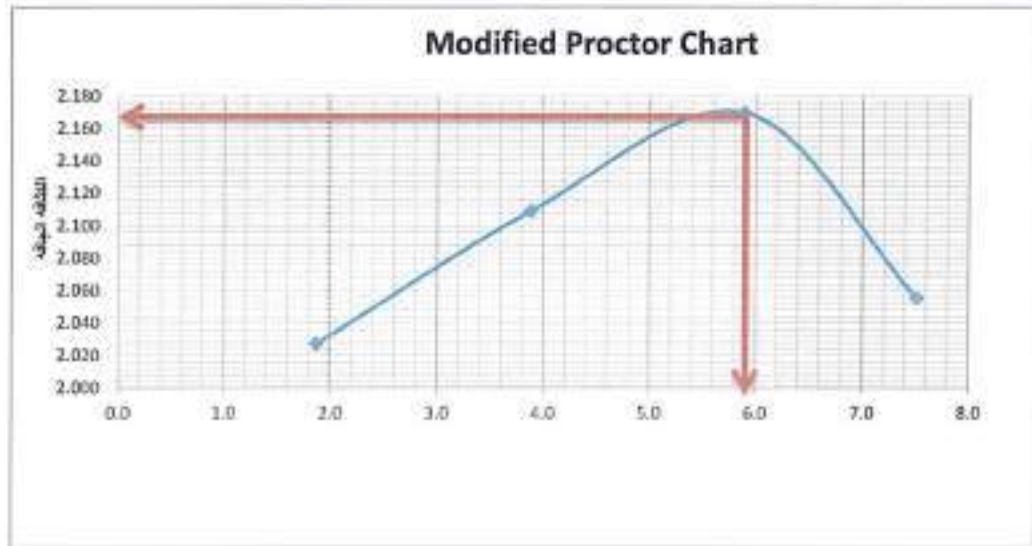
مهندس المعمل
م. م. م. م.
التوقيع

Modified Proctor : ASTM D1557

نوع العينة:		عينة محجر	
تصنيف العينة:		A-1-a	
نتائج الاختبار:			
وزن قالب		5731	
حجم قالب		2140	
الحدس كتلة جافه		2.170	
المياه الاسويه		5.9	

رقم الاختبار	1	2	3	4
وزن القالب + العينة رطبه	10150.0	10420	10648	10460
وزن القالب + العينة جافه	4419.0	4689	4917	4729
الكتلة الرطبه	2.065	2.191	2.298	2.210

رقم الطبقة	1	2	3	4	5	6	7	8
وزن الطبقة	53.9	55.4	54.5	52.7	55.5	55.8	53.2	53.6
وزن الطبقة + العينة رطبه	150.0	150.0	150.0	150.0	150.0	150.0	150.0	150.0
وزن الطبقة + العينة جافه	148	148.5	146	145.8	144.9	144.6	143	143.5
وزن المياه	2.0	1.5	4.0	3.2	5.1	5.4	7.0	6.5
وزن العينة جافه	94.1	93.1	91.5	94.1	89.4	88.8	89.8	89.9
المحتوى المائي %	2.1	1.6	4.4	3.4	5.7	6.1	7.8	7.2
متوسط المحتوى المائي %	1.9		3.9		5.9		7.5	
المتانة الجافه	2.027		2.109		2.170		2.055	



ملاحظات:



مهندس المسجل

التوقيع:

فني المسجل

التوقيع:

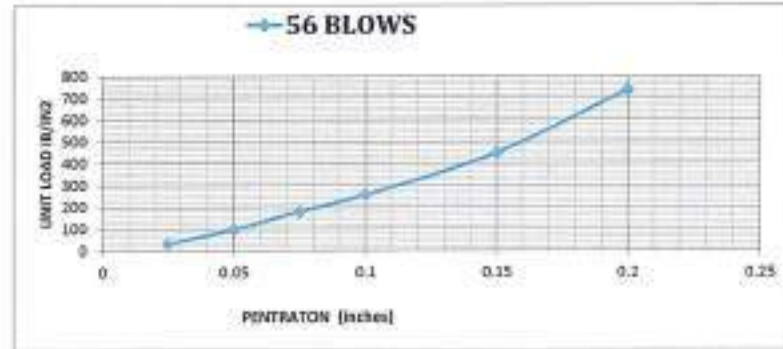
اختبار نسبة تحميل كاليفورنيا (C . B . R) ASTM D1883

A-1-a		تصنيف العينة	
56	عدد الضربات	56	عدد الضربات
10	رقم الجقنة	2131	حجم القالب (سم3)
55.2	وزن الجقنة	5289	وزن القالب (جم)
150	وزن الجقنة +العينة رطبة جم	19120	وزن القالب +وزن العينة رطبة (جم)
144.6	وزن الجقنة +العينة جافة جم	4831	وزن العينة رطبة (جم)
5.2	وزن الماء جم	2.297	كثافة الرطبة (جم/سم3)
89.6	وزن العينة جافة جم	2.143	القيمة كثره جافة (جم/سم3)
5.8%	المحتوى المائي %	2.170	كثافة البروتكتور (جم/سم3)
		95.7%	نسبة الدمك

نسبة الانتفاش	0.20%	غير قابلة للانتفاش
---------------	-------	--------------------

حساب نسبة تحميل كاليفورنيا

7.62	5.08	3.81	2.54	1.9%	1.27	0.635	الاختراق في بالسم
0.3	0.2	0.15	0.1	0.075	0.05	0.025	الاختراق في بال بوصة
1403	1001	610	349	245	132	44	القراءة kg
3092.327	2207.01128	1343.671	769.1576	539.98	291.966	97.32197674	القراءة بالباوند
1031.243	736.004215	448.0936	256.5022	180.075	97.3661	32.45537791	الحمل lb/in2



49.1%	قيمة C . B . R
-------	----------------

ملاحظات : تم حفر القالب في الماء لمدة 96 ساعة خلفا لمواسفة المشروع



مهندس المعمل
د. محمد بن
التوقيع

في المعمل
د. محمد بن
التوقيع

استشاري أبحاث التربة والاساسات :
أ.د.م. هشام محمد حلمي



مشروع :
قطار اسوان الكهربائي السريع - القطاع الثاني

تقرير نتائج اختبارات صلاحية أترية للتأسيس

مقدمة : تم إعداد هذا التقرير بناءا على طلب شركة / ابو عجيبة
وذلك لتحديد خصائص ومدي صلاحية عينة تراب للإستخدام في / طبقات الردم لجسر القطار الكهربائي
مصدر العينة : عند المحطة / تشوينة بعين المسار ٢٠٢+٢٢٠
- المنسوب: وقد تم توريد العينة بمعرفة ١- م/ محمود الحيتي رقم الهاتف = ٠١٠٣٠٣٤٤٣٤٢
- تتبيه هام : العينة مسنولية من أحضرها
- تاريخ توريد العينة : ٢٠٢٣/١٢/٢
اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفوط)

وقد تم عمل الاختبارات الآتية :

- ١- التدرج الحبيبي
- ٢- حد السيولة واللدونة
- ٣- اختبار البرونكتور
- ٤- اختبار CBR
- ٥- اختبار المواد العضوية

وكانت نتائج الاختبارات كالآتي :

م	نوع الاختبار	النتائج	حدود القبول والرفض طبقا للمواصفات
1	تصنيف العينة	A-1-a	(A-1-a) - (A-1-b) - (A-2-4)
2	نسبة الماء من منخل 200	١١.٨%	لا تزيد عن (15 %)
3	مجال اللدونة	NP	(A-1-a or A-1-b = 6 max) (A-2-4 = 10 max)
4	أقصى كثافة جافة (البرونكتور) yd max	2.171 gm/cm3	لا تقل عن 1.88 gm/cm3
5	نسبة العيالة الأمولية	6.1%	--
6	قيمة CBR المغمورة	51.1%	لا تقل عن 20%
8	المواد العضوية	لا يوجد	لا تزيد عن 1%

• و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للتأسيس عليها

مهندس المعمل

التوقيع

فني المعمل

التوقيع



Coarse & Fine Aggregate Grading - ASTM C136 & AASHTO T27

202+220	الموقع : تشوين يمين المسار
---------	----------------------------

12/06/2023	التاريخ :
------------	-----------

نتائج الاختبار :-

رقم المنخل (mm)	رقم المنخل (inch)	وزن المحجوز على كل منخل	وزن المحجوز التراكمي	المحجوز %	المرار %
127	5"	0	0	0%	100%
101.6	4"	0	0	0.00%	100.00%
76.2	3"	0	0	0.00%	100.00%
63.5	2.5"	0	0	0.00%	100.00%
50.8	2"	1425	1425	12.12%	87.88%
37.5	1.5"	475	1900	16.16%	83.84%
25	1"	625	2525	21.47%	78.53%
19	3/4"	475	3000	25.51%	74.49%
12.7	1/2"	485	3485	29.63%	70.37%
9.5	3/8"	475	3960	33.67%	66.33%
4.75	# 4	410	4370	37.16%	62.84%
	المرار من منخل # 4	7390			62.84%
	وزن العينة الكلى	11760			
	وزن عينة التاعم	500			
2.36	# 10	118	118	52.0%	48.0%
0.425	# 40	168	286	73.1%	26.9%
0.075	# 200	120	406	88.2%	11.8%

NP	المسبلة و اللدونة
A-1-a	التصنيف

ملاحظات :



مهندس المعمل

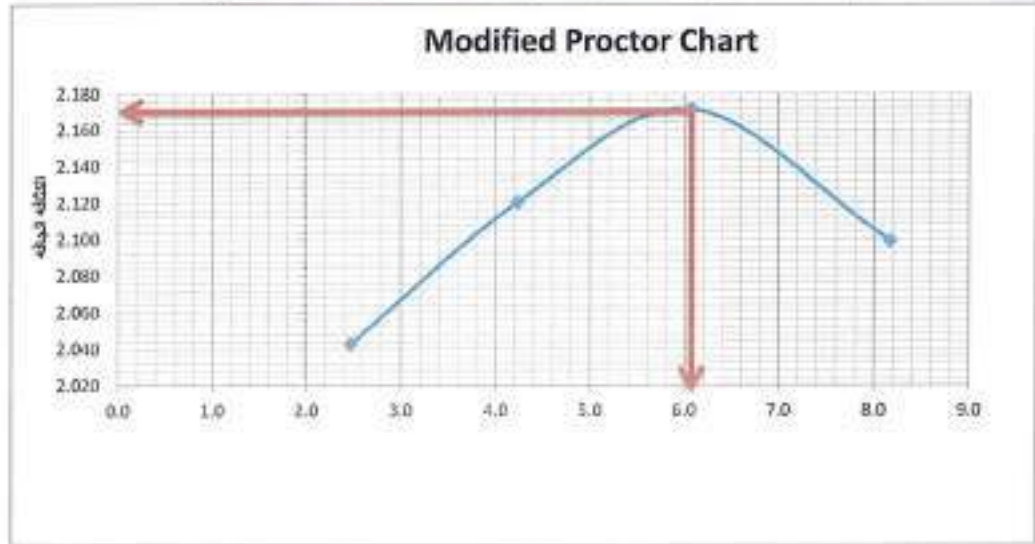
التوقيع

Modified Proctor : ASTM D1557

نوع العينة:	عينة محجر
تصنيف العينة:	A-1-a
نتائج الاختبار:	
وزن قالب	5731
حجم قالب	2140
المنسب 80% جافه	2.171
المياه الاسريه	6.1

رقم الاختبار	1	2	3	4
وزن القالب + العينة رطبه	10210.0	10460	10660	10590
وزن التربه الرطبه	4479.0	4729	4929	4859
الكثافه الرطبه	2.093	2.210	2.303	2.271

رقم المحطه	1	2	3	4	5	6	7	8
وزن الجفنه	53.9	55.4	54.5	52.7	55.5	55.8	53.2	53.8
وزن الجفنه + العينه رطبه	150.0	150.0	150.0	150.0	150.0	150.0	150.0	150.0
وزن الجفنه + العينه جافه	147.5	147.9	145.5	146.7	144.3	144.9	142.5	142.9
وزن المياه	2.5	2.1	4.5	3.3	5.7	5.1	7.5	7.1
وزن العينه جافه	93.6	92.5	91	94	88.8	89.1	89.3	89.3
المحتوى المائى %	2.7	2.3	4.9	3.5	6.4	5.7	8.4	8.0
متوسط المحتوى المائى %	2.5	4.2	6.1	8.2				
الكثافه الجافه	2.043	2.120	2.171	2.099				



ملاحظات:



بشده ****

مهندس المعمل
التوقيع

فنى المعمل
التوقيع

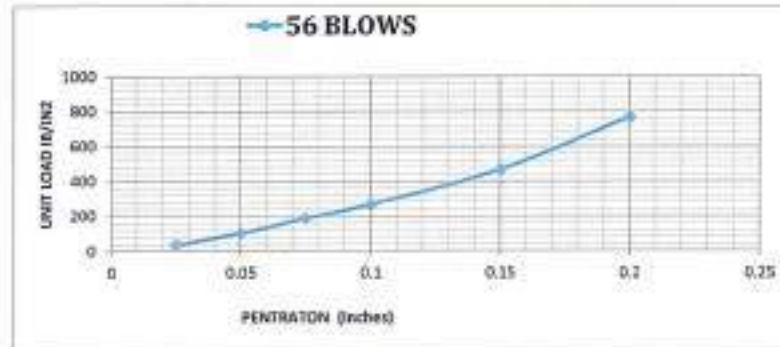
اختبار نسبة تحميل كاليفورنيا (C . B . R) ASTM D1883

A-1-a		تصنيف العينة	
56	عدد الضربات	56	عدد الضربات
30	رقم الجقنة	2131	حجم القلب (سم3)
45.6	وزن الجقنة	5289	وزن القلب (جم)
150	وزن الجقنة + العينة رطبة جم	10115	وزن القلب + وزن العينة رطبة (جم)
144	وزن الجقنة + العينة جافة جم	4826	وزن العينة رطبة (جم)
6	وزن الماء جم	2.265	كثافة الرطبة (جم/سم3)
96.4	وزن العينة جافة جم	2.136	القياس كثافة جافة (جم/سم3)
6.1%	المحتوى المائي %	2.171	كثافة البرونكتور (جم/سم3)
		98.3%	نسبة التشبع

نسبة الانتفاش	0.20%	غير قابلة للانتفاش
---------------	-------	--------------------

حساب نسبة تحمل كاليفورنيا

7.62	5.08	3.81	2.54	1.95	1.27	0.635	الاختراق بالملم
0.3	0.2	0.15	0.1	0.075	0.05	0.025	الاختراق بالثبوصه
1460	1042	635	363	255	138	46	القراءة kg
3218.545	2297.09337	1398.515	800.5517	562.02	303.883	101.2943023	القراءة بالباوند
1073.335	766.045203	466.3831	266.9717	187.425	101.34	33.78008721	الحمل lb/in2



51.1%	قيمة C . B . R
-------	----------------

ملاحظات: تم غمر القلب في الماء لمدة 96 ساعة طبقاً لمواصفة المشروع



مهندس شمس
م. شمس
توقيع

المسجل
الم. شمس
توقيع

تقرير بنتائج إختبارات صلاحية أترية للتأسيس

مقدمة : تم إعداد هذا التقرير بناءا علي طلب شركة / ابو عجيبة

وذلك لتحديد خصائص ومذي صلاحية عينة تراب للإستخدام في / طبقات الردم لجسر القطار الكهربائي

مصدر العينة : عند المحطة / تشوينة يمين المسار 202+220

المنسوب: وقد تم توريد العينة بمعرفة 1- م/ محمود الحيني رقم الهاتف =01030344342

تنبيه هام : العينة مسنولة من أحضرها

تاريخ توريد العينة : 2023/12/21

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بنى مزار - منفلووط)

وقد تم عمل الإختبارات الآتية :

- 1-التدرج الحبيبي
- 2-حد السيولة واللدونة
- 3-إختبار البروكتور
- 4-إختبار CBR
- 5-إختبار المواد العضوية

وكانت نتائج الاختبارات كالآتي :

م	نوع الإختبار	النتائج	حدود القبول والرفض طبقا للمواصفات
1	تصنيف العينة	A-1-a	(A-1-a) - (A-1-b) - (A-2-4)
2	نسبة المار من ملخل 200	9.4%	لا تزيد عن (15 %)
3	مجال اللدونة	NP	(A-1-a or A-1-b = 6 max) (A-2-4 = 10 max)
4	أقصى كثافة جافة (البروكتور) γ_d max	2.171 gm/cm3	لا تقل عن 1.88 gm/cm3
5	نسبة المياه الأصولية	6.3%	--
6	قيمة CBR المغمورة	49.1%	لا تقل عن 20%
8	المواد العضوية	لا يوجد	لا تزيد عن 1%

• و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للتأسيس عليها



مهندس المعمل
م/أ
التوقيع

فني المعمل
أ/أ
التوقيع

Coarse & Fine Aggregate Grading - ASTM C136 & AASHTO T27

202+220	الموقع : تشوين يمين المسار	25/12/2023	التاريخ :
---------	----------------------------	------------	-----------

لنتائج الاختبار :-

المر %	المحجوز %	وزن المحجوز التراكمي	وزن المحجوز على كل منخل	رقم المنخل (inch)	رقم المنخل (mm)
100%	0%	0	0	5"	127
100.00%	0.00%	0	0	4"	101.6
89.34%	10.66%	1135	1135	3"	76.2
79.44%	20.56%	2190	1055	2.5"	63.5
78.97%	21.03%	2240	50	2"	50.8
74.55%	25.45%	2710	470	1.5"	37.5
71.64%	28.36%	3020	310	1"	25
68.45%	31.55%	3360	340	3/4"	19
64.51%	35.49%	3780	420	1/2"	12.7
56.06%	43.94%	4680	900	3/8"	9.5
47.65%	52.35%	5575	895	# 4	4.75
47.65%			5075	المر من منخل # 4	
			10650	وزن العينة الكلية	
			500	وزن عينة الناعم	
40.5%	59.5%	75	75	# 10	2.36
19.3%	80.7%	298	223	# 40	0.425
9.4%	90.6%	401	103	# 200	0.075

NP	السيولة و اللدونة
A-1-a	التصنيف

ملاحظات :



مهندس

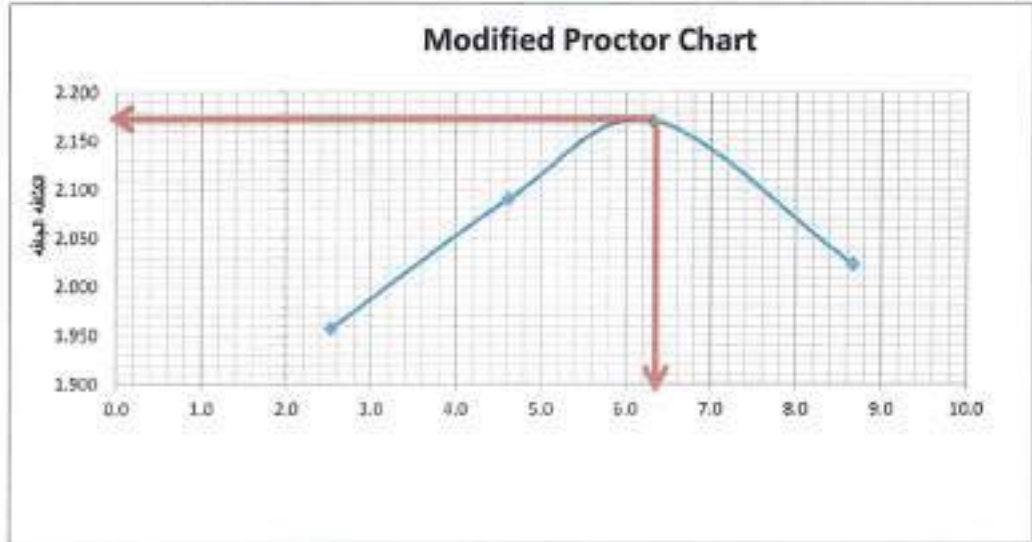
مهندس المعمول
التوقيع

Modified Proctor : ASTM D1557

نوع العينة:	عينة محضر
تصنيف العينة:	A-1-a
نتائج الاختبار:-	
وزن القالب	5731
حجم القالب	2140
القيمة القصوى جافه	2.171
المياه الاسويه	6.3

رقم الاختبار	1	2	3	4
وزن القالب + العينة رطبه	10025.0	10410	10670	10436
وزن القالب الرطبه	4294.0	4679	4939	4705
الكثافه الرطبه	2.007	2.186	2.308	2.199

رقم الجبله	1	2	3	4	5	6	7	8
وزن الجبله	53.9	55.4	54.5	52.7	55.5	55.8	53.2	53.6
وزن الجبله + العينة رطبه	150.0	150.0	150.0	150.0	150.0	150.0	150.0	150.0
وزن الجبله + العينة جافه	147.3	148	145.6	145.9	144.8	144	142.8	142
وزن المياه	2.7	2.0	4.4	4.1	5.2	8.0	7.4	8.0
وزن الجبله جافه	93.4	92.6	91.1	93.2	89.3	88.2	89.4	88.4
المستوى المائي %	2.9	2.2	4.8	4.4	5.8	8.8	8.3	9.0
متوسط المستوى المائي %	2.5	4.6	6.3	8.7				
الكثافه الجافه	1.957	2.090	2.171	2.023				



ملاحظات:



مختبر

مهندس المعمل
توقيع

فني المعمل
التوقيع

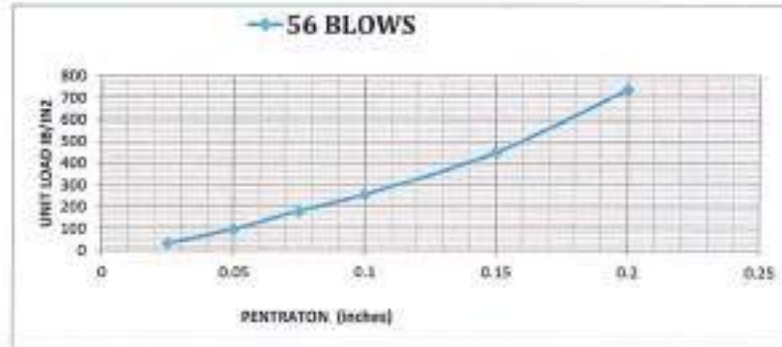
اختبار نسبة تحميل كاليفورنيا (C . B . R) ASTM D1883

A-1-a		تصنيف العينة	
66	عدد الضربات	66	عدد الضربات
f	رقم البقعة	2131	حجم القالب (سم ³)
33.7	وزن البقعة	6269	وزن القالب (جم)
150	وزن البقعة + العينة رطبة جم	10136	وزن القالب + وزن العينة رطبة (جم)
143.1	وزن البقعة + العينة جافة جم	4847	وزن العينة رطبة (جم)
6.9	وزن الماء جم	2.275	الكثافة الرطبة (جم/سم ³)
109.4	وزن العينة جافة جم	2.140	الكتلة جافة (جم/سم ³)
6.3%	المحتوى المائي %	2.171	كثافة البرونكتور (جم/سم ³)
		98.6%	نسبة الدمك

نسبة الإنفلات	0.20%	غير قابلة للإنفلات
---------------	-------	--------------------

حساب نسبة تحمل كاليفورنيا

7.62	5.08	3.81	2.54	1.95	1.27	0.635	الأختران بالملم
0.3	0.2	0.15	0.1	0.075	0.05	0.025	الأختران بالانوصه
1403	1001	610	349	245	132	44	التراند kg
3092.327	2207.01128	1343.671	769.1576	539.98	291.966	97.32197674	التراند بالانوانه
1031.243	736.004215	448.0936	256.5022	180.075	97.3661	32.45537791	المسل IB/IN2



49.1%	قيمة " C . B . R "
-------	--------------------

ملاحظات : تم اختبار القالب في الماء لمدة 96 ساعة طبقا لوصفية المشروع



مهندس العمل
التوقيع

لمشي العمل
التوقيع



التاريخ : 2024-9-22

اسم المشروع : مشروع القطار الكهربائي السريع قطاع (أكتوبر - أبو سمبل)
الموضوع : اعتماد الهيئة العامة للطرق والكبارى لطلبات استلام الأعمال الخاصة بالمشروع
الشركة المنفذة : ابوعجيلة للمقاولات العامة والتوريدات العمومية في المسافة
من (200+876) الى (202+376) بطول 1.5 كم.

عقد رقم : - (2023-2022-1968) بتاريخ 2023-5-17

- (2023-2023-142) بتاريخ 2023-8-3

- (2023-2023-143) بتاريخ 2023-8-3

- (2023-2023-499) بتاريخ 2023-10-12

- (2023-2023-1021) بتاريخ 2024-1-18

- (2023-2023-1229) بتاريخ 2024-2-26

- (2024-2024-209) بتاريخ 2024-8-21

تم الإطلاع ظاهريا على طلبات الفحص الخاصة بالمشروع المذكور عاليه والمرفقة بمستخلصات
المذكورة عالية لعدد (77) طلبات فحص وذلك بعد مراجعتها وتوقيعها من استشارى المساحة (XYZ)
واستشارى ضبط الجودة (مكتب أ.د حسن مهدي) وعليه تم اعتمادها

وتنقسم الى :

- (53) طلبات فحص لأعمال الردم .
- (14) طلبات فحص لأعمال الحفر .
- (4) طلبات فحص لأعمال التطهير .

عن الاستشاري (أ.د حسن مهدي)
مشاريع القطار السريع

مهندس الاستشاري
أ.د حسن مهدي

يعتمد،،،

مهندس الهيئة العامة للطرق والكبارى

مهندس الهيئة العامة للطرق والكبارى

جدول توزيع اجهادات الصخر للقطاع من ٢٠٠+٨٧٦ الى ٢٠١+٦٤٠
تنفيذ شركة ابو عجيله للمقاولات العامة القطاع من المحطة ٢٠٠+٨٧٦ كم الي المحطة ٢٠٢+٨٧٦ كم

حتى تاريخ ٢٠٢٢/١١/١٤

الاجهاده بالمقاييس ٢٠٠+٨٧٦ (كجم / سم ^٢)	الاجهاده بالمقاييس ٢٠١+٦٤٠ (كجم / سم ^٢)	الاجهاده بالمقاييس ٢٠٢+٨٧٦ (كجم / سم ^٢)	الاجهاده بالمقاييس ٢٠٣+١٠٠٠ (كجم / سم ^٢)	الاجهاده بالمقاييس ٢٠٤+١٢٠٠ (كجم / سم ^٢)	الاجهاده بالمقاييس ٢٠٥+١٤٠٠ (كجم / سم ^٢)	المسبوق (م)	الاجهاده (كجم / سم ^٢)	المحطة	مبنة
0.00			0.00			89.12	590.0	200+876.01	1
2,451.68			2,451.68			89.08	560.0	200+880.00	2
9,893.34			9,893.34			88.88	600.0	200+900.00	3
9,701.29	9,701.29					88.67	250.0	200+920.00	4
9,197.66			9,197.66			88.46	500.0	200+940.00	5
8,834.38				8,834.38		88.26	630.0	200+960.00	6
9,215.85		9,215.85				88.05	400.0	200+980.00	7
9,804.14		9,804.14				87.85	390.0	201+000.00	8
9,977.50				9,977.50		87.64	610.0	201+020.00	9
10,398.13			10,398.13			87.43	550.0	201+040.00	10
10,812.59			10,812.59			87.23	500.0	201+060.00	11
10,695.49			10,695.49			87.02	570.0	201+080.00	12
10,067.13	10,067.13					86.82	267.0	201+100.00	13
10,011.24				10,011.24		86.61	620.0	201+120.00	14
9,758.73			9,758.73			85.76	500.0	201+140.00	15
10,318.80			10,318.80			85.55	450.0	201+160.00	16
11,130.49			11,130.49			85.35	440.0	201+180.00	17
11,103.67	11,103.67					85.14	260.0	201+200.00	18
11,234.40		11,234.40				84.93	390.0	201+220.00	19
10,299.42				10,299.42		84.73	650.0	201+240.00	20
8,039.35				8,039.35		84.52	630.0	201+260.00	21

الشركة المنفذة

محمد قنبح

١٩٧٨

عن الاستشاري ا.د حسن مهدي
مدير المشروع
م/محمود غريب
المكتب الفني
م/أحمد عزب





يهتمد ٤٤٤
مهندس الهيئة العامة للطرق والكبارى

عن الاستشاري ا.د حسن مهدي
مدير المشروع
م/محمود عريب
المكتب الفني
م/احمد عريب

الشركة المتفردة
حمداً فتيماً

فريق / محمد فتوح

1979年





جدول توزيع اجهادات الصخر للقطاع من ٢٠٠+٨٧٦ الى ٢٠١+٦٤٠
تنفيذ شركة ابو عجيله للمقاولات العامة القطاع من المحطة ٢٠٠+٨٧٦ الى المحطة ٢٠٢+٨٧٦ كم

حتى تاريخ ٢٠٢٣/٨/٢٤

الاجهادات بالمقاييسه ٢٠٠٠-٢٠٠٠ (كجم / سم)	الاجهادات بالمقاييسه ٤٠٠٠-٢٠٠٠ (كجم / سم)	الاجهادات بالمقاييسه ٨٠٠٠-٤٠٠٠ (كجم / سم)	الاجهادات بالمقاييسه ٦٠٠٠-٤٠٠٠ (كجم / سم)	الاجهادات بالمقاييسه ٧٠٠٠-٦٠٠٠ (كجم / سم)	المشوب (م)	الاجهات (كجم / سم)	المحطة	متر
0.00			0.00		89.12	590.0	200+876.01	1
2,382.75			2,382.75		89.08	560.0	200+880.00	2
9,672.89			9,672.89		88.88	600.0	200+900.00	3
9,397.29	9,397.29				88.67	250.0	200+920.00	4
8,828.23			8,828.23		88.46	500.0	200+940.00	5
8,622.69				8,622.69	88.26	630.0	200+960.00	6
9,056.30	9,056.30				88.05	400.0	200+980.00	7
9,633.59	9,633.59				87.85	390.0	201+000.00	8
9,816.77				9,816.77	87.64	610.0	201+020.00	9
10,161.19			10,161.19		87.43	550.0	201+040.00	10
10,316.01			10,316.01		87.23	500.0	201+060.00	11
10,106.96			10,106.96		87.02	570.0	201+080.00	12
9,326.54	9,326.54				86.82	267.0	201+100.00	13
9,085.07				9,085.07	86.61	620.0	201+120.00	14
8,723.87			8,723.87		85.76	500.0	201+140.00	15
9,427.85		9,427.85			85.55	450.0	201+160.00	16
10,627.76		10,627.76			85.35	440.0	201+180.00	17
10,619.76	10,619.76				85.14	260.0	201+200.00	18
10,688.55	10,688.55				84.93	390.0	201+220.00	19
9,805.55				9,805.55	84.73	650.0	201+240.00	20
7,513.81				7,513.81	84.52	630.0	201+260.00	21

عن الاستشاري أد حسن مهدي

مدير المشروع

م/محمود عريب

المكتب الفني

م/أحمد عريب

الشركة المنفذة

حمد فتوح

بيع/





جدول توزيع اجهادات الصخر للقطاع من ٢٠٠+٨٧٦ إلى ٢٠١+٦٤٠
تنفيذ شركة ابوعجيلة للمقاولات العامة القطاع من المحطة ٢٠٠+٨٧٦ كم إلى المحطة ٢٠٢+٨٧٦ كم

حتى تاريخ ٢٠٢٢/٨/٢٤

مرتبة	المحطة	الاجهاد (كجم / سم ²)	المسبوب (م)	الاجهاد بالمقاييسه ٧٠٠-٦٠٠ (كجم / سم ²)	الاجهاد بالمقاييسه ٦٠٠-٥٠٠ (كجم / سم ²)	الاجهاد بالمقاييسه ٥٠٠-٤٠٠ (كجم / سم ²)	الاجهاد بالمقاييسه ٤٠٠-٣٠٠ (كجم / سم ²)	الاجهاد بالمقاييسه ٣٠٠-٢٠٠ (كجم / سم ²)	الإجمالي
22	201+280.00	510.0	84.32	6,493.55					6,493.55
23	201+300.00	550.0	84.11	8,857.74					8,857.74
24	201+320.00	600.0	83.90	7,644.47					7,644.47
25	201+340.00	640.0	83.70	7,805.04					7,805.04
26	201+360.00	590.0	83.49	7,599.15					7,599.15
27	201+380.00	520.0	83.28	7,628.19					7,628.19
28	201+400.00	500.0	83.08	7,945.26					7,945.26
29	201+420.00	570.0	82.87	8,261.94					8,261.94
30	201+440.00	510.0	83.27	8,539.07					8,539.07
31	201+460.00	550.0	83.07	11,153.78					11,153.78
32	201+480.00	490.0	82.86		9,333.44				9,333.44
33	201+500.00	280.0	82.65					7,785.49	7,785.49
34	201+520.00	350.0	82.45				7,419.14		7,419.14
35	201+540.00	570.0	82.24	7,686.87					7,686.87
36	201+560.00	460.0	82.03		7,940.71				7,940.71
37	201+580.00	500.0	81.83		8,284.23				8,284.23
38	201+600.00	500.0	81.62		8,304.76				8,304.76
39	201+620.00	580.0	81.42	8,030.34					8,030.34
40	201+640.00	540.0	81.21	3,942.38					3,942.38
اجمالي الكمية (م ³)				52,648.93	153,974.64	53,918.75	36,797.58	37,129.08	334,468.98
الكمية المتفاد من شهر يوليو حتى شهر أغسطس				11,888.32	30,183.91	19,517.48	8,336.98	8,958.92	78,885.62
المتفاد في يوليو ٢٠٢٢				5,944.16	15,091.95	9,758.74	4,168.49	4,479.46	39,442.81
المتفاد في أغسطس ٢٠٢٢				5,944.16	15,091.95	9,758.74	4,168.49	4,479.46	39,442.81

يعتمد !!!
مهندس الهيئة العامة للطرق والكباري

عن الاستشاري أ.د حسن مهدي
مدير المشروع
م/محمود شريب
المكتب الفني
م/أحمد عزب
م/

الشركة المنفذة
حمد فتيح
فريق /





جدول توزيع اجهادات الصخر للقطاع من ٢٠٠٠+٨٧٦ الى ٢٠٠٦+٦٤٠
تنفيذ شركة ابو عجيله للمقاولات العامة للقطاع من المحطة ٢٠٠٠+٨٧٦ كم الي المحطة ٢٠٠٢+٨٧٦ كم

حتى asbuilt بتاريخ ٢٠٢٢/٦/١٣

الاجمالي	الاجهات بالمقاييس ٢٠٠٠-١٠٠٠ (كجم / سم ³)	الاجهات بالمقاييس ٢٠٠٠-١٠٠٠ (كجم / سم ³)	الاجهات بالمقاييس ٢٠٠٠-١٠٠٠ (كجم / سم ³)	الاجهات بالمقاييس ٢٠٠٠-١٠٠٠ (كجم / سم ³)	الاجهات بالمقاييس ٢٠٠٠-١٠٠٠ (كجم / سم ³)	المستوي (م)	الاجهات (كجم / سم ³)	المحطة	العمق
0.00				0.00		89.12	590.0	200+876.01	1
112.38				112.38		89.08	560.0	200+880.00	2
2,663.76				2,663.76		88.88	600.0	200+900.00	3
1,435.54	1,435.54					88.67	250.0	200+920.00	4
1,064.63				1,064.63		88.46	500.0	200+940.00	5
1,920.04					1,920.04	88.26	630.0	200+960.00	6
2,125.51		2,125.51				88.05	400.0	200+980.00	7
1,834.39		1,834.39				87.85	390.0	201+000.00	8
1,879.09					1,879.09	87.64	610.0	201+020.00	9
2,578.06				2,578.06		87.43	550.0	201+040.00	10
3,143.58				3,143.58		87.23	500.0	201+060.00	11
2,954.06				2,954.06		87.02	570.0	201+080.00	12
2,223.81	2,223.81					86.82	267.0	201+100.00	13
2,473.07					2,473.07	86.61	620.0	201+120.00	14
1,698.26				1,698.26		85.76	500.0	201+140.00	15
1,254.30			1,254.30			85.55	450.0	201+160.00	16
1,565.36			1,565.36			85.35	440.0	201+180.00	17
1,349.70	1,349.70					85.14	260.0	201+200.00	18
1,103.95		1,103.95				84.93	390.0	201+220.00	19
1,023.98					1,023.98	84.73	650.0	201+240.00	20
783.13					783.13	84.52	630.0	201+260.00	21

عن الاستشاري ا.د حسن مهدي
مدير المشروع
م/محمود غريب

المكتب الفني
م/احمد عرب

عن الشركة المنفذة
م/احمد فتح
التوقيع





جدول توزيع اجهادات الصخر للقطاع من ٢٠٠+٨٧٦ إلى ٢٠١+٦٤٠
تنفيذ شركة ايوغلا للمقاولات العامة القطاع من المحطة ٢٠٠+٨٧٦ كم إلى المحطة ٢٠٢+٨٧٦ كم

حتى التكلفة بتاريخ ٢٠٢٢/٦/١٢

القيمة	المنطقة	الاجهات (كجم / سم ^٢)	المسبوق (م)	الاجهات بالمقاييس ٢٠٠٠-٦٠٠٠ (كجم / سم ^٢)	الاجهات بالمقاييس ٦٠٠٠-١٠٠٠٠ (كجم / سم ^٢)	الاجهات بالمقاييس ١٠٠٠٠-٢٠٠٠٠ (كجم / سم ^٢)	الاجهات بالمقاييس ٢٠٠٠٠-٢٠٠٠٠٠ (كجم / سم ^٢)	الإجمالي
22	201+280.00	510.0	84.32		626.38			626.38
23	201+300.00	550.0	84.11		729.41			729.41
24	201+320.00	600.0	83.90		1,458.37			1,458.37
25	201+340.00	640.0	83.70	2,205.69				2,205.69
26	201+360.00	590.0	83.49		2,709.16			2,709.16
27	201+380.00	520.0	83.28		3,092.92			3,092.92
28	201+400.00	500.0	83.08		2,936.12			2,936.12
29	201+420.00	570.0	82.87		2,322.45			2,322.45
30	201+440.00	510.0	83.27		773.02			773.02
31	201+460.00	550.0	83.07		236.87			236.87
32	201+480.00	490.0	82.86		236.87			236.87
33	201+500.00	280.0	82.65				236.87	236.87
34	201+520.00	350.0	82.45				236.87	236.87
35	201+540.00	570.0	82.24		236.87			236.87
36	201+560.00	460.0	82.03		236.87			236.87
37	201+580.00	500.0	81.83		236.87			236.87
38	201+600.00	500.0	81.62		236.87			236.87
39	201+620.00	580.0	81.42		236.87			236.87
40	201+640.00	540.0	81.21		236.87			236.87
اجمالي الكمية (م ^٣)								
	المنفذ في يناير ٢٠٢٢	1,714.17	4,968.34	627.85	883.45	874.32	5,245.92	54,408.78
	المنفذ في فبراير ٢٠٢٢	1,714.17	4,968.34	627.85	883.45	874.32	5,245.92	9,068.13
	المنفذ في مارس ٢٠٢٢	1,714.17	4,968.34	627.85	883.45	874.32	5,245.92	9,068.13
	المنفذ في ابريل ٢٠٢٢	1,714.17	4,968.34	627.85	883.45	874.32	5,245.92	9,068.13
	المنفذ في مايو ٢٠٢٢	1,714.17	4,968.34	627.85	883.45	874.32	5,245.92	9,068.13
	المنفذ في يونيو ٢٠٢٢	1,714.17	4,968.34	627.85	883.45	874.32	5,245.92	9,068.13

يعتمد !!!
مهندس الهيئة العامة للطرق والكباري

المكتب الفني
م/أحمد عزب
م/أحمد عزب
م/أحمد عزب
م/أحمد عزب

عن الشركة المنفذة
م/أحمد فتوح
التوقيع





جدول توزيع اجهادات الصخر للقطاع من ٨٧٦+٢٠٠ الي ٦٤٠+٢٠١
تنفيذ شركة ابوعجيلة للمقاولات العامة القطاع من المحطة ٨٧٦+٢٠٠ كم الي المحطة ٨٧٦+٢٠٢ كم

حتى asbuilt بتاريخ ٢٠٢٣/١/٣

الاجمالي	الاجمالي بالعملة (كجم / سم)	الاجمالي بالعملة (كجم / سم)	الاجمالي بالعملة (كجم / سم)	الاجمالي بالعملة (كجم / سم)	الاجمالي بالعملة (كجم / سم)	المتوسط (م)	الاجمالي (كجم / سم)	المحطة	هيك
0.00				0.00		89.12	590.0	200+876.01	1
2,184.54				2,184.54		89.08	560.0	200+880.00	2
6,343.73				6,343.73		88.88	600.0	200+900.00	3
6,968.18	6,968.18					88.67	250.0	200+920.00	4
6,513.96				6,513.96		88.46	500.0	200+940.00	5
5,620.74					5,620.74	88.26	630.0	200+960.00	6
5,904.97		5,904.97				88.05	400.0	200+980.00	7
6,487.94		6,487.94				87.85	390.0	201+000.00	8
6,468.92					6,468.92	87.64	610.0	201+020.00	9
6,183.40				6,183.40		87.43	550.0	201+040.00	10
5,642.90				5,642.90		87.23	500.0	201+060.00	11
5,417.11				5,417.11		87.02	570.0	201+080.00	12
5,413.19	5,413.19					86.82	267.0	201+100.00	13
4,925.54					4,925.54	86.61	620.0	201+120.00	14
5,300.81				5,300.81		85.76	500.0	201+140.00	15
5,929.39			5,929.39			85.55	450.0	201+160.00	16
6,154.93			6,154.93			85.35	440.0	201+180.00	17
6,044.32	6,044.32					85.14	260.0	201+200.00	18
6,073.37		6,073.37				84.93	390.0	201+220.00	19
5,341.24					5,341.24	84.73	650.0	201+240.00	20
3,477.38					3,477.38	84.52	630.0	201+260.00	21

الشركة المنفصلة

عن الاستشاري أ.د حسن مهدي

مدير المشروع

المكتب الطبي

م/محمود حميد

م/أحمد عزب

19788 ت.ج.م





جدول توزيع اجهادات الصخر للقطاع من ٨٧٦+٢٠٠ الى ٦٤٠+٢٠١
تنفيذ شركة ابروجيلا للمقاولات العامة القطاع من المحطة ٨٧٦+٢٠٠ كم الى المحطة ٨٧٦+٢٠٢ كم

حتى asbuilt بتاريخ ٢٠٢٢/١/٢

محطة	المحطة	الاجمالي (كجم / سم ٢)	المتوسط (م)	الاجمالي بالمقاييس (كجم / سم ٢)	الاجمالي بالمقاييس (كجم / سم ٢)	الاجمالي بالمقاييس (كجم / سم ٢)	الاجمالي بالمقاييس (كجم / سم ٢)	الاجمالي
22	201+280.00	510.0	84.32	2,510.82				2,510.82
23	201+300.00	550.0	84.11	5,380.56				5,380.56
24	201+320.00	600.0	83.90	4,293.43				4,293.43
25	201+340.00	640.0	83.70	4,641.79				4,641.79
26	201+360.00	590.0	83.49	4,380.66				4,380.66
27	201+380.00	520.0	83.28	3,951.10				3,951.10
28	201+400.00	500.0	83.08	3,792.97				3,792.97
29	201+420.00	570.0	82.87	5,054.19				5,054.19
30	201+440.00	510.0	83.27	7,939.23				7,939.23
31	201+460.00	550.0	83.07	8,491.55				8,491.55
32	201+480.00	490.0	82.86	5,674.33		5,674.33		5,674.33
33	201+500.00	280.0	82.65	4,498.55	4,498.55			4,498.55
34	201+520.00	350.0	82.45	4,693.60	4,693.60			4,693.60
35	201+540.00	570.0	82.24	4,346.00				4,346.00
36	201+560.00	460.0	82.03	4,378.58	4,378.58			4,378.58
37	201+580.00	500.0	81.83	4,401.76	4,401.76			4,401.76
38	201+600.00	500.0	81.62	4,095.15	4,095.15			4,095.15
39	201+620.00	580.0	81.42	4,076.95				4,076.95
40	201+640.00	540.0	81.21	2,176.80				2,176.80
	اجمالي الكمية (م)			30,475.61	93,980.71	30,634.14	23,159.88	22,924.24
								201,174.58

يعتمد !!!
مهندس الهيئة العامة للطرق والكباري

عن الاستشاري لاد حسن مهدي
المكتب الفني
م/احمد عزب
م/محمود غريب
مدير المشروع

الشركة المنفذة
احمد فتوح
وقفا





مركز الاستشارات الهندسية
Engineering Consultation Center

معمل الخرسانة
Concrete plant



رؤية الكلية : تسعى الكلية إلى أن تكون مؤسسة تعليمية وبحثية عالية الجودة متميزة بتقديم خدمات مجتمعية لتنمية البيئة وتعويضها

نتائج اختبارات عينات من مكعبات الحجر		
خاص بعملية : القطار السريع (أكتوبر - أسوان) القطاع الثاني بطول ١٥٨ كم المسافة من ١٧٦ + ٨٠٠ : ٢٣٤ + ٨٠٠		
مقاول : شركة أبو عجيلة للمقاولات - القطاع ٨٥٠ + ٢٠٠ : ٢٥٠ + ٢٠٢ بطول ١,٥ كم		
توريد : ٨٣٦٨٨٨٦٤١٥	بتاريخ : ٢٣ / ٥ / ٢٠٢٣	رقم القيد : ١

نتائج الاختبارات

القطاع من ٢٠١ + ٦٤٠ : ٢٠١ + ٤٤٠

م	الأبعاد / سم	المحطة	منسوب	حمل الكسر / طن	إجهاد الكسر / كجم/سم ^٢
١	١٠ × ١٠ × ١٠	٢٠١ + ٤٤٠	٨٣,٢٧١	٥١	٥١٠
٢	١٠ × ١٠ × ١٠	٢٠١ + ٤٦٠	٨٣,٠٦٥	٥٥	٥٥٠
٣	١٠ × ١٠ × ١٠	٢٠١ + ٤٨٠	٨٢,٨٥٨	٤٩	٤٩٠
٤	١٠ × ١٠ × ١٠	٢٠١ + ٥٠٠	٨٢,٦٥٢	٢٨	٢٨٠
٥	١٠ × ١٠ × ١٠	٢٠١ + ٥٢٠	٨٢,٤٤٦	٣٥	٣٥٠
٦	١٠ × ١٠ × ١٠	٢٠١ + ٥٤٠	٨٢,٢٤	٥٧	٥٧٠
٧	١٠ × ١٠ × ١٠	٢٠١ + ٥٦٠	٨٢,٠٣٤	٤٦	٤٦٠
٨	١٠ × ١٠ × ١٠	٢٠١ + ٥٨٠	٨١,٨٢٨	٥٠	٥٠٠
٩	١٠ × ١٠ × ١٠	٢٠١ + ٦٠٠	٨١,٦٢٢	٥٠	٥٠٠
١٠	١٠ × ١٠ × ١٠	٢٠١ + ٦٢٠	٨١,٤١٥	٥٨	٥٨٠
١١	١٠ × ١٠ × ١٠	٢٠١ + ٦٤٠	٨١,٢٠٩	٥٤	٥٤٠

* تم توريد العينات بمعرفة م / محمود الحيني دون أدنى مسئولية على المعمل

يعتمد ،
الرأي الاستشاري على مسئولية اللجنة
مركز الاستشارات الهندسية



المشرف على المعمل

أ. د. / أسامة

التوقيع :

فنى المعمل

أ. د. / أسامة

التوقيع :

التوقيع :

رسالة الكلية : تتلزم كلية الهندسة جامعة المنيا بتقديم برامج تعليمية وفقاً للمعايير القومية لإعداد خريج متميز وقادر على المنافسة في أسواق العمل محلياً وإقليمياً وعالمياً، كما تتلزم بالتشجيع والتطوير في البحث العلمي بما يخدم البيئة والتطور التكنولوجي .



مركز الاستشارات الهندسية
Engineering Consultation Center

معمل الخرسانة
Concrete plant



رؤية الكلية : تسعى الكلية إلى أن تكون مؤسسة تعليمية وبحثية عالية الجودة متميزة بتقديم خدمات مجتمعية لتنمية البيئة وتعميرها

نتائج اختبارات عينات من مكعبات الحجر		
خاص بعملية : القطار السريع (أكتوبر - أسوان) القطاع الثاني بطول ١٥٨ كم المسافة من ٨٠٠ + ١٧٦ : ٨٠٠ + ٣٣٤		
مقاول : شركة أبو عجيلة للمقاولات - القطاع ٨٥٠ + ٢٠٠ : ٢٠٢ + ٣٥٠ بطول ١,٥ كم		
توريد : ٨٣٦٨٨٨٦٤١٥	بتاريخ : ٢٣ / ٥ / ٢٠٢٣	رقم القيد : ٢

نتائج الاختبارات

القطاع من ٨٧٦ + ٢٠٠ : ١٢٠ + ٢٠١

م	الأبعاد / سم	المحطة	منسوب	حمل الكسر / طن	إجهاد الكسر / كجم/سم ^٢
١	١٠ × ١٠ × ١٠	٢٠٠ + ٨٧٦,٠١	٨٩,١٢٤	٥٩	٥٩٠
٢	١٠ × ١٠ × ١٠	٢٠٠ + ٨٨٠	٨٩,٠٨٣	٥٦	٥٦٠
٣	١٠ × ١٠ × ١٠	٢٠٠ + ٩٠٠	٨٨,٨٧٧	٦٠	٦٠٠
٤	١٠ × ١٠ × ١٠	٢٠٠ + ٩٢٠	٨٨,٦٧	٢٥	٢٥٠
٥	١٠ × ١٠ × ١٠	٢٠٠ + ٩٤٠	٨٨,٤٦٤	٥٠	٥٠٠
٦	١٠ × ١٠ × ١٠	٢٠٠ + ٩٦٠	٨٨,٢٥٨	٦٣	٦٣٠
٧	١٠ × ١٠ × ١٠	٢٠٠ + ٩٨٠	٨٨,٠٥٢	٤٠	٤٠٠
٨	١٠ × ١٠ × ١٠	٢٠١ + ٠٠٠	٨٧,٨٤٦	٣٩	٣٩٠
٩	١٠ × ١٠ × ١٠	٢٠١ + ٠٢٠	٨٧,٦٤	٦١	٦١٠
١٠	١٠ × ١٠ × ١٠	٢٠١ + ٠٤٠	٨٧,٤٣٤	٥٥	٥٥٠
١١	١٠ × ١٠ × ١٠	٢٠١ + ٠٦٠	٨٧,٢٢٧	٥٠	٥٠٠
١٢	١٠ × ١٠ × ١٠	٢٠١ + ٠٨٠	٨٧,٠٢١	٥٧	٥٧٠
١٣	١٠ × ١٠ × ١٠	٢٠١ + ١٠٠	٨٦,٨١٥	٦٠	٢٦٧
١٤	١٠ × ١٠ × ١٠	٢٠١ + ١٢٠	٨٦,٦٠٩	٦٢	٦٢٠

* تم توريد العينات بمعرفة م / محمود الحيني دون أدنى مسئولية علي المعمل

المشرف على المعمل
أ. د. / السيد محمد
التوقيع :
مركز الاستشارات الهندسية

فني المعمل
/ السيد محمد
التوقيع :

رسالة الكلية : تتلزم كلية الهندسة جامعة المنيا بتقديم برامج تعليمية وفقاً للمعايير القومية لإعداد خريج متميز وقادر على المنافسة في اسواق العمل محلياً وإقليمياً وعالمياً، كما تتلزم بالتشجيع والتطوير في البحث العلمي بما يخدم البيئة والتطور التكنولوجي .



مركز الاستشارات الهندسية
Engineering Consultation Center

معمل الخرسانة
Concrete plant



رؤية الكلية : تسعى الكلية إلى أن تكون مؤسسة تعليمية وبحثة عالية الجودة متميزة بتقديم خدمات مجتمعية لتنمية البيئة وتعميرها

نتائج اختبارات عينات من مكعبات الحجر		
خاص بعملية : القطار السريع (أكتوبر - أسوان) القطاع الثاني بطول ١٥٨ كم المسافة من ٨٠٠ + ١٧٦ : ٨٠٠ + ٣٣٤		
مقاوله : شركة أبو عجيلة للمقاولات - القطاع ٨٥٠ + ٢٠٠ : ٢٠٢ + ٣٥٠ بطول ١,٥ كم		
توريد : ٨٢٤٩١١٤٩٨٤	بتاريخ : ٢٧ / ٤ / ٢٠٢٣	رقم القيد : ١

نتائج الاختبارات

القطاع من ١٤٠ + ٢٠٠ : ٢٠١ + ٤٢٠

م	الأبعاد / سم	المحطة	متسوب	حمل الكسر / طن	إجهاد الكسر / كجم/سم ^٢
١	١٠ × ١٠ × ١٠	٢٠١ + ١٤٠	٨٥,٧٥٨	٥٠	٥٠٠
٢	١٠ × ١٠ × ١٠	٢٠١ + ١٦٠	٨٥,٥٥٢	٤٥	٤٥٠
٣	١٠ × ١٠ × ١٠	٢٠١ + ١٨٠	٨٥,٣٥٤	٤٤	٤٤٠
٤	١٠ × ١٠ × ١٠	٢٠١ + ٢٠٠	٨٥,١٣٩	٢٦	٢٦٠
٥	١٠ × ١٠ × ١٠	٢٠١ + ٢٢٠	٨٤,٩٣٣	٢٩	٢٩٠
٦	١٠ × ١٠ × ١٠	٢٠١ + ٢٤٠	٨٤,٧٢٧	٦٥	٦٥٠
٧	١٠ × ١٠ × ١٠	٢٠١ + ٢٦٠	٨٤,٥٢١	٦٣	٦٣٠
٨	١٠ × ١٠ × ١٠	٢٠١ + ٢٨٠	٨٤,٣١٥	٥١	٥١٠
٩	١٠ × ١٠ × ١٠	٢٠١ + ٣٠٠	٨٤,١٠٩	٥٥	٥٥٠
١٠	١٠ × ١٠ × ١٠	٢٠١ + ٣٢٠	٨٣,٩٠٢	٦٠	٦٠٠
١١	١٠ × ١٠ × ١٠	٢٠١ + ٣٤٠	٨٣,٦٩٦	٦٤	٦٤٠
١٢	١٠ × ١٠ × ١٠	٢٠١ + ٣٦٠	٨٣,٤٩٠	٥٩	٥٩٠
١٣	١٠ × ١٠ × ١٠	٢٠١ + ٣٨٠	٨٣,٢٨٢	٥٢	٥٢٠
١٤	١٠ × ١٠ × ١٠	٢٠١ + ٤٠٠	٨٣,٠٧٨	٥٠	٥٠٠
١٥	١٠ × ١٠ × ١٠	٢٠١ + ٤٢٠	٨٢,٨٧٢	٥٧	٥٧٠

* تم توريد العينات بمعرفه م / محمود الحيني دون أدنى مسئولية على المعمل

يعتمد ،
الرأي الاستشاري على مسئولية اللجنة
مركز الاستشارات الهندسية

المشرف على المعمل

أ. د. / محمد /

التوقيع : محمد /

فنى المعمل

أ. د. / محمد /

التوقيع : محمد /

رسالة الكلية : تلتزم كلية الهندسة جامعه المنيا بتقديم برامج تعليمية وفقاً للمعايير القومية لإعداد خريج متميز وقادر على المنافسة في اسواق العمل محلياً وإقليمياً وعالمياً، كما تلتزم بالتشجيع والتطوير في البحث العلمي بما يخدم البيئة والتطور التكنولوجي.

اتجاه ابوقرقاص

من المحطة ٨٥٠+٢٠٠ الى المحطة ٣٥٠+٢٠٢ بطول ١,٥ كم رقم العقد (٢٠٢٤/٢٠٢٣/١٤٢)

أعمال الجسر الترابي لمسار القطر الكهربائي السريع الخط الثاني (الفيوم / بني سويف - أبوسمبل) القطاع الثاني (بني مزار / منفلوط)

البرنامج الزمني

تاريخ استلام الموقع ٢٠٢٣/٨/١٠

مدة تنفيذ العملية ٨ شهور

تاريخ نهو الاعمال ٢٠٢٤/٤/٩

رقم البند	بيان الاعمال	الوحدة	الكمية	أغسطس-٢٠٢٣	سبتمبر-٢٠٢٣	أكتوبر-٢٠٢٣	نوفمبر-٢٠٢٣	ديسمبر-٢٠٢٣	يناير-٢٠٢٤	فبراير-٢٠٢٤	مارس-٢٠٢٤	أبريل-٢٠٢٤
١	أعمال التطهير											
٢-١	بالعدد إزالة اشجار و نخيل بأرتفاع لا يقل عن ٤ متر و القطر لا يقل عن ٣٠ سم و إزالة الجنور بالكامل و نقلها خارج الموقع طبقا لتعليمات المهندس المشرف	بالعدد	١٥٠٠		٥٠٠,٠٠	٥٠٠,٠٠	٥٠٠,٠٠					
٢	أعمال الحفر											
٥-٢	المتر المكعب أعمال حفر باستخدام المعدات الميكانيكية في السفو و تسوية السطح بألات التسوية والرش بالمياه الاصلوية للوصول إلى نسبة الرطوبة المطلوبة والدمك الجيد بالهراسات للوصول إلى أقصى كثافة جافة (95 % من الكثافة الجافة القصوى) ومحمل على البند تحميل ونقل الأتربة الزائدة لمسافة ١,٥ كم من محور الطريق مع نقطية ناتج الحفر بالمقلب بطبقة آتربة بسمك متوسط ٢٠ سم و القبة تشمل استخدام المياه في تثبيت السفو و اعداد مدقات على السفو لحركة المعدات و و يتم التنفيذ طبقاً للمناسيب التصميمية والقطاعات العرضية النموذجية والرسومات التفصيلية المعتمدة والبند بجميع مشتملاته طبقاً لأصول الصناعة ومواصفات الهيئة العامة للطرق والكباري وتعليمات المهندس المشرف .	م³										
١٠-٥-٢	نفس البند رقم ٥-٢ في شهر يوليو ٢٠٢٣	م³	١٠٠٠٠		٢,٥٠٠,٠٠	٢,٥٠٠,٠٠	٢,٥٠٠,٠٠	٢,٥٠٠,٠٠				
٢٠-٥-٢	نفس البند رقم ٥-٢ في شهر اغسطس ٢٠٢٣	م³	١٠٠٠٠		٢,٥٠٠,٠٠	٢,٥٠٠,٠٠	٢,٥٠٠,٠٠	٢,٥٠٠,٠٠				
٤-٢	بالمتر المكعب اعمال حفر بالمعدات الميكانيكية في تربة صخرية ومحمل على البند الات ١- تحميل ونقل ناتج الحفر لمسافة لا تقل عن ٥٠٠ متر ٢- ازالة الميول الجانبية باستخدام المعدات الميكانيكية ٣- توريد تربة مطابقة للمواصفات وتشغيلها باستخدام الات التسوية بسمك لا يزيد عن ٢٥ سم لاستكمال المنسوب التصميمي لتشكيل الجسر والاكتاف (نسبة تحمل كاليفورنيا لا تقل عن ١٠ %) ورشها بالمياه الاصلوية للوصول إلى نسبة الرطوبة المطلوبة والدمك الجيد بالهراسات للوصول إلى أقصى كثافة جافة (95% من الكثافة الجافة القصوى). ويتم التنفيذ طبقاً للمناسيب التصميمية والقطاعات العرضية النموذجية والرسومات التفصيلية المعتمدة والبند بجميع مشتملاته طبقاً لأصول الصناعة ومواصفات الهيئة العامة للطرق والكباري وتعليمات المهندس المشرف.	م³										
	المنفذ في شهر مارس ٢٠٢٣											
٢-٤-٢	ذات اجهاد (٦٠٠-٥٠٠) كجم/سم² لمسافة نقل حتي ٥٠٠ متر في مارس ٢٠٢٣ .	م³	٣٢١٩		١,٠٧٣,٠٠	١,٠٧٣,٠٠	١,٠٧٣,٠٠					
٣-٤-٢	ذات اجهاد (٧٠٠-٦٠٠) كجم/سم² لمسافة نقل حتي ٥٠٠ متر في مارس ٢٠٢٣ .	م³	١٧١٤		٥٧١,٣٣	٥٧١,٣٣	٥٧١,٣٣					

مهندس الشركة المنفذة

م/ احمد فتحي

التوقيع / أحمد فتحي

عن الاستشاري أ.د حسن مهدي

م/ محمود غريب

التوقيع

م/ احمد عزب

التوقيع

يعتمد؟؟؟

مهندس الهيئة العامة للطرق والكباري

اتجاه ابوقرقاص

من المحطة ٨٥٠+٢٠٠ الى المحطة ٢٠٢+٣٥٠ بطول ١,٥ كم رقم العقد (٢٠٢٤/٢٠٢٣/١٤٢)

أعمال الجسر الترابي لمسار القطر الكهربائي السريع الخط الثاني (الفيوم / بني سويف - أبوسمبل) القطاع الثاني (بني مزار / منفلوط)

البرنامج الزمني

تاريخ نهو الاعمال ٢٠٢٤/٤/٩

مدة تنفيذ العملية ٨ شهور

تاريخ استلام الموقع ٢٠٢٣/٨/١٠

رقم البيد	بيان الاعمال	الوحدة	الكمية	أغسطس-٢٠٢٣	سبتمبر-٢٠٢٣	أكتوبر-٢٠٢٣	نوفمبر-٢٠٢٣	ديسمبر-٢٠٢٣	يناير-٢٠٢٤	فبراير-٢٠٢٤	مارس-٢٠٢٤	أبريل-٢٠٢٤
	المنفذ في ابريل ٢٠٢٣											
٦-٤-٢	ذات اجهاد (٢٠٠-٢٠٠) كجم/سم ^٢ لمسافة نقل حتي ٥٠٠ متر في ابريل ٢٠٢٣	م ^٣	٨٧٤			٢٩١,٣٣	٢٩١,٣٣	٢٩١,٣٣				
٧-٤-٢	ذات اجهاد (٤٠٠-٢٠٠) كجم/سم ^٢ لمسافة نقل حتي ٥٠٠ متر في ابريل ٢٠٢٣	م ^٣	٨٨٣			٢٩٤,٣٣	٢٩٤,٣٣	٢٩٤,٣٣				
٨-٤-٢	ذات اجهاد (٥٠٠-٤٠٠) كجم/سم ^٢ لمسافة نقل حتي ٥٠٠ متر في ابريل ٢٠٢٣	م ^٣	٦٢٧			٢٠٩,٠٠	٢٠٩,٠٠	٢٠٩,٠٠				
٩-٤-٢	ذات اجهاد (٦٠٠-٥٠٠) كجم/سم ^٢ لمسافة نقل حتي ٥٠٠ متر في ابريل ٢٠٢٣	م ^٣	٤٩٦٨			١,٦٥٦,٠٠	١,٦٥٦,٠٠	١,٦٥٦,٠٠				
١٠-٤-٢	ذات اجهاد (٧٠٠-٦٠٠) كجم/سم ^٢ لمسافة نقل حتي ٥٠٠ متر في ابريل ٢٠٢٣	م ^٣	١٧١٤			٥٧١,٣٣	٥٧١,٣٣	٥٧١,٣٣				
	المنفذ في مايو ٢٠٢٣											
١٣-٤-٢	ذات اجهاد (٢٠٠-٢٠٠) كجم/سم ^٢ لمسافة نقل حتي ٥٠٠ متر في مايو ٢٠٢٣	م ^٣	٨٧٤			٢٩١,٣٣	٢٩١,٣٣	٢٩١,٣٣				
١٤-٤-٢	ذات اجهاد (٤٠٠-٢٠٠) كجم/سم ^٢ لمسافة نقل حتي ٥٠٠ متر في مايو ٢٠٢٣	م ^٣	٨٨٣			٢٩٤,٣٣	٢٩٤,٣٣	٢٩٤,٣٣				
١٥-٤-٢	ذات اجهاد (٥٠٠-٤٠٠) كجم/سم ^٢ لمسافة نقل حتي ٥٠٠ متر في مايو ٢٠٢٣	م ^٣	٦٢٧			٢٠٩,٠٠	٢٠٩,٠٠	٢٠٩,٠٠				
١٦-٤-٢	ذات اجهاد (٦٠٠-٥٠٠) كجم/سم ^٢ لمسافة نقل حتي ٥٠٠ متر في مايو ٢٠٢٣	م ^٣	٤٩٦٨			١,٦٥٦,٠٠	١,٦٥٦,٠٠	١,٦٥٦,٠٠				
١٧-٤-٢	ذات اجهاد (٧٠٠-٦٠٠) كجم/سم ^٢ لمسافة نقل حتي ٥٠٠ متر في مايو ٢٠٢٣	م ^٣	١٧١٤			٥٧١,٣٣	٥٧١,٣٣	٥٧١,٣٣				
	المنفذ في يونيو ٢٠٢٣											
٢٠-٤-٢	ذات اجهاد (٢٠٠-٢٠٠) كجم/سم ^٢ لمسافة نقل حتي ٥٠٠ متر في يونيو ٢٠٢٣	م ^٣	٨٧٤			٢٩١,٣٣	٢٩١,٣٣	٢٩١,٣٣				
٢١-٤-٢	ذات اجهاد (٤٠٠-٢٠٠) كجم/سم ^٢ لمسافة نقل حتي ٥٠٠ متر في يونيو ٢٠٢٣	م ^٣	٨٨٣			٢٩٤,٣٣	٢٩٤,٣٣	٢٩٤,٣٣				
٢٢-٤-٢	ذات اجهاد (٥٠٠-٤٠٠) كجم/سم ^٢ لمسافة نقل حتي ٥٠٠ متر في يونيو ٢٠٢٣	م ^٣	٦٢٧			٢٠٩,٠٠	٢٠٩,٠٠	٢٠٩,٠٠				
٢٣-٤-٢	ذات اجهاد (٦٠٠-٥٠٠) كجم/سم ^٢ لمسافة نقل حتي ٥٠٠ متر في يونيو ٢٠٢٣	م ^٣	٤٩٦٨			١,٦٥٦,٠٠	١,٦٥٦,٠٠	١,٦٥٦,٠٠				
٢٤-٤-٢	ذات اجهاد (٧٠٠-٦٠٠) كجم/سم ^٢ لمسافة نقل حتي ٥٠٠ متر في يونيو ٢٠٢٣	م ^٣	١٧١٤			٥٧١,٣٣	٥٧١,٣٣	٥٧١,٣٣				
	المنفذ في يوليو ٢٠٢٣											
٢٧-٤-٢	ذات اجهاد (٢٠٠-٢٠٠) كجم/سم ^٢ لمسافة نقل حتي ٥٠٠ متر في يوليو ٢٠٢٣	م ^٣	٤٤٧٩			١,٤٩٣,٠٠	١,٤٩٣,٠٠	١,٤٩٣,٠٠				
٢٨-٤-٢	ذات اجهاد (٤٠٠-٢٠٠) كجم/سم ^٢ لمسافة نقل حتي ٥٠٠ متر في يوليو ٢٠٢٣	م ^٣	١٢٧١			٤٢٣,٦٧	٤٢٣,٦٧	٤٢٣,٦٧				

عن الاستشاري أ.د حسن مهدي

م/ احمد عزب

م/ محمود غريب

التوقيع

مهندس الشركة المنفذة

م/ احمد فتحي

التوقيع

يعتمد

مهندس الهيئة العامة للطرق والكباري





الهيئة العامة
للطرق والكباري
مملكة البحرين



هيكل تنظيمي للعاملين بمشروع القطار السريع شركة أبو عجيله للمقاولات العامة

التاريخ : ٢٠٢٢-٩-٢٤

اسم المشروع : مشروع القطار السريع (أكتوبر-أبوسمبل)

رقم العقد: (٢٠٢٤/٢٠٢٢/١٤٢)

مستسل	الاسم	الوظيفة	عدد سنوات الخبرة	رقم التليفون
1	محمد حامد يحي	مدير المشروع	10	01009742637
2	احمد احمد محمود	مدير المكتب الفني	5	01017199596
3	نادي عادل	مدير ضبط الجودة	5	01019930593
4	ربيع توحيد	مدير السلامة الوقائية	10	01114562154
5	وليد محمود محمد	مهندس التنفيذ	5	01090254469
6	محمد عماد الدين محمد	مهندس صيانة (ميكانيكا وكهرباء)	5	01559856322
7	احمد قاسم	مهندس التخطيط والبرمجة الزمنية	5	01223691236
8	احمد السيد احمد	مراقب تنفيذ (فني مواد)	5	01002612002
	محمد نادي			01063768307
9	عبدالعال رجب	حساب كميات	5	01029734478
10	حسين محمد جبريل	مساح	7	01064950832
	محمد جمال		7	01033806848
11	محمد ابو غنيمه	فني سلامة مرورية	5	01092355765
	محمد حسين		5	01022245866

يعتمد
مهندس الهيئة العامة للطرق والكباري

عن الاستشاري ا.د حسن مهدي
م/ احمد عزب
م/ محمود فريب
التوقيع /
9/٢٤

التوقيع /



مهندس الشركة المنفذة
أ. م. محمد

مهندس الشركة المنفذة
وليد محمد محمد

أحمد هادي

مجلس الشركة المنفصلة

محضر استلام موقع

مشروع إنشاء خط القطار الكهربائي السريع (أكتوبر - أبو سمبل) من الكم 200+850 حتى الكم 202+350 بطول 1.5 كم
تنفيذ شركة أبو عجيبة للمقاولات العامة والتوريدات العمومية.

انه في يوم الاثنين الموافق 26 / 8 / 2024 وبناء على عقد العملية رقم 209 / 2024 / 2025

اجتمعت اللجنة المشكلة من السادة الاتي اسماؤهم بعد وهم :-

عن الهيئة العامة للطرق والكباري (طرف اول)

مدير عام المشروعات
مهندس الإشراف بالمنطقة السادسة
مدير المشروع
ممثل الاستشاري (مكتب أ.د/حسن مهدي)
استشاري المساحة (XYZ)

- 1- السيد المهندس / مصطفى شعبان البدري
 - 2- السيد المهندس / محمود حسين
 - 3- السيد المهندس / محمود غريب
 - 4- السيد المهندس / احمد عزب
 - 5- السيد المهندس / محمد عبدالرحمن
- عن الشركة المنفذة (طرف ثاني)


مهندس عن الشركة المنفذة


- 1- السيد المهندس / احمد قتيح


وقد قامت اللجنة بالانتقال علي الطبيعة للموقع عالية بالمعاينة الظاهرية علي المطبوعة قام الطرف الاول بتسليم الطرف الثاني الموقع خاليا من العوائق الظاهرية ولا مانع من استلام الموقع والبدء في الاعمال ويعتبر تاريخ 26 / 8 / 2024 هو تاريخ استلام الموقع .

وقفل المحضر علي ذلك .

اللجنة من الهيئة (طرف اول)

5- 

4- 

3- 

2- 

1- 

مشروع القطار السريع
الهيئة العامة للطرق والكباري
بني سويف

الشركة المنفذة (طرف ثاني)

1- 

19788 م ت

ABUAGLA

بني سويف 199-161-009

رئيس الإدارة المركزية للمنطقة
السادسة بني سويف
مهندس / طارق الجزار

محضر معاينة مسافة نقل توريد تربة صالحة من محجر (أبو هشيمة)

مشروع القطار السريع (6 أكتوبر / أبو سمبل)
القطاع الثاني بطول 158 كم من 176+700 كم الى 334+800
تنفيذ شركة : أبو عجيلة للمقاولات العامة بطول 1.5 كم
من كم 200+876 الى كم 202+376

بالإشارة الى التكاليف الصادر من الهيئة العامة للطرق والكباري لصالح شركة أبو عجيلة
للمقاولات العامة و التوريدات العمومية بشأن تنفيذ الجسر الترابي والأعمال الصناعية
بمشروع القطار الكهربائي السريع (أكتوبر - أسوان) في المسافة الكيلومترية 200+876
الى العلامة الكيلومترية 202+ 376

بناءً على تعليمات السيد المهندس / رئيس قطاع التنفيذ والمناطق بالتوريد من محاجر
خارجية مرخصة بصفة مؤقتة لحين اعتماد وترخيص محاجر اخرى اقرب للقطاع

فقد اجتمعت اللجنة يوم الاثنين الموافق 2023/8/28 قامت اللجنة المشكلة من :-

- (1) السيد المهندس / محمد السيد شعبان
(2) السيد المهندس / حاتم مهران
(3) السيد المهندس / محمد عبدالرحمن سالم
(4) السيد المهندس / محمد حامد أبو عجيلة
- مهندس الاشراف بالهيئة
مدير المشروع
مهندس المكتب الاستشاري (X,Y,Z)
مدير المشروع شركة أبو عجيلة للمقاولات المتكاملة والتوريدات
- وقامت اللجنة بالذهاب الى مكان محجر (أبو هشيمة) حيث وجد ان المسافة من القطاع (من محطة 200+876 حتى
202+376) حتى مكان المحجر (49 كم) وذلك بسبب تعذر وجود محجر قريب على ان يتم التوريد بعد عمل اختبارات
الصلاحية اللازمة والتأكد من صلاحية مواد المحجر للتوريد .

Easting	Northing	Longitude (E)	Latitude (N)	Station	الشركة	من
260126.0446	3137487.7094	30° 33' 10.74 "	28° 20' 30.11 "	200+876	أبو عجيلة	البداية
260129.6907	3135991.0284	30° 33' 11.98 "	28° 19' 41.52 "	202+376	أبو عجيلة	النهاية
270048.623	3178136.045	30° 38' 45.6 "	28° 42' 36.3 "	-	محجر	أبو هشيمة

-هذا المحضر اعتماد مؤقت لحين اعتماد محجر بجوار القطاع ، ولا يعد إثبات لتوريد أية كميات من المحجر المذكور ، ويجب
على إستشاري ضبط الجودة متابعة وحصر أي كميات يتم توريدها من المحجر المذكور ومتابعة صلاحية المحجر بصفة دورية
مستمرة ومقارنتها بصلاحية المواد المثبوتة لتوريدها على القطاع .

واقفل المحضر على ذلك ؟؟؟

مدير المشروع
د.م/حاتم مهران

استشاري المساحة (X,Y,Z)
م/محمد عبدالرحمن سالم

عن الشركة المنفذة

م/محمد حامد أبو عجيلة

يعتمد...
مهندس الهيئة العامة للطرق والكباري





مكتب أ.د/حسن مهدي
للإستشارات الهندسية

SYSTRA



مشروع القطار السريع (6 أكتوبر / أبو سمبل)
القطاع الثاني بطول 158 كم من 176+700 كم الى 334+800
تنفيذ شركة : أبو عجيبة للمقاولات العامة بطول 1.5 كم
من كم 200+876 الى كم 202+376

محضر إجمال

اسم الشركة : أبو عجيبة للمقاولات العامة والتوريدات العمومية

القطاع: (201+920) الى (202+376)

أنه في يوم الثلاثاء الموافق 26 / 9 / 2023 قامت اللجنة المكونة من السادة :-

- 1- السيد المهندس/ حاتم مهران
مدير المشروع
- 2- السيد المهندس/ محمود عبدالرحيم الحينى
مكتب أ.د / حسن مهدي
- 3- السيد المهندس/ محمد حامد أبو عجيبة
شركة أبو عجيبة للمقاولات العامة

قامت اللجنة بالمعاينة الظاهرية وأخذ عينات وإجراء اختبارات صلاحية للقطاع
من (201+920) احداثي (260168.4582E, 3136445.233N) الى (202+376) احداثي
(260129.6912E, 3135991.0324N) وطبقاً لنتيجة العينة المرفقة تبين أن التربة غير صالحة

للتأسيس (سفو) ويلزم إزالتها وذلك حسب توصيات استشاري التربة وتوصيات سيفكون جروب .

ملحوظات : ...
التوقيع : ...
التوقيعات :-

لجنة
مجلس
مجلس

عن مكتب أ.د حسن مهدي
مدير المشروع
م. محمود عثمان
م. محمد عثمان
م. محمد عثمان

عن الشركة المنفذة
م. محمد عثمان
م. محمد عثمان
م. محمد عثمان

استشاري أبحاث التربة والاساسات :
أ.د.م. هشام محمد حلمي



مشروع :
قطار اسوان الكهربائي السريع - القطاع الثاني

تقرير بنتائج اختبارات صلاحية اترية للتأسيس

مقدمة : تم إعداد هذا التقرير بناءا على طلب شركة / ابو عجيله

وذلك لتحديد خصائص ومدي صلاحية عينة تراب للإستخدام في / طبقات الردم لجسر القطار الكهربائي

مصدر العينة : عند المحطة / 202+280 عينة ارض طبيعيه

المنذوبين : وقد تم توريد العينة بمعرفة م/ محمود الحيني . بتاريخ : 2023/8/21

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفلوط)

التوصيف الظاهري للعينة : كتبان رملية ناعسة (سفو)

- تنبيه العينة مستولية من احضرها

وقد تم عمل الاختبارات الآتية :

- 1-التدرج الحبيبي
- 2-حد السيولة واللدونة
- 3-اختبار البروكتور
- 4-اختبار CBR
- 5-اختبار المواد العضوية

وكانت نتائج الاختبارات كالآتي :

م	نوع الاختبار	النتائج
1	تصنيف العينة	A-3
2	نسبة العار من منخل 200	2.6 %
3	مجال اللدونة	عديمة اللدونة
4	أقصى كثافة جافة (البروكتور) $\gamma_d \max$	1.871 gm/cm3
5	نسبة للماء الأمولية	9.7%
6	قيمة CBR المغمورة	8.4%
8	المواد العضوية	لا يوجد

• و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي غير صالحة للتأسيس عليها



احمد حبيب
مهندس

مهندس المعمل
م. محمد البنا
التوقيع

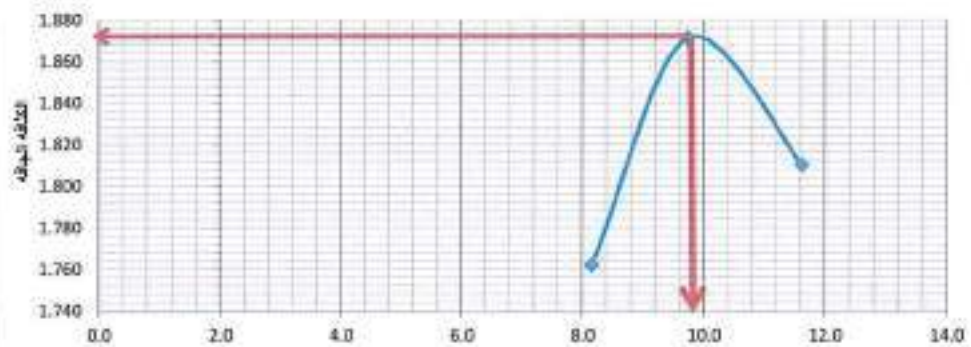
Modified Proctor : ASTM D1557

نوع العينة:	عينة كاشان رملية
تصنيف العينة:	A-3
نتائج الاختبار:	
وزن القالب:	5731
حجم القالب:	2140
القيمة الجافة:	1.871
البيانات الأولية:	9.7

رقم الاختبار	1	2	3
وزن القالب + العينة رطبة	9810.0	10126	10055
وزن التربة الرطبة	4079.0	4396	4324
الكتلة الرطبة	1.906	2.054	2.021

رقم الجفنة	1	2	3	4	5	6
وزن الجفنة	53.85	55.31	54.35	54.15	55.14	53.4
وزن الجفنة + العينة رطبة	150.0	150.0	150.0	150.0	150.0	150.0
وزن الجفنة + العينة جافة	142.5	143.1	141.6	141.4	140.2	139.87
وزن المياه	7.5	6.9	8.4	8.6	9.8	10.1
وزن العينة جافة	88.65	87.79	87.25	87.25	85.06	86.47
المحتوى المائي %	8.5	7.9	9.6	9.9	11.5	11.7
متوسط المحتوى المائي %	8.2	9.7	11.6			
الكتلة الجافة	1.762	1.871	1.810			

Modified Proctor Chart



ملاحظات:



احمد محمد هادي
مهندس

مهندس المعمول
د. محمد هادي محمد البنا
التوقيع:

Coarse & Fine Aggregate Grading - ASTM C136 & AASHTO T27

التاريخ :	25-08-23	الموقع : St 202+280	ارض طبيعيه
-----------	----------	---------------------	------------

نتائج الاختبار :-

رقم المنخل (mm)	رقم المنخل (inch)	وزن المحجوز على كل منخل	وزن المحجوز التراكمي	المحجوز %	المرار %
127	5"	0	0	0%	100%
101.6	4"	0	0	0.00%	100.00%
76.2	3"	0	0	0.00%	100.00%
63.5	2.5"	0	0	0.00%	100.00%
50.8	2"	0	0	0.00%	100.00%
37.5	1.5"	0	0	0.00%	100.00%
25	1"	0	0	0.00%	100.00%
19	3/4"	0	0	0.00%	100.00%
12.7	1/2"	0	0	0.00%	100.00%
9.5	3/8"	0	0	0.00%	100.00%
4.75	# 4	0	0	0.00%	100.00%
	المرار من منخل # 4	500			100.00%
	وزن العينة الكلى	500			
	وزن عينة الناعم	500			
2.36	# 10	0	0	0.0%	100.0%
0.425	# 40	51	51	10.2%	89.8%
0.075	# 200	436	487	97.4%	2.6%
السيولة و اللدونة		N.P			
التصنيف		A-3			

ملاحظات : توصيف العينة : كثبان رملية ناعمة (Sand Dunes)



المهندس
المختبر

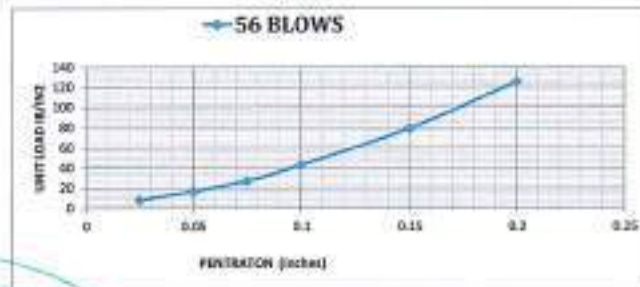
مهندس العمل
المختبر
التوقيع

اختبار نسبة تحميل كاتيلورتيا (C . B . R) ASTM D1883

تصنيف العينة		A-3	
عدد الضربات	56	عدد الضربات	56
حجم القالب (سم ³)	2131	رقم البقعة	2
وزن القالب (جم)	5289	وزن البقعة	54.3
وزن القالب موزن العينة رطبة (جم)	9682	وزن البقعة «العينة رطبة» جم	150
وزن العينة رطبة (جم)	4313	وزن البقعة «العينة جافة» جم	141.3
الكثافة (غ/سم ³) (جم/سم ³)	2.024	وزن الماء جم	8.5
نسبة الماء جافة (جم/سم ³)	1.844	وزن العينة جافة جم	87.3
كثافة البوراكور (جم/سم ³)	1.871	المحتوى المائي %	9.7%
نسبة الدمك	86.6%		
نسبة الانكماش	0.08%	غير قابلة للتكلس	

جواب نسبة تحميل كاتيلورتيا

7.62	5.08	3.81	2.54	1.95	1.27	0.635	الأحجار الخشنة	بعد الضرب
0.3	0.2	0.15	0.1	0.075	0.05	0.025	الأحجار الخشنة	
258.0	171	108.0	59.0	37.0	23.0	11.0	التراب ناعم	بعد الضرب
568.632	376.884	238.032	130.036	81.548	50.692	24.244	التراب بالمراد	
189.63	125.685	79.38	43.365	27.195	16.905	8.085	المراد 10/102	



8.4%

قيمة C . B . R

ملاحظات: تم إجراء القالب في الماء لمدة 96 ساعة قبل المراقبة المبرمجة



احمد صديقه

مهندس المحسن
محمد بن محمد البنا

مشروع :
قطار اسوان الكهربائي السريع - القطاع الثاني

استشاري أبحاث التربة والاساسات :
أ.م. هشام محمد حلمي



تقرير بنتائج اختبارات صلاحية أترية للتأسيس

مقدمة : تم إعداد هذا التقرير بناءً على طلب شركة / ابو عجيله

وذلك لتحديد خصائص ومدى صلاحية عينة تراب للإستخدام في / طبقات الردم لجسر القطار الكهربائي

مصدر العينة : عند المحطة / 202+020 عينه ارض طبيعيه

- المندوب: وقد تم توريد العينة بمعرفة م/ محمود الحيني . بتاريخ : 2023/9/21

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفلووط)

- التوصيف الظاهري للعينة : كتبان رملية ناعمة (مغو)

- تبييه العينة مسئولية من احضرها

وقد تم عمل الاختبارات الآتية :

- 1-التنرج الحبيبي
- 2-حد السيولة واللونة
- 3-اختبار البروكتور
- 4-اختبار CBR
- 5-اختبار المواد العضوية

وكانت نتائج الاختبارات كالآتي :

م	نوع الاختبار	النتائج
1	تصنيف العينة	A-3
2	نسبة الماء من مخل 200	4 %
3	مجال اللونة	عديمة اللونة
4	أقصى كثافة جافة (البروكتور) $\gamma_d \max$	1.863 gm/cm3
5	نسبة المياه الأصولية	10 %
6	قيمة CBR المغسورة	7.7%
8	المواد العضوية	لا يوجد

• و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي غير صالحة للتأسيس عليها



أ.م. هشام محمد حلمي

مهندس المعمول
أ.م. هشام محمد حلمي
التوقيع

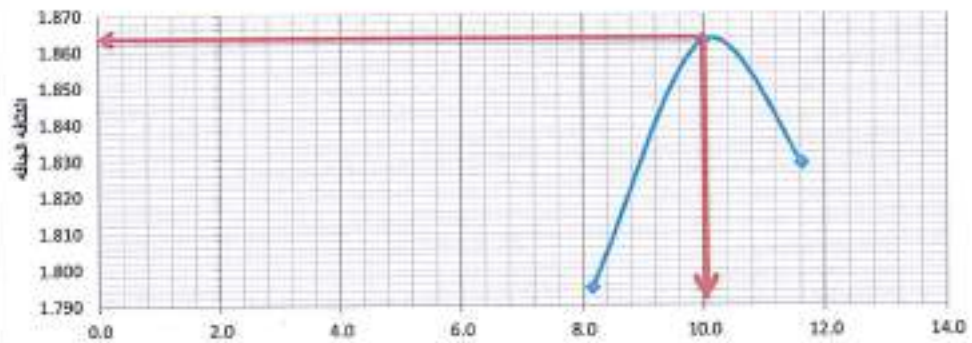
Modified Proctor : ASTM D1557

نوع العينة:	عينة كتيان رملية
تصنيف العينة:	A-3
تاريخ الاختبار:	
وزن القالب:	5731
حجم القالب:	2140
المسح ككثافة جافة:	1.883
البيانات الاسمية:	10.0

رقم الاختبار	1	2	3
وزن القالب + العينة رطبة	9886.0	10116	10100
وزن التربة الرطبة	4155.0	4385	4369
كثافة الرطبة	1.942	2.049	2.042

رقم الحقل	1	2	3	4	5	6
وزن الحقل	53.85	55.31	54.35	54.15	55.14	53.4
وزن الحقل + العينة رطبة	150.0	150.0	150.0	150.0	150.0	150.0
وزن الحقل + العينة جافة	142.5	143.1	141.4	141.2	140.2	139.87
وزن المياه	7.5	8.9	8.6	8.8	9.8	10.1
وزن العينة جافة	88.65	87.79	87.05	87.05	85.06	86.47
المحتوى المائي %	8.5	7.9	9.9	10.1	11.5	11.7
متوسط المحتوى المائي %	8.2	10.0	11.6			
كثافة الحقل	1.795	1.863	1.829			

Modified Proctor Chart



ملاحظات:



أحمد مصطفى
مهندس

مهندس المعمل
أحمد مصطفى
التوقيع
مهندس

Coarse & Fine Aggregate Grading - ASTM C136 & AASHTO T27

التاريخ :	25-09-23	الموقع : St= 202+020	ارض طبيعية
-----------	----------	----------------------	------------

نتائج الاختبار :-

رقم المنخل (mm)	رقم المنخل (inch)	وزن المحجوز على كل منخل	وزن المحجوز التراكمي	المحجوز %	العار %
127	5"	0	0	0%	100%
101.6	4"	0	0	0.00%	100.00%
76.2	3"	0	0	0.00%	100.00%
63.5	2.5"	0	0	0.00%	100.00%
50.8	2"	0	0	0.00%	100.00%
37.5	1.5"	0	0	0.00%	100.00%
25	1"	0	0	0.00%	100.00%
19	3/4"	0	0	0.00%	100.00%
12.7	1/2"	0	0	0.00%	100.00%
9.5	3/8"	0	0	0.00%	100.00%
4.75	# 4	0	0	0.00%	100.00%
	العار من منخل # 4	500			100.00%
	وزن العينة الكلي	500			
	وزن عينة التام	500			
2.36	# 10	10	10	2.0%	98.0%
0.425	# 40	51	61	12.2%	87.8%
0.075	# 200	419	480	96.0%	4.0%
المبيولة و اللدونة		N.P			
التصنيف		A-3			

ملاحظات : توصيف العينة : كتيان رملية ناعمة (Sand Dunes)



احمد محمد علي
مهندس

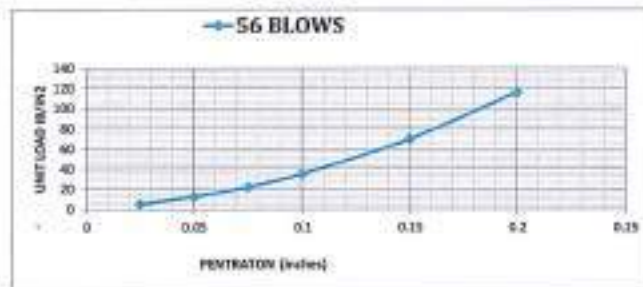
مهندس المعمل
د. مصطفى محمد البنا
التوقيع

اختبار نسبة تحميل كاتيلورنيا (C . B . R) ASTM D1883

A-3		تصنيف العينة	
56	عدد الضربات	56	عدد الضربات
2	رقم البقعة	2131	ختم القالب (سم)
21.6	وزن البقعة	5289	وزن القالب (جم)
193	وزن البقعة + العينة رطبة (جم)	5590	وزن القالب + وزن العينة رطبة (جم)
198.3	وزن البقعة + العينة جافة (جم)	4391	وزن العينة رطبة (جم)
11.7	وزن الماء (جم)	2.018	كثافة الرطبة (جم / سم ³)
116.7	وزن العينة جافة (جم)	1.834	القيمة كاتيلورنيا (جم / سم ²)
10.0%	المسحور المائي %	1.863	كثافة البرونز (جم / سم ³)
		98.5%	نسبة الماء
	غير قابلة للتشقق	0.00%	نسبة الانكماش

خصائص نسبة تحميل كاتيلورنيا

7.62	5.08	3.81	2.54	1.95	1.27	0.635	الأخضر لـ 1 ملم
0.3	0.2	0.15	0.1	0.075	0.05	0.025	الأخضر لـ 1/4 بوصة
240.0	158	95.0	48.0	30.0	17.0	7.0	الفراد kg
528.96	348.232	209.38	105.792	66.12	37.468	15.428	الفراد والبرونز
176.4	116.13	69.825	35.28	22.05	12.495	5.145	المعدل 8/IN2



7.7%	قيمة C . B . R
------	----------------

ملاحظات : تم عمل القالب في الماء لمدة 96 ساعة قبل الاختبار



احمد محمد عيسى
مهندس

مهندس محمد البنا
مهندس

	مشروع القطار الكهربائي السريع	 الهيئة العامة للإستشارات الهندسية مكتب أ.د/حسن مهدي للإستشارات الهندسية
	إستكمال إسناد أعمال الجسر الترابي والأعمال الصناعية بقطاعات مشروع إنشاء القطار الكهربائي السريع (أكتوبر-أبوسمبل)	
	تنفيذ شركة أبو عجيبة للمقاولات العامة والتوريدات العمومية مستخلص (١) جارى	

الحصر الإجمالي لكميات القطاع حتى تاريخ ٢٠٢٤/٤/١

Station	Total Cut Area(m2)	Cum. Cut Vol(m3)	As Built vol.cut		
				CUT VOL(m3)	Total.Qty
200+876.01	580.84	0	cut	0	529753.21
200+880.00	586.05	2,325.62		2,325.62	
200+900.00	630.8	14,494.09		12,168.47	
200+920.00	667.79	27,479.99		12,985.90	
200+940.00	665.5	40,812.95		13,332.96	
200+960.00	635.92	53,827.17		13,014.23	
200+980.00	655.55	66,741.85		12,914.68	
201+000.00	650.46	79,801.90		13,060.05	
201+020.00	610.45	92,410.94		12,609.04	
201+040.00	622.17	104,737.11		12,326.16	
201+060.00	621.82	117,176.99		12,439.89	
201+080.00	624.05	129,635.71		12,458.71	
201+100.00	616.97	142,045.96		12,410.26	
201+120.00	615.77	154,373.38		12,327.42	
201+140.00	617.82	166,709.30		12,335.92	
201+160.00	623.52	179,122.78		12,413.48	
201+180.00	614.79	191,505.94		12,383.16	
201+200.00	633.1	203,984.90		12,478.96	
201+220.00	599.85	216,314.49		12,329.59	
201+240.00	499.13	227,304.33		10,989.84	
201+260.00	445.74	236,753.04		9,448.72	
201+280.00	450.78	245,718.30		8,965.26	
201+285.93	449.56	248,387.80		2669.5	
201+300.00	460.6	254,790.75		6,402.95	
201+320.00	478.13	264,178.05		9,387.30	
201+340.00	476.54	273,724.79		9,546.74	
201+360.00	473.02	283,220.47		9,495.68	
201+380.00	467.7	292,627.66		9,407.19	
201+400.00	480.96	302,114.23		9,486.57	
201+420.00	473.9	311,662.81		9,548.58	
201+440.00	516.53	321,567.07		9,904.26	
201+460.00	579.3	332,525.35		10,958.28	
201+465.93	585.45	335,978.82		3453.48	
201+480.00	583.85	344,204.87		8,226.04	
201+500.00	576.27	355,806.07		11,601.20	
201+520.00	563.45	367,203.19		11,397.13	
201+540.00	521.62	378,053.86		10,850.67	
201+560.00	446.24	387,732.49		9,678.63	
201+580.00	417	396,364.88		8,632.38	
201+600.00	431.82	404,853.04		8,488.16	
201+620.00	454.9	413,720.28		8,867.24	
201+640.00	461.11	422,880.41		9,160.14	

عن الاستشاري أ.د حسن مهدي

م/ عبد الحميد علاء الدين م/ احمد عزب

عن استشاري المساحة

م/ محمد عبدالرحمن م/ محمد عبد الله

عن الشركة

م/ محمد حامد أبو عجيبة م/ محمد عبد الله

9/11



	مشروع القطار الكهربائي السريع	 الهيئة العامة للطرق والنقل مكتب أ.د/حسن مهدي للإستشارات الهندسية
	إستكمال إسناد أعمال الجسر الترابي والأعمال الصناعية بقطاعات مشروع إنشاء القطار الكهربائي	
	السريع (أكتوبر - أبوسمبل) تنفيذ شركة أبو عجيله للمقاولات العامة والتوريدات العمومية	

حصر كمية الاحلال في السفو ابتداء من شهر سبتمبر ٢٠٢٢

Station	Total Cut Area(m2)	Cum. Cut Vol(m3)	As Built vol.cut		
				CUT VOL(m3)	Total.Qty
201+920.00	172.54	495,420.53	CUT	1,725.37	36058.01
201+940.00	117.37	498,319.63		2,899.09	
201+960.00	121.91	500,712.41		2,392.78	
201+980.00	141.36	503,345.11		2,632.70	
202+000.00	131.55	506,074.23		2,729.12	
202+020.00	123.82	508,627.92		2,553.69	
202+040.00	93.18	510,797.88		2,169.96	
202+060.00	50.98	512,239.45		1,441.57	
202+080.00	49.6	513,245.30		1,005.85	
202+100.00	43	514,171.38		926.08	
202+120.00	38.08	514,982.21		810.83	
202+140.00	0	515,362.98		380.78	
202+160.00	0	515,362.98		0.00	
202+180.00	0	515,362.98		0.00	
202+200.00	0	515,362.98		0.00	
202+220.00	73.22	516,095.23		732.24	
202+240.00	80.7	517,634.50		1,539.28	
202+260.00	97.19	519,413.44		1,778.93	
202+280.00	119.49	521,580.25		2,166.81	
202+300.00	140.13	524,176.43		2,596.18	
202+320.00	63.81	526,215.81		2,039.38	
202+340.00	66.23	527,516.19		1,300.37	
202+360.00	64.12	528,819.69		1,303.50	
202+376.01	52.46	529,753.19		933.50	

عن الاستشاري أ.د حسن مهدي

م/ احمد عزب
م/ محمود غرابي

عن استشاري المساحة

م/ محمد عبدالرحمن

م/ محمد عبدالرحمن
م/ محمد عبدالرحمن

عن الشركة

م/ احمد فتحي

م/ احمد فتحي
م/ احمد فتحي
ABUAGLA
إستشارات الهندسية - القاهرة
١٩٩-١٦١-٦٠٩

	مشروع القطار الكهربائي السريع	
	إستكمال أعمال الجسر الترابي لمسار القطار الكهربائي السريع الخط الثاني (الفيوم / بني سويف - أوسمبل) (مرحلة الجسور والأساس والأسياس) القطاع الثاني (بني مزار / منقلاوط)	
	تنفيذ شركة أبو عجيبة للمقاولات العامة والتوريدات العمومية كميات حتي مستخلص جاري (١) جاري لعقد رقم (٢٠٢٥/٢٠٢٤/٢٠٩) بتاريخ 2024/4/1 ASBUILT	

بند رقم (١-٣) : أعمال تحميل وتوريد ونقل أتربة مطابقة للمواصفات وتشغيلها باستخدام آلات التسوية بسمك لا يزيد عن ٥٠ سم حتى منسوب (-2 متر) أسفل منسوب الفرمة و بسمك لا يزيد عن ٢٥ سم اعلي من منسوب (-2 متر) من منسوب الفرمة لإستكمال المنسوب التصميمي الخ

Station	Total Fill Area(m2)	Cum. Fill Vol(m3)	As Built vol.Fill				اجمالي الكميات ابتداء من ٢٠٢٤/٢/٢٢
			FILL	Fill VOL(m3)	Total.Qty	Fill VOL(m3) ابتداء من ٢٠٢٤/٢/٢٢	
201+920.00	202.61	2026.07	FILL	2026.07	100122.28	582.22	9669.67
201+940.00	227.66	6,328.78		4,302.71		1,170.55	
201+960.00	248.2	11,087.40		4,758.61		1,162.28	
201+980.00	274.47	16,314.06		5,226.57		1,140.36	
202+000.00	262.01	21,578.88		5,364.82		1,142.87	
202+020.00	243.79	26,736.89		5,058.01		1,149.44	
202+040.00	194.01	31,114.85		4,377.95		1,134.32	
202+060.00	362.48	36,679.73		5,564.88		561.35	
202+080.00	341.72	43,721.80		7,042.07		0.00	
202+100.00	314.56	50,284.61		6,562.81		0.00	
202+120.00	301.56	56,445.77		6,161.16		0.00	
202+140.00	0	59,461.36		3,015.59		0.00	
202+160.00	0	59,461.36		0.00		0.00	
202+180.00	0	59,461.36		0.00		0.00	
202+200.00	0	59,461.36		0.00		0.00	
202+220.00	317.97	62,641.01		3,179.66		162.54	
202+240.00	312.67	68,947.36		6,306.35		325.06	
202+260.00	320.6	75,280.03		6,332.66		321.62	
202+280.00	330.13	81,787.33		6,507.30		322.02	
202+300.00	335.88	88,447.44		6,660.11		328.98	
202+320.00	141.42	93,220.38		4,772.95		166.06	
202+340.00	132.47	95,959.23		2,738.85		0.00	
202+360.00	116.74	98,451.35		2492.11		0	
202+376.01	91.94	100,122.29		1,670.94		0.00	

عن الاستشاري أد حسن مهدي
مدير المشروع
م / محمود هريش
م / أحمد عزب

المساحة
م / محمد عبدالرحمن
١٨/٤

عن الشركة
م / أحمد فتح
م / أحمد
١٢
١٩٧٨
ABUAGLA
ب ض ١٥٩ - ١٥٩ - ٦٠٩

	مشروع القطار الكهربائي السريع إستكمال أعمال الجسر الترابي لمسار القطار الكهربائي السريع الخط الثاني (الفيوم / بني سويف - أبو سمبل) (مرحلة الجسور والتأسيس والأساس) القطاع الثاني (بني مزار / متفلوط) تنفيذ شركة أبو عجيبة للمقاولات العامة والتوريدات العمومية حصر اجمالي لكميات الردم	الهيئة القومية للإتفاق مكتب أ.د/حسن مهدي للإستشارات الهندسية
--	--	--

بند رقم (١-٣) : أعمال تحميل وتوريد ونقل أتربة مطابقة للمواصفات وتشغيلها باستخدام آلات التسوية بسمك لا يزيد عن ٥٠ سم حتى منسوب (-2 متر) أسفل منسوب القرمه و بسمك لايزيد عن ٢٥سم اعلي من منسوب (-2٠ متر) من منسوب القرمه لاستكمال المنسوب التصميميالخ

Station	Total Fill Area(m2)	Cum. Fill Vol(m3)	As Built vol.Fill		
			Fill VOL(m3)	Total.Qty	
201+920.00	202.61	2026.07	2026.07	100122.28	
201+940.00	227.66	6,328.78	4,302.71		
201+960.00	248.2	11,087.40	4,758.61		
201+980.00	274.47	16,314.06	5,226.67		
202+000.00	262.01	21,678.88	5,364.82		
202+020.00	243.79	26,736.89	5,058.01		
202+040.00	194.01	31,114.85	4,377.95		
202+060.00	362.48	36,679.73	5,564.88		
202+080.00	341.72	43,721.80	7,042.07		
202+100.00	314.56	50,284.61	6,562.81		
202+120.00	301.56	56,445.77	6,161.16		
202+140.00	0	59,461.36	3,015.59		
202+160.00	0	59,461.36	0.00		
202+180.00	0	59,461.36	0.00		
202+200.00	0	59,461.36	0.00		
202+220.00	317.97	62,641.01	3,179.66		
202+240.00	312.67	68,947.36	6,306.35		
202+260.00	320.6	75,280.03	6,332.66		
202+280.00	330.13	81,787.33	6,507.30		
202+300.00	335.88	88,447.44	6,660.11		
202+320.00	141.42	93,220.38	4,772.95		
202+340.00	132.47	95,959.23	2,738.85		
202+360.00	116.74	98,451.35	2492.11		
202+376.01	91.94	100,122.29	1,670.94		
اجمالي كميات الردم المصروفة سابقا					0
اجمالي كميات الردم الفعلية الحالية بعد خصم سمك خرسانه الميول					100122.28
كمية خصم سمك خرسانه الميول					911

عن الاستشاري المساحة
م/محمد عبد الرحمن
م/احمد عزب
م/محمود غريب
عن الاستشاري أ.د/حسن مهدي
م/احمد عزب
م/محمود غريب



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name [Signature]	Sign [Signature]	Date 15-8-2022
Received by Employers Representative	UIR	C1 KP	C2 EW
		C3 OT	DD 15
		MM 8	YY 22
		HH 22	MM 22
CODE-1	CODE-2	CODE-3	CODE-4

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 202+376	
	E=260126.0446 N=3137487.7094	E=260129.6912 N=3135991.0324
Inspection description[Disinfection Of Trees Cutting From st (200+876) to st (202+376)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

تصوير وازالة الحمايات بواسطة فريق العمل	- Trees No. was checked only by xyz and under their own responsibility - you must follow specs and design dr
--	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	[Signature]	[Signature]			A-AWC-R	
Contractor QA\QC*	XYZ	[Signature]	15-8-2022		A	
	H.M.C	[Signature]	15-8-2022		A	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024		AWC	

* Designer

** Alignment: Bridges: Culvert Only

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name [Signature]	Sign [Signature]	Date 15-8-2022
Received by Employers Representative	UIR	C1 KP	C2 EW
		C3 OT	DD 15
		MM 8	YY 22
		HH 22	MM 22
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 202+376	
	E=260126.0446 N=3137487.7094	E=260129.6912 N=3135991.0324
Inspection description[Disinfection Of Trees Cutting From st (200+876) to st (202+376)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

تصوير وازالة الاشجار بمساحة 200+876 الى 202+376	- Trees No. was checked only by xyz and under their own responsibility - you must follow specs and design dr
--	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	[Signature]	[Signature]			A-AWC-R	
Contractor QA\QC*	XYZ	[Signature]	15-8-2022		A	
	H.M.C	[Signature]	15-8-2022		A	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024		AWC	

* Designer

** Alignment: Bridges: Culvert Only

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيل للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
	20-10-2022	3								
Received by Employers Representative			C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	20	10	22		

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+686 E=260126.0446 E=260172.2356 N=3137487.7094 N=3136679.1711	
Inspection description/ تطهير بعد قطع الاشجار Disinfection of crops and trees cutting from st (200+876) to st (201+686)		

مقطع مقص

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
---	--

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA/QC*	XYZ		20-10-2022	14:30	A	
	H.M.C		20/10/2022	15:00	A	
GARB**						
Employers Representative						

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name أبو عجلة	Sign أبو عجلة	Date 20-10-2022	Time 4																
Received by Employers Representative			<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>EW</td> <td>OT</td> <td>20</td> <td>10</td> <td>22</td> <td></td> <td></td> </tr> </table>		C1	C2	C3	DD	MM	YY	HH	MM	KP	EW	OT	20	10	22		
C1	C2	C3	DD	MM	YY	HH	MM													
KP	EW	OT	20	10	22															
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+686 TO 201+846 E=260172.2356 N=3136679.1711	E=260170.8362 N=3136519.1841
<u>Inspection description/</u> Disinfection of crops and trees cutting from st (201+686) to st (201+846)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
--	--

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	أبو عجلة	أبو عجلة				
Contractor QA/QC*	XYZ	أبو عجلة	20-10-2022	16:00	A	
	H.M.C	أبو عجلة	20/10/2022	16:30		
GARB**						
Employers Representative						

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
	محمد بن محمد	[Signature]	20-10-2022	5						
Received by Employers Representative		[Signature]	C1	C2	C3	DD	MM	YY	HH	MM
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+966 TO 202+376		
	E=260166.4277	E=260129.6912	
	N=3136399.268	N=3135991.0324	
<u>Inspection description/</u> Disinfection of crops and trees cutting from st (201+966) to st (202+376)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT: (xyz))

[Signature]

Comments by: General consultant (systra)

- Levels and coordinater were checked only by xyz and under their own responsibility
 - you must follow specs, design drawing and geo-technical report.
 - this work was inspected only by xyz and

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	محمد بن محمد	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	[Signature]	20-10-2022	14:30		
	H.M.C	[Signature]	20/10/2022	14:30		
GARB**						
Employers Representative	Khaled alr	[Signature]	23/10/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)					
Issued by Contractor	Name	Sign	Date					
			25-10-2022					
Received by Employers Representative	Name	Sign	Time					
			6					
C1		C2	C3	DD	MM	YY	HH	MM
KP		EW	OT	25	10	22		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+466 TO 201+666	
	E=260165.8013	E=260172.0505
	N=3136899.0593	N=3136699.1703
Inspection description/		
As-Built for rock surface from st (201+466) to st (201+666)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)




- Levels and coordinates were checked only by xyz and under their own responsibility
- This work was inspected only by xyz and H.M.C
- you must follow spec and geo-technical report

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer					A-AWC-R	
Contractor QA/QC*	XYZ		25-10-2022	13:00	A	
	H.M.C		25/10/2022	13:00	A	
GARB**						
Employers Representative	Khaled ali		23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
			29-10-2022	7						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	29	10	28		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	200+876 TO 201+466		
	E=260126.0446	E=260165.8013	
	N=3137487.7094	N=3136899.0593	
Inspection description[الرفع المساحي + المعاينة للطرح المرفوض (المسوح الأول) As-Built for rock surface from st (200+876) to st (201+466)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate






Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. (xyz))

Comments by: General consultant (systra)

	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C. - you must follow specs and design drawings.
---	--

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer					A-AWC-R	
Contractor QA/QC*	XYZ		29-10-2022	12:00	A	
	H.M.C		29/10/22		A	
GARB**						
Employers Representative	Khaleed ali		23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عبيدة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
	محمد أبو بكر	[Signature]	6-11-2022	10						
Received by Employers Representative	[Signature]	[Signature]	C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	6	11	2022		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+156 TO 201+246	
	E=260145.4242 N=3137208.3848	E=260151.6535 N=3137118.6007
Inspection description/		
الرفع المساحي + معاينة سطح صغرى (المنسوب الثالث)		
As-Built for rock surface from st (201+156) to st (201+246)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time


Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))

Comments by: General consultant (systra)

	- Levels and Coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C you must follow specs and geo-technical report
---	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	محمد أبو بكر	[Signature]			A-AWC-R	
Contractor QA\QC*	XYZ	[Signature]	6-11-2022	14:00	A	
	H.M.C	[Signature]	6/11/2022	14:30	A	
GARB**						
Employers Representative	Khaled Ali	[Signature]	23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name أبو عجلة	Sign أبو عجلة	Date 7-12-2022																
Received by Employers Representative			Time 13																
		UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>EW</td> <td>OT</td> <td>7</td> <td>12</td> <td>23</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	EW	OT	7	12	23		
C1	C2	C3	DD	MM	YY	HH	MM												
KP	EW	OT	7	12	23														
CODE-1	CODE-2	CODE-3	CODE-4																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+286 TO 201+386	
	E=260154.422 N=3137078.6966	E=260161.1582 N=3136978.9239
<u>Inspection description</u> As-Built for rock surface from st (201+286) to st (201+386)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT-(xyz))	Comments by: General consultant (systra)
	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C. - you must follow specs and geo-technical report

INSPECTION RESULT						Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	Approval Status	
Contractor Engineer	أبو عجلة	أبو عجلة				
Contractor QA/QC*	XYZ	أبو عجلة	7-12-2022	14:00	A	
	H.M.C	أبو عجلة	7/12/2022	14:30	A	
GARB**						
Employers Representative	Khaled ali	أبو عجلة	23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR ,Hassan Mahdy (H.M.C)
Issued by Contractor	Name Sign	Date	Time
Received by Employers Representative	Sign	13-12-2022	14
UIR	C1 KP	C2 EW	C3 OT
	DD 13	MM 12	YY 22
	HH	MM	
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+386 TO 201+426	
	E=260161.1582 N=3136978.9239	E=260163.6041 N=3136938.9988
Inspection description: الرفع المساحي + معاينة سطح صخره (المستوي الثالث) As-Built for rock surface from st (201+386) to st (201+426)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)



- Levels and coordinates were checked only by systra and under their own responsibility
- This work was inspected only by systra and H.M.C
- you must follow specs and geo-technical report

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer					A-AWC-R	
Contractor QA/QC*	XYZ		13-12-2022	12:16	A	
	H.M.C		13/12/2022	12:17	A	
GARB**						
Employers Representative	Khaled al.		23/12/2022			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)			
Issued by Contractor	Name	Sign	Date	Time			
	13-12-2022	16					
Received by Employers Representative	C1	C2	C3	DD	MM	YY	HH
	13	12	23				
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+036	
	E=260126.0446	E=260137.1186
	N=3137487.7094	N=3137328.0971
Inspection description/		
As-Built for rock surface from st (200+876) to st (201+036)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C - you must follow spec and geotechnical rep

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer						
Contractor QA/QC*	XYZ		13-12-2022	13:30	A	
	H.M.C		13/12/2022	14:00	A	
GARB**						
Employers Representative	Phaked ali		23/12/2022		A	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR ,Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
			2023-1-3	17						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	3	1	23		
CODE-1		CODE-2	CODE-3	CODE-4		CODE-5				

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	200+876 TO 201+666		
	E=260126.0446	E=260172.0505	
	N=3137487.7094	N=3136699.1703	
Inspection description/			
As-Built for cut from st (200+876) to st (201+666)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
2023/1/3	

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
	- Levels and coordinates were checked only by XYZ and under their own responsibility - you must follow specs and design drawings

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor	XYZ		3-1-2023	14:00	A	
QA/QC*	H.M.C		3/1/2023	19:00		
GARB**						
Employers Representative	Khaled ali		23/9/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name 1375 Sign 	Date	13-6-2023
Received by Employers Representative	Time 18	Time	18
Received by Employers Representative	UIR	C1 KP	C2 EW
		C3 OT	DD 13
		MM 6	YY 23
		HH	MM
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+660	
	E=260126.0446 N=3137487.7094	E=260171.9793 N=3136705.1798
Inspection description		
As-Built for cut from st (200+876) to st (201+660)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
12/6/2023	

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

as built for cut from st (200+876) to st (201+660)

- Levels and coordinates were checked only by xyz and under their own responsibility
- you must follow spec and design dwg.

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA/QC*	XYZ		13-6-2023	9:00	A	
	H.M.C		13/6/2023			
GARB**						
Employers Representative	Khaled ali		23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name Sign 24-8-2023	Date	Time 19
Received by Employers Representative	Sign 23	UIR	
CODE-1	CODE-2	CODE-3	CODE-4
CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+840 E=260126.0446 N=3137487.7094	E=260170.9813 N=3136525.1923
Inspection description: As-Built for cut from st (200+876) to st (201+840)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
24/8/2023	

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
asbuilt قطاع القطر	- Levels and coordinates were checked only by xyz and under their own responsibility - you must follow specs and design drawings

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer					A-AWC-R	
Contractor QA/QC*	XYZ		26-8-2023	10:00	A	
	H.M.C		26/8/2023	10:15	A	
GARB**						
Employers Representative	Khaled ali		23/8/2023			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name وليد فهد محمد	Date	9-11-2023
Received by Employers Representative	Sign وليد فهد محمد	REQ.NUM	20
Received by Employers Representative	UIR	C1 KP	C2 SU
		C3 OT	DD 9
		MM 11	YY 23
		HH	MM
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description/ تشييد قاع إحلل from st (202+220) to st (202+300)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))	Comments by: General consultant (systra)
	- levels and coordinates were checked only by xyz and under their own responsibility - No objection according to the attached reports and lab. results.

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد فهد محمد	وليد فهد محمد	19-11-2023	10:00	(A)	
Contractor QA/QC*	XYZ	محمد عبد الله	9/11/2023	11:00	A	
GARB**						
Employers Representative	Khaled ali		23/9/2024			

* Designer

** Alignment: Bridges; Culvert Only

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عبيدة للمقاولات 2023	Designer Company*	DR ,Hassan Mahdy (H.M.C)															
Issued by Contractor	Name Sign 20-11-2023	Date	REQ. NUM 22															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>21</td> <td>11</td> <td>23</td> <td>2</td> <td>30</td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	21	11	23	2	30
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT	21	11	23	2	30											
CODE-1	CODE-2	CODE-3	CODE-4															
CODE-5																		

EXPLANATION OF WORK TO BE INSPECTED


Area	Element	Item
From 200+876 To 202+376	202+000 TO 202+120 E=260164.6561 N=3136365.3242	E=260156.5571 N=3136245.6007
Inspection description/ تشغيل قاع إحلال from st (202+000) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was checked only by xyz and H.M. - you must follow speed and design drawing and geo-technical report

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time			
Contractor Engineer	وليد محمد	وليد محمد					
Contractor QA/QC*	XYZ	محمد	21-11-2023	3:15	(A)		
	H.M.C	عبدالله	21/11/2023	3:00	A		
GARB**							
Employers Representative	Khaled ali		23/11/2024		Any		

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown:

Contractor Company	أبو عجمية للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name وليد محمد علي	Date	22-11-2023
Received by Employers Representative	Sign وليد محمد علي	REQ. NUM	23
Received by Employers Representative	UIR	C1 KP	C2 SU
		C3 OT	DD 22
		MM 11	YY 23
		HH	MM
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED


Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description/		
from st (202+220) to st (202+300) طبقة ردم منسوب (-9.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time



Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
	- No objection, according to the attached reports and Lab. results. - you must follow specs and design drawings

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد محمد علي	وليد محمد علي					
Contractor QA/QC*	XYZ	وليد محمد علي	22-11-2023	3:45	(A)		
	H.M.C	وليد محمد علي	22/11/2023	11:00	A		
GARB**							
Employers Representative	Fhaled ali	فهد علي	23/11/2023				


RECEIPT of NOTIFICATION Minimum Notice Period not less than 24 Hours The Work described below will be complete and ready for inspection at planned time shown											
Contractor Company	شركة المقاولات العامة 				Designer Company*	DR .Hassan Mahdy (H.M.C)					
Issued by Contractor	Name	Sign	Date	REQ.NUM 24							
			25-11-2023								
Received by Employers Representative			UIR	C1	C2	C3	D0	MM	YY	HH	MM
				AP	SU	OT	25	11	23		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
From 200+876 To 202+376	202+000 TO 202+020	
	E=260164.6561	E=260163.5058
	N=3136365.3242	N=3136345.3573
<u>Inspection description:</u> من طبقة ردم منسوب (13) متر from st (202+000) to st (202+020)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (systra)) 	Comments by: General consultant (systra) - No objection, according to the attached reports and lab. results. - you must follow specs and design drawings
--	--

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد محمد						
Contractor QA/QC*	XYZ		25-11-2023	12:30	(A)		
	H.M.C		25/11/2023	11:00	A		
GARB**							
Employers Representative	Khaled ali		23/9/2024				

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name [Signature]	Sign [Signature]	Date 28-11-2023
Received by Employers Representative	UIR	C1 KP	C2 SU
		C3 OT	DD 28
		MM 11	YY 23
		HH 11	MM 00
CODE-1	CODE-2-109	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300 E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description from st (202+220) to st (202+300) ردم طبقة ردم منسوب (-9) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

تم استلام استمارة المعاينة
والتأكد من مطابقتها
للمواصفات والمواصفات
المطلوبة.

- No objection, according to the attached reports and lab. results
- you must follow specs and design dng.

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمد	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	عبد الله	28/11/2023	3:30	A	
	H.M.C	عبد الله	28/11/2023	11:00	A	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	Name		Sign	Designer Company*	DR .Hassan Mahdy (H.M.C)				
Issued by Contractor	29-11-2023		REQ.NUM		26				
Received by Employers Representative	C1		C2	C3	DO	MM	YY	HH	MM
	KP		SU	OT	29	11	23		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5	

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+060 TO 202+080		
	E=260160.9658 N=3136305.4382	E=260159.576 N=3136285.4865	
Inspection description[from st (202+060) to st (202+080) طبقة ردم منسوب (-11) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))	Comments by: General consultant (systra)
 المهندس خالد علي - الهندس	- No objection, according to the attached reports and lab. results. - you must follow specs and design draw

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	Waleed Elmaghrabi	Waleed Elmaghrabi	29-11-2023	1:15	(A)	
Contractor QA/QC*	XYZ	Khaled Ali	29-11-2023	12:45	A	
GARB**						
Employers Representative	Khaled Ali	Khaled Ali	29/11/2023		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)					
Issued by Contractor	Name وليد محمود محمد	Date	29-11-2023					
Received by Employers Representative	Sign [Signature]	REQ.NUM	27					
UIR	C1 KP	C2 SU	C3 OT	DD 29	MM 11	YY 23	HH	MM
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5				

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+080 TO 202+120 E=260159.576 N=3136285.4865	E=260156.5571 N=3136245.6007
Inspection description: منطقة ردم منسوب (-10.5) متر from st (202+080) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSANTANT.(xyz))

Comments by: General consultant (systra)

-No objection, according to the attached reports and lab. results
-you must follow specs and design dwg

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمود محمد	[Signature]	29-11-2023	11:30	(A)	
Contractor QA/QC*	H.M.C	[Signature]	29-11-2023	12:30	A11	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	157137 أبو عزة للتقانات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name م.د/حسن مهدي	Date	30-11-2023
Received by Employers Representative	Sign م.د/حسن مهدي	REQ.NUM	28
Received by Employers Representative	UIR	C1 KP	C2 SU
		C3 OT	DD 30
		MM 11	YY 23
		HH	MM

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+000 TO 202+020 E=260164.6561 N=3136365.3242	E=260163.5058 N=3136345.3573
Inspection description: ردم طبقة ردم منسوب (-12.5) متر from st (202+000) to st (202+020)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (XYZ)) م.د/حسن مهدي	Comments by: General consultant (systra) -No objection, according to the attached reports and lab. results. -you must follow spec and design draw
---	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	م.د/حسن مهدي	م.د/حسن مهدي	30-11-2023	13:00	A	
Contractor QA/QC*	XYZ	م.د/حسن مهدي	30-11-2023	12:30pm	A	
GARB**						
Employers Representative	Khaled Ali	م.د/حسن مهدي	23/9/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 57537	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name [Signature]	Date	2-12-2023																
Received by Employers Representative	Sign [Signature]	REQ.NUM	29																
UIR		<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>2</td> <td>12</td> <td>23</td> <td></td> <td></td> </tr> </table>		C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	2	12	23		
C1	C2	C3	DD	MM	YY	HH	MM												
KP	SU	OT	2	12	23														
CODE-1	CODE-2	CODE-3	CODE-4																
CODE-5	CODE-6	CODE-7	CODE-8																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description[from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (-8.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (sysra)

تم استلام نتائج الاختبار
من مختبر الطرق السريعة - الخط الثاني

- No objection, according to the attached reports and lab. results.
- you must follow specs and design dr

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمد	[Signature]				
Contractor QA/QC*	XYZ	عبد الرحمن الوالد	21/12/2023	3:15	A	
	H.M.C	أحمد مصطفى	21/12/23	3:00	AWC	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/12/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أد/حسن مهدي
للإشراف الهندسية



الهيئة العامة للإشراف
على الطرق



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name 	Sign 	Date 3-12-2023
Received by Employers Representative		UIR	REQ.NUM 30

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+100 E=260160.9658 N=3136305.4382	E=260158.1064 N=3136265.5406
Inspection description طيفة ردم مسوب (-10.5) متر from st (202+060) to st (202+100)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz)) 	Comments by: General consultant (systra) - No objection, according to the attached reports and lab. results. - you must follow specs and design d.
---	--

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA/QC*	XYZ		3-12-2023	4:15	(A)	
	H.M.C		3/12/2023	2:30 PM	AWC	
GARB**						
Employers Representative	Khaled ali		28/9/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown.

Contractor Company	شركة البترول العالمية		Designer Company*	DR. Hassan Mahdy (H.M.C)																
Issued by Contractor	Name وليد عيسى	Sign [Signature]	Date 5-12-2023	REQ. NUM 31																
Received by Employers Representative	[Signature]		UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DO</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>23</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DO	MM	YY	HH	MM	KP	SU	OT			23		
C1	C2	C3	DO	MM	YY	HH	MM													
KP	SU	OT			23															
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147	E=260139.0278
	N=3136146.003	N=3136066.4661
<u>Inspection description:</u> from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (8-متر)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (-xyz))

[Signature]

مهندس أحمد عبد الرحمن السريج - الخدم

Comments by: General consultant (systra)

- No objection, according to the attached reports and lab. results.
 - you must follow specs and design dwg.

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد عيسى	[Signature]	6-12-2023	10:30	(A)	يتم اضافة لسانه قبل اكمال التواقيع
Contractor QA/QC*	XYZ	[Signature]	6-12-2023	10:30	(A)	
	H.M.C	[Signature]	5/12/2023	4:15 PM	AWC	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024		AWC	




RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours The Work described below will be complete and ready for inspection at planned time shown										
Contractor Company	أبو عجيبة للمقاولات العامة				Designer Company*	DR .Hassan Mahdy (H.M.C)				
Issued by Contractor	Name	Sign	Date	REQ. NUM						
	وليد زكريا	وليد زكريا	7-12-2023	32						
Received by Employers Representative	UIR		C1	C2	C3	DD	MM	YY	HH	MM
			XP	SU	OT			23		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED			
Area	Element		Item
From 200+876 To 202+376	200+876 TO 202+120		
	E=260160.9658	E=260156.5571	
	N=3136305.4382	N=3136245.6007	
<u>Inspection description/</u> from st (202+060) to st (202+120) طبقة ردم ملمسوب (10-) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz)) 	Comments by: General consultant (systra) - No objection, according to the attached reports and lab. results. - you must follow specs and design drawing
--	---

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد زكريا	وليد زكريا	7-12-2023	1:30	(A)		
	H.M.C	H.M.C				7/12/2023	12:15
GARB**							
Employers Representative	Khaled ali	Khaled ali	23/12/2024		AWC		



UNIVERSAL INSPECTION REQUEST



مكتب أ.أ.أ.أ.أ.أ.
للإشراف الهندسية



الهيئة العامة للإشراف
على الطرق



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR. Hassan Mahdy (H.M.C)					
Issued by Contractor	Name	Sign	Date	REQ. NUM					
	13-12-2023	35							
Received by Employers Representative	UIR	G1 KP	C2 SU	C3 OT	DD 13	MM 12	YY 23	HH 3	MM 00
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description/ منطقة ردم منسوب (9- متر from st (202+060) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT. (xyz))	Comments by: General consultant (systra)
	- No objection, according to the attached reports and lab. results. - you must follow specs and design drawings.

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	أبو عجيبة للمقاولات العامة	أبو عجيبة للمقاولات العامة	13-12-2023	4:00	(A)		
Contractor QA/QC*	XYZ	أبو عجيبة للمقاولات العامة	13-12-2023	3:00	Awc		
GARB**							
Employers Representative	Khaled ali	أبو عجيبة للمقاولات العامة	23/9/2024		Awc		

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



شركة أديس مهدي
للإستشارات الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name	Sign	Date	REQ.NUM																
	أبو عجلة	أبو عجلة	16-12-2023	36																
Received by Employers Representative	Signature	Signature	UIR	<table border="1"> <tr> <td>G1</td> <td>G2</td> <td>G3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>XP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>23</td> <td></td> <td></td> </tr> </table>	G1	G2	G3	DD	MM	YY	HH	MM	XP	SU	OT			23		
				G1	G2	G3	DD	MM	YY	HH	MM									
XP	SU	OT			23															
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+220 TO 202+300 E=260147.6147 N=3136146.003 E=260139.0278 N=3136066.4661	
Inspection description: من تسليم طبقة ردم مسلوب (7-متر) from st (202+220) to st (202+300)		

INSPECTION DETAILS The following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT: (xyz))

أبو عجلة
مستشار
الهندسة المدنية - الخطة الانشائية

Comments by: General consultant (systra)

- No objection, according to the attached reports and lab. results.
- you must follow specs and design dng.

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	أبو عجلة	أبو عجلة	16-12-2023	3:15	A	
Contractor QA/QC*	H.M.C	أبو عجلة	16/12/2023	3:00	A	
GARB**						
Employers Representative	Khaled ali	أبو عجلة	28/12/2024		Awc	



UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للطرق
والبنية التحتية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	وليد فلاح	وليد فلاح	17-12-2023	37						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT				23	

CODE-1

CODE-2

CODE-3

CODE-4

CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007	
Inspection description:			
من (202+060) إلى (202+120) طبقة ردم ملسوب (8.5) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by (GARB SURVEY CONSULTANT xyz)	Comments by: General consultant (systra)
استاذ المهندس مستوى التفتيش الكفائي	- No objection, according to the attached reports and lab. results. - you must follow specs and design dwg

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد فلاح	وليد فلاح				تم العمل
Contractor QA/QC*	XYZ		17-12-2023	13:00	A	OK
	H.M.C		17-12-2023	11:00	Amc	OK
GARB**						
Employers Representative	Khaled ali		20/12/24		Amc	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



المشاور الهندسي الدكتور
أحمد محمد عبد الله



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown:

Contractor Company			Designer Company*	DR. Hassan Mahdy (H.M.C)																
Issued by Contractor	Name	Sign	Date	REQ. NUM																
			19-12-2023	38																
Received by Employers Representative			<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>AP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>YY</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	AP	SU	OT			YY			
C1	C2	C3	DD	MM	YY	HH	MM													
AP	SU	OT			YY															
CODE-1	CODE-2 2603-1615-199	CODE-3	CODE-4	CODE-5																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+576	202+220 TO 202+300	
	E=260147.5147	E=260139.0278
	N=3136146.003	N=3136066.4661
Inspection description (from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (7,0-)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	M5 Reference	


Comments by: (GARB SURVEY CONSULTANT: XYZ)

تم فحص القطاع ووافق عليه
مستوى تقنيات الترسيع - الخط الذي

Comments by: General consultant (systra)

- No objection, according to the attached reports and lab. results.
- you must follow specs and design drawings

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	د. هادي					
Contractor QA/QC*	XYZ	عبد الرحمن العلي	19-12-2023	3:30	A	
	H.M.C	محمود	19-12-2023	11:30	A	
GARB**						
Employers Representative	Khaled ali		23/9/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name وليد محمود محمد	Sign 	Date 20-12-2023
Received by Employers Representative			REQ.NUM 39

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120 E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description/ من (202+060) to st (202+120) طبقة ردم منسوب (8-) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz)) 	Comments by: General consultant (systra) - No objection, according to the attached reports and lab. results. - You must follow specs and design draw
--	--

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد محمود محمد	وليد حلاف					
Contractor QA/QC*	XYZ	عبد الرحمن الشراوي	20-12-2023	3:40	A		
	H.M.C	محمد شحات	20-12-2023	1:45	A		
GARB**							
Employers Representative	Khaled ali		23/9/2024		A		

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name Sign 21-12-2023	Date	REQ.NUM 40															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>21</td> <td>12</td> <td>23</td> <td>11</td> <td>30</td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	21	12	23	11	30
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT	21	12	23	11	30											
CODE-1	CODE-2	CODE-3	CODE-4															
CODE-5	CODE-6	CODE-7	CODE-8															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description: from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (6-متر)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT: xyz)	Comments by: General consultant (systra)
	- No objection, according to the attached reports and lab. results. - you must follow specs and design d.

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمد	وليد محمد				
Contractor QA/QC*	XYZ	عبد الرحمن العرابي	21-12-2023	11:00	A	
	H.M.C	محمد بن عبد الله العرابي	21/12/23	11:30	A	
GARB**						
Employers Representative	Khaled ali		23/12/2023		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب المهندس مهدي
للإشراف الهندسية



الهيئة العامة للطرق
والمواصلات



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name وليد محمود محمد	Sign 	Date 23-12-2023	REQ.NUM 41																
Received by Employers Representative			<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>23</td> <td></td> <td></td> </tr> </table>		C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			23		
C1	C2	C3	DD	MM	YY	HH	MM													
KP	SU	OT			23															
CODE-1		CODE-2	CODE-3	CODE-4	CODE-5															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
<u>Inspection description</u> from st (202+220) to st (202+300) تسليم طبقة ردم ملسوب (-5.5) متر		

INSPECTION DETAILS The following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
	- No objection, according to the attached reports and lab. results. - you must follow specs and design dr.

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود محمد	وليد محمود محمد				
Contractor QA/QC*	XYZ	عبدالله العبدالله	23/12/2023	1:00	A	
	H.M.C	محمود علي النور	23/12/2023	12:00	A	
GARB**						
Employers Representative	Khaled ali		23/12/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أ.إ.ص.ن مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	DR. Hassan Mahdy (H.M.C)	Designer Company*	DR. Hassan Mahdy (H.M.C)
Issued by Contractor	Name: وليد محمود	Date	23-12-2023
Received by Employers Representative	Sign: [Signature]	REQ.NUM	42
	UIR	C1	C2
		KP	SU
		C3	OT
		DD	MM
		YY	HH
		MM	MM
		23	
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+920 TO 202+000	
	E=260168.4582 N=3136445.233	E=260164.6561 N=3136365.3242
Inspection description:		
from st (201+920) to st (202+000)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSANTANT (xyz))	Comments by: General consultant (systra)
	- Levels and coordinates were checked only by XYZ and under their own responsibility - This work was checked only by XYZ and - you must follow specs and design H.M.C

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمود	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	[Signature]	23/12/2023	12:00	A	
	H.M.C	[Signature]	23/12/2023	11:00	A	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024			

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للمستشارات الهندسية



الهيئة العامة للإسكان



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name: <u>وليد محمود</u> Sign: <u>[Signature]</u>	Date	REQ.NUM																
Received by Employers Representative		23-12-2023	43																
		<table border="1"> <tr> <td>G1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>23</td> <td>12</td> <td>23</td> <td></td> <td></td> </tr> </table>	G1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	23	12	23			
G1	C2	C3	DD	MM	YY	HH	MM												
KP	SU	OT	23	12	23														
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description/ from st (202+060) to st (202+120) طبقة ردم منسوب (-7.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT. (xyz))	Comments by: General consultant (systra)
<u>[Signature]</u>	- No objection, according to the attached reports and lab. results. - you must follow specs and design draw

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	<u>وليد محمود</u>	<u>[Signature]</u>				
Contractor QA/QC*	XYZ	<u>[Signature]</u>	23-12-2023	4:30	A	
	H.M.C	<u>[Signature]</u>	23/12/23	4:00	AWC	
GARB**						
Employers Representative	<u>Khaled Nale</u>	<u>[Signature]</u>	23/12/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أراضين مهدي
للإستشارات الهندسية



الهيئة العامة للإعتماد
والتقنين



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	المشروعات العامة		Designer Company*	DR. Hassan Mahdy (H.M.C)																
Issued by Contractor	Name وليد محمود	Sign 	Date 25-12-2023	REQ. NUM 44																
Received by Employers Representative			<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DO</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>23</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DO	MM	YY	HH	MM	KP	SU	OT			23			
C1	C2	C3	DO	MM	YY	HH	MM													
KP	SU	OT			23															

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description:		
من 202+060 to 202+120 طبقه ردم منسوب (-7) متر		

INSPECTION DETAILS The following will be ready at the Planned inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT. xyz)	Comments by: General consultant (systra)
	- No objection, according to the attached reports and lab. results. - you must follow specs and design data

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود					
Contractor QA/QC*	XYZ	عبد الرحمن الخولي	25-12-2023	4:13	A	
	H.M.C	محمد كعود	25-12-2023	4:10	AWC	
GARB**						
Employers Representative	Khaled ali		23/9/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أديسن مهندسي
الاستشارات الهندسية



الهيئة العامة للإستثمار



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أ.م. عجيلان للاستشارات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Signature	Date	REQ.NUM						
	وليد محمود	[Signature]	28-12-2023	46						
Received by Employers Representative		[Signature]	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT				23	

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
From 200+876 To 202+376	201+980 E=260165.727 N=3136385.3	
Inspection description: منطقة ردم منسوب (-14) من st (201+980)		

INSPECTION DETAILS The Following will be ready at the Planned inspection Time	
Planned inspection Date	Planned inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))	Comments by: General consultant (systra)
[Signature]	- No objection, according to the attached reports and lab. results. you must follow specs and design drawings

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود	[Signature]				
Contractor QA/QC*	XYZ	[Signature]	28-12-2023	12:00	A	
	H.M.C	[Signature]	28-12-2023	11:00		
GARB**						
Employers Representative	Khaled Ali	[Signature]	23/9/2024		ANC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	إم جي سي للمقاولات العامة	Designer Company*	DR. Hassan Mahdy (H.M.C)
Issued by Contractor	Name: وليد محمود Sign: [Signature]	Date	REQ. NUM
Received by Employers Representative	أبو شادية لستورمانه إنشاد UIR 202-123-199	28-12-2023	47
		C1 KP	C2 SU
		C3 OT	DO
		MM	YY
		HH	MM
			23
CODE-1		CODE-2	CODE-3
		CODE-4	CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description:		
من (-6.5) متر from st (202+060) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT: (xyz))

[Signature]

مفتي شوقي الشمراني - القدس

Comments by: General consultant (systra)

- No objection, according to the attached reports and lab. results.

- you must follow specs and design dwg.

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود	[Signature]				
Contractor QA/QC*	XYZ	[Signature]	28-12-2023	1:00	A	
	H.M.C	[Signature]	28-12-2023	1:00	A	
GARB**						
Employers Representative	Ikhaled Ali	[Signature]	23/9/2024		Awe	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company			Designer Company*	DR. Hassan Mahdy (H.M.C)																
Issued by Contractor	Name	Sign	Date	REQ. NUM																
			2-1-2024	49																
Received by Employers Representative			UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			24		
C1	C2	C3	DD	MM	YY	HH	MM													
KP	SU	OT			24															
CODE-1		CODE-2		CODE-3																
				CODE-4																
				CODE-5																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+060 TO 202+120		
	E=260160.9658	E=260156.5571	
	N=3136305.4382	N=3136245.6007	
<u>Inspection description</u> from st (202+060) to st (202+120) طبقة ردم منسوب (-6) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))

Comments by: General consultant (systra)

- No objection, according to the attached reports and lab. results

- you must follow specs and design drawings

INSPECTION RESULT

Approval Status

Please Tick if Not Attend

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمد	وليد محمد			A-AWC-R	
Contractor QA/QC*	XYZ	عبدالله العبدالله	2-1-2024	11:40	A	
	H.M.C	محمد بن علي	2-1-2024	11:50	AWC	
GARB**						
Employers Representative	Khaleed ali	Khaleed ali	23/1/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة المهندسين مهدي للإستشارات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name وليد محمود	Sign 	Date 2-1-2024																
Received by Employers Representative	UIR	REQ NUM 50																	
		<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			24			
C1	C2	C3	DD	MM	YY	HH	MM												
KP	SU	OT			24														
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+960 TO 202+000 E=260166.717 E=260164.6561 N=3136405.271 N=3136365.1247	
<u>Inspection description</u> from st (201+960) to st (202+000) طبقة ردم منسوب (-13.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. (xyz)) 	Comments by: General consultant (systra) -No objection, according to the attached reports and lab. results. -you must follow specs and design dr
---	--

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود					
Contractor QA\QC*	XYZ	عبد الرحمن الشراي	2-1-2024	11:15	A	
	H.M.C	محمود احمد	2-1-2024	11:00	AUC	
GARB**						
Employers Representative	Khaled ali		23/9/2024		AUC	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الشركة العامة للإنشاء



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	[Signature]		6-1-2024	51						
Received by Employers Representative	[Signature]	UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT				20	

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+960 TO 202+000		
	E=260166.717 N=3136405.271	E=260164.6561 N=3136365.3242	
<u>Inspection description</u> from st (201+960) to st (202+000) طبقه ردم منسوب (-13) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: [GARB SURVEY CONSATANT. (xyz)]	Comments by: General consultant (systra)
[Signature]	- No objection, according to the attached reports and lab. results. - you must follow specs and design drag

INSPECTION RESULT

						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time		A-AWC-R	
Contractor Engineer	وليد محمدي	[Signature]					
Contractor QA/QC*	XYZ	عبد الرحمن العرابي	6-1-2024	4:20		A	يرجى إعادة المعايرة قبل العمل
	H.M.C	محمود عولمة	6/1/2023	4:15		AWC	
GARB**							
Employers Representative	Khaled ali	[Signature]	29/9/2024			AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإشراف الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	[Signature]		6-1-2024	52						
Received by Employers Representative	[Stamp]	UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT				24	

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+060 TO 202+120		
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007	
Inspection description/			
من (202+060) to st (202+120) طبقة ردم منسوب (5.5) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))

تم الاستعراض وفقاً للمواصفات
المرفقة مع التقرير.

Comments by: General consultant (systra)

- No objection, according to the attached reports and lab results.
- you must follow spec and design

INSPECTION RESULT

					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	أبو عجيله	[Signature]				
Contractor QA/QC*	XYZ	[Signature]	6-1-2024	5:00	A	
	H.M.C	[Signature]	6/1/2024	4:40	Awc	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024		Anrc	

UNIVERSAL INSPECTION REQUEST



مكتب أ.أ.أ. من مهاي
للإشراف الهندسية



الهيئة العامة للإشراف
على الطرق



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أ.أ.أ. من مهاي للمقاولات العامة 57577	Designer Company*	DR. Hassan Mahdy (H.M.C)						
Issued by Contractor	Name: Sign:	Date	10-1-2024						
Received by Employers Representative	UIR	REQ. NUM	53						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT			28		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120 E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description: من (5- متر from st (202+060) to st (202+120) طبقة ردم منسوب		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate



Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSALTANT. (xyz)) 	Comments by: General consultant (systra) - No objection, according to the attached reports and lab. results. - you must follow specs and design dwg
--	---

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد الحويهد					
Contractor QA/QC*	XYZ	عبد الرحمن العرياني	10-1-2024	12:30	A	
	H.M.C	محمد العرياني	10-1-2024	12:00	A	
GARB**						
Employers Representative	Khaled chi		23/9/2024		Awc	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name:  Sign: 	Date	REQ.NUM
Received by Employers Representative	UIR	10-1-2024	54
		C1 C2 C3 DD MM YY HH MM	
		KP SU OT	23
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+300 TO 202+376	
	E=260139.0278 N=3136066.4661	E=260129.6912 N=3135991.0324
Inspection description/		
from st (202+300) to st (202+376)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time


Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))

Comments by: General consultant (systra)





- levels and coordinates were checked only by xyz and under their own responsibility

- you must follow specs and designing and geo-technical report.

- This work was inspected only by xyz and H.M.C

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمود				A-AWC-R	
Contractor QA/QC*	XYZ		10-1-2024	10:30	A	
	H.M.C		10-1-2024	10:30	AWC	
GARB**						
Employers Representative	Khaled ali		23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date							
			15-1-2024							
Received by Employers Representative		UIR	REQ. NUM							
			55							
		C1	C2	C3	DD	MM	YY	HH	MM	
		KP	SU	OT			20			
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5						

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+300 TO 202+340	
	E=260139.0278	E=260134.2574
	N=3136066.4661	N=3136026.7517
<u>Inspection description/</u> from st (202+300) to st (202+340) تسليم طبقة ردم منسوب (8.5-) متر		


INSPECTION DETAILS The following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT - (xyz))	Comments by: General consultant (systra)
	-you must follow specs and design drug- -you must do leveling and lining -the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	علي محمد					
Contractor QA/QC*	XYZ	عبد الرحمن العزاد	16-1-2024	8:30	A	
	H.M.C	محمود علي	15/1/2024	4:30pm	A	
GARB**						
Employers Representative	Khaled ali		26/1/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أ.إ.ص.ن مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name:  Sign: 	Date	REQ. NUM						
Received by Employers Representative	UIR	15-1-2024	56						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT			24		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description/		
تسليم طبقة ردم منسوب (4) متر from st (202+220) to st (202+300)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	


Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)



-you must follow specs and design by
-you must do leveling and lining
the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود محمد		16-1-2024			
Contractor QA/QC*	XYZ	عبد الرحمن الزمراني	16-1-2024	9:18	A	
	H.M.C	محمد علي	15/1/2024	5:10	A	
GARB**						
Employers Representative	Khaled ali		16/1/2024		AWC	



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name [Signature] Sign [Signature]	Date	REQ.NUM 57															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			24		
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT			24													
CODE-1	CODE-2	CODE-3	CODE-4															
			CODE-5															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description/		
منطقة ردم منسوب (4.5) متر from st (202+060) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT-xyz)	Comments by: General consultant (systra)
 مشروع القمم الكبريتات السريعة - القمم الثاني	- you must follow specs and design durg. - you must do landing and lining the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد عيسى	[Signature]				
Contractor QA\QC*	XYZ	[Signature]	16-1-2024	3:30	A	
	H.M.C	[Signature]	16/1/24	3:00	AWC	
GARB**						
Employers Representative	Khaled ali	[Signature]	16/1/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name: 157537 Sign: وليد خلافة وليد محمود	Date	17-1-2024						
Received by Employers Representative	UIR	REQ.NUM	58						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT	17	1	24	4	00
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300 E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description/ منسوب (3.5-) متر from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (3.5-) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: GARB SURVEY CONSATANT (xyz)	Comments by: General consultant (systra)
تم اكتشاف وجود خلل في التسليم - القيد 15	-you must follow specs and design dng -you must do leveling and lining the compacted side slope & filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليده خلافة وليد محمود					
Contractor QA/QC*	XYZ	عليه الرحمه الهادي	17-1-2024	5:10	A	
	H.M.C	عليه الرحمه الهادي	17/1/2024	4:00	A	
GARB**						
Employers Representative	Khaled Ali		17/1/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أديان مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR. Hassan Mahdy (H.M.C)
Issued by Contractor	Name: 137537 Sign: وليد محمد	Date	REQ. NUM
Received by Employers Representative	UIR	20-1-2024	59
		C1 C2 C3 DO MM YY HH MM	
		KP SU OT	24
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+300 TO 202+360	
	E=260139.0278 N=3136066.4661	E=260131.7531 N=3136006.9091
Inspection description:		
منسوب (8-متر) from st (202+300) to st (202+360) تسليم طبقة ردم منسوب		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: GARB SURVEY CONSATANT. (xyz)	Comments by: General consultant (systra)
مستشار الاستشارات العامة	- you must follow specs and design dwg.
مستشار الاستشارات العامة	- you must do leveling and lining
مستشار الاستشارات العامة	the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	علي محمد	علي محمد	20/1/2024	10:00	A	
Contractor QA/QC*	XYZ	علي محمد	20/1/2024	9:00	A	
	H.M.C	علي محمد				
GARB**						
Employers Representative	Khaled ali	علي محمد	20/1/2024		Amr	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name: <u>علي محمد</u> Sign: <u>علي محمد</u>	Date	REQ.NUM
Received by Employers Representative	UIR	18-1-2024	60
		C1 C2 C3 DD MM YY HH MM	
		KP SU OT	24
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+920 TO 202+000	
	E=260168.4582 N=3136445.233	E=260164.6561 N=3136365.3242
Inspection description:		
منسوب (12.5) متر from st (201+920) to st (202+000)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
تم العمل على الحفر والردم في المنطقة المذكورة في المخطط	- you must follow specs and design drawing - you must do leveling and lining - the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	علي محمد	علي محمد				
Contractor QA/QC*	XYZ	علي محمد	20-1-2024	11:15	A	
	H.M.C	علي محمد	20-1-2024	3:45	A	
GARB**						
Employers Representative	Khaled ali	علي محمد	20/1/2024	Amrc		

UNIVERSAL INSPECTION REQUEST



مكتب أ.د. حسن مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والتقنية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR. Hassan Mahdy (H.M.C)																
Issued by Contractor	Name: Sign:	Date	REQ.NUM																
Received by Employers Representative	UIR	18-1-2024	61																
		<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DO</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>23</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DO	MM	YY	HH	MM	KP	SU	OT			23			
C1	C2	C3	DO	MM	YY	HH	MM												
KP	SU	OT			23														
CODE-1	CODE-2	CODE-3	CODE-4																
			CODE-5																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+020 TO 202+060	
	E=260163.5058 N=3136345.3573	E=260160.9658 N=3136305.4382
Inspection description/		
from st (202+020) to st (202+060) طبقة ردم منسوب (12.5-) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	


Comments by: (GARB SURVEY CONSATANT: xyz)	Comments by: General consultant (systra)
	- you must follow specs and design dw - you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	رليطلاف					
Contractor QA/QC*	XYZ		21-1-2024	5:15	A	
	H.M.C		21-1-2024	5:00	A	
GARB**						
Employers Representative	Ali K		20/9/2024		Awc	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name:  Sign:  Date: 21-1-2024	REQ. NUM	62															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			24		
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT			24													

CODE-1

CODE-2

CODE-3

CODE-4

CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+300 TO 202+376 E=260139.0278 E=260129.6912 N=3136066.4661 N=3135991.0324	
Inspection description: منسوب (7.5) متر from st (202+300) to st (202+376) تسليم طبقة ردم منسوب (7.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time


Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate


Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

	-you must follow specs and design dng -you must do leveling and lining the compacted side slope + filling layer
---	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمود				A-AWC-R	
Contractor QA/QC*	XYZ	عبد الرحمن الابرار	21-1-2024	5:10	A	
	H.M.C	شودا شادي	21-1-2024	5:28	A	
GARB**						
Employers Representative	Khaled ali		21/1/2024		A	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجمية للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name [Signature]	Date	22-1-2024															
Received by Employers Representative	Sign [Signature]	REQ.NUM	63															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>20</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			20		
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT			20													
CODE-1	CODE-2	CODE-3	CODE-4															
CODE-5																		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+920 TO 202+040	
	E=260168.4582 N=3136445.233	E=260162.2757 N=3136325.3952
Inspection description:		
منسوب (12-) متر from st (201+920) to st (202+040)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. (xyz))

Comments by: General consultant (systra)



-you must follow specs and design dwg
-you must do leveling and lining
the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمد	[Signature]				
Contractor QA/QC*	XYZ	عبد الرحمن الخياط	23-1-2024	9:00	A	
	H.M.C	محمود العبدى	22-1-2024	5:15	AWC	
GARB**						
Employers Representative	Khaled	[Signature]	23/1/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	REQ. NUM							
	وليد محمود	وليد علاف	27-1-2024	65							
Received by Employers Representative			UIR	C1	C2	C3	DD	MM	YY	HH	MM
				KP	SU	OT			23		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+875 To 202+376	201+920 TO 202+060		
	E=260168.4582	E=260160.9658	
	N=3136445.233	N=3136305.4382	
Inspection description/			
من 200+875 إلى 202+376 من st (201+920) إلى st (202+060) طبقة ردم منسوب (-11.5) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time


Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)



-you must follow specs and design dng
-you must do leveling and lining
the compacted sideslope of filling layer

INSPECTION RESULT

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد علاف	وليد علاف					
Contractor QA/QC*	XYZ	أحمد محمد	27-1-24	5:00	A		
	H.M.C	محمود محمد	27-1-24	4:15	A		
GARB**							
Employers Representative	Khaled ali		27/1/2024				

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	REQ. NUM							
	رئيس محمور	رئيس هلاف	30-1-2024	66							
Received by Employers Representative			UIR	C1	C2	C3	DD	MM	YY	HH	MM
				KP	SU	OT				24	
CODE-1		CODE-2 ب من لال 1-1		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+300 TO 202+376		
	E=260139.0278	E=260129.6912	
	N=3136066.4661	N=3135991.0324	
<u>Inspection description:</u> from st (202+300) to st (202+376) تسليم طبقة ردم منسوب (6.5) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
	-you must follow specs and design drug -you must do leveling and lining the compacted sube slp & filling layer

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد محمور	وليد هلاف				يتم صيانة القطر قبل التورب	
Contractor QA/QC*	XYZ	محمد رافع	30-1-2024	4:00	(A)		
	H.M.C	محمد منتصر قزوه	30-1-24	12:30	AWC		
GARB**							
Employers Representative	Khated ali		30/1/2024				

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإشراف الهندسية



إشراف هندسي عام
General Consultancy and Supervision



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	وليد محمود	وليد محمود	18-2-2024	68						
Received by Employers Representative	[Stamp]	UIR	C1	C2	C3	DD	MM	YY	HH	MM
			ICP	SU	OT			24		
CODE-3		CODE-2	CODE-3	CODE-4		CODE-5				

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+300 TO 202+376		
	E=260139.0278	E=260129.6912	
	N=3136066.4661	N=3135991.0324	
<u>Inspection description:</u>			
من تسليم طبقة ردم منسوب (6-) متر from st (202+300) to st (202+376)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT - xyz)

تم استلام المخطط (مخطط) من السيد [Signature] - الفد الذي

Comments by: General consultant (systra)

- you must follow specs and design durg
- you must do leveling and lining
the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود	وليد محمود				
Contractor QA/QC*	XYZ	عبد الرحمن الطراوي	19-2-2024	11:30	A	
	H.M.C	محمد منعم فوزي	19-2-2024	12:00	A	
GARB**						
Employers Representative	rehaled ale	[Signature]	19/2/2024		Arre	

UNIVERSAL INSPECTION REQUEST



مكتب أديان مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	وليد محمود	وليد محمود	22-2-2024	69						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT				24	
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+920 TO 202+060		
	E=260168.4582 N=3136445.233	E=260160.9658 N=3136305.4382	
Inspection description/			
من (10.5-) متر طبقة ردم منسوب (201+920) to st (202+060)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))

مستشار الاستشارات العامة
مستشار الاستشارات العامة
مستشار الاستشارات العامة

Comments by: General consultant (systra)

-you must follow specs and design
-you must do leveling and lining
the compacted side slope & filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود	وليد محمود				
Contractor QA/QC*	XYZ	عبد الرحمن الوائلي	24-2-2024	3:30	A	
	H.M.C	محمد منعم فوزي	24-2-2024	11:00	A	
GARB**						
Employers Representative	Khaled ali	كhaled ali	24/2/2024		Amr	

UNIVERSAL INSPECTION REQUEST



مكتب أديسن مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أديسن مهدي للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	وليد طاي و ليلى محمد		23-3-2024	74						
Received by Employers Representative	UIR		C1	C2	C3	DO	MM	YY	HH	MM
			KP	SU	OT			24		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+920 TO 202+060		
	E=260168.4582 N=3136445.233	E=260160.9658 N=3136305.4382	
Inspection description/			
منطقة ردم منسوب (10- متر) from st (201+920) to st (202+060)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
تم اتمام العمل في المنطقة (الطريق) - الخبير السيد - السيد الخبير	- you must follow specs and design drawings - you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد طاي و ليلى محمد						
Contractor QA/QC*	XYZ	محمد مشهور	23-3-2024	12:15	A		
	H.M.C	محمد مشهور	23/3/2024	12:00	A		
GARB**							
Employers Representative	Khaled ali		23/3/2024				

UNIVERSAL INSPECTION REQUEST



مكتب أ.أ.حسن مهدي
للإستشارات الهندسية



الهيئة العامة للإعانة
SHARER



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name: Sign:	Date	REQ. NUM						
Received by Employers Representative	UIR	31-3-2024	75						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT			24		
CODE -1	CODE -2	CODE -3	CODE -4	CODE -5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+920 TO 202+060 E=260168.4582 N=3136445.233	E=260160.9658 N=3136305.4382
Inspection description منطقة ردم منسوب (9.5) متر from st (201+920) to st (202+060)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))

Comments by: General consultant (systra)

تم فحص الموقع والتأكد من وجوده
نموذج شتر كمبراندو التسوية - التفت الذي

-you must follow specs and design data
-you must do leveling and lining
the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود محمد					
Contractor QA/QC*	XYZ عبد الرحمن الطرطوسي		1-4-2024	12:00	A	
	H.M.C	محمود علي	31-3-2024	11:00	A	
GARB**						
Employers Representative	Khakdali		1/4/2024		Done	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name:  Sign:  Date: 1-4-2024	REQ.NUM	76															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			24		
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT			24													
CODE-1	CODE-2	CODE-3	CODE-4															
CODE-5																		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description(		
تسليم طبقة ردم منسوب (3-متر) from st (202+220) to st (202+300)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate




Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))

Comments by: General consultant (systra)

تسليم طبقة الردم منسوب (3-متر) - التسليم
- you must follow specs and design dra
- you must do leveling and lining
the compacted side slope of filling layer

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	أبو عجلة					
Contractor QA/QC*	XYZ		1-4-2024	11:30	A	
	H.M.C		1-4-2024	11:00	A	
GARB**						
Employers Representative	Khaled ali		1/4/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name:  Sign: 	Date	Time
Received by Employers Representative	UIR	1-4-2024	77
		C1 C2 C3 DD MM YY HH MM	
		KP SU OT	24
CODE -1	CODE -2	CODE -3	CODE -4
			CODE -5

EXPLANATION OF WORK TO BE INSPECTED


Area	Element	Item
From 200+876 To 202+376	201+920 TO 202+376	
	E=260168.4582 N=3136445.233	E=260129.6912 N=3135991.0324
Inspection description/		
As-Built for Fill from st (201+920) to st (202+376)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time




Planned Inspection Date	Planned Inspection Time
1/4/2024	

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
	

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer					A-AWC-R	☒
Contractor QA/QC*	XYZ		2-4-2024	9:00	A	☒
	H.M.C		2-4-2024	9:30	A	☒
GARB**						☐
Employers Representative						☐
