

استشاري أبحاث التربة والاماسات :
أ.د.م. هشام محمد حلمي



مشروع :
قطار اسوان الكهربائي السريع - القطاع الثاني

تقرير بنتائج اختبارات صلاحية تربة للتأسيس

مقدمة : تم إعداد هذا التقرير بناءً على طلب شركة / ابو عجيبة

وذلك لتحديد خصائص ومذي صلاحية عينة تراب للاستخدام في / طبقات الردم لجسر القطار الكهربائي

مصدر العينة : عند المحطة / تشويبة يعين المسار 202+220

- الملتصق : وقد تم توريد العينة بمعرفة 1- م/ محمود الحيلي رقم الهاتف = 01030344342

- تنبيه هام : العينة مسنولة من أعضائها

- تاريخ توريد العينة : 2023/11/21

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفلوط)

وقد تم عمل الاختبارات الآتية :

- 1- التخرج الحبيبي
- 2- حد السيولة واللدونة
- 3- اختبار البرونكتور
- 4- اختبار CBR
- 5- اختبار المواد العضوية

وكانت نتائج الاختبارات كالآتي :

م	نوع الاختبار	النتائج	حدود القبول والرفض طبقاً للمواصفات
1	تصنيف العينة	A-1-a	(A-1-a) - (A-1-b) - (A-2-4)
2	نسبة الماء من مغل 200	9.4%	لا تزيد عن (15 %)
3	مجال اللدونة	NP	(A-1-a or A-1-b = 6 max) (A-2-4 = 10 max)
4	أقصى كثافة جافة (البرونكتور) yd max	2.170 gm/cm3	لا تقل عن 1.88 gm/cm3
5	نسبة المياه الأصلية	5.9%	---
6	قيمة CBR المقصورة	49.1%	لا تقل عن 20%
8	المواد العضوية	لا يوجد	لا تزيد عن 1%

= و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للتأسيس عليها



مهندس المعمل

التوقيع

فني المعمل

التوقيع

Coarse & Fine Aggregate Grading - ASTM C136 & AASHTO T27

202+220	الموقع : تشوين يمين الممر	25/11/2023	التاريخ :
---------	---------------------------	------------	-----------

نتائج الاختبار :-

المر %	المحجوز %	وزن المحجوز التراكمي	وزن المحجوز على كل منخل	رقم المنخل (inch)	رقم المنخل (mm)
100%	0%	0	0	5"	127
100.00%	0.00%	0	0	4"	101.6
100.00%	0.00%	0	0	3"	76.2
93.25%	6.75%	790	790	2.5"	63.5
87.67%	12.33%	1443	653	2"	50.8
83.74%	16.26%	1902	459	1.5"	37.5
78.32%	21.68%	2537	635	1"	25
75.21%	24.79%	2900	363	3/4"	19
70.26%	29.74%	3480	580	1/2"	12.7
66.32%	33.68%	3940	460	3/8"	9.5
62.82%	37.18%	4350	410	# 4	4.75
62.82%			7350	المر من منخل # 4	
			11700	وزن العينة الكلي	
			500	وزن عينة القاع	
47.7%	52.3%	120	120	# 10	2.36
25.4%	74.6%	298	178	# 40	0.425
9.4%	90.6%	425	127	# 200	0.075

NP	السيولة و اللدونة
A-1-a	التصنيف

ملاحظات :



Handwritten signature in blue ink.

مهندس المعمول
م
التوقيع

Modified Proctor : ASTM D1557

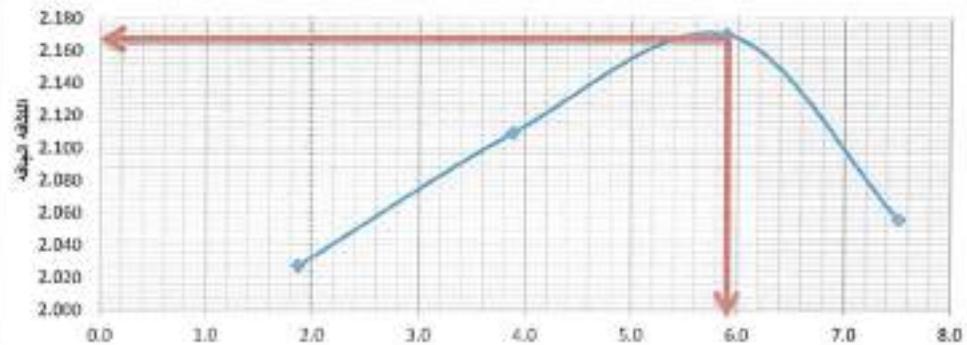
نوع العينة:	عينة محجر
تصنيف العينة:	A-1-a
نتائج الاختبار:	
وزن قالب:	5731
حجم قالب:	2140

المسح كلاله جافه	2.170
المياه الاصليه	5.9

رقم الاختبار	1	2	3	4
وزن القالب + العينة رطبه	10150.0	10420	10648	10460
وزن القالب + العينة جافه	4419.0	4689	4917	4729
الكثافه الرطبه	2.065	2.191	2.298	2.210

رقم الطبقة	1	2	3	4	5	6	7	8
وزن الطبقة	53.9	55.4	54.5	52.7	55.5	55.8	53.2	53.6
وزن الطبقة + العينة رطبه	150.0	150.0	150.0	150.0	150.0	150.0	150.0	150.0
وزن الطبقة + العينة جافه	148	148.5	146	145.8	144.9	144.6	143	143.5
وزن المياه	2.0	1.5	4.0	3.2	5.1	5.4	7.0	6.5
وزن العينة جافه	94.1	93.1	91.5	94.1	89.4	88.8	89.8	89.9
المحتوى المائي %	2.1	1.6	4.4	3.4	5.7	6.1	7.8	7.2
متوسط المحتوى المائي %	1.9	3.9	5.9	7.5				
الكثافه الجافه	2.027	2.109	2.170	2.055				

Modified Proctor Chart



ملاحظات:



مهندس المعمل

التوقيع

فني المعمل

التوقيع

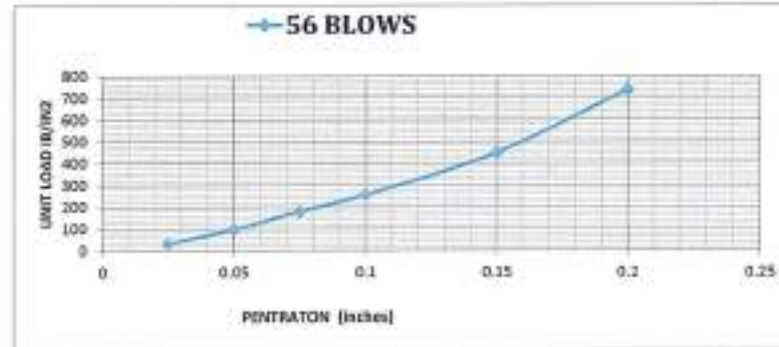
اختبار نسبة تحميل كاليفورنيا (C . B . R) ASTM D1883

A-1-a		تصنيف العينة	
56	عدد الضربات	56	عدد الضربات
10	رقم الجقنة	2131	حجم القالب (سم3)
55.2	وزن الجقنة	5289	وزن القالب (جم)
150	وزن الجقنة +العينة رطبة جم	19120	وزن القالب +وزن العينة رطبة (جم)
144.8	وزن الجقنة +العينة جافة جم	4831	وزن العينة رطبة (جم)
5.2	وزن الماء جم	2.297	كثافة الرطبة (جم/سم3)
89.6	وزن العينة جافة جم	2.143	الغسي كتلة جافة (جم/سم3)
5.8%	المحتوى المائي %	2.170	كثافة البرونكتور (جم/سم3)
		95.7%	نسبة الدمك

نسبة الانتفاش	0.20%	غير قابلة للانتفاش
---------------	-------	--------------------

حساب نسبة تحميل كاليفورنيا

7.62	5.08	3.81	2.54	1.9%	1.27	0.635	الاختراق في بالسم
0.3	0.2	0.15	0.1	0.075	0.05	0.025	الاختراق في بال بوصة
1403	1001	610	349	245	132	44	القراءة kg
3092.327	2207.01128	1343.671	769.1576	539.98	291.966	97.32197674	القراءة بالباوند
1031.243	736.004215	448.0936	256.5022	180.075	97.3661	32.45537791	الحمل lb/in2



49.1%	قيمة C . B . R
-------	----------------

ملاحظات : تم حفر القالب في الماء لمدة 96 ساعة قبل مواصلة المشروع



مهندس المعمل
د. م. م. م.
التوقيع

م. م. م.
التوقيع

استشاري أبحاث التربة والاساسات :
أ.د.م. هشام محمد حلمي



مشروع :
قطار اسوان الكهربائي السريع - القطاع الثاني

تقرير نتائج اختبارات صلاحية أترية للتأسيس

مقدمة : تم إعداد هذا التقرير بناءا على طلب شركة / ابو عجيبة

وذلك لتحديد خصائص ومدي صلاحية عينة تراب للإستخدام في / طبقات الردم لجسر القطار الكهربائي

مصدر العينة : عند المحطة / تشوينة بمين المسار ٢٠٢+٢٢٠

المنسوب: وقد تم توريد العينة بمعرفة ١- م/ محمود الحيتي رقم الهاتف = ٠١٠٣٠٣٤٤٣٤٢

تتبيه هام : العينة مسنولية من أحضرها

تاريخ توريد العينة : ٢٠٢٣/١٢/٢

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفوط)

وقد تم عمل الاختبارات الآتية :

١- التدرج الحبيبي

٢- حد السيولة واللدونة

٣- اختبار البرونكتور

٤- اختبار CBR

٥- اختبار المواد العضوية

وكانت نتائج الاختبارات كالآتي :

م	نوع الاختبار	النتائج	حدود القبول والرفض طبقا للمواصفات
1	تصنيف العينة	A-1-a	(A-1-a) - (A-1-b) - (A-2-4)
2	نسبة الماء من منخل 200	١١.٨%	لا تزيد عن (15 %)
3	مجال اللدونة	NP	(A-1-a or A-1-b = 6 max) (A-2-4 = 10 max)
4	أقصى كثافة جافة (البرونكتور) yd max	2.171 gm/cm3	لا تقل عن 1.88 gm/cm3
5	نسبة العيية الأصولية	6.1%	--
6	قيمة CBR المغمورة	51.1%	لا تقل عن 20%
8	المواد العضوية	لا يوجد	لا تزيد عن 1%

• و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للتأسيس عليها

مهندس المعمل

التوقيع

فني المعمل

التوقيع



Coarse & Fine Aggregate Grading - ASTM C136 & AASHTO T27

الموقع : تشوين يمين المسار 202+220

التاريخ : 12/06/2023

نتائج الاختبار :-

رقم المنخل (mm)	رقم المنخل (inch)	وزن المحجوز على كل منخل	وزن المحجوز التراكمي	المحجوز %	المر %
127	5"	0	0	0%	100%
101.6	4"	0	0	0.00%	100.00%
76.2	3"	0	0	0.00%	100.00%
63.5	2.5"	0	0	0.00%	100.00%
50.8	2"	1425	1425	12.12%	87.88%
37.5	1.5"	475	1900	16.16%	83.84%
25	1"	625	2525	21.47%	78.53%
19	3/4"	475	3000	25.51%	74.49%
12.7	1/2"	485	3485	29.63%	70.37%
9.5	3/8"	475	3960	33.67%	66.33%
4.75	# 4	410	4370	37.16%	62.84%
	المر من منخل # 4	7390			62.84%
	وزن العينة الكلى	11760			
	وزن عينة التاعم	500			
2.36	# 10	118	118	52.0%	48.0%
0.425	# 40	168	286	73.1%	26.9%
0.075	# 200	120	406	88.2%	11.8%

المسبلة و اللدونة	NP
التصنيف	A-1-a

ملاحظات :



Handwritten signature

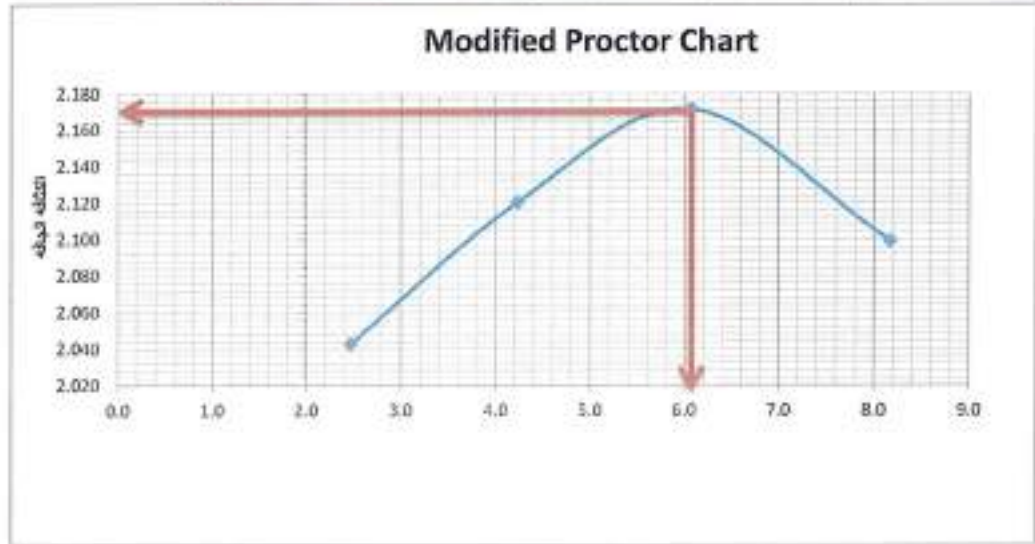
مهندس المعمل
التوقيع

Modified Proctor : ASTM D1557

نوع العينة:	عينة مجهر
تصنيف العينة:	A-1-a
نتائج الاختبار:	
وزن القالب	5731
حجم القالب	2140
الكتلة الجافة	2.171
المياه الامروية	6.1

رقم الاختبار	1	2	3	4
وزن القالب + العينة رطبه	10210.0	10460	10660	10590
وزن التربة الرطبه	4479.0	4729	4929	4859
الكتلة الرطبة	2.093	2.210	2.303	2.271

رقم العينة	1	2	3	4	5	6	7	8
وزن الجفنه	53.9	55.4	54.5	52.7	55.5	55.8	53.2	53.8
وزن الجفنه + العينة رطبه	150.0	150.0	150.0	150.0	150.0	150.0	150.0	150.0
وزن الجفنه + العينة جافه	147.5	147.9	145.5	146.7	144.3	144.9	142.5	142.9
وزن المياه	2.5	2.1	4.5	3.3	5.7	5.1	7.5	7.1
وزن العينة جافه	93.6	92.5	91	94	88.8	89.1	89.3	89.3
المحتوى المائي %	2.7	2.3	4.9	3.5	6.4	5.7	8.4	8.0
متوسط المحتوى المائي %	2.5	4.2	6.1	8.2				
الكتلة الجافه	2.043	2.120	2.171	2.099				



ملاحظات:



بشده ****

مهندس المعمل
التوقيع

فني المعمل
التوقيع

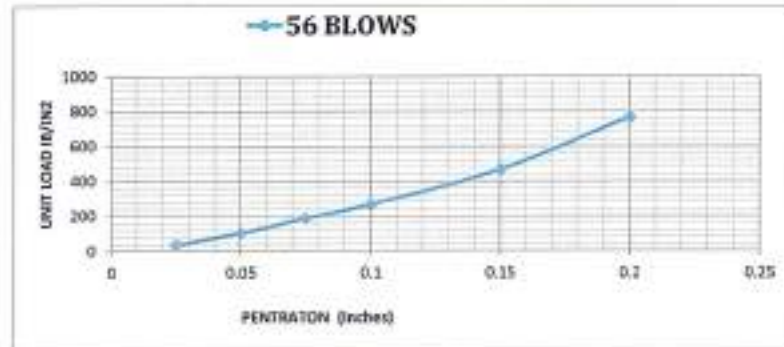
اختبار نسبة تحميل كاليفورنيا (C . B . R) ASTM D1883

A-1-a		تصنيف العينة	
56	عدد الضربات	56	عدد الضربات
30	رقم الجقنة	2131	حجم القالب (سم3)
45.6	وزن الجقنة	5289	وزن القالب (جم)
150	وزن الجقنة + العينة رطبة جم	10115	وزن القالب + وزن العينة رطبة (جم)
144	وزن الجقنة + العينة جافة جم	4826	وزن العينة رطبة (جم)
6	وزن الماء جم	2.265	كثافة الرطبة (جم/سم3)
96.4	وزن العينة جافة جم	2.136	القياس كثافة جافة (جم/سم3)
6.1%	المحتوى المائي %	2.171	كثافة البرونكتور (جم/سم3)
		98.3%	نسبة الدمك

نسبة الانتفاش	0.20%	غير قابلة للانتفاش
---------------	-------	--------------------

حساب نسبة تحمل كاليفورنيا

7.62	5.08	3.81	2.54	1.95	1.27	0.635	الاختراق بالملم
0.3	0.2	0.15	0.1	0.075	0.05	0.025	الاختراق بالبوليمر
1460	1042	635	363	255	138	46	القياس kg
3218.545	2297.09337	1398.515	800.5517	562.02	303.883	101.2943023	بعد المعالجة بالبوليمر
1073.335	766.045203	466.3831	266.9717	187.425	101.34	33.78008721	الحمل lb/in2



51.1%	قيمة C . B . R
-------	----------------

ملاحظات: تم نشر القالب في الماء لمدة 96 ساعة طبقاً لمواصفة المشروع



مهندس العمل
م. م. م. م.
توقيع

المسجل
م. م. م. م.
توقيع

تقرير بنتائج إختبارات صلاحية أترية للتأسيس

مقدمة : تم إعداد هذا التقرير بناءا علي طلب شركة / ابو عجيبة

وذلك لتحديد خصائص ومذي صلاحية عينة تراب للإستخدام في / طبقات الردم لجسر القطار الكهربائي

مصدر العينة : عند المحطة / تشوينة يمين المسار 202+220

المنسوب: وقد تم توريد العينة بمعرفة 1- م/ محمود الحيني رقم الهاتف =01030344342

تنبيه هام : العينة مسنولية من أحضرها

تاريخ توريد العينة : 2023/12/21

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بنى مزار - منفلووط)

وقد تم عمل الإختبارات الآتية :

- 1-التدرج الحبيبي
- 2-حد السيولة واللدونة
- 3-إختبار البروكتور
- 4-إختبار CBR
- 5-إختبار المواد العضوية

وكانت نتائج الإختبارات كالآتي :

م	نوع الإختبار	النتائج	حدود القبول والرفض طبقا للمواصفات
1	تصنيف العينة	A-1-a	(A-1-a) - (A-1-b) - (A-2-4)
2	نسبة المار من ملخل 200	9.4%	لا تزيد عن (15 %)
3	مجال اللدونة	NP	(A-1-a or A-1-b = 6 max) (A-2-4 = 10 max)
4	أقصى كثافة جافة (البروكتور) γ_d max	2.171 gm/cm3	لا تقل عن 1.88 gm/cm3
5	نسبة المياه الأصولية	6.3%	--
6	قيمة CBR المغمورة	49.1%	لا تقل عن 20%
8	المواد العضوية	لا يوجد	لا تزيد عن 1%

• و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للتأسيس عليها



مهندس المعمل
م/أ
التوقيع

فني المعمل
أ/أ
التوقيع

Coarse & Fine Aggregate Grading - ASTM C136 & AASHTO T27

202+220	الموقع : تشوين يمين المسار	25/12/2023	التاريخ :
---------	----------------------------	------------	-----------

لنتائج الاختبار :-

المر %	المحجوز %	وزن المحجوز الترافمي	وزن المحجوز على كل منخل	رقم المنخل (inch)	رقم المنخل (mm)
100%	0%	0	0	5"	127
100.00%	0.00%	0	0	4"	101.6
89.34%	10.66%	1135	1135	3"	76.2
79.44%	20.56%	2190	1055	2.5"	63.5
78.97%	21.03%	2240	50	2"	50.8
74.55%	25.45%	2710	470	1.5"	37.5
71.64%	28.36%	3020	310	1"	25
68.45%	31.55%	3360	340	3/4"	19
64.51%	35.49%	3780	420	1/2"	12.7
56.06%	43.94%	4680	900	3/8"	9.5
47.65%	52.35%	5575	895	# 4	4.75
47.65%			5075	المر من منخل # 4	
			10650	وزن العينة الكلية	
			500	وزن عينة الناعم	
40.5%	59.5%	75	75	# 10	2.36
19.3%	80.7%	298	223	# 40	0.425
9.4%	90.6%	401	103	# 200	0.075

NP	السيولة و اللدونة
A-1-a	التصنيف

ملاحظات :



مهندس

مهندس العمل
م. ك.
التوقيع

Modified Proctor : ASTM D1557

نوع العينة:	عينة محضر
تصنيف العينة:	A-1-a

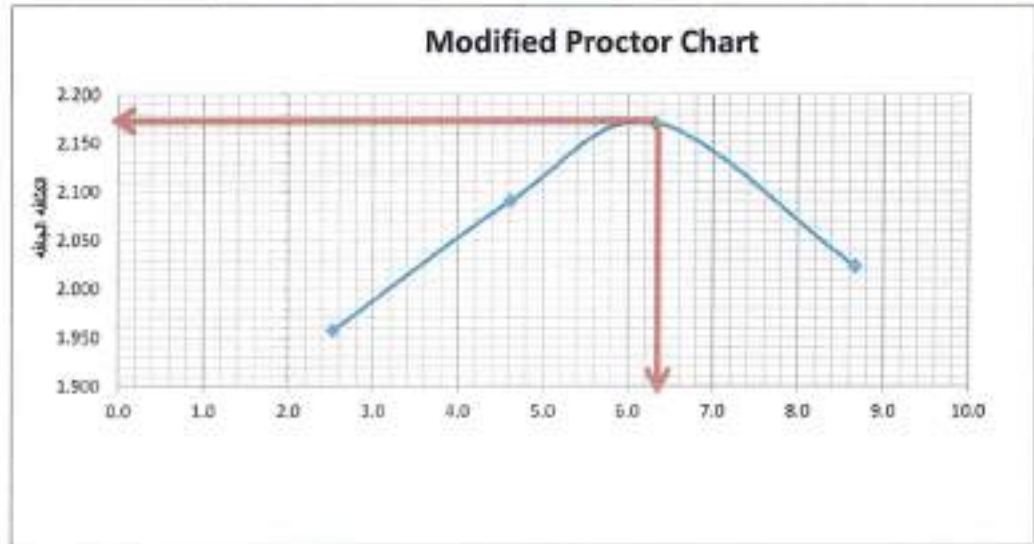
نتائج الاختبار:-

الحد الأقصى لوزن الحبله	2.171
الحد الأدنى لوزن الحبله	6.3

وزن القالب	5731
حجم القالب	2140

رقم الاختبار	1	2	3	4
وزن القالب + العينة رطبه	10025.0	10410	10670	10436
وزن القالب الرطبه	4294.0	4679	4939	4705
الكثافه الرطبه	2.007	2.186	2.308	2.199

رقم الحبله	1	2	3	4	5	6	7	8
وزن الحبله	53.9	55.4	54.5	52.7	55.5	55.8	53.2	53.6
وزن الحبله + العينة رطبه	150.0	150.0	150.0	150.0	150.0	150.0	150.0	150.0
وزن الحبله + العينة جافه	147.3	148	145.6	145.9	144.8	144	142.8	142
وزن الحبله	2.7	2.0	4.4	4.1	5.2	8.0	7.4	8.0
وزن الحبله جافه	93.4	92.6	91.1	93.2	89.3	88.2	89.4	88.4
المستوى المائي %	2.9	2.2	4.8	4.4	5.8	8.8	8.3	9.0
متوسط المستوى المائي %	2.5	4.6	6.3	8.7				
الكثافه الجافه	1.957	2.090	2.171	2.023				



ملاحظات:



مختبر

مهندس المعمل
توقيع

فني المعمل
التوقيع

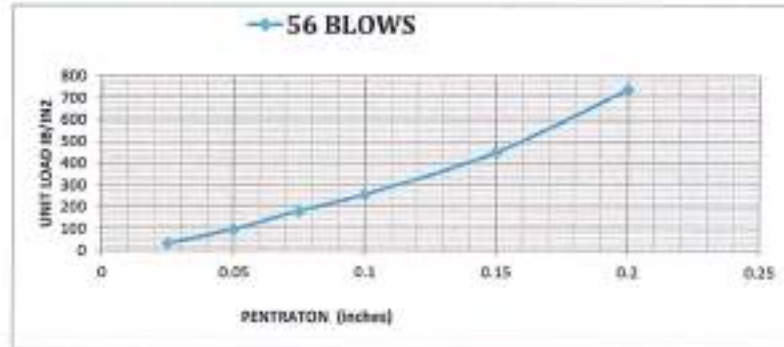
اختبار نسبة تحميل كاليفورنيا (C . B . R) ASTM D1883

A-1-a		تصنيف العينة	
66	عدد الضربات	66	عدد الضربات
f	رقم البقعة	2131	حجم القالب (سم3)
33.7	وزن البقعة	6269	وزن القالب (جم)
150	وزن البقعة + العينة رطبة جم	10136	وزن القالب + وزن العينة رطبة (جم)
143.1	وزن البقعة + العينة جافة جم	4847	وزن العينة رطبة (جم)
6.9	وزن الماء جم	2.275	الكثافة الرطبة (جم/سم3)
109.4	وزن العينة جافة جم	2.140	الكتلة الجافة (جم/سم3)
6.3%	المحتوى المائي %	2.171	كثافة البرونز (جم/سم3)
		98.6%	نسبة الدمك

نسبة الانتفاش	0.20%	غير قابلة للانتفاش
---------------	-------	--------------------

حساب نسبة تحمل كاليفورنيا

7.62	5.08	3.81	2.54	1.95	1.27	0.635	الاختراق بالملم
0.3	0.2	0.15	0.1	0.075	0.05	0.025	الاختراق بالقبو صه
1403	1001	610	349	245	132	44	التراد كج
3092.327	2207.01128	1343.671	769.1576	539.98	291.966	97.32197674	التراد بالباوند
1031.243	736.004215	448.0936	256.5022	180.075	97.3661	32.45537791	المسل IB/IN2



49.1%	قيمة " C . B . R "
-------	--------------------

ملاحظات : تم اختبار القالب في الماء لمدة 96 ساعة طبقاً لوصفية المشروع



مهندس العمل
التوقيع

لمس العمل
التوقيع



التاريخ : 2024-9-22

اسم المشروع : مشروع القطار الكهربائي السريع قطاع (أكتوبر - أبو سمبل)
الموضوع : اعتماد الهيئة العامة للطرق والكبارى لطلبات استلام الأعمال الخاصة بالمشروع
الشركة المنفذة : ابوعجيلة للمقاولات العامة والتوريدات العمومية في المسافة
من (200+876) الى (202+376) بطول 1.5 كم.

عقد رقم : - (2023-2022-1968) بتاريخ 2023-5-17

- (2023-2023-142) بتاريخ 2023-8-3

- (2023-2023-143) بتاريخ 2023-8-3

- (2023-2023-499) بتاريخ 2023-10-12

- (2023-2023-1021) بتاريخ 2024-1-18

- (2023-2023-1229) بتاريخ 2024-2-26

- (2024-2024-209) بتاريخ 2024-8-21

تم الإطلاع ظاهريا على طلبات الفحص الخاصة بالمشروع المذكور عاليه والمرفقة بمستخلصات
المذكورة عالية لعدد (77) طلبات فحص وذلك بعد مراجعتها وتوقيعها من استشارى المساحة (XYZ)
واستشارى ضبط الجودة (مكتب أ.د حسن مهدي) وعليه تم اعتمادها

وتنقسم الى :

- (53) طلبات فحص لأعمال الردم .
- (14) طلبات فحص لأعمال الحفر .
- (4) طلبات فحص لأعمال التطهير .

عن الاستشاري (أ.د حسن مهدي)
مشاريع القطار السريع

مهندس الاستشاري
أ.د حسن مهدي

يعتمد،،،

مهندس الهيئة العامة للطرق والكبارى

مهندس الهيئة العامة للطرق والكبارى

أعمال الجسر الترابي لمسار القطار الكهربائي السريع الخط الثاني (الفيوم / بني سويف - أبو سمبل) (مرحلة الجسور والتأسيس والأساس) القطاع الثاني (بني مزار / منفلووط) أعمال قطع للقطاع لتنفيذ المسافة من ٢٠٠+٨٥٠ إلى ٢٠٢+٣٥٠

البرنامج الزمني

تاريخ نهو الاعمال ٢٠٢٥/٤/٢٥

مدة تنفيذ العمل ٨ شهور

تاريخ استلام الموقع ٢٠٢٤/٨/٢٦

رقم البند	بيان الاعمال	الوحدة	الكمية	أغسطس-٢٠٢٤	سبتمبر-٢٠٢٤	أكتوبر-٢٠٢٤	نوفمبر-٢٠٢٤	ديسمبر-٢٠٢٤	يناير-٢٠٢٥	فبراير-٢٠٢٥	مارس-٢٠٢٥	أبريل-٢٠٢٥
١	أعمال تطهير											
٢-١	بالعدد إزالة لشجار من مسار الطريق و التخلص منها على الا يقل قطر الشجرة عن ٣٠ سم وإزالة الجنود بالكامل و نقلها خارج الموقع طبقا لتعليمات المهندس المشرف	بالعدد	٢,٥٣٩,٠	٨٤٦,٣٣	٨٤٦,٣٣	٨٤٦,٣٣						
٢	أعمال الحفر											
٤-٢	بالمتر المكعب اعمال حفر بالمعدات الميكانيكية في تربة صخرية ومحمل على البند الاتي ١- تحميل ونقل ناتج الحفر لمسافة لا تقل عن ٥٠٠ متر ٢ - ارنكة العيول الجاتية باستخدام المعدات الميكانيكية ٣- توريد اترية مطابقة للمواصفات وتشغيلها باستخدام الات السوية بسمك لا يزيد عن ٢٥ سم لاستكمال المنسوب التصميمي لتشكيل الجسر والاكتاف (نسبة تحمل كاليفورنيا حتى ١٠ %) ورشها بالمياه الاصولية للوصول الى نسبة الرطوبة المطلوبة والدمك الجيد بالهراسات للوصول الى أقصى كثافة جافة (95% من الكثافة الجافة القصوى). ويتم التنفيذ طبقاً للمناسيب التصميمية والقطاعات العرضية النموذجية والرسومات التفصيلية المعتمدة والبند بجمع مستملات طبقاً لاصول الصناعة ومواصفات الهيئة العامة للطرق والكباري وتعليمات المهندس المشرف. - علاوة ١ جنيه/كم لمسافة نقل ناتج الحفر وتصيح ١,١ جنيه/كم ابتداء من ٢٠٢٢/٥/٤.	م³										
١-٤-٢	ذات اجهاد (٢٠٠-٢٠٠) كجم/سم² لمسافة نقل حتى ٥٠٠ متر ابتداء من ٢٠٢٤/٣/٢٢	م³	٤,١٨٢,٠	١,٣٩٤,٠٠	١,٣٩٤,٠٠	١,٣٩٤,٠٠						
٢-٤-٢	ذات اجهاد (٤٠٠-٤٠٠) كجم/سم² لمسافة نقل حتى ٥٠٠ متر ابتداء من ٢٠٢٤/٣/٢٢	م³	٤,٠٤٠,٠	١,٣٤٦,٦٧	١,٣٤٦,٦٧	١,٣٤٦,٦٧						
٣-٤-٢	ذات اجهاد (٥٠٠-٥٠٠) كجم/سم² لمسافة نقل حتى ٥٠٠ متر ابتداء من ٢٠٢٤/٣/٢٢	م³	٩,٠٠٠,٠	٣,٠٠٠,٠٠	٣,٠٠٠,٠٠	٣,٠٠٠,٠٠						
٤-٤-٢	ذات اجهاد (٦٠٠-٦٠٠) كجم/سم² لمسافة نقل حتى ٥٠٠ متر ابتداء من ٢٠٢٤/٣/٢٢	م³	١٨,٦٢٠,٠	٦,٢٠٦,٦٧	٦,٢٠٦,٦٧	٦,٢٠٦,٦٧						
٥-٤-٢	ذات اجهاد (٧٠٠-٧٠٠) كجم/سم² لمسافة نقل حتى ٥٠٠ متر ابتداء من ٢٠٢٤/٣/٢٢	م³	٤,٥٦٠,٠	١,٥٢٠,٠٠	١,٥٢٠,٠٠	١,٥٢٠,٠٠						

مهندس الشركة المنفذة



م / احمد فتح

التوقيع /

عن الاستشاري أ.د حسن مهدي

م / محمد عفيف
التوقيع

م / احمد عزب

التوقيع

يعتمد؟؟؟

مهندس الهيئة العامة للطرق والكباري

التوقيع

البرنامج الزمني

أعمال الجسر الترابي لمسار القطار الكهربائي السريع الخط الثاني (الفيوم / بني سويف - أبو سمبل) (مرحلة الجسور والتأسيس والأساس) القطاع الثاني (بني مزار / متفوط) أعمال قطع للقطاع لتنفيذ المسافة من ٨٥٠+٢٠٠ إلى ٣٥٠+٢٠٢

من المحطة ٨٥٠+٢٠٠ إلى المحطة ٣٥٠+٢٠٢ بطول ١,٥ كم رقم العقد (٢٠٢٥/٢٠٢٤/٢٠٩)

تاريخ استلام الموقع ٢٠٢٤/٨/٢٦

مدة تنفيذ العملية ٨ شهور

تاريخ نهو الاعمال ٢٠٢٥/٤/٢٥

رقم البند	بيان الاعمال	الوحدة	الكمية	أغسطس-٢٠٢٤	سبتمبر-٢٠٢٤	أكتوبر-٢٠٢٤	نوفمبر-٢٠٢٤	ديسمبر-٢٠٢٤	يناير-٢٠٢٥	فبراير-٢٠٢٥	مارس-٢٠٢٥	أبريل-٢٠٢٥
٥-٢	بالمتر المكعب اعمال حفر باستخدام المعدات الميكانيكية في السفو وتسوية السطح بالآلات التسوية والرش بالمياه الاصلية للوصول الى نسبة الرطوبة المطلوبة والدمك الجيد بالهراسات للوصول الى أقصى كثافة جافة (٩٥% من الكثافة الجافة القصوى) ومحمل على البند تحميل ونقل الأتربة الزائدة لمسافة ١,٥ كم من محور الطريق والقناة تشمل استخدام المياه في تثبيت السفو واعداد مدقات على السفو لحركة المعدات ويتم التنفيذ طبقاً للمناسيب التصميمية والقطاعات العرضية النموذجية والرسومات التفصيلية المعتمدة والبند بجميع مشتملاته طبقاً لأصول الصناعة ومواصفات الهيئة العامة للطرق والكباري وتعليمات المهندس المشرف علاوة ١ جنية / كم لمسافة نقل ناتج الحفر وتصبح ١,١ جنية / كم ابتداءً من ٢٠٢٣/٥/٤.	م٣	٧٣,١٣١,٠									
٣	أعمال الردم											
١-٣	أعمال تحميل وتوريد ونقل أتربة مطابقة للمواصفات ولشغلها باستخدام آلات التسوية بسماك لا يزيد عن ٥٠ سم حتى مسلوب (2٠ متر) أسفل مسلوب الفرمة و بسماك لا يزيد عن ٢٥ سم اعلى من مسلوب (2٠ متر) من مسلوب الفرمة لاستكمال المنسوب التصميمي لتشكيل الجسر والاكتاف (نسبة تحمل كاليفورنيا لا تقل عن ١٥%) ورشها بالمياه الاصلية للوصول الى نسبة الرطوبة المطلوبة والدمك الجيد بالهراسات للوصول الى أقصى كثافة جافة (95% من الكثافة الجافة القصوى) ويتم التنفيذ طبقاً للمناسيب التصميمية والقطاعات العرضية النموذجية والرسومات التفصيلية المعتمدة والبند بجميع مشتملاته طبقاً لأصول الصناعة ومواصفات الهيئة العامة للطرق والكباري وتعليمات المهندس المشرف.	م٣										
١-٣-١	- في حالة طلب جهاز الإشراف زيادة نسبة الدمك عن ٩٥% بحسب زيادة ١ جنية على زيادة نسبة الدمك لكل ١%.											
١-٣-٢	- مسافة النقل حتى ٢ كم ويتم احتساب علاوة ١,٤ جنية لكل كم بالزيادة او التقصير وتصبح ١,٥ جنية لكل كم اعتباراً من ٢٠٢٣/٥/٤.											
١-٣-٣	- السعر يشمل عمل تشوينات و تخليط واختبارات ونقل لموقع العمل حتي مسافة ٢ كم.											
١-٣-٤	- والبند لا يشمل القيمة المحجرة.											
١-٣-١	نفس بند رقم (١-٣) في شهر سبتمبر ٢٠٢٣	م٣	٥,٤٤١,٠									
١-٣-٤	نفس بند رقم (١-٣) ابتداء من ٢٠٢٤/٣/٢٢	م٣	٩,٦٦٩,٠									

مهندس الشركة المنقذة

م / احمد فتوح

التوقيع /



عن الاستشاري أ.د حسن مهدي

م / احمد عزب

التوقيع /

م / محمود غريب
التوقيع /

يعتمد:

مهندس الهيئة العامة للطرق والكباري

التوقيع /

بيان المعدات

التاريخ : ٢٠٢٤-٩-٢٢

اسم المشروع : مشروع القطار السريع (أكتوبر-أوسمبل)
المسافة من كم ٢٠٠+٨٥٠ وحتى كم ٢٠٢+٣٥٠ بطول ١,٥ كم

بالإشارة الى العقد المبرم بين الهيئة العامة للطرق والكباري وشركة أبوعحيلة للمقاولات العامة
رقم (٢٠٢٥/٢٠٢٤/٢٠٩) بتاريخ ٢٠٢٤-٨-٢١
لتنفيذ المشروع عاليه بالمعدات الآتية :

المعدة	العدد	تاريخ الصنع
حفار	3	2009
		2005
لودر	4	2010
		2001
عربية قلاب	4	2015
	5	2008
	2	2005
بلدوزر	1	2000
تانك مياة	1	2015
جريد	1	2003
هراس	2	2002

عن الاستشاري أ.د حسن مهدي

م/محمود عريب

م/ احمد عريب

التوقيع

يعتمد!!!
مهندس الهيئة العامة للطرق والكباري

لدى الشركة المتفذة

احمد فتوح

يوقع / المصنف





هيكل تنظيمي للعاملين بمشروع القطار السريع شركة أبوعجيلة للمقاولات العامة

التاريخ : ٢٠٢٢-٩-٢٤

اسم المشروع : مشروع القطار السريع (أكتوبر-أوسمبل)

رقم العقد: (٢٠٢٥/٢٠٢٤/٢٠٩)

مستسل	الاسم	الوظيفة	عدد سنوات الخبرة	رقم التليفون
1	محمد حامد يحي	مدير المشروع	10	01009742637
2	احمد احمد محمود	مدير المكتب الفني	5	01017199596
3	نادي عادل	مدير ضبط الجودة	5	01019930593
4	ربيع نوحيد	مدير السلامة الوقائية	10	01114562154
5	وليد محمود محمد	مهندس التنفيذ	5	01090254469
6	محمد عماد الدين محمد	مهندس صيانة (ميكانيكا وكهرباء)	5	01559856322
7	احمد قاسم	مهندس التخطيط والبرمجة الزمنية	5	01223691236
8	احمد السيد احمد	مراقب تنفيذ (فني مواد)	5	01002612002
	محمد نادي			01063768307
9	عبدالعال رجب	حساب كميات	5	01029734478
10	حسين محمد جبريل	مساح	7	01064950832
	محمد جمال		7	01033806848
11	محمد ابوغنيمه	فني سلامة مرورية	5	01092355765
	محمد حسين		5	01022245866

مهندس الشركة المنفذة

م / احمد فتوح

التوقيع /

عن الاستشاري أ.د حسن مهدي

م / احمد عزب

م / محمود عزب

التوقيع /

التوقيع /

يعتمد!!!

مهندس الهيئة العامة للطرق والكباري



مهندس الشركة المنفذة
 زكية محمود

001-101-113

مهندس الشركة المنفذة
وليد محمد محمد

أحمد هادي

محضر استلام موقع

مشروع إنشاء خط القطار الكهربائي السريع (أكتوبر - أبو سمبل) من الكم 200+850 حتى الكم 202+350 بطول 1.5 كم
تنفيذ شركة أبو عجيبة للمقاولات العامة والتوريدات العمومية.

انه في يوم الاثنين الموافق 26 / 8 / 2024 وبناء على عقد العملية رقم 209 / 2024 / 2025

اجتمعت اللجنة المشكلة من السادة الاتي اسماؤهم بعد وهم :-

عن الهيئة العامة للطرق والكباري (طرف اول)

مدير عام المشروعات
مهندس الإشراف بالمنطقة السادسة
مدير المشروع
ممثل الاستشاري (مكتب أ.د/حسن مهدي)
استشاري المساحة (XYZ)

- 1- السيد المهندس / مصطفى شعبان البدري
 - 2- السيد المهندس / محمود حسين
 - 3- السيد المهندس / محمود غريب
 - 4- السيد المهندس / احمد عزب
 - 5- السيد المهندس / محمد عبدالرحمن
- عن الشركة المنفذة (طرف ثاني)


مهندس عن الشركة المنفذة

1- السيد المهندس / احمد قتيح

وقد قامت اللجنة بالانتقال علي الطبيعة للموقع عالية بالمعاينة الظاهرية علي المبيعة قام الطرف الاول بتسليم الطرف الثاني الموقع خاليا من العوائق الظاهرية ولا مانع من استلام الموقع والبدء في الاعمال ويحضر تاريخ 26 / 8 / 2024 هو تاريخ استلام الموقع .

وقفل المحضر علي ذلك .

اللجنة من الهيئة (طرف اول)

- 5- 
- 4- 
- 3- 
- 2- 
- 1- 

مشروع القطار السريع
السيد / محمد شعبان البدري

الشركة المنفذة (طرف ثاني)

1- 

19788 م ت

ABUAGLA

بجس 199-161-009

رئيس الإدارة المركزية للمنطقة
السادسة بني سويف
مهندس / طارق الجزار

محضر معاينة مسافة نقل توريد تربة صالحة من محجر (أبو هشيمة)

مشروع القطار السريع (6 أكتوبر / أبو سمبل)
القطاع الثاني بطول 158 كم من 176+700 كم الى 334+800
تنفيذ شركة : أبو عجيبة للمقاولات العامة بطول 1.5 كم
من كم 200+876 الى كم 202+376

بالإشارة الى التكاليف الصادر من الهيئة العامة للطرق والكباري لصالح شركة أبو عجيبة
للمقاولات العامة و التوريدات العمومية بشأن تنفيذ الجسر الترابي والأعمال الصناعية
بمشروع القطار الكهربائي السريع (أكتوبر - أسوان) في المسافة الكيلومترية 200+876
الى العلامة الكيلومترية 202+ 376

بناءً على تعليمات السيد المهندس / رئيس قطاع التنفيذ والمناطق بالتوريد من محاجر
خارجية مرخصة بصفة مؤقتة لحين اعتماد وترخيص محاجر اخرى اقرب للقطاع

فقد اجتمعت اللجنة يوم الاثنين الموافق 2023/8/28 قامت اللجنة المشكلة من :-

- مهندس الاشراف بالهيئة
مدير المشروع
مهندس المكتب الاستشاري (X,Y,Z)
مدير المشروع شركة أبو عجيبة للمقاولات المتكاملة والتوريدات
- (1) السيد المهندس / محمد السيد شعبان
(2) السيد المهندس / حاتم مهران
(3) السيد المهندس / محمد عبدالرحمن سالم
(4) السيد المهندس / محمد حامد أبو عجيبة
- وقامت اللجنة بالذهاب الى مكان محجر (أبو هشيمة) حيث وجد ان المسافة من القطاع (من محطة 200+876 حتى
202+376) حتى مكان المحجر (49 كم) وذلك بسبب تعذر وجود محجر قريب على ان يتم التوريد بعد عمل اختبارات
الصلاحية اللازمة والتأكد من صلاحية مواد المحجر للتوريد .

Easting	Northing	Longitude (E)	Latitude (N)	Station	الشركة	من
260126.0446	3137487.7094	30° 33' 10.74 "	28° 20' 30.11 "	200+876	أبو عجيبة	البداية
260129.6907	3135991.0284	30° 33' 11.98 "	28° 19' 41.52 "	202+376	أبو عجيبة	النهاية
270048.623	3178136.045	30° 38' 45.6 "	28° 42' 36.3 "	-	محجر	أبو هشيمة

-هذا المحضر اعتماد مؤقت لحين اعتماد محجر بجوار القطاع ، ولا يعد إثبات لتوريد أية كميات من المحجر المذكور ، ويجب
على إستشاري ضبط الجودة متابعة وحصر أي كميات يتم توريدها من المحجر المذكور ومتابعة صلاحية المحجر بصفة دورية
مستمرة ومقارنتها بصلاحية المواد المثبوتة لتوريدها على القطاع .

واقفل المحضر على ذلك ؟؟؟

مدير المشروع
د.م/حاتم مهران

استشاري المساحة (X,Y,Z)
م/محمد عبدالرحمن سالم

عن الشركة المنفذة
م/محمد حامد أبو عجيبة

مهندس الهيئة العامة للطرق والكباري
يعتمد...

نسخة ختم أكتوبر 2023





مكتب أ.د/حسن مهدي
للإستشارات الهندسية

SYSTRA



مشروع القطار السريع (6 أكتوبر / أبو سمبل)
القطاع الثاني بطول 158 كم من 176+700 كم الى 334+800
تنفيذ شركة : أبو عجيبة للمقاولات العامة بطول 1.5 كم
من كم 200+876 الى كم 202+376

محضر إجمال

اسم الشركة : أبو عجيبة للمقاولات العامة والتوريدات العمومية

القطاع: (201+920) الى (202+376)

أنه في يوم الثلاثاء الموافق 26 / 9 / 2023 قامت اللجنة المكونة من السادة :-

- 1- السيد المهندس/ حاتم مهران
- 2- السيد المهندس/ محمود عبدالرحيم الحيني
- 3- السيد المهندس/ محمد حامد أبو عجيبة

قامت اللجنة بالمعاينة الظاهرية وأخذ عينات وإجراء اختبارات صلاحية للقطاع
من (201+920) احداثي (260168.4582E, 3136445.233N) الى (202+376) احداثي
(260129.6912E, 3135991.0324N) وطبقاً لنتيجة العينة المرفقة تبين أن التربة غير صالحة

للتأسيس (سفو) ويلزم إزالتها وذلك حسب توصيات استشاري التربة وتوصيات سيفكون جروب .

ملحوظات : ...
التوقيع : ...

لجنة
مجلس
مجلس

عن مكتب أ.د/حسن مهدي
مدير المشروع
م. محمود علي

عن الشركة المنفذة
م. محمد علي

استشاري أبحاث التربة والاساسات :
أ.د.م. هشام محمد حلمي



مشروع :
قطار اسوان الكهربائي السريع - القطاع الثاني

تقرير بنتائج اختبارات صلاحية اترية للتأسيس

مقدمة : تم إعداد هذا التقرير بناءا على طلب شركة / ابو عجيله

وذلك لتحديد خصائص ومدي صلاحية عينة تراب للإستخدام في / طبقات الردم لجسر القطار الكهربائي

مصدر العينة : عند المحطة / 202+280 عينة ارض طبيعيه

- المنذوبين : وقد تم توريد العينة بمعرفة م/ محمود الحيني . بتاريخ : 2023/8/21

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفلوط)

- التوصيف الظاهري للعينة : كتبان رملية ناعمة (ملو)

- تنبيه العينة مستوية من احضرها

وقد تم عمل الاختبارات الآتية :

- 1-التدرج الحبيبي
- 2-حد السيولة واللدونة
- 3-إختبار البروكتور
- 4-إختبار CBR
- 5-إختبار المواد العضوية

وكانت نتائج الاختبارات كالآتي :

م	نوع الإختبار	النتائج
1	تصنيف العينة	A-3
2	نسبة العار من منخل 200	2.6 %
3	مجال اللدونة	عديمة اللدونة
4	أقصى كثافة جافة (البروكتور) $\gamma_d \max$	1.871 gm/cm3
5	نسبة للماء الأمولية	9.7%
6	قيمة CBR المغمورة	8.4%
8	المواد العضوية	لا يوجد

• و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي غير صالحة للتأسيس عليها



احمد حبيب
مهندس

مهندس المعمل
م/ محمد البنا
التوقيع

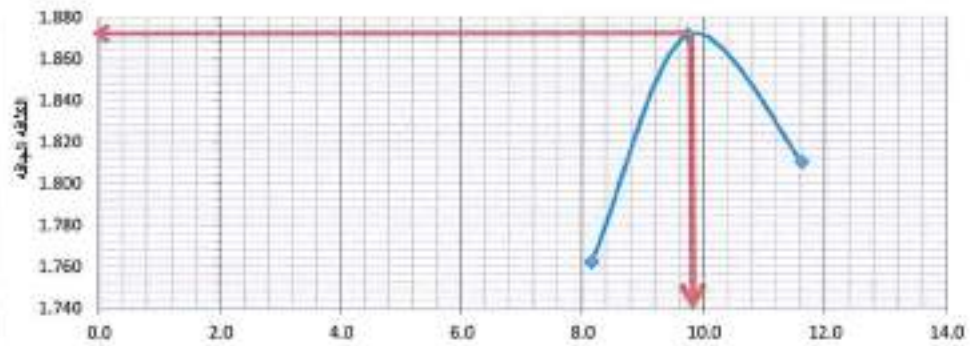
Modified Proctor : ASTM D1557

نوع العينة:	عينة كاشان رملية
تصنيف العينة:	A-3
نتائج الاختبار:	
وزن القالب:	5731
حجم القالب:	2140
القيمة الجافة جافه:	1.871
البيانات الاصوليه:	9.7

رقم الاختبار	1	2	3
وزن القالب + العينة رطبه	9810.0	10126	10055
وزن القالب + العينة جافه	4079.0	4396	4324
الوزن الجافه	1.906	2.054	2.021

رقم الجافه	1	2	3	4	5	6
وزن الجافه	53.85	55.31	54.35	54.15	55.14	53.4
وزن الجافه + العينة رطبه	150.0	150.0	150.0	150.0	150.0	150.0
وزن الجافه + العينة جافه	142.5	143.1	141.6	141.4	140.2	139.87
وزن العياد	7.5	6.9	8.4	8.6	9.8	10.1
وزن العينة جافه	88.65	87.79	87.25	87.25	85.06	86.47
المحتوى المائي %	8.5	7.9	9.6	9.9	11.5	11.7
متوسط المحتوى المائي %	8.2	9.7	11.6			
الوزن الجافه	1.762	1.871	1.810			

Modified Proctor Chart



ملاحظات :



احمد محمد علي
مهندس

مهندس المعمل
د. محمد علي محمد البنا
التوقيع :

Coarse & Fine Aggregate Grading - ASTM C136 & AASHTO T27

التاريخ :	25-08-23	الموقع : St 202+280	ارض طبيعيه
-----------	----------	---------------------	------------

نتائج الاختبار :-

رقم المنخل (mm)	رقم المنخل (inch)	وزن المحجوز على كل منخل	وزن المحجوز التراكمي	المحجوز %	المر %
127	5"	0	0	0%	100%
101.6	4"	0	0	0.00%	100.00%
76.2	3"	0	0	0.00%	100.00%
63.5	2.5"	0	0	0.00%	100.00%
50.8	2"	0	0	0.00%	100.00%
37.5	1.5"	0	0	0.00%	100.00%
25	1"	0	0	0.00%	100.00%
19	3/4"	0	0	0.00%	100.00%
12.7	1/2"	0	0	0.00%	100.00%
9.5	3/8"	0	0	0.00%	100.00%
4.75	# 4	0	0	0.00%	100.00%
	المر من منخل # 4	500			100.00%
	وزن العينة الكلي	500			
	وزن عينة الناعم	500			
2.36	# 10	0	0	0.0%	100.0%
0.425	# 40	51	51	10.2%	89.8%
0.075	# 200	436	487	97.4%	2.6%
السيولة و اللدونة		N.P			
التصنيف		A-3			

ملاحظات : توصيف العينة : كثبان رملية ناعمة (Sand Dunes)



المهندس
المختبر

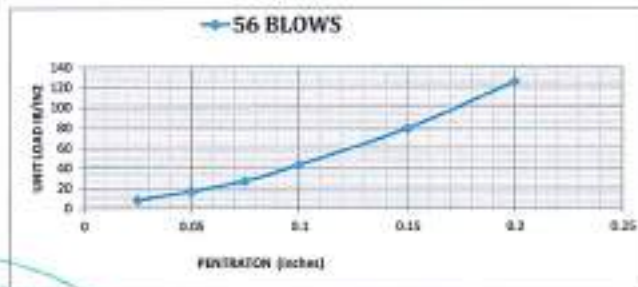
مهندس العمل
المختبر
التوقيع

اختبار نسبة تحميل كاتيلورتيا (C . B . R) ASTM D1883

A-3		تصنيف العينة	
56	عدد الضربات	56	عدد الضربات
2	رقم البقعة	2131	مجم الغالب (سم)
54.3	وزن البقعة	5289	وزن البقعة (جم)
150	وزن البقعة +العينة رطبة جم	9682	وزن الغالب +وزن العينة رطبة (جم)
141.3	وزن البقعة +العينة جافة جم	4313	وزن البقعة رطبة (جم)
8.5	وزن الماء جم	2.024	الترسيب (متر) (سم)
87.8	وزن العينة جافة جم	1.044	نسبة الماء جافة (جم/سم)
9.7%	المحتوى المائي %	1.071	ثقل البقايا (جم/سم)
		96.6%	نسبة التماسك
	غير قابلة للتفتت	0.00%	نسبة التفتت

حساب نسبة تحميل كاتيلورتيا

7.62	5.08	3.81	2.54	1.95	1.27	0.635	الأحجار الخشنة
0.3	0.2	0.15	0.1	0.075	0.05	0.025	الأحجار الخشنة
258.0	171	108.0	59.0	37.0	23.0	11.0	الترسيب (سم)
568.632	376.884	238.032	130.036	81.548	50.692	24.244	الترسيب بالمتر
189.63	125.685	79.38	43.365	27.195	16.905	8.085	الترسيب (سم)



8.4%

قيمة C . B . R

ملاحظات : تم إجراء اختبار في تمام الساعة 95 ساعة قبل المرافعة المشروع



احمد صديقه

مهندس المحسن
مهندس محمد البنا

مشروع :
قطار اسوان الكهربائي السريع - القطاع الثاني

استشاري أبحاث التربة والاساسات :
أ.د.م. هشام محمد حلمي



تقرير بنتائج اختبارات صلاحية أترية للتأسيس

مقدمة : تم إعداد هذا التقرير بناءً على طلب شركة / ابو عجيله

وذلك لتحديد خصائص ومدى صلاحية عينة تراب للإستخدام في / طبقات الردم لجسر القطاع الكهربائي

مصدر العينة : عند المحطة / 202+020 عينه ارض طبيعيه

- المندوب : وقد تم توريد العينة بمعرفة م/ محمود الحيني . بتاريخ : 2023/9/21

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفلووط)

- التوصيف الظاهري للعينة : كتبان رملية ناعمة (مغو)

- تبييه العينة مسئولية من احضرها

وقد تم عمل الاختبارات الآتية :

- 1-النترج الحبيبي
- 2-حد السيولة واللونة
- 3-إختبار البروكتور
- 4-إختبار CBR
- 5-إختبار المواد العضوية

وكانت نتائج الاختبارات كالآتي :

م	نوع الإختبار	النتائج
1	تصنيف العينة	A-3
2	نسبة الماء من مخلل 200	4 %
3	مجال اللدونة	عديمة اللدونة
4	أقصى كثافة جافة (البروكتور) $\gamma_d \max$	1.863 gm/cm3
5	نسبة المياه الأصولية	10 %
6	قيمة CBR المغمورة	7.7%
8	المواد العضوية	لا يوجد

• و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي غير صالحة للتأسيس عليها



أ.د.م. هشام محمد حلمي

مهندس المعمول
أ.م.م. محمد البنا
التوقيع

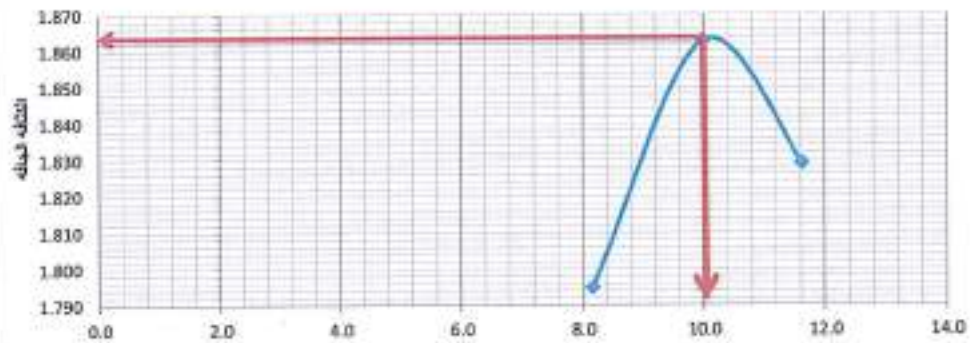
Modified Proctor : ASTM D1557

نوع العينة:	عينة كتيان رملية
تصنيف العينة:	A-3
تاريخ الاختبار:	
وزن القالب:	5731
حجم القالب:	2140
المسح ككثافة جافة:	1.883
البيانات الاسمية:	10.0

رقم الاختبار	1	2	3
وزن القالب + العينة رطبة	9886.0	10116	10100
وزن التربة الرطبة	4155.0	4385	4369
كثافة الرطبة	1.942	2.049	2.042

رقم الحقل	1	2	3	4	5	6
وزن الحقل	53.85	55.31	54.35	54.15	55.14	53.4
وزن الحقل + العينة رطبة	150.0	150.0	150.0	150.0	150.0	150.0
وزن الحقل + العينة جافة	142.5	143.1	141.4	141.2	140.2	139.87
وزن المياه	7.5	8.9	8.6	8.8	9.8	10.1
وزن العينة جافة	88.65	87.79	87.05	87.05	85.06	86.47
المحتوى المائي %	8.5	7.9	9.9	10.1	11.5	11.7
متوسط المحتوى المائي %	8.2	10.0	11.6			
كثافة الحقل	1.795	1.863	1.829			

Modified Proctor Chart



ملاحظات:



أحمد مصطفى
مهندس

مهندس المعمل
أحمد مصطفى
التوقيع
مهندس

Coarse & Fine Aggregate Grading - ASTM C136 & AASHTO T27

التاريخ :	25-09-23	الموقع : St= 202+020	ارض طبيعية
-----------	----------	----------------------	------------

نتائج الاختبار :-

رقم المنخل (mm)	رقم المنخل (inch)	وزن المحجوز على كل منخل	وزن المحجوز التراكمي	المحجوز %	العار %
127	5"	0	0	0%	100%
101.6	4"	0	0	0.00%	100.00%
76.2	3"	0	0	0.00%	100.00%
63.5	2.5"	0	0	0.00%	100.00%
50.8	2"	0	0	0.00%	100.00%
37.5	1.5"	0	0	0.00%	100.00%
25	1"	0	0	0.00%	100.00%
19	3/4"	0	0	0.00%	100.00%
12.7	1/2"	0	0	0.00%	100.00%
9.5	3/8"	0	0	0.00%	100.00%
4.75	# 4	0	0	0.00%	100.00%
	العار من منخل # 4	500			100.00%
	وزن العينة الكلي	500			
	وزن عينة التام	500			
2.36	# 10	10	10	2.0%	98.0%
0.425	# 40	51	61	12.2%	87.8%
0.075	# 200	419	480	96.0%	4.0%
المسبولة و اللدونة		N.P			
التصنيف		A-3			

ملاحظات : توصيف العينة : كتيان رملية ناعمة (Sand Dunes)



احمد محمد علي
مهندس

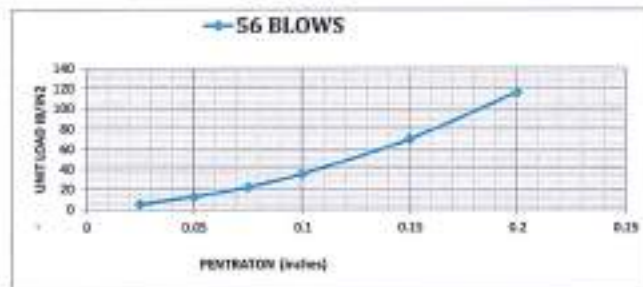
مهندس المعمل
د. مصطفى محمد البنا
التوقيع

اختبار نسبة تحميل كاتيلورنيا (C . B . R) ASTM D1883

A-3		تصنيف العينة	
56	عدد الضربات	56	عدد الضربات
2	رقم البقعة	2131	ختم القالب (سم)
21.6	وزن البقعة	5289	وزن القالب (جم)
193	وزن البقعة + العينة رطبة (جم)	5590	وزن القالب + وزن العينة رطبة (جم)
198.3	وزن البقعة + العينة جافة (جم)	4391	وزن العينة رطبة (جم)
11.7	وزن الماء (جم)	2.018	كثافة الرطبة (جم / سم ³)
116.7	وزن العينة جافة (جم)	1.834	القيمة كاتيلورنيا (جم / سم ²)
10.0%	المستوى المائي %	1.863	كثافة البرونز (جم / سم ³)
		98.5%	نسبة الماء
		0.00%	نسبة الفراغ
			غير قابلة للتحميل

خصائص نسبة تحميل كاتيلورنيا

7.62	5.08	3.81	2.54	1.95	1.27	0.635	الأختبار لباريسيم
0.3	0.2	0.15	0.1	0.075	0.05	0.025	الأختبار لباريسيم
240.0	158	95.0	48.0	30.0	17.0	7.0	الفراد kg
528.96	348.232	209.38	105.792	66.12	37.468	15.428	الفراد والبرونز
176.4	116.13	69.825	35.28	22.05	12.495	5.145	المعدل 8/IN2



7.7%	قيمة C . B . R
------	----------------

ملاحظات : تم عمل القالب في الماء لمدة 96 ساعة قبل الاختبار



احمد محمد عيسى
مهندس

مهندس محمد البنا
مهندس

	مشروع القطار الكهربائي السريع إستكمال أعمال الجسر الترابي لمسار القطار الكهربائي السريع الخط الثاني (القيوم / بني سويف - أبو سمبل) (مرحلة الجسور والتأسيس والأساس) القطاع الثاني (بني مزار / منفلوط) تنفيذ شركة أبو عجيبة للمقاولات العامة والتوريدات العمومية حصر اجمال لكميات الردم	الهيئة العامة للإحصاء مكتب أدمس مهندي للمستشارات الهندسية
---	---	--

الهيئة العامة للإشراف
مكتب أ.د/سن مهدي
للإشراف الهندسية

بند رقم (١٠٣) : أعمال تحميل وتوريد ونقل أتربة مطابقة للمواصفات وتشغيلها باستخدام آلات التسيبة بسك لا يزيد عن ٥٠ سم حتى منسوب (2٠ متر) أسفل منسوب الغرمة و بسك لا يزيد عن ٢٥ سم اعلي من منسوب (2٠ متر) من منسوب الغرمة لاستكمال المنسوب التصميمي الخ

Station	Total Fill Area(m2)	Cum. Fill Vol(m3)	As Built vol.Fill		
			Fill VOL(m3)	Total.Qty	
201+920.00	202.61	2026.07	2026.07	100122.28	
201+940.00	227.66	6,328.78	4,302.71		
201+960.00	248.2	11,087.40	4,758.61		
201+980.00	274.47	16,314.06	5,226.67		
202+000.00	262.01	21,678.88	5,364.82		
202+020.00	243.79	26,736.89	5,058.01		
202+040.00	194.01	31,114.85	4,377.95		
202+060.00	362.48	36,679.73	5,564.88		
202+080.00	341.72	43,721.80	7,042.07		
202+100.00	314.56	50,284.61	6,562.81		
202+120.00	301.56	56,445.77	6,161.16		
202+140.00	0	59,461.36	3,015.59		
202+160.00	0	59,461.36	0.00		
202+180.00	0	59,461.36	0.00		
202+200.00	0	59,461.36	0.00		
202+220.00	317.97	62,641.01	3,179.66		
202+240.00	312.67	68,947.36	6,306.35		
202+260.00	320.6	75,280.03	6,332.66		
202+280.00	330.13	81,787.33	6,507.30		
202+300.00	335.88	88,447.44	6,660.11		
202+320.00	141.42	93,220.38	4,772.95		
202+340.00	132.47	95,959.23	2,738.85		
202+360.00	116.74	98,451.35	2492.11		
202+376.01	91.94	100,122.29	1,670.94		
اجمالي كميات الردم المصروفة سابقا					0
اجمالي كميات الردم الفعلية الحالية بعد خصم سمك خرسانه الميول					100122.28
كمية خصم سمك خرسانه الميول				911	

[illegible]



بند رقم (١٠٣): أعمال تحميل وتوريد ونقل أثرية مطابقة للمواصفات وتشغيلها باستخدام آلات التسوية بسمك لا يزيد عن ٥٠ سم حتى مسلوب (-2 متر) أسفل مسلوب الغرمة و بسمك لا يزيد عن ٢٥ سم اعلي من مسلوب (-2 متر) من مسلوب الغرمة لاستكمال العسوب التصميميالخ

Station	Total Fill Area(m2)	Cum. Fill Vol(m3)	As Built vol.Fill			
			Fill VOL(m3)	Total.Qty	Fill VOL(m3) ابتداء من ٢٠٢٤/٢/٢٢	اجمالي الكميات ابتداء من ٢٠٢٤/٢/٢٢
201+920.00	202.61	2026.07	2026.07	100122.28	582.22	9669.67
201+940.00	227.66	6,328.78	4,302.71		1,170.55	
201+960.00	248.2	11,087.40	4,758.61		1,162.28	
201+980.00	274.47	16,314.06	5,226.67		1,140.36	
202+000.00	262.01	21,678.88	5,364.82		1,142.87	
202+020.00	243.79	26,736.89	5,058.01		1,149.44	
202+040.00	194.01	31,114.85	4,377.95		1,134.32	
202+060.00	362.48	36,679.73	5,564.88		561.35	
202+080.00	341.72	43,721.80	7,042.07		0.00	
202+100.00	314.56	50,284.61	6,562.81		0.00	
202+120.00	301.56	56,445.77	6,161.16		0.00	
202+140.00	0	59,461.36	3,015.59		0.00	
202+160.00	0	59,461.36	0.00		0.00	
202+180.00	0	59,461.36	0.00		0.00	
202+200.00	0	59,461.36	0.00		0.00	
202+220.00	317.97	62,641.01	3,179.66		162.54	
202+240.00	312.67	68,947.36	6,306.35		325.06	
202+260.00	320.6	75,280.03	6,332.66		321.62	
202+280.00	330.13	81,787.33	6,507.30		322.02	
202+300.00	335.88	88,447.44	6,660.11		328.98	
202+320.00	141.42	93,220.38	4,772.95		166.06	
202+340.00	132.47	95,959.23	2,738.85		0.00	
202+360.00	116.74	98,451.35	2492.11		0	
202+376.01	91.94	100,122.29	1,670.94		0.00	

عن الاستشاري أد حسن مهدي
المكتب الفني مدير المشروع م / محمود عريب
م / احمد عزب

مشروع التطوير السريع

أ. د. محمد عبد الحليم

المساحة
م/محمد عبدالرحمن

عن الشركة
م/ احمد طبع
11
ت 1978
ABUAGLA
الوكالة العامة
609-161-109

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name [Signature]	Sign [Signature]	Date 15-8-2022																
Received by Employers Representative		Time 2																	
		UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>EW</td> <td>OT</td> <td>15</td> <td>8</td> <td>22</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	EW	OT	15	8	22		
C1	C2	C3	DD	MM	YY	HH	MM												
KP	EW	OT	15	8	22														
CODE-1	CODE-2	CODE-3	CODE-4																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 202+376	
	E=260126.0446 N=3137487.7094	E=260129.6912 N=3135991.0324
Inspection description[Disinfection Of Trees Cutting From st (200+876) to st (202+376)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

تصوير وازالة الحمايات بواسطة عمال المشاة	- Trees No. was checked only by xyz and under their own responsibility - you must follow specs and design dr
---	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	[Signature]	[Signature]			A-AWC-R	
Contractor QA\QC*	XYZ	[Signature]	15-8-2022		A	
	H.M.C	[Signature]	15-8-2022		A	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024		AWC	

* Designer

** Alignment: Bridges: Culvert Only

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name [Signature]	Sign [Signature]	Date 15-8-2022
Received by Employers Representative		Time 2	
		UIR	
		C1 KP	C2 EW
		C3 OT	DD 15
		MM 8	YY 22
		HH 22	MM 22
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 202+376	
	E=260126.0446 N=3137487.7094	E=260129.6912 N=3135991.0324
Inspection description[Disinfection Of Trees Cutting From st (200+876) to st (202+376)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

تصوير وازالة الاشجار بمساحة 200+876 الى 202+376	- Trees No. was checked only by xyz and under their own responsibility - you must follow specs and design dr
--	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	[Signature]	[Signature]			A-AWC-R	
Contractor QA\QC*	XYZ	[Signature]	15-8-2022		A	
	H.M.C	[Signature]	15-8-2022		A	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024		AWC	

* Designer

** Alignment: Bridges: Culvert Only

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيل للمقاولات العامة		Designer Company*	DR. Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
	20-10-2022	3								
Received by Employers Representative			C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	20	10	22		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5						

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+686 E=260126.0446 E=260172.2356 N=3137487.7094 N=3136679.1711	
Inspection description/ تطهير بعد قطع الاشجار Disinfection of crops and trees cutting from st (200+876) to st (201+686)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. (xyz))	Comments by: General consultant (systra)
---	--

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA/QC*	XYZ		20-10-2022	14:30	A	
	H.M.C		20/10/2022	15:00	A	
GARB**						
Employers Representative						

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
	20-10-2022	4								
Received by Employers Representative			C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	20	10	28		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+686 TO 201+846	
	E=260172.2356 N=3136679.1711	E=260170.8362 N=3136519.1841
Inspection description/		
Disinfection of crops and trees cutting from st (201+686) to st (201+846) تم تعقيم بعد قطع الأشجار		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. (xyz))	Comments by: General consultant (systra)

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer							
Contractor QA/QC*	XYZ		20-10-2022	16:00	A		
	H.M.C		20/10/2022	16:30			
GARB**							
Employers Representative							

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
	20-10-2022	5								
Received by Employers Representative			C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	20	10	22		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+966 TO 202+376	
	E=260166.4277	E=260129.6912
	N=3136399.268	N=3135991.0324
Inspection description/ Disinfection of crops and trees cutting from st (201+966) to st (202+376)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	





Comments by: (GARB SURVEY CONSATANT: (xyz))

Comments by: General consultant (systra)


 Khaled al-Mur

- Levels and coordinates were checked only by xyz and under their own responsibility
 - you must follow specs, design drawing and geo-technical report.
 - this work was inspected only by xyz and

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	محمد بن محمد				A-AWC-R	
Contractor QA/QC*	XYZ		20-10-2022	14:30		
	H.M.C		20/10/2022	14:30		
GARB**						
Employers Representative	Khaled al-Mur		23/10/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR. Hassan Mahdy (H.M.C)					
Issued by Contractor	Name	Sign	Date					
			25-10-2022					
Received by Employers Representative	Name	Sign	Time					
			6					
C1		C2	C3	DD	MM	YY	HH	MM
KP		EW	OT	25	10	22		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+466 TO 201+666	
	E=260165.8013	E=260172.0505
	N=3136899.0593	N=3136699.1703
Inspection description/ As-Built for rock surface from st (201+466) to st (201+666) الرفع المساحي + معاينة السطح الصخري (المستوى الأول)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

اعمل قطع جانبي الهيئة العامة للمقاولات العامة	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C - you must follow spec and geo-technical report
---	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer					A-AWC-R	
Contractor QA/QC*	XYZ		25-10-2022	13:00	A	
	H.M.C		25/10/2022	13:00	A	
GARB**						
Employers Representative	Khaled ali		23/9/2024			



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
			29-10-2022	7						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	29	10	28		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5						

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	200+876 TO 201+466		
	E=260126.0446	E=260165.8013	
	N=3137487.7094	N=3136899.0593	
Inspection description[الرفع المساحي + المعاينة للطرح المقصود (المسوح الأول) As-Built for rock surface from st (200+876) to st (201+466)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

(as built) المهندس طارق محمد السيد - الخبير	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C. - you must follow specs and design drawings.
--	--

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer					A-AWC-R	
Contractor QA/QC*	XYZ		29-10-2022	12:00	A	
	H.M.C		29/10/22		A	
GARB**						
Employers Representative	Khaleed ali		23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة زينة حيلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
	أحمد محمد	[Signature]	2-11-2022	8						
Received by Employers Representative	[Signature]	[Signature]	C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	2	11	22		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+036 TO 201+086	
	E=260137.1186	E=260140.5793
	N=3137328.0971	N=3137278.217
<u>Inspection description/</u> As-Built for rock surface from st (201+036) to st (201+086)		

الرفع المسامى + معاينة السطح المجرى (المستوى المظن) فريق

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
2/11/2022	

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C - you must follow spec and geo-technical report

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	أحمد محمد	[Signature]					
Contractor QA/QC*	XYZ	محمد أحمد	2-11-2022	17:30	A		
	H.M.C	محمد أحمد	2/11/2022	13:30	A		
GARB**							
Employers Representative	Khaled ali	[Signature]	23/9/2024				

مكتبة A / مكتبة A
التقنية / التقنية
مكتبة A / مكتبة A

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عبيدة المقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)	
Issued by Contractor	Name	محمد أبو بكر	Date	6-11-2022	
	Sign		Time	10	
Received by Employers Representative	UIR		C1	C2	C3
			DD	MM	YY
			KP	EW	OT
			6	11	2022
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5	

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+156 TO 201+246	
	E=260145.4242	E=260151.6535
	N=3137208.3848	N=3137118.6007
<u>Inspection description:</u> As-Built for rock surface from st (201+156) to st (201+246)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate:

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))

Comments by: General consultant (systra)

 مستشار استشارات المقاولات العامة - الخ	- Levels and Coordinates were checked only by xyz and under their own responsibility. - This work was inspected only by xyz and H.M.C. you must follow specs and geo-technical report
--	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	محمد أبو بكر				A-AWC-R	
Contractor QA\QC*	XYZ		6-11-2022	14:00	A	
	H.M.C		6/11/2022	14:30	A	
GARB**						
Employers Representative	Khaled Ali		23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name أبو عجلة	Sign أبو عجلة	Date 7-12-2022																
Received by Employers Representative			Time 13																
		UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>EW</td> <td>OT</td> <td>7</td> <td>12</td> <td>23</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	EW	OT	7	12	23		
C1	C2	C3	DD	MM	YY	HH	MM												
KP	EW	OT	7	12	23														
CODE-1	CODE-2	CODE-3	CODE-4																

EXPLANATION OF WORK TO BE INSPECTED


Area	Element	Item
From 200+876 To 202+376	201+286 TO 201+386	
	E=260154.422 N=3137078.6966	E=260161.1582 N=3136978.9239
<u>Inspection description/</u> As-Built for rock surface from st (201+286) to st (201+386)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT: (xyz))	Comments by: General consultant (systra)
	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C. - you must follow specs and geo-technical report

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	XYZ	أبو عجلة	7-12-2022	14:00	A		
Contractor QA/QC*	H.M.C	أبو عجلة	7/12/2022	14:30	A		
GARB**							
Employers Representative	Khaled ali	أبو عجلة	23/9/2024				

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name Sign 13-12-2022	Date	Time 14															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>EW</td> <td>OT</td> <td>13</td> <td>12</td> <td>22</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	EW	OT	13	12	22		
C1	C2	C3	DD	MM	YY	HH	MM											
KP	EW	OT	13	12	22													
CODE-1	CODE-2	CODE-3	CODE-4															
CODE-5																		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+386 TO 201+426	
	E=260161.1582 N=3136978.9239	E=260163.6041 N=3136938.9988
Inspection description/ الرفع المساحي + معاينة سطح صخره (المستوي الثالث) As-Built for rock surface from st {201+386} to st {201+426}		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

	- Levels and coordinates were checked only by systra and under their own responsibility - This work was inspected only by systra and H.M.C - you must follow specs and geo-technical report
---	--

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer					A-AWC-R	
Contractor QA/QC*	XYZ		13-12-2022	12:10	A	
	H.M.C		13/12/2022	12:10	A	
GARB**						
Employers Representative	Khaled al.		23/12/2022			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أ.م.م. العامة للمطارات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
	أ.م.م. العامة للمطارات العامة	أ.م.م. العامة للمطارات العامة	13-12-2022	15						
Received by Employers Representative	UIR		C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	13	12	22		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5						

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+246 TO 201+286		
	E=260151.6535 N=3137118.6007	E=260154.422 N=3137078.6966	
<u>Inspection description/</u> As-Built for rock surface from st (201+246) to st (201+286)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
أ.م.م. العامة للمطارات العامة	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected and checked only by xyz and H.M.C - you must follow specs and geo.technical report

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	أ.م.م. العامة للمطارات العامة	أ.م.م. العامة للمطارات العامة					
Contractor QA/QC*	XYZ	أ.م.م. العامة للمطارات العامة	13-12-2022	14:00	A		
	H.M.C	أ.م.م. العامة للمطارات العامة	13/12/2022	14:00	A		
GARB**							
Employers Representative	Khaled ah	أ.م.م. العامة للمطارات العامة	23/9/2024				

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)			
Issued by Contractor	Name	Sign	Date	Time			
	13-12-2022	16					
Received by Employers Representative	C1	C2	C3	DD	MM	YY	HH
	KP	EW	OT	13	12	23	
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5			

EXPLANATION OF WORK TO BE INSPECTED


Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+036	
	E=260126.0446 N=3137487.7094	E=260137.1186 N=3137328.0971
Inspection description: الرفع المساحي + معاينة السطح المهيض (المسوح الكاف) - بحسب As-Built for rock surface from st (200+876) to st (201+036)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C - you must follow spec and geotechnical rep.

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	XYZ		13-12-2022	13:30	A	
Contractor QA/QC*	H.M.C		13/12/2022	14:00	A	
GARB**						
Employers Representative	Phaked ali		23/12/2022		A	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR ,Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
			2023-1-3	17						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	3	1	23		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	200+876 TO 201+666		
	E=260126.0446	E=260172.0505	
	N=3137487.7094	N=3136699.1703	
Inspection description/			
As-Built for cut from st (200+876) to st (201+666)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
2023/1/3	

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

1- Levels and coordinates were checked only by XYZ and under their own responsibility

- Levels and coordinates were checked only by XYZ and under their own responsibility
- you must follow specs and design drawings

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor	XYZ		3-1-2023	14:00	A	
QA/QC*	H.M.C		3/1/2023	19:00		
GARB**						
Employers Representative	Khaled Ali		23/9/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name 1575 Sign 	Date	13-6-2023
Received by Employers Representative	Time 18	Time	18
Received by Employers Representative	UIR	C1 KP	C2 EW
		C3 OT	DD 13
		MM 6	YY 23
		HH	MM
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+660	
	E=260126.0446 N=3137487.7094	E=260171.9793 N=3136705.1798
Inspection description		
As-Built for cut from st (200+876) to st (201+660)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
12/6/2023	

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

as built for cut from st (200+876) to st (201+660)

- Levels and coordinates were checked only by xyz and under their own responsibility
- you must follow spec and design dwg.

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA/QC*	XYZ		13-6-2023	9:00	A	
	H.M.C		13/6/2023			
GARB**						
Employers Representative	Khaled Ali		23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله والمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name Sign 24-8-2023	Date	Time 19
Received by Employers Representative	Sign 23	Time	

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+840 E=260126.0446 N=3137487.7094	E=260170.9813 N=3136525.1923
Inspection description/ As-Built for cut from st (200+876) to st (201+840)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
24/8/2023	

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

as built قطاع الضلع القطاع الشرقي	- Levels and coordinates were checked only by xyz and under their own responsibility - you must follow specs and design dwg.
---	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	محمد زكريا	محمد زكريا			A-AWC-R	
Contractor QA/QC*	XYZ	محمد زكريا	26-8-2023	10:00	A	
	H.M.C	محمد زكريا	26/8/2023	10:15	A	
GARB**						
Employers Representative	Khaled ali	محمد زكريا	23/8/2023		A	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name وليد فهد محمد	Date	9-11-2023
Received by Employers Representative	Sign وليد فهد محمد	REQ.NUM	20
Received by Employers Representative	UIR	C1 KP	C2 SU
		C3 OT	DD 9
		MM 11	YY 23
		HH	MM
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description/ تشييد قاع إحلل from st (202+220) to st (202+300)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
ملاحظات: تم فحص القاع وإحلاله	- levels and coordinates were checked only by xyz and under their own responsibility - No objection according to the attached reports and lab. results.

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد فهد محمد	وليد فهد محمد	19-11-2023	10:00	(A)	
Contractor QA/QC*	XYZ	محمد عبد الرحمن	9/11/2023	11:00	A	
GARB**						
Employers Representative	Khaled ali	Khaled ali	23/11/2023			

* Designer

** Alignment: Bridges: Culvert Only

UNIVERSAL INSPECTION REQUEST



مكتب أ.د. حسن مهدي
للإشراف الهندسية





الهيئة العامة للغذاء والدواء
Saudi Food & Drug Authority



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name:  Sign: 	Date	REQ. NUM																
Received by Employers Representative	UIR	18-11-2023	21																
		<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>18</td> <td>11</td> <td>23</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	18	11	23			
C1	C2	C3	DD	MM	YY	HH	MM												
KP	SU	OT	18	11	23														
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+280 TO 202+300	
	E=260141.2938 N=3136086.3373	E=260139.0278 N=3136066.4661
[Inspection description]		
من (10-متر from st (202+280) to st (202+300)		



INSPECTION DETAILS The Following will be ready at the Planned inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
	- No objection, according to the attached reports and lab. results. - you must follow specs and design dng.

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود		18/11/2023	10:10		
Contractor QA/QC*	XYZ		18-11-2023	13:30	A	
	H.M.C		18/11/2023	11:30	AWC	
GARB**						
Employers Representative	Khaled ali		23/9/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عبيدة للمقاولات 2023	Designer Company*	DR .Hassan Mahdy (H.M.C)					
Issued by Contractor	Name [Signature]	Date	20-11-2023					
Received by Employers Representative	Signature [Signature]	REQ. NUM	22					
UIR	C1 KP	C2 SU	C3 OT	DD 21	MM 11	YY 23	HH 2	MM 30
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5				

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+000 TO 202+120	
	E=260164.6561 N=3136365.3242	E=260156.5571 N=3136245.6007
Inspection description/ تشغيل قاع إحلال from st (202+000) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSANTANT (xyz))	Comments by: General consultant (systra)
تم فحص مستويات قاع إحلال تم فحص إحلال الكهربي - الخ	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was checked only by xyz and H.M. - you must follow speed and design drawing and geo-technical report

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	[Signature]	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	[Signature]	21-11-2023	3:15	(A)	
	H.M.C	[Signature]	21/11/2023	3:00	A	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/11/2024		Any	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown:

Contractor Company	أبو عجمية للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	REQ. NUM							
	[Signature]		22-11-2023	23							
Received by Employers Representative	[Signature]	[Signature]	UIR	C1	C2	C3	DD	MM	YY	HH	MM
				KP	SU	OT	22	11	23		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED


Area	Element		Item
From 200+876 To 202+376	202+220 TO 202+300		
	E=260147.6147	E=260139.0278	
	N=3136146.003	N=3136066.4661	
<u>Inspection description/</u> طبقة ردم منسوب (-9.5) متر from st (202+220) to st (202+300)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
	- No objection, according to the attached reports and Lab. results. - you must follow specs and design drawings


INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time			
Contractor Engineer	وليد محمد	[Signature]					
Contractor QA/QC*	XYZ	[Signature]	22-11-2023	3:45	(A)		
	H.M.C	[Signature]	22/11/2023	11:00	A		
GARB**							
Employers Representative	Fhaled ali	[Signature]	23/11/2023				

RECEIPT of NOTIFICATION Minimum Notice Period not less than 24 Hours The Work described below will be complete and ready for inspection at planned time shown											
Contractor Company	شركة المقاولات العامة 				Designer Company*	DR .Hassan Mahdy (H.M.C)					
Issued by Contractor	Name	Sign	Date	REQ.NUM							
			25-11-2023	24							
Received by Employers Representative			UIR	C1	C2	C3	DD	MM	YY	HH	MM
				AP	SU	OT	25	11	23		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
From 200+876 To 202+376	202+000 TO 202+020	
	E=260164.6561	E=260163.5058
	N=3136365.3242	N=3136345.3573
<u>Inspection description:</u> from st (202+000) to st (202+020) طبقة ردم منسوب (-13) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (systa)) 	Comments by: General consultant (systa) - No objection, according to the attached reports and lab. results. - you must follow specs and design drawings
---	---

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد محمد	وليد محمد					
Contractor QA/QC*	XYZ	محمد ادريس مهدي	25-11-2023	12:30	(A)		
	H.M.C	محمد علي	25/11/2023	11:00	A		
GARB**							
Employers Representative	Khaled ali	كhaled ali	23/9/2024				

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name 157537 Sign [Signature]	Date	28-11-2023
Received by Employers Representative	UIR	REQ NUM	25
		C1 KP	C2 SU
		C3 OT	DD 28
		MM 11	YY 23
		HH 11	MM 00

CODE-1

CODE-2-109

CODE-3

CODE-4

CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description		
from st (202+220) to st (202+300) طبقة ردم منسوب (-9) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

تم استلام استمارة المعاينة
والتأكد من مطابقتها
للمواصفات والمواصفات
المطلوبة.

- No objection, according to the attached reports and lab. results
- you must follow specs and design dng.

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمود	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	عبد الرحمن العبد	28/11/2023	3:30	A	
	H.M.C	عبد الله العبد	28/11/2023	11:00	A	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	Name		Sign	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	29-11-2023		REQ.NUM	26	
Received by Employers Representative	C1 C2 C3 DO MM YY HH MM		UIR		
	KP SU OT 29 11 23				
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5	

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+080	
	E=260160.9658 N=3136305.4382	E=260159.576 N=3136285.4865
Inspection description[from st (202+060) to st (202+080) طبقة ردم منسوب (-11) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))	Comments by: General consultant (systra)
	- No objection, according to the attached reports and lab. results. - you must follow specs and design draw

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد فريد	وليد فريد				
Contractor XYZ	خالد احمد	خالد احمد	29-11-2023	1:15	(A)	
Contractor QA\QC*	H.M.C	خالد احمد	29-11-2023	12:45	A	
GARB**						
Employers Representative	Khaled ali	خالد علي	29/11/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name Sign 29-11-2023	Date	REQ.NUM 27															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>29</td> <td>11</td> <td>23</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	29	11	23		
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT	29	11	23													
CODE-1	CODE-2	CODE-3	CODE-4															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+080 TO 202+120	
	E=260159.576	E=260156.5571
	N=3136285.4865	N=3136245.6007
Inspection description/		
منطقة ردم منسوب (10.5-) متر from st (202+080) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSANTANT.(xyz))

Comments by: General consultant (systra)

-No objection, according to the attached reports and lab. results
-you must follow specs and design dwg

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد عجلان	وليد عجلان				
Contractor QA/QC*	XYZ	عبدالله بن محمد	29-11-2023	11:30	(A)	
	H.M.C	محمد رشيد	29-11-2023	12:30	A	
GARB**						
Employers Representative	Khaled ali	كhaled ali	23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company			Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name	Sign	Date	REQ. NUM																
			30-11-2023	28																
Received by Employers Representative			UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>30</td> <td>11</td> <td>23</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	30	11	23		
C1	C2	C3	DD	MM	YY	HH	MM													
KP	SU	OT	30	11	23															

CODE-1

CODE-2

CODE-3

CODE-4

CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+000 TO 202+020		
	E=260164.6561	E=260163.5058	
	N=3136365.3242	N=3136345.3573	
<u>Inspection description</u> 12.5 متر from st (202+000) to st (202+020)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (XYZ))	Comments by: General consultant (systra)
	-No objection, according to the attached reports and lab. results. -you must follow spec and design draw

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمد	وليد محمد				
Contractor QA/QC*	XYZ	محمد علي	30-11-2023	13:00	A	
	H.M.C	محمد علي	30/11/2023	12:30 pm	A	
GARB**						
Employers Representative	Khaled Ali		23/9/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name 157537	Sign	Date 3-12-2023
Received by Employers Representative		UIR	REQ.NUM 30
		C1 KP	C2 SU
		C3 OT	DD
		MM	YY 23
		HH	MM
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+100 E=260160.9658 N=3136305.4382	E=260158.1064 N=3136265.5406
Inspection description from st (202+060) to st (202+100) طبقة ردم ملسوب (-10.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz)) مستشاري المساحة (جارب) مستشاري المساحة (جارب)	Comments by: General consultant (systra) - No objection, according to the attached reports and lab. results. - you must follow specs and design d.
---	--

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA\QC*	XYZ		3-12-2023	4:15	(A)	
	H.M.C		3/12/2023	2:30pm	AWC	
GARB**						
Employers Representative	Khaled ali		28/9/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown.

Contractor Company	شركة البعثة للخدمات الهندسية		Designer Company*	DR. Hassan Mahdy (H.M.C)
Issued by Contractor	Name	Sign	Date	REQ. NUM
	أحمد محمد	أحمد محمد	5-12-2023	31
Received by Employers Representative	UIR		C1 C2 C3 DO MM YY HH MM	
			KP SU OT	23
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147	E=260139.0278
	N=3136146.003	N=3136066.4661
Inspection description/		
من تسليم طبقة ردم منسوب (8-متر) from st (202+220) to st (202+300)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (-xyz))

Comments by: General consultant (systra)

مكتب أدريس مهدي للإستشارات الهندسية مشاريع الطرق السريعة - الخط ٢٠٢	- No objection, according to the attached reports and lab. results. - you must follow specs and design dwg.
---	---

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	أحمد محمد	أحمد محمد				
Contractor QA/QC*	XYZ	أحمد محمد	6-12-2023	10:30	(A)	
	H.M.C	أحمد محمد	5/12/2023	4:15Pm	AWC	
GARB**						
Employers Representative	Khaled ali	أحمد محمد	23/9/2024		AWC	



UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للمشاورات الهندسية



شركة السيترا للاستشارات



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ. NUM						
	وليد عيسى	وليد عيسى	7-12-2023	32						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT				23	
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5						

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+060 TO 202+120		
	E=260160.9658	E=260156.5571	
	N=3136305.4382	N=3136245.6007	
Inspection description/			
من طرقة ردم ملسوب (10-) متر from st (202+060) to st (202+120)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as Indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
لا يوجد اعتراض على النتائج	-No objection, according to the attached reports and lab. results. -you must follow specs and design drug

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد عيسى	وليد عيسى	7-12-2023	1:30	(A)		
Contractor QA/QC*	XYZ	محمد علي	7/12/2023	12:15	A		
GARB**							
Employers Representative	Khaled ali	كhaled ali	23/12/2024		AWC		

UNIVERSAL INSPECTION REQUEST



مكتب أمان مدي
البنية التحتية



الهيئة العامة للمواصلات



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name	Sign	Date	REQ.NUM
	وليد محمود	وليد	9-12-2023	33
Received by Employers Representative	UIR		C1 C2 C3 DO MM YY HH MM	
			KP SU OT	23
CODE-1		CODE-2	CODE-3	CODE-4
				CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+220 TO 202+300		
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661	
Inspection description/ من تسليم طبقة ردم ملسوب (-7.5) متر from st (202+220) to st (202+300)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT,(xyz))

Comments by: General consultant (sysra)

م.م. وليد محمود

-No objection, according to the attached reports and lab. results.
-you must follow specs and design

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمود				A-AWC-R	
Contractor QA/QC*	XYZ	وليد محمود	9-12-2023	3:30	(A)	
	H.M.C	وليد محمود	9/12/2023	3:10	A	
GARB**						
Employers Representative	Khaled ali		23/12/2023		AWC	



UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



المكتب الهندسي للدراسات
SYSTRA



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)					
Issued by Contractor	Name	Sign	Date	REQ.NUM					
	16-12-2023	36							
Received by Employers Representative	UIR	G1 KP	G2 SU	G3 OT	DD	MM	YY 23	HH	MM
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description: تسليم طبقة ردم مسلوب (-7) متر from st (202+220) to st (202+300)		

INSPECTION DETAILS The following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT: xyz)

مستشار
مكتب أدريس مهدي
للإستشارات الهندسية

Comments by: General consultant (systra)

- No objection, according to the attached reports and lab. results.
- you must follow specs and design dirg.

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	أبو عجلة					
Contractor QA/QC*	XYZ		16-12-2023	3:15	A	
	H.M.C		16/12/2023	3:00	A	
GARB**						
Employers Representative	Khaled ali		28/12/2024		Awc	



UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للطيران المدني



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)					
Issued by Contractor	Name	Sign	Date	REQ.NUM					
	وليد فلاح	وليد فلاح	17-12-2023	37					
Received by Employers Representative	UIR	C1	C2	C3	DD	MM	YY	HH	MM

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
From 200+876 To 202+376	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description: منطقة ردم ملسوب (-8.5) متر from st (202+060) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by (GARB SURVEY CONSULTANT xyz)	Comments by: General consultant (systra)
استاذ المهندس مستوى التفتيش الكفائي الى الحد	- No objection, according to the attached reports and lab. results. - you must follow specs and design dwg

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد فلاح	وليد فلاح				تزامنا مع العمل
Contractor QA/QC*	XYZ	وليد فلاح	17-12-2023	13:00	A	OK
	H.M.C	كروان محمد	17-12-2023	11:00	AWC	OK
GARB**						
Employers Representative	Khaled ali	كhaled ali	20/12/2024		AWC	



UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإشراف الهندسية




المشاور الهندسي الدكتور
أدريس مهدي



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown:

Contractor Company	البنية التحتية للطرق والبنية التحتية	Designer Company*	DR. Hassan Mahdy (H.M.C)															
Issued by Contractor	Name:  Sign:  Date: 19-12-2023	Date	REQ. NUM 38															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DO</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>AP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>YY</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DO	MM	YY	HH	MM	AP	SU	OT			YY		
C1	C2	C3	DO	MM	YY	HH	MM											
AP	SU	OT			YY													
CODE-1	CODE-2: 203-161-199	CODE-3	CODE-4															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+576	202+220 TO 202+300	
	E=260147.5147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description (		
from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (7,0-)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	M5 Reference	


Comments by: (GARB SURVEY CONSULTANT: XYZ)

تم فحص القطاع ووجدنا
مستوى تسليط التكرار للسحب - الخط الذي

Comments by: General consultant (systra)

- No objection, according to the attached reports and lab. results.
- you must follow specs and design drug

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	عليان وليد				A-AWC-R	
Contractor QA/QC*	XYZ	عليان وليد	19-12-2023	3:30	A	
	H.M.C	عليان وليد	19-12-2023	11:30	A	
GARB**						
Employers Representative	Khaled ali		23/9/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)				
Issued by Contractor	Name	Sign	Date				
	وليد محمود محمد		20-12-2023				
Received by Employers Representative		REQ.NUM	39				
C1	C2	C3	DD	MM	YY	HH	MM
	KP	SU	OT			23	

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description/		
من (8-) متر from st (202+060) to st (202+120) طبقة ردم منسوب		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
	- No objection, according to the attached reports and Lab. results. - You must follow specs and design draw

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد محمود محمد						
Contractor QA/QC*	XYZ		20-12-2023	3:40	A		
	H.M.C		20-12-2023	1:45	A		
GARB**							
Employers Representative	Khaled ali		23/9/2024		A		

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



شركة أديس مهدي
للإستشارات الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name Sign 21-12-2023	Date	REQ.NUM 40															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>21</td> <td>12</td> <td>23</td> <td>11</td> <td>30</td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	21	12	23	11	30
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT	21	12	23	11	30											
CODE-1	CODE-2	CODE-3	CODE-4															
CODE-5	CODE-6	CODE-7	CODE-8															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300 E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description: منسوب (6-متر) تسليم طبقة ردم منسوب (202+220) إلى (202+300)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT: xyz)	Comments by: General consultant (systra)
	- No objection, according to the attached reports and lab. results. - you must follow specs and design d.

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	أديس مهدي	أديس مهدي	21-12-2023	11:00	A	
Contractor QA/QC*	XYZ	عبد الرحمن العرابي	21/12/23	11:30	A	
GARB**						
Employers Representative	Khaled ali	كhaled ali	23/12/2023		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للمستشارات الهندسية



الهيئة العامة للإعانة
SHAKOR



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name أبو عجيبة للمقاولات العامة Sign [Signature]	Date	REQ.NUM																
Received by Employers Representative		23-12-2023	43																
		<table border="1"> <tr> <td>G1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>23</td> <td>12</td> <td>23</td> <td></td> <td></td> </tr> </table>	G1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	23	12	23			
G1	C2	C3	DD	MM	YY	HH	MM												
KP	SU	OT	23	12	23														
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120 E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description/ منسوب (7.5-) متر from st (202+060) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time


COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT. (xyz)) [Signature]	Comments by: General consultant (systra) - No objection, according to the attached reports and lab. results. - you must follow specs and design data
---	--

INSPECTION RESULT



Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	أبو عجيبة للمقاولات العامة	[Signature]	23-12-2023	4:13	A	
Contractor QA/QC*	XYZ	[Signature]	23/12/23	4:00	AWC	
GARB**						
Employers Representative	Khaled Ali	[Signature]	23/12/2023		AWC	








RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours											
The Work described below will be complete and ready for inspection at planned time shown											
Contractor Company					Designer Company*	DR. Hassan Mahdy (H.M.C)					
Issued by Contractor	Name	Sign	Date	REQ. NUM							
			25-12-2023	44							
Received by Employers Representative				C1	C2	C3	DO	MM	YY	HH	MM
				KP	SU	OT			23		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382 E=260156.5571 N=3136245.6007	
<u>Inspection description:</u> من st (202+060) to st (202+120) طبقة ردم مملووب (-7) متر		

INSPECTION DETAILS The following will be ready at the Planned inspection Time	
Planned inspection Date	Planned inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.: xyz) 	Comments by: General consultant (systra) 
--	--

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer							
	XYZ			25-12-2023	4:13		
Contractor QA/QC*	H.M.C			25-12-2023	4:10	AWC	
GARB**							
Employers Representative	Khaled ali		23/9/2024		AWC		

UNIVERSAL INSPECTION REQUEST



مكتب أ.إ.م.م.م
للإستشارات الهندسية



الهيئة العامة
للإستشارات الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	DR. Hassan Mahdy (H.M.C)	Designer Company*	REQ. NUM																
Issued by Contractor	Name: <u>وليد محمود</u> Sign: <u>[Signature]</u>	Date	27-12-2023																
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>TT</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			TT			45
C1	C2	C3	DD	MM	YY	HH	MM												
KP	SU	OT			TT														

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description / تسليم طبقة ردم منسوب (-5) متر from st (202+220) to st (202+300)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSALTANT (xyz))	Comments by: General consultant (systra)
<u>[Signature]</u>	-No objection, according to the attached reports and lab results. -you must follow specs and design dr

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	<u>وليد محمود</u>	<u>[Signature]</u>				
Contractor QA/QC*	XYZ	<u>[Signature]</u>	28-12-2023	11:00	A	
	H.M.C	<u>[Signature]</u>	27-12-2023	4:40	A	
GARB**						
Employers Representative	<u>Khaled Ali</u>	<u>[Signature]</u>	23/9/2024		ANC	

UNIVERSAL INSPECTION REQUEST



مكتب أديسن مهندسي
الاستشارات الهندسية



الهيئة العامة للإسكان



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أيم جيليم للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	وليد محمود	[Signature]	28-12-2023	46						
Received by Employers Representative		[Signature]	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT			23		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5						

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+980	
	E=260165.727 N=3136385.3	
Inspection description: منطقة ردم منسوب (-14) متر from st (201+980)		

INSPECTION DETAILS The Following will be ready at the Planned inspection Time

Planned inspection Date	Planned inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))	Comments by: General consultant (systra)
[Signature]	- No objection, according to the attached reports and lab. results. you must follow spec and design drawings

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود	[Signature]				
Contractor QA/QC*	XYZ	[Signature]	28-12-2023	12:00	A	[Signature]
	H.M.C	[Signature]	28-12-2023	11:00		
GARB**						
Employers Representative	Khaled Ali	[Signature]	23/9/2024		ANC	

Page 1 of 1

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	157537 مكتب المهندس مهدي للإستشارات الهندسية	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name وليد محجور محمد	Sign 	Date 2-1-2024																
Received by Employers Representative			REQ.NUM 48																
		<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>IP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	IP	SU	OT			24			
C1	C2	C3	DD	MM	YY	HH	MM												
IP	SU	OT			24														

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300 E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description/ من تسليم طبقة ردم منسوب (4.5) متر from st (202+220) to st (202+300)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz)) مستوفى القياسات للكميات التسليم - الفتح الذري	Comments by: General consultant (systra) - No objection, according to the attached reports and lab. results. - you must follow specs and design drawings
---	--

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محجور محمد					
Contractor QA/QC*	XYZ غير ملحق بالملف		2-1-2024	10:40	A	
	H.M.C محمود محمد		2-1-2024	10:30	A	
GARB**						
Employers Representative	Khaled ali		23/1/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company			Designer Company*	DR. Hassan Mahdy (H.M.C)																
Issued by Contractor	Name	Sign	Date	REQ. NUM																
			2-1-2024	49																
Received by Employers Representative			UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			24		
C1	C2	C3	DD	MM	YY	HH	MM													
KP	SU	OT			24															
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+060 TO 202+120		
	E=260160.9658	E=260156.5571	
	N=3136305.4382	N=3136245.6007	
<u>Inspection description</u> from st (202+060) to st (202+120) طبقة ردم منسوب (-6) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))	Comments by: General consultant (systra)
	- No objection, according to the attached reports and lab. results - you must follow specs and design drawings

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد بن وليد بن محمد						
Contractor QA/QC*	XYZ	عبدالله بن محمد	2-1-2024	11:40	A		
	H.M.C	محمد بن محمد	2-1-2024	11:50	AWC		
GARB**							
Employers Representative	Khaleed ali		23/1/2024		AWC		

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة استشارات المصالح العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name وليد محمور	Sign 	Date 2-1-2024																
Received by Employers Representative	UIR	REQ NUM 50																	
		<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			24			
C1	C2	C3	DD	MM	YY	HH	MM												
KP	SU	OT			24														
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+960 TO 202+000	
	E=260166.717 N=3136405.271	E=260164.6561 N=3136365.1247
<u>Inspection description</u> from st (201+960) to st (202+000) طبقة ردم منسوب (-13.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. (xyz)) مهندس الاستشارات العامة - الهندسة المدنية	Comments by: General consultant (systra) -No objection, according to the attached reports and lab. results. -you must follow specs and design dr
--	--

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمور					
Contractor QA\QC*	XYZ	عبد الرحمن الشراي	2-1-2024	11:15	A	
	H.M.C	محمود محمد	2-1-2024	11:00	AUC	
GARB**						
Employers Representative	Khaled ali		23/9/2024		AUC	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



المهنة العامة الإستشارية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	REQ.NUM							
	[Signature]		6-1-2024	51							
Received by Employers Representative	[Signature]	[Signature]	UIR	C1	C2	C3	DD	MM	YY	HH	MM
				KP	SU	OT				20	
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+960 TO 202+000		
	E=260166.717 N=3136405.271	E=260164.6561 N=3136365.3242	
<u>Inspection description</u> from st (201+960) to st (202+000) طبقه ردم منسوب (-13) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: [GARB SURVEY CONSATANT. (xyz)]	Comments by: General consultant (systra)
[Signature]	- No objection, according to the attached reports and Lab. results.
[Signature]	- you must follow specs and design drag

INSPECTION RESULT

					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمدي	[Signature]				
Contractor QA/QC*	XYZ	عبد الرحمن العرابي	6-1-2024	4:20	A	[Signature]
	H.M.C	محمود عولمة	6/1/2023	4:15	AWC	
GARB**						
Employers Representative	Khaled ali	[Signature]	29/9/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
			6-1-2024	52						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT				24	
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5						

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+060 TO 202+120		
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007	
Inspection description/			
from st (202+060) to st (202+120) طبقة ردم منسوب (5.5) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSANTANT (xyz))	Comments by: General consultant (systra)
	- No objection, according to the attached reports and lab results. - you must follow spec and design

INSPECTION RESULT

					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA/QC*	XYZ		6-1-2024	5:00	A	
	H.M.C		6/1/2024	4:40	Awc	
GARB**						
Employers Representative	Khaled ali		23/9/2024		Anrc	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



شركة القوسية للإنشاءات



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	إي. عجيبة للمقاولات العامة 57577	Designer Company*	DR. Hassan Mahdy (H.M.C)						
Issued by Contractor	Name: Sign:	Date	10-1-2024						
Received by Employers Representative	UIR	REQ.NUM	53						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT			24		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120 E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description: من (202+060) to st (202+120) طبقة ردم متسوب (-5) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate



Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSALTANT. xyz)	Comments by: General consultant (systra)
تم استلام القسط من أرضية حوض حوض تسوية القسط الكمبرلين السريع - القسط الذي	-No objection, according to the attached reports and lab. results. -you must follow specs and design dwg

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد الحويج	وليد حواف				
Contractor QA/QC*	XYZ	عبد الرحمن العرياني	10-1-2024	12:30	A	
	H.M.C	عبد الله العرياني	10-1-2024	12:00	A	
GARB**						
Employers Representative	Khaled chi		23/9/2024		Awc	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157337	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name:  Sign: 	Date	REQ.NUM
Received by Employers Representative	UIR	10-1-2024	54
		C1 C2 C3 DD MM YY HH MM	
		KP SU OT	23
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+300 TO 202+376	
	E=260139.0278 N=3136066.4661	E=260129.6912 N=3135991.0324
Inspection description/		
from st (202+300) to st (202+376) تشغيل قاع إحلال		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time


Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))

Comments by: General consultant (systra)





- levels and coordinates were checked only by xyz and under their own responsibility

- you must follow specs and designing and geo-technical report.


- This work was inspected only by xyz and H.M.C

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمود				A-AWC-R	
Contractor QA/QC*	XYZ		10-1-2024	10:30	A	
	H.M.C		10-1-2024	10:30	AWC	
GARB**						
Employers Representative	Khaled ali		23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name:  Sign: 	Date	REQ. NUM
Received by Employers Representative	UIR	15-1-2024	55
		C1 C2 C3 DD MM YY HH MM	
		KP SU OT	20

CODE-3

CODE-2

CODE-3

CODE-4

CODE-5

EXPLANATION OF WORK TO BE INSPECTED


Area	Element	Item
From 200+876 To 202+376	202+300 TO 202+340 E=260139.0278 E=260134.2574 N=3136066.4661 N=3136026.7517	
Inspection description/ منسوب (8.5-) متر from st (202+300) to st (202+340)		


INSPECTION DETAILS The following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT - (xyz))  تم استلام المخطط من مهندس مستشار المشاورات الهندسية - أ.د. حسن مهدي	Comments by: General consultant (systra) -you must follow specs and design drug- -you must do leveling and lining the compacted side slope of filling layer
---	--

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	أبو عجلة للمقاولات العامة					
Contractor QA/QC*	XYZ	عبد الرحمن العزبان	16-1-2024	8:30	A	
	H.M.C	محمود علي	15/1/2024	4:30pm	A	
GARB**						
Employers Representative	Khaled ali		26/1/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أ.إ.ص.ن مهدي
للإستشارات الهندسية





الهيئة العامة للإستشارات
والبحوث الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name:  Sign: 	Date	REQ. NUM						
Received by Employers Representative	UIR	15-1-2024	56						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT			21		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description:		
تسليم طبقة ردم منسوب (4) متر from st (202+220) to st (202+300)		




INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time


COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSANTANT.(xyz)) Comments by: General consultant (systra)

  
--

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمود محمد		15-1-2024			
Contractor QA/QC*	XYZ	عبد الرحمن الزينادي	16-1-2024	9:18	A	
	H.M.C	محمد علي	15/1/2024	5:10	A	
GARB**						
Employers Representative	Khaled ali		15/1/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name [Signature] Sign [Signature]	Date	REQ. NUM
Received by Employers Representative	UIR	16-1-2024	57
		C1 C2 C3 DD MM YY HH MM	
		KP SU OT	24
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description/		
منطقة ردم منسوب (-4.5) متر from st (202+060) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT-xyz)	Comments by: General consultant (systra)
 مشروع القمم الكبريتات السريعة - القمم الثاني	- you must follow specs and design durg. - you must do landing and lining the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد عمار	[Signature]				
Contractor QA\QC*	XYZ	[Signature]	16-1-2024	3:30	A	
	H.M.C	[Signature]	16/1/24	3:00	Awc	
GARB**						
Employers Representative	Khaled ali	[Signature]	16/1/2024		Awc	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name: 157537 Sign: وليد خلافة	Date	17-1-2024						
Received by Employers Representative	UIR	REQ.NUM	58						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT	17	1	24	4	00
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300 E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description/ منسوب (3.5) متر from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (3.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: GARB SURVEY CONSATANT (xyz)	Comments by: General consultant (systra)
تم اكتشاف خلل في التسليم في المنطقة المذكورة في المخطط - الخط 157537	-you must follow specs and design dng -you must do leveling and lining the compacted side slope & filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد خلافة	وليد خلافة				
Contractor QA/QC*	XYZ	عبد الرحمن العرابي	17-1-2024	5:10	A	
	H.M.C	عبد الرحمن العرابي	17/1/2024	4:00	A	
GARB**						
Employers Representative	Khaled Ali	Khaled Ali	17/1/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أديان مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)					
Issued by Contractor	Name	137537	Sign	Date	REQ.NUM				
	وليد محمد		20-1-2024		59				
Received by Employers Representative	UIR	C1	C2	C3	DO	MM	YY	HH	MM
		KP	SU	OT				24	
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5	

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+300 TO 202+360		
	E=260139.0278 N=3136066.4661	E=260131.7531 N=3136006.9091	
Inspection description			
منسوب (8-متر) from st (202+300) to st (202+360) تسليم طبقة ردم منسوب (8-متر)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: GARB SURVEY CONSATANT. (xyz)	Comments by: General consultant (systra)
مستشار الاستشارات العامة	- you must follow specs and design dng.
مستشار الاستشارات العامة	- you must do leveling and lining
مستشار الاستشارات العامة	the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمد	وليد محمد				
Contractor QA/QC*	XYZ	عبد الرحمن الزباري	20/1/2024	10:00	A	
	H.M.C	محمود علي	20/1/2024	9:00	A	
GARB**						
Employers Representative	Khaled ali	كhaled ali	20/1/2024		Amr	

UNIVERSAL INSPECTION REQUEST



مكتب أد/حسن مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name:  Sign: 	Date	REQ.NUM
Received by Employers Representative	UIR	18-1-2024	60
		C1 C2 C3 DD MM YY HH MM	
		KP SU OT	24
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+920 TO 202+000	
	E=260168.4582 N=3136445.233	E=260164.6561 N=3136365.3242
Inspection description/		
منسوب (12.5-) متر from st (201+920) to st (202+000)		


INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
	- you must follow specs and design dng - you must do leveling and lining - the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	علي محمد					
Contractor QA/QC*	XYZ	علي محمد	20-1-2024	11:15	A	
	H.M.C	علي محمد	20-1-2024	3:45	A	
GARB**						
Employers Representative	Khaled ali		20/1/2024		Amrc	

UNIVERSAL INSPECTION REQUEST



مكتب أ.د/حسن مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR. Hassan Mahdy (H.M.C)
Issued by Contractor	Name: Sign:	Date	REQ.NUM
Received by Employers Representative	UIR	18-1-2024	61
		C1 C2 C3 DO MM YY HH MM	
		KP SU OT	234
CODE-1	CODE-2	CODE-3	CODE-4
CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+020 TO 202+060	
	E=260163.5058 N=3136345.3573	E=260160.9658 N=3136305.4382
Inspection description/ منسوب (12.5-) متر from st (202+020) to st (202+060)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT: xyz)	Comments by: General consultant (systra)
	- you must follow specs and design dwg - you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT

					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	ر.ع. محمد					
Contractor QA/QC*	XYZ		21-1-2024	5:15	A	
	H.M.C		21-1-2024	5:00	A	
GARB**						
Employers Representative	Ali K		21/1/2024		Awc	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name: Sign:	Date	REQ. NUM
Received by Employers Representative	UIR	21-1-2024	62
		C1 C2 C3 DD MM YY HH MM	
		KP SU OT	24

CODE-1

CODE-2

CODE-3

CODE-4

CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+300 TO 202+376	
	E=260139.0278 N=3136066.4661	E=260129.6912 N=3135991.0324
Inspection description/ منسوب (7.5) متر from st (202+300) to st (202+376) تسليم طبقة ردم منسوب (7.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

	-you must follow specs and design dng -you must do leveling and lining the compacted side slope & filling layer
--	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمود				A-AWC-R	
Contractor QA/QC*	XYZ	عبد الرحمن الابرار	21-1-2024	5:13	A	
	H.M.C	شودا شادي	21-1-2024	5:28	A	
GARB**						
Employers Representative	Khaled ali		21/1/2024		A	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name [Signature]	Date	22-1-2024															
Received by Employers Representative	Sign [Signature]	REQ.NUM	63															
UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>20</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			20			
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT			20													
CODE-1	CODE-2	CODE-3	CODE-4															
CODE-5																		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+920 TO 202+040 E=260168.4582 N=3136445.233	E=260162.2757 N=3136325.3952
Inspection description[طبقة ردم منسوب (12-) متر from st (201+920) to st (202+040)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. (xyz))	Comments by: General consultant (systra)
	-you must follow specs and design dw -you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	علي محمد الخياط	[Signature]	23-1-2024	9:00	A	
Contractor QA/QC*	H.M.C	[Signature]	22-1-2024	5:15	AWC	
GARB**						
Employers Representative	Khaled al	[Signature]	23/1/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	وليد محمود	وليد علاف	27-1-2024	65						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT			23		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+920 TO 202+060		
	E=260168.4582	E=260160.9658	
	N=3136445.233	N=3136305.4382	
Inspection description/			
من 200+876 إلى 202+376 من st (201+920) إلى st (202+060) طبقة ردم منسوب (-11.5) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))

Comments by: General consultant (systra)




-you must follow specs and design dng
-you must do leveling and lining
the compacted sideslope of filling layer

INSPECTION RESULT

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد علاف	وليد محمود					
Contractor QA/QC*	XYZ	أحمد محمد	27-1-24	5:00	A		
	H.M.C	محمود محمد	27-1-24	4:15	A		
GARB**							
Employers Representative	Khaled ali		27/1/2024				

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	رئيس المحور	رئيس خلاف	30-1-2024	66						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT			24		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+300 TO 202+376		
	E=260139.0278	E=260129.6912	
	N=3136066.4661	N=3135991.0324	
<u>Inspection description:</u> from st (202+300) to st (202+376) تسليم طبقة ردم منسوب (6.5-) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
	-you must follow specs and design drug -you must do leveling and lining the compacted sube slp & filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محور	وليد علان				يتم صيانة القطار في التور
Contractor QA/QC*	XYZ	محمد رافع	30-1-2024	4:00	(A)	
	H.M.C	محمد منتصر فوزه	30-1-24	12:30	AWC	
GARB**						
Employers Representative	Khated ali		30/1/2024			

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



شركة أديس مهدي
للإستشارات الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	وليد محمود	وليد عارف	18-2-2024	68						
Received by Employers Representative	[Stamp]	UIR	C1	C2	C3	DD	MM	YY	HH	MM
			ICP	SU	OT			24		
CODE-3		CODE-2	CODE-3	CODE-4		CODE-5				

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+300 TO 202+376		
	E=260139.0278	E=260129.6912	
	N=3136066.4661	N=3135991.0324	
<u>Inspection description:</u>			
من تسليم طبقة ردم منسوب (6-متر) from st (202+300) to st (202+376)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT - xyz)	Comments by: General consultant (systra)
	- you must follow specs and design durg - you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد محمود	وليد عارف					
Contractor QA/QC*	XYZ	عبد الرحمن الطراوي	19-2-2024	11:30	A		
	H.M.C	محمد مشهور فوزي	19-2-2024	12:00	A		
GARB**							
Employers Representative	rehaled ale	[Signature]	19/2/2024		Arre		

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	REQ.NUM							
	وليد محمود	وليد محمود	22-2-2024	69							
Received by Employers Representative	[Signature]	[Signature]	UIR	C1	C2	C3	DD	MM	YY	HH	MM
				KP	SU	OT			24		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+920 TO 202+060		
	E=260168.4582 N=3136445.233	E=260160.9658 N=3136305.4382	
Inspection description/			
منطقة ردم منسوب (10.5-) متر from st (201+920) to st (202+060)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time:

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))

مستشار الاستشارات العامة
للمقاولات العامة

Comments by: General consultant (systra)

-you must follow specs and design details
-you must do leveling and lining
the compacted side slope & filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود	وليد محمود				
Contractor QA/QC*	XYZ	عبد الرحمن الوائلي	24-2-2024	3:30	A	
	H.M.C	محمد منعم فوزي	24-2-2024	11:00	A	
GARB**						
Employers Representative	Khaled ali	[Signature]	24/2/2024		Amr	

UNIVERSAL INSPECTION REQUEST



مكتب أ.د. حسن مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والمصممات الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أ.د. حسن مهدي للإستشارات الهندسية		Designer Company*	DR .Hassan Mahdy (H.M.C)					
Issued by Contractor	Name	Sign	Date	REQ.NUM					
	و. ل. م. ه. د. أ. د. حسن مهدي		23-3-2024	74					
Received by Employers Representative	UIR	C1	C2	C3	DO	MM	YY	HH	MM
		KP	SU	OT			24		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5	

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+920 TO 202+060		
	E=260168.4582 N=3136445.233	E=260160.9658 N=3136305.4382	
Inspection description/			
منطقة ردم منسوب (10- متر) from st (201+920) to st (202+060)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
تم استلام الموقع (الطريق) - 23/3/2024	- you must follow specs and design drawings - you must do leveling and Cinning the compacted side slope of filling layer

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	و. ل. م. ه. د. أ. د. حسن مهدي						
Contractor QA\QC*	XYZ	محمد مشهور فوزي	23-3-2024	12:15	A		
	H.M.C	محمد مشهور فوزي	23/3/2024	12:00	A		
GARB**							
Employers Representative	Khaled ali		23/3/2024				

UNIVERSAL INSPECTION REQUEST



مكتب أ.د. حسن مهدي
للإستشارات الهندسية



الهيئة العامة للإعانة
SHARER



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name: Sign:	Date	REQ. NUM						
Received by Employers Representative	UIR	31-3-2024	75						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT			24		
CODE -1	CODE -2	CODE -3	CODE -4	CODE -5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+920 TO 202+060		
	E=260168.4582	E=260160.9658	
	N=3136445.233	N=3136305.4382	
Inspection description:			
منطقة ردم منسوب (9.5) متر from st (201+920) to st (202+060)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (systra))

Comments by: General consultant (systra)

نموذج شتر الكونسلانج - الهندس
- you must follow specs and design draw
- you must do leveling and lining
the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود محمد					
Contractor QA/QC*	XYZ عبد الرحمن الطريري		1-4-2024	12:00	A	
	H.M.C محمود علي		31-3-2024	11:00	A	
GARB**						
Employers Representative	Khakdali		1/4/2024		Done	

UNIVERSAL INSPECTION REQUEST



مكتب أ.د. حسن مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name:  Sign: 	Date	REQ.NUM						
Received by Employers Representative	UIR	1-4-2024	76						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT			24		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description(		
منسوب (3-متر) from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (3-متر)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	



Comments by: (GARB SURVEY CONSATANT (xyz))

Comments by: General consultant (systra)

تأكد من أن العمل يتم وفقاً للمواصفات والمواصفات المطلوبة - التفت إلى

- you must follow specs and design dra
- you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	أبو عجلة					
Contractor QA/QC*	XYZ		1-4-2024	11:30	A	
	H.M.C		1-4-2024	11:00	A	
GARB**						
Employers Representative	Khaled ali		1/4/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours									
The Work described below will be complete and ready for inspection at planned time shown									
Contractor Company	أبو عجيبة للمقاولات العامة				Designer Company*	DR .Hassan Mahdy (H.M.C)			
Issued by Contractor	Name Sign				Date	1-4-2024		Time	
Received by Employers Representative	UIR C1 C2 C3 DD MM YY HH MM KP SU OT 24								
CODE-1 CODE-2 CODE-3 CODE-4 CODE-5									

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
From 200+876 To 202+376	201+920 TO 202+376	
	E=260168.4582	E=260129.6912
	N=3136445.233	N=3135991.0324
<u>Inspection description:</u> As-Built for Fill from st (201+920) to st (202+376)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time	
Planned Inspection Date	Planned Inspection Time
1/4/2024	

COMPLIANCE EVIDENCE Must be included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA/QC*	XYZ		2-4-2024	9:00	A	
	H.M.C		2-4-2024	9:30	A	
GARB**						
Employers Representative						
