



أعمال إنشاء الحرس القنصلي للقطار الكهربائي السريع (أكتوبر / أوسمبيل)

القطاع الثاني (بشرى / مناقصة) من محطة ١٧٦+٧٠٠ حتى محطة ٢٢٤+٢٨٠٠ بطول ١٠٨ كم (إنشاء ملهى)

لتفويض شركة / أبو صبحية للمقاولات العامة والتوريدات العمومية من محطة ٢٠٠+٨٥٠ الى ٢٠٢+٣٥٠ بطول ١٠,٥ كم

رقم البند	بيان الأعمال	الوحدة	سعر البند	الكمية	الاجمالي
١	أعمال الإنشاء والتجهيز				
١-١	إزالة المسطح أصلاً لتجهيز الموقع من الركنين والحزومات والمسطحات والتي يستعملها لاستخدام الشبكية بناءً على الخطة التمهيدية الكثيرة بعمق حتى ٢٠ سم والعمق منها والمعادب الموضوعة لتهوية الأرصفة المماسية لكل حذو الشروع طبقاً للشروط والوصف والمواصفات الهندسية المشار إليها مسافة النقل حتى ٥٠ متر ويتم احتساب عاكس ٢٠٠ جنيه لكل ١ كم و١٢٠ الجنيه في شهر يناير ٢٠٢٣	م ^٢	٦,٠٠٠	٥	٣٠,٠٠٠
٢	إنشاء الجدران				
٢-١	المعدلة في سبتمبر ٢٠٢٢				
٢-٢	إزالة المسطح أصلاً حفر واستعمال المعدات الميكانيكية لجمع أنواع التربة عدا التربة البسيطة واستبدالها بالخرق أو الخرقة الموضوعة تحت المرءاء الأولية للوصول إلى نسبة الرطوبة المطلوبة والحد من الهبوط والحد من الترسبات للوصول إلى أقصى كثافة جافة ٩٥٪ من الكثافة الجافة المقصودة) ويحسب على البند تحميل ونقل التربة الزائدة لمسافة ٥٠٠ متر من محور الطريق ويتم احتساب حذاء الماسبب التمهيدية والخرقات الموضوعة التمهيدية والخرقات الموضوعة التمهيدية المسطحة والتدريج مسطحة طبقاً لآصول المصانعة ومواصفات الهيئة المعدلة للخرق والتكوير والمعدات الهندسية المشار إليها مطابقاً ١ جنيه لكل مسافة نقل خارج الحفر وتصبح ١,١ جنيه لكل البند من ١-٢٢٢٨٢١	م ^٢	٢٨,٢٠	١	٢٨,٢٠
٢-٣	إزالة المسطح أصلاً حفر واستعمال المعدات الميكانيكية في التربة الموضوعة عدا التربة البسيطة (استخدام الخرقة) واستبدالها بالخرق أو الخرقة الموضوعة تحت المرءاء الأولية للوصول إلى نسبة الرطوبة المطلوبة والحد من الهبوط والحد من الترسبات للوصول إلى أقصى كثافة جافة ٩٥٪ من الكثافة الجافة المقصودة) ويحسب على البند تحميل ونقل التربة الزائدة لمسافة ٥٠٠ متر من محور الطريق ويتم احتساب حذاء الماسبب التمهيدية والخرقات الموضوعة التمهيدية والخرقات الموضوعة التمهيدية المسطحة والتدريج مسطحة طبقاً لآصول المصانعة ومواصفات الهيئة المعدلة للخرق والتكوير والمعدات الهندسية المشار إليها مطابقاً ١ جنيه لكل مسافة نقل خارج الحفر وتصبح ١,١ جنيه لكل البند من ١-٢٢٢٨٢١	م ^٢			
٢-٤	نفس البند رقم ٢-٢ في شهر يناير ٢٠٢٣	م ^٢	٢٧,١٠	٣,٢٦٩	٨٨,٥٨٩,٩٠
٢-٥	نفس البند رقم ٢-٢ في شهر فبراير ٢٠٢٣	م ^٢	٢٨,٨٠	٣,٢٦٩	٩٤,١٤٧,٢٠
٢-٦	نفس البند رقم ٢-٢ في شهر مارس ٢٠٢٣	م ^٢	٣٠,٢٠	٣,٢٦٩	٩٨,٧٢٣,٨٠
٢-٧	نفس البند رقم ٢-٢ في شهر أبريل ٢٠٢٣	م ^٢	٣٠,٣٠	٣,٢٦٩	٩٩,٠٥٠,٧٠
٢-٨	نفس البند رقم ٢-٢ في شهر مايو ٢٠٢٣	م ^٢	٣٠,٥٠	٣,٢٦٩	٩٩,٧٠٤,٥٠
٢-٩	نفس البند رقم ٢-٢ في شهر يونيو ٢٠٢٣	م ^٢	٣٠,٩٠	٣,٢٦٩	١٠١,٠١٢,١٠
٢-١٠	نفس البند رقم ٢-٢ في شهر يوليو ٢٠٢٣	م ^٢	٣١,٠٠	٤,٦٥١	١٤٤,١٨١,٠٠
٢-١١	نفس البند رقم ٢-٢ في شهر أغسطس ٢٠٢٣	م ^٢	٣٢,٨٠	٤,٦٥١	١٥٢,٥٥٢,٨٠
٢-١٢	نفس البند رقم ٢-٢ في شهر سبتمبر ٢٠٢٢	م ^٢	٣٢,٩٠	٧٨١	٢٥,٦٩٤,٩٠
٢-١٣	نفس البند رقم ٢-٢ في شهر أكتوبر ٢٠٢٢	م ^٢	٢,٧٥	٢٩,٦٩٧	٨١,٦٦٦,٧٥
٢-١٤	مطابقاً ١,١ جنيه لكل ١ كم مسافة النقل المعدلة ٢٠٢٢-٢٠٢٣	م ^٢			
٢-١٥	المعدلة في سبتمبر ٢٠٢٢				
٢-١٦	إزالة المسطح أصلاً حفر واستعمال المعدات الميكانيكية في التربة الموضوعة عدا التربة البسيطة (استخدام الخرقة) واستبدالها بالخرق أو الخرقة الموضوعة تحت المرءاء الأولية للوصول إلى نسبة الرطوبة المطلوبة والحد من الهبوط والحد من الترسبات للوصول إلى أقصى كثافة جافة ٩٥٪ من الكثافة الجافة المقصودة) ويحسب على البند تحميل ونقل التربة الزائدة لمسافة ٥٠٠ متر من محور الطريق ويتم احتساب حذاء الماسبب التمهيدية والخرقات الموضوعة التمهيدية والخرقات الموضوعة التمهيدية المسطحة والتدريج مسطحة طبقاً لآصول المصانعة ومواصفات الهيئة المعدلة للخرق والتكوير والمعدات الهندسية المشار إليها مطابقاً ١ جنيه لكل مسافة نقل خارج الحفر وتصبح ١,١ جنيه لكل البند من ١-٢٢٢٨٢١	م ^٢	٣٧,٠٠	١	٣٧,٠٠
٢-١٧	إزالة المسطح أصلاً حفر واستعمال المعدات الميكانيكية في التربة البسيطة ويحسب على البند التحميل ونقل خارج الحفر مسافة ٥٠٠ متر من محور الطريق ١- إزالة المسطح أصلاً حفر واستعمال المعدات الميكانيكية لجمع أنواع التربة عدا التربة البسيطة واستبدالها بالخرق أو الخرقة الموضوعة تحت المرءاء الأولية للوصول إلى نسبة الرطوبة المطلوبة والحد من الهبوط والحد من الترسبات للوصول إلى أقصى كثافة جافة ٩٥٪ من الكثافة الجافة المقصودة) ويحسب على البند تحميل ونقل التربة الزائدة لمسافة ٥٠٠ متر من محور الطريق ويتم احتساب حذاء الماسبب التمهيدية والخرقات الموضوعة التمهيدية والخرقات الموضوعة التمهيدية المسطحة والتدريج مسطحة طبقاً لآصول المصانعة ومواصفات الهيئة المعدلة للخرق والتكوير والمعدات الهندسية المشار إليها مطابقاً ١ جنيه لكل مسافة نقل خارج الحفر وتصبح ١,١ جنيه لكل البند من ١-٢٢٢٨٢١	م ^٢			
٢-١٨	نفس البند رقم ٢-١٧ في شهر أغسطس ٢٠٢٢	م ^٢	٩٣,٣٠	٣١	٢,٨٩٢,٣٠
٢-١٩	نفس البند رقم ٢-١٧ في شهر سبتمبر ٢٠٢٢	م ^٢	١٠,٨١,٣٠	٤,٦٦٨	٤٥١,٣٩٤,٤٠
٢-٢٠	نفس البند رقم ٢-١٧ في شهر أكتوبر ٢٠٢٢	م ^٢	١١٦,٩٠	٩,٧٥٨	١,١٤٠,٧١٠,٢٠
٢-٢١	نفس البند رقم ٢-١٧ في شهر نوفمبر ٢٠٢٢	م ^٢	١٢٥,٥٠	١٣,١٣٠	١,٦٤٧,٨١٥,٠٠
٢-٢٢	نفس البند رقم ٢-١٧ في شهر ديسمبر ٢٠٢٢	م ^٢	٨,٦٠	١	٨,٦٠
٢-٢٣	مطابقاً ١,١ جنيه لكل ١ كم مسافة النقل المعدلة ٢٠٢٢-٢٠٢٣	م ^٢	٢,٧٥	٢٧,٠٨٧	٧٤,٤٨٩,٢٥



أعمال إنشاء الجسر القروي للقطار الكهربائي السريع (أكتوبر / أوسمحل)

القطاع الثاني (بني مزار / منطوط) من محطة ١٧٦+٧٠٠ حتى محطة ٢٣٤+٨٠٠ بطول ١٥٨ كم (تجاه طلوس)

تنفيذ شركة / أبو عجلة للمقاولات العامة والتي بدأت العمومية من محطة ٢٠٠+٨٥٠ إلى ٢٠٢+٣٥٠ بطول ١,٥ كم

رقم البند	بيان الأعمال	الوحدة	سعر وحدة	الكمية	الاجمالي
٥-٢	باعت المكتب أعمال عمر باستخدام المصداق المبكك في السور وأسوية الدفان آلات السوية وآلات الرصا والمواد الأساسية للوصول إلى نسبة الرطوبة المطلوبة والمبكك الجيد بالخرسانات الوصول إلى أقصى كثافة ماله (٩٩٪ من الكثافة الجافة القصوى) ومحمّل على البند تحميل ونقل الكمية الزائدة لسفافة ١,٨ كم من محور الطريق و آلة تحميل استخدام الماء في تثبيت السور و اعداد سقالات على السور حركة المعدات وتم التخليطة طبقاً للمنسبب التصميمية والمقايضة الموازنة والرسومات التصميمية المصنوعة والرداء وحصى مستخلصة طبقاً لأصول الريادة ومواصفات الريادة العامة للطرق والكباري والمعدات الهندسية المشرف بطول ١ حبة / كم مسافة على تاج السور ونسج ١:١ حبة / كم حبات من ٢٢/١٠٠.	٢٥	٣٩,٤٠	٣٤,٠٣٥	١,٣٤٠,٩٧٩,٠٠٠
٦-١	الحفر البند رقم ٥-٢ في شهر سبتمبر ٢٠٢٢	٢٥	٣٩,٤٠	٣٤,٠٣٥	١,٣٤٠,٩٧٩,٠٠٠
٦-٢	طائرة ١,٨ حبة لكل ١ كم (مسافة النقل المصنوعة ١:١ = ١,٨ كم)	٢٥	١,٦٥	٣٤,٠٣٥	٥٦,١٥٧,٧٥٠
٢	تسليم البند				
	المبلغ لعدد من ٢٠٢٢/٩/٢٢				
١-٢	أعمال تحميل وتوريد ونقل الكمية المطلوبة للمواصفات واستخدام آلات السوية بسفافة لا يزيد عن ١,٥ سم على منسوب ٢-١ مائل أسفل منسوب القربة وسفافة لا يزيد عن ١,٥ سم على منسوب ٢-٢ مائل (من منسوب القربة لاستكمال المنسوب التصميمي التكميلي الجسر واللافتة) (نسبة تحميل الكيلوغرام لا تقل عن ١٠١٦) ورشها بالماء الأساسية للوصول إلى نسبة الرطوبة المطلوبة والمبكك الجيد بالخرسانات الوصول إلى أقصى كثافة ماله (٩٩٪ من الكثافة الجافة القصوى) ويتم التعديل طبقاً للمنسبب التصميمية والمقايضة الموازنة والرسومات التصميمية المستندة والرداء وجميع مستخلصة طبقاً لأصول الريادة ومواصفات الريادة العامة للطرق والكباري والمعدات الهندسية المشرف بطول ١ حبة / كم مسافة على تاج السور ونسج ١:١ حبة / كم حبات من ٢٢/١٠٠.	٢٥	٧٤,٥٠	١,٠١١٤,٩٣٩,٥	٧٥,٣٥
١-٢	في حالة طلب جهاز الإشراف زيادة نسبة التعداد من ١٠٩٨ ونسج زيادة ١ حبة على زيادة نسبة التعداد لكل ١,٥ كم مسافة النقل حتى ٢ كم و يتم احداثها طائراً ١:١ حبة لكل كم وارتداء أو التعداد ونسج ١:١ حبة لكل كم التعداد من ٢٠٢٢/٩/٢٢.				
١-٢	المسح يشمل عمل تسويات و تخطيط و استمارات و علم توقيع العمل حتى مسافة ٢ كم				
١-٢	و البند لا يشمل القيمة المصنوعة.				
١-٢	طائرة مسافة على ٢ كم	٢٥	١,٥٠	١	١,٥٠
١-٢	كثيرة توريد كربة	٢٥	١٣,٠٠	١	١٣,٠٠
٢-١	قيمة البند المصنوعة الكربة والإضافة إلى نسبة التعداد ١:١ = ١٣,٠٠	٢٥	١٣,٠٠	١	١٣,٠٠

تتم احداثها مساحات في بنود المرسلة طبقاً لتسليم القائمة الموضحة ٢-٢٤ على ان يتم احتساب الزيادة حسب سعر السوق الفروق ليعبر.

الاجمالي	خمسة مليون ومئة مائة الف جنبها لا غير	٥,٧٠٠,٠٠٠,٠٠٠
----------	---------------------------------------	---------------



مدير عام المشروعات
الهندس / مصطفى قسبان
الفرع

مهندس اللجنة
الفرع

مدير المشروع والإستشاري
الفرع

مهندس الشركة المقولة
الفرع



المنطقة السادسة - بيني سوف

مذكرة

للعرض على السيد المهندس / رئيس قطاع التنفيذ و المناطق

بخصوص: طلب شركة ابو عجيبة للمقاولات العامة اضافة مدة لعملية "انشاء الجسر الترابي لمشروع القطر الكهربائي السريع
من كم 200+850 الى كم 202+350 بطول 1.5 كم (اتجاه ملوي) .

- اسندت الهيئة المشروع عالية الى الشركة المنفذة بالعقد رقم (2024/2023/499) المؤرخ في 2023/10/12 بقيمة اجمالية قدرها 57000000 جنيها ولمدة (8) شهور .
- بتاريخ 2023/10/19 تم تسليم الموقع للشركة المنفذة ليكون تاريخ النهو طبقا للعقد الاصيلي في 2024/06/18 .
- وردنا كتاب الشركة المنفذة تطلب فيه اضافة مدة ستة شهور للعملية لوجود بعض المعوقات التي تسببت في تاخر نهو الاعمال (مرفق) .

الرأي

- التفضل بالإحاطة.
- التكرم بالموافقة على اضافة مدة قدرها (6) شهور من تاريخ إنتهاء العقد في 2024/06/18 ليصبح تاريخ النهو 2024/12/18 وذلك للمبررات الاتية :-

- 1- بناءا على قرار مجلس الوزراء بجلسته رقم (254) المنعقدة بتاريخ 2023/08/30 .
- 2- بناءا على المذكرة المعروضة على السيد اللواء مهندس رئيس مجلس الادارة بخصوص الموافقة على مد مدة عقود المشروعات (6 اشهر) في ضوء كتاب الوزارة رقم (13793) والمرفق به كتاب دوري السيد اللواء / امين عام مجلس الوزراء رقم (3-27815) بذات الخصوص (مرفق) .
- 3- تاخر التنفيذ بسبب تحرير سعر الصرف وزيادة تكلفة أسعار المواد الخام وارتفاع اسعار نقلها .
- 4- نقص الدعم الدولارى بالاسواق .
- 5- ارتفاع اسعار قطع الغيار ونذرة توافرها بالاسواق .

والأمر مفوض

وتفضلوا سيادتكم بقبول فائق الاحترام

وتفضلوا سيادتكم بقبول فائق الاحترام

تحرير في: 2024/ /

رئيس الإدارة المركزية

المنطقة السادسة - بيني سوف

مهندس /

طارق يوسف الجزار



استشاري أبحاث التربة والاساسات :
أ.د. هشام محمد حلمي



مشروع :
قطار اسوان الكهربائي السريع - القطاع الثاني

تقرير بنتائج اختبارات صلاحية تربة للتأسيس

مقدمة : تم إعداد هذا التقرير بناءا على طلب شركة / ابو عجيبة
ولذلك لتحديد خصائص ومدى صلاحية عينة تراب كثر من طينية تصلح للتأسيس

مصدر العينة : عند المحطة / (٢٠١ + ٨٠٠) أرض طينية

- المندوب : وقد تم توريد العينة بمعرفة ١- م/ محمود عبد الرحيم الحيني (مهندس الإشراف مكتب د/ حسن مهدي) رقم الهاتف = ٠١١٥٩٤٠٠١٠٨

- تاريخ توريد العينة : ٢٠٢٣/٨/١٦

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفلووط)

- التوضيف الظاهري للعينة : كثبان رملية ناعمة (سفو)

وقد تم عمل الاختبارات الآتية :

- ١- التدرج الحبيبي
- ٢- حد السيولة واللدونة
- ٣- اختبار البروكتور
- ٤- اختبار CBR
- ٥- اختبار المواد العضوية

وكالت نتائج الاختبارات كالتالي :

م	نوع الاختبار	النتائج	ملاحظات
١	تصنيف العينة	A-3	
٢	مجال اللدونة	--	
٣	أقصى كثافة جافة (البروكتور) $\gamma_d \max$	1.902 gm/cm3	
٤	نسبة للماء الأمولية	9.10%	
٥	رقعة CBR المغمورة	9.30%	
6	المواد العضوية	لا يوجد	

• و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي غير صالحة للتأسيس عليها .



مهندس المعمل
م/ محمد إسماعيل
التوقيع / محمد إسماعيل

فني المعمل
أ/ أحمد حسن عبيد
التوقيع / أحمد حسن عبيد

Coarse & Fine Aggregate Grading - ASTM C136 & AASHTO T27

أرض طبيعية

الموقع: ST = 201+800

21/08/2023

التاريخ:

نتائج الاختبار :-

رقم المنخل (mm)	رقم المنخل (inch)	وزن المحجوز على كل منخل	وزن المحجوز الفرغس	المحجوز %	الباقي %
125	5"	0	0	0%	100%
101.6	4"	0	0	0.00%	100.00%
76.2	3"	0	0	0.00%	100.00%
63.5	2.5"	0	0	0.00%	100.00%
50.8	2"	0	0	0.00%	100.00%
37.5	1.5"	0	0	0.00%	100.00%
25	1"	0	0	0.00%	100.00%
19	3/4"	0	0	0.00%	100.00%
12.7	1/2"	0	0	0.00%	100.00%
9.5	3/8"	0	0	0.00%	100.00%
4.75	# 4	0	0	0.00%	100.00%
	الباقي من منخل # 4	500			100.00%
	وزن العينة الكلية	500			
	وزن عينة التام	500			
2.36	# 10	0	0	0.0%	100.0%
0.425	# 40	80	80	16.0%	84.0%
0.075	# 200	392	472	94.4%	5.6%
السيولة و اللدونة		N.P			
التصنيف		A-3			

ملاحظات : توصيف العينة : غثيان رملية ناعمة (Sand Dunes)



مهندس المعمل
د. محمد بن عبد الله
التوقيع: محمد بن عبد الله

في المعمل
أحمد حسن عتيبة
التوقيع: أحمد حسن عتيبة

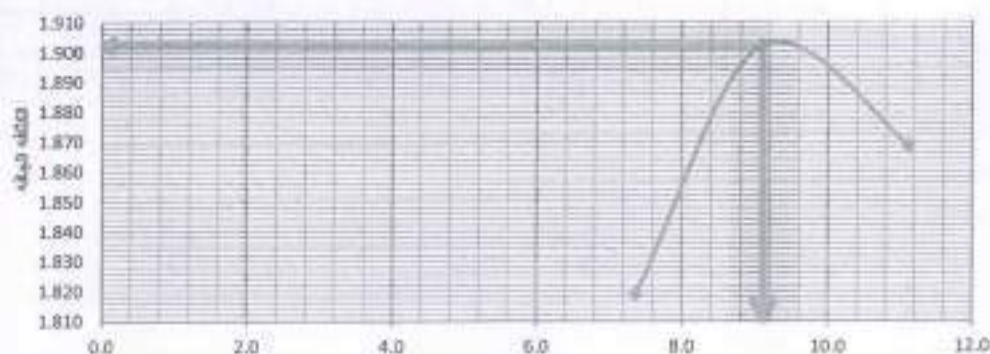
Modified Proctor : ASTM D1557

نوع العين:	عينة كابل رملية
تصنيف العين:	A-3
نتائج الاختبار:	
وزن القالب:	5731
حجم القالب:	2140
الغسالة جافة:	1.902
الغسالة الرطبة:	9.10

رقم الاختبار:	1	2	3
وزن القالب + العينة رطبة:	9910.0	10172	10174
وزن القرينة الرطبة:	4179.0	4441	4443
الوزن الرطبة:	1.953	2.075	2.076

رقم العينة:	1	2	3	4	5	6
وزن العينة:	25.2	25.33	52.2	54.11	53.11	52.31
وزن القالب + العينة رطبة:	150.0	150.0	150.0	150.0	150.0	150.0
وزن القالب + العينة جافة:	141.22	141.66	141.8	142.05	140.31	140.21
وزن الغسالة:	8.8	8.3	8.2	7.9	9.7	9.8
وزن العينة جافة:	116.02	116.33	89.6	87.94	87.2	87.9
المستوى المائي %:	7.6	7.2	9.2	9.0	11.1	11.1
متوسط المستوى المائي %:	7.4	9.1	11.1			
المتانة الجافة:	1.819	1.902	1.868			

Modified Proctor Chart



ملاحظات:



مهندس العمل
د. محمد بن عبد الله
الرياض / المملكة العربية السعودية

في العمل
أحمد حسن عتيق
توقيع المهندس

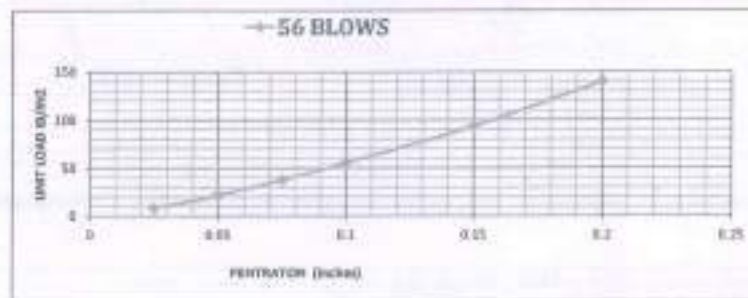
المعيار نسبة تحمل كاليفورنيا (ASTM D1883) (C, B, R)

A-3		تصنيف العينة	
56	عدد الضربات	56	عدد الضربات
2	رقم القالب	3131	حجم القالب (سم ³)
83.68	وزن القالب	5286	وزن القالب (كجم)
150	وزن القالب والحملية رطبة دم	9545	وزن القالب وحملية رطبة (دم)
149	وزن القالب والحملية جافة دم	4255	وزن القالب رطبة (دم)
8	وزن الماء دم	1.997	معدل الرطوبة (دم/سم ³)
88.3	وزن القالب جافة دم	1.831	نسبة الماء جافة (دم/سم ³)
9.1%	المحتوى المائي %	1.900	معدل الكثافة (دم/سم ³)
		96.3%	نسبة التسك

نسبة التماسك	0.00%	غير قابلة للتماسك
--------------	-------	-------------------

حسابات نسبة تحمل كاليفورنيا

7.62	5.08	3.81	2.54	1.95	1.27	0.635	الأحمر في بالم
0.3	0.2	0.15	0.1	0.075	0.05	0.025	الأحمر في بالم حبة
329.0	190	127.0	75.0	51.0	29.0	11.0	الوزن kg
722.912	418.78	279.908	185.3	112.404	63.916	24.244	الوزن بالبراون
241.08	139.65	93.345	55.125	37.485	21.315	8.085	الحمل lb/in ²



9.3%	قيمة C.B.R
------	------------

ملاحظات: تم نشر القالب في الماء لمدة 24 ساعة قبل إجراء الاختبار.

مهندس العمل
د. محمد عبد الله
قوله: أحمد عبد الله

في العمل
أحمد حسن عبد
محمد عبد الله



استشاري أبحاث التربة والاساسات :
أ.د.م. هشام محمد حلمي



مشروع :
قطار اسوان الكهربائي السريع - القطاع الثاني

تقرير بنتائج اختبارات صلاحية تربة للتأسيس

مقدمة : تم إعداد هذا التقرير بناءا على طلب شركة /ابو عجيلة

وذلك لتحديد خصائص ومدى صلاحية عينة تراب كل من طبعية تصلح للتأسيس

مصدر العينة : عند المحطة / (٢٠١٠٧٠٠) أرض طبيعية

- المندوب : وقد تم توريد العينة بمعرفة ١- م/محمود عبدالرحيم الحيني (مهندس الإشراف مكتب د/ حسن مهدي) رقم الهاتف = ٠١١٥٩٤٠٠١٠٨

تاريخ توريد العينة : ٢٠٢٣ / ٨ / ١٦

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفلوط)

- التوصيف الظاهري للعينة : كتبان رملية ناعمة (سقا)

وقد تم عمل الاختبارات الآتية :

- ١- اختبار الحبيبي
- ٢- حد السيولة واللدونة
- ٣- اختبار البرونكتور
- ٤- اختبار CBR
- ٥- اختبار المواد العضوية

وكلفت نتائج الاختبارات كالآتي :

ملاحظات	النتائج	نوع الاختبار	م
	A-3	تصنيف العينة	١
	--	مجال اللدونة	٢
	1.910 gm/cm3	أقصى كثافة جافة (البرونكتور) yd max	٣
	9.6%	نسبة المياه الأموية	٤
	8.50%	قيمة CBR المغورة	٥
	لا يوجد	المواد العضوية	٦

• و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي غير صالحة للتأسيس عليها .



مهندس المعمل
أ.م. احمد حليم
التوقيع / احمد حليم

فني المعمل
أ. احمد حسنة عطيه
التوقيع / احمد حسنة عطيه

Coarse & Fine Aggregate Grading - ASTM C136 & AASHTO T27

الشارخ :	21/06/2023	الموقع : ST = 201+700	أرض طبيعية
----------	------------	-----------------------	------------

نتائج الاختبار :-

رقم مخل (mm)	رقم المخل (inch)	وزن المجهز على كل مخل	وزن المجهز الفراسي	المجهز %	المز %
127	5"	0	0	0%	100%
101.6	4"	0	0	0.00%	100.00%
76.2	3"	0	0	0.00%	100.00%
63.5	2.5"	0	0	0.00%	100.00%
50.8	2"	0	0	0.00%	100.00%
37.5	1.5"	0	0	0.00%	100.00%
25	1"	0	0	0.00%	100.00%
19	3/4"	0	0	0.00%	100.00%
12.7	1/2"	0	0	0.00%	100.00%
9.5	3/8"	0	0	0.00%	100.00%
4.75	# 4	0	0	0.00%	100.00%
	المز من مخل # 4	500			100.00%
	وزن العينة الكلي	500			
	وزن عينة الناعم	500			
2.36	# 10	10	10	2.0%	98.0%
0.425	# 40	77	87	17.4%	82.6%
0.075	# 200	379	466	93.2%	6.8%
المسبوبة و الدونة		N.P			
التصنيف		A-3			

ملاحظات : توصيف العينة : تليان رملية ناعمة (Sand Dunes)



مهندس العمل
أحمد حسن عتيق
التوقيع

أحمد حسن عتيق
مهندس العمل

Modified Proctor : ASTM D1557

نوع العينة:	عينة بثلاث رملية
تصنيف العينة:	A-3

نتائج الاختبار:

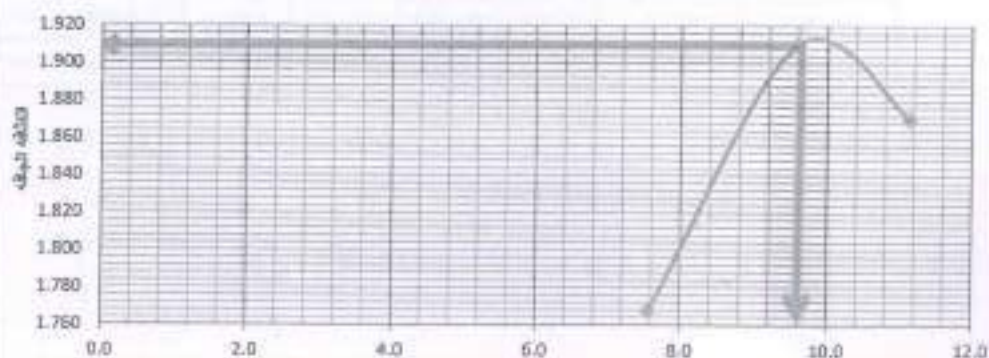
1.910	القيمة الجافة
9.59	المراد الأمثل

5731	وزن القالب
2140	حجم القالب

رقم الاختبار	1	2	3
وزن القالب + العينة رطبة	9799.0	10210	10179
وزن التربة الرطبة	4068.0	4479	4648
الكثافة الرطبة	1.901	2.093	2.079

رقم الجهد	1	2	3	4	5	6
وزن الجهد	52.31	54.32	52.12	53.66	54.21	52.32
وزن الجهد + العينة رطبة	150.0	150.0	150.0	150.0	150.0	150.0
وزن الجهد + العينة جافة	143.21	143.2	141.4	141.61	140.5	140.1
وزن المياه	6.8	6.8	8.6	8.4	9.5	9.9
وزن العينة جافة	90.9	88.86	89.28	87.95	86.29	87.78
المحتوى المائي %	7.5	7.7	9.6	9.5	11.0	11.3
متوسط المحتوى المائي %	7.6	9.6	11.1			
الكثافة الجافة	1.767	1.910	1.870			

Modified Proctor Chart



ملاحظات:



مهندس العمل
د. أحمد سليمان
التوقيع: أحمد سليمان

مهندس العمل
أحمد سليمان عليه
التوقيع: أحمد سليمان

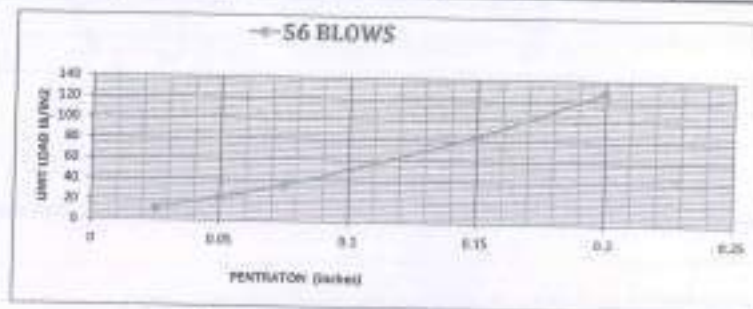
اختبار نسبة تحميل كاليفورنيا (C . B . R) ASTM D1683

A-3		تصنيف العينة	
55	عدد الضربات	36	عدد الضربات
9	زمن التوقف	2131	حجم القالب (سم ³)
93.88	وزن القالب	5288	وزن القالب (جم)
150	وزن الحفلة بالحجم رطبة (جم)	9030	وزن القالب + وزن الحفلة رطبة (جم)
141.8	وزن الحفلة بالحجم رطبة (جم)	4941	وزن الحفلة رطبة (جم)
8.4	وزن الماء (جم)	2.037	كمية الرطوبة (جم/سم ³)
87.9	وزن الحفلة رطبة (جم)	1.859	المسافة المقاسة (جم/سم ³)
9.8%	المستوى المائي %	1.910	كمية التورخور (جم/سم ³)
		97.4%	نسبة الدمك

نسبة الانتفاش	0.08%	غير قابلة للحساب
---------------	-------	------------------

حساب نسبة تحميل كاليفورنيا

7.62	5.08	3.81	2.54	1.95	1.27	0.635	الاختبار في الماء
0.3	0.2	0.15	0.1	0.075	0.05	0.025	الاختبار في الماء
234.0	174	115.0	69.0	48.0	31.0	15.0	التراب kg
515.736	383.496	253.46	152.076	105.792	68.324	33.06	التراب بالتراب
171.99	127.89	84.525	50.715	35.28	22.785	11.025	التراب 1B/1N2



8.5%	قيمة C . B . R
------	----------------

ملاحظة: تم إجراء الاختبار في الماء لمدة 96 ساعة قبل إجراء الاختبار



مهندس المساحة
د. أحمد محمد حسن
مهندس المساحة

مهندس المساحة
أحمد محمد حسن
مهندس المساحة



التاريخ : 2024-9-22

اسم المشروع : مشروع القطار الكهربائي السريع قطاع (أكتوبر - أبو سمبل)
الموضوع : اعتماد الهيئة العامة للطرق والكبارى لطلبات استلام الأعمال الخاصة بالمشروع
الشركة المنفذة : ابوعجيلة للمقاولات العامة والتوريدات العمومية في المسافة
من (200+876) الى (202+376) بطول 1.5 كم.

عقد رقم : - (2023-2022-1968) بتاريخ 2023-5-17

- (2023-2023-142) بتاريخ 2023-8-3

- (2023-2023-143) بتاريخ 2023-8-3

- (2023-2023-499) بتاريخ 2023-10-12

- (2023-2023-1021) بتاريخ 2024-1-18

- (2023-2023-1229) بتاريخ 2024-2-26

- (2024-2024-209) بتاريخ 2024-8-21

تم الإطلاع ظاهريا على طلبات الفحص الخاصة بالمشروع المذكور عاليه والمرفقة بمستخلصات
المذكورة عالية لعدد (77) طلبات فحص وذلك بعد مراجعتها وتوقيعها من استشارى المساحة (XYZ)
واستشارى ضبط الجودة (مكتب أ.د حسن مهدي) وعليه تم اعتمادها

وتنقسم الى :

- (53) طلبات فحص لأعمال الردم .
- (14) طلبات فحص لأعمال الحفر .
- (4) طلبات فحص لأعمال التطهير .

عن الاستشاري (أ.د حسن مهدي)
مشاريع القطار السريع

مهندس الاستشاري
أ.د حسن مهدي

يعتمد،،،

مهندس الهيئة العامة للطرق والكبارى

مهندس الهيئة العامة للطرق والكبارى

اتجاه ملوي

من المحطة ٨٥٠+٢٠٠ الى المحطة ٢٠٢+٣٥٠ بطول ١,٥ كم رقم العقد (٢٠٢٤/٢٠٢٣/٤٩٩)

البرنامج الزمني

أعمال الجسر الترابي لمسار القطر الكهربائي السريع الخط الثاني (الفيوم / بني سويف - أبوسمبل) القطاع الثاني (بني مزار / منفلووط)

تاريخ استلام الموقع ٢٠٢٣/١٠/١٩

مدة تنفيذ العمل ٨ شهور

تاريخ نهو الاعمال ٢٠٢٤/٦/١٨

رقم البند	بيان الاعمال	الوحدة	الكمية	أكتوبر-٢٠٢٣	نوفمبر-٢٠٢٣	ديسمبر-٢٠٢٣	يناير-٢٠٢٤	فبراير-٢٠٢٤	مارس-٢٠٢٤	أبريل-٢٠٢٤	مايو-٢٠٢٤	يونيو-٢٠٢٤
٥-٢	التراب المكعب أعمال حفر باستخدام المعدات الميكانيكية في السفو وتسوية السطح بألات التسوية والريش بالمياه الأسولية للوصول إلى نسبة الرطوبة المطلوبة والتمك الجيد بالهراسات للوصول إلى أقصى كثافة جافة (95 % من الكثافة الجافة القصوى) ومحمل على البند تحميل ونقل الأتربة الزائدة لمسافة ١,٥ كم من محور الطريق مع تغطية ناتج الحفر بالمقلب بطبقة أتربة بسمك متوسط ٢٠ سم و الفنة تشمل استخدام المياه في تثبيت السفو و اعداد مدقات على السفو لحركة المعدات و ويتم التنفيذ طبقاً للمناسيب التصميمية والقطاعات العرضية النموذجية والرسومات التفصيلية المعتمدة والبند بجميع محتلاته طبقاً لأصول الصناعة ومواصفات الهيئة العامة للطرق والكباري وتعليمات المهندس المشرف .	م³										
	نفس البند رقم ٥-٢ في شهر سبتمبر ٢٠٢٣	م³	٣٤٠٣٥									
٤-٢	بالتراب المكعب اعمال حفر بالمعدات الميكانيكية في تربة صخرية ومحمل على البند الاتي ١- تحميل ونقل ناتج الحفر لمسافة لا تقل عن ٥٠٠ متر ٢- اربكة الميول الجانبية باستخدام المعدات الميكانيكية ٣- توريد التربة مطابقة للمواصفات ولشغلها باستخدام الات التسوية بسمك لا يزيد عن ٢٥ سم لاستكمال المنسوب التصميمي لتشكل الجسر والاكتاف (نسبة تحمل كالفورنيا لا تقل عن ١٠ %) ورشها بالمياه الاسولية للوصول الى نسبة الرطوبة المطلوبة والتمك الجيد بالهراسات للوصول الى أقصى كثافة جافة (95% من الكثافة الجافة القصوى). ويتم التنفيذ طبقاً للمناسيب التصميمية والقطاعات العرضية النموذجية والرسومات التفصيلية المعتمدة والبند بجميع محتلاته طبقاً لأصول الصناعة ومواصفات الهيئة العامة للطرق والكباري وتعليمات المهندس المشرف.	م³	توزيع الكميات									
	المنفذ في أغسطس ٢٠٢٣											
١-٤-٢	ذات اجهاد (٢٠٠-٣٠٠) كجم/سم² لمسافة نقل حتي ٥٠٠ متر في اغسطس ٢٠٢٣	م³	٣١									
٢-٤-٢	ذات اجهاد (٣٠٠-٤٠٠) كجم/سم² لمسافة نقل حتي ٥٠٠ متر في اغسطس ٢٠٢٣	م³	٤١٦٨									
٣-٤-٢	ذات اجهاد (٤٠٠-٥٠٠) كجم/سم² لمسافة نقل حتي ٥٠٠ متر في اغسطس ٢٠٢٣	م³	٩٧٥٨									
٤-٤-٢	ذات اجهاد (٥٠٠-٦٠٠) كجم/سم² لمسافة نقل حتي ٥٠٠ متر في اغسطس ٢٠٢٣	م³	١٣١٣٠									

عن الاستشاري أ.د حسن مهدي

مهندس الشركة المنفذة

يعتمد

مهندس الهيئة العامة للطرق والكباري

م/احمد عزب

م/محمود غريب

التوقيع

التوقيع

م/احمد فتوح

التوقيع





البرنامج الزمني

أعمال الجسر الترابي لمسار القطر الكهربائي السريع الخط الثاني (الفيوم / بني سويف - أبوسمبل) القطاع الثاني (بني مزار / منفلووط)

من المحطة ٨٥٠+٢٠٠ الي المحطة ٢٠٢+٣٥٠

بطول ١,٥ كم رقم العقد (٢٠٢٤/٢٠٢٣/٤٩٩)

اتجاه ملوي

تاريخ استلام الموقع ٢٠٢٣/١٠/١٩

مدة تنفيذ العمليه ٨ شهور

تاريخ نهو الاعمال ٢٠٢٤/٦/١٨

رقم البند	بيان الاعمال	الوحدة	الكمية	أكتوبر-٢٠٢٣				نوفمبر-٢٠٢٣				ديسمبر-٢٠٢٣				يناير-٢٠٢٤				فبراير-٢٠٢٤				مارس-٢٠٢٤				أبريل-٢٠٢٤				مايو-٢٠٢٤				يونيو-٢٠٢٤																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
				من ٧-١	من ١٥-٨	من ٢٢-١٦	من ٣٠-٢٣	من ٧-١	من ١٥-٨	من ٢٢-١٦	من ٣٠-٢٣	من ٧-١	من ١٥-٨	من ٢٢-١٦	من ٣٠-٢٣	من ٧-١	من ١٥-٨	من ٢٢-١٦	من ٣٠-٢٣	من ٧-١	من ١٥-٨	من ٢٢-١٦	من ٣٠-٢٣	من ٧-١	من ١٥-٨	من ٢٢-١٦	من ٣٠-٢٣	من ٧-١	من ١٥-٨	من ٢٢-١٦	من ٣٠-٢٣																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																														
٢	أعمال الحفر																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												

عن الاستشاري أ.د حسن مهدي

مهندس الشركة المنفذة

يعتمد؟؟؟

مهندس الهيئة العامة للطرق والكباري

م/احمد عزب

م/محمود عزب

التوقيع

التوقيع

م/احمد فتوح
التوقيع /





هيكل تنظيمي للعاملين بمشروع القطار السريع شركة أبوعجيلة للمقاولات العامة

التاريخ : ٢٠٢٢-٩-٢٤

اسم المشروع : مشروع القطار السريع (أكتوبر-أوسمبل)

رقم العقد: (٢٠٢٤/٢٠٢٣/٤٩٩)

رقم التليفون	عدد سنوات الخبرة	الوظيفة	الاسم	مستسل
01009742637	10	مدير المشروع	محمد حامد يحي	1
01017199596	5	مدير المكتب الفني	احمد احمد محمود	2
01019930593	5	مدير ضبط الجودة	نادي عادل	3
01114562154	10	مدير السلامة الوقائية	زبيح توحيد	4
01090254469	5	مهندس التنفيذ	وليد محمود محمد	5
01559856322	5	مهندس صيانة (ميكانيكا وكهرباء)	محمد عماد الدين محمد	6
01223691236	5	مهندس التخطيط والبرمجة الزمنية	احمد قاسم	7
01002612002	5	مراقب تنفيذ (فني مواد)	احمد السيد احمد	8
01063768307			محمد نادي	
01029734478	5	حساب كميات	عبدالعال رجب	9
01064950832	7	مساح	حسين محمد جبريل	10
01033806848	7		محمد جمال	
01092355765	5	فني سلامة مرورية	محمد ابوغنيمه	11
0102245866	5		محمد حسين	

مهندس الشركة المنفذة

م / احمد فنيح

التوقيع /

عن الاستشاري أ.د حسن مهدي
م / احمد عزب
م / محمود عزب
التوقيع /

يعتمد:؟؟

مهندس الهيئة العامة للطرق والكباري



بيان المعدات

التاريخ : ٢٠٢٢-٩-٢٤

اسم المشروع : مشروع القطار السريع (أكتوبر-أوسمبل)
المسافة من كم ٢٠٠+٨٥٠ وحتى كم ٢٠٢+٣٥٠ بطول ١,٥ كم

بالإشارة الى العقد المبرم بين الهيئة العامة للطرق والكباري وشركة أبوعحيلة للمقاولات العامة
رقم (٢٠٢٤/٢٠٢٣/٤٩٩) بتاريخ ١٢-١٠-٢٠٢٣
لتنفيذ المشروع عاليه بالمعدات الآتية :

المعدة	العدد	تاريخ الصنع
حفار	3	2009
		2005
لودر	4	2010
		2001
عربية قلاب	4	2015
		2008
		2005
بلدوزر	1	2000
		2015
تانك مياة	1	2003
جريد	1	2002
هراس	2	

عن الاستشاري أد حسن مهدي

م/محمود غريب
التوقيع

م/ احمد عزب
التوقيع

مهندس الهيئة العامة للطرق والكباري

ندس الشركة المنفذة

احمد فتوح

يفع / احمد فتوح



جدول توزيع اجهادات الصخر للقطاع من ٢٠٠+٨٧٦ الى ٢٠١+٦٤٠
تنفيذ شركة ابو عجيله للمقاولات العامة القطاع من المحطة ٢٠٠+٨٧٦ كم الي المحطة ٢٠٢+٨٧٦ كم

حتى تاريخ ٢٠٢٢/١١/١٤

الاجهات بالمقاييس ٢٠٠+٨٧٦ (كجم / سم)	الاجهات بالمقاييس ٢٠٠+٨٧٦ (كجم / سم)	الاجهات بالمقاييس ٢٠٠+٨٧٦ (كجم / سم)	الاجهات بالمقاييس ٢٠٠+٨٧٦ (كجم / سم)	الاجهات بالمقاييس ٢٠٠+٨٧٦ (كجم / سم)	المسبوق (م)	الاجهات (كجم / سم)	المحطة	مبنة
0.00			0.00		89.12	590.0	200+876.01	1
2,451.68			2,451.68		89.08	560.0	200+880.00	2
9,893.34			9,893.34		88.88	600.0	200+900.00	3
9,701.29	9,701.29				88.67	250.0	200+920.00	4
9,197.66			9,197.66		88.46	500.0	200+940.00	5
8,834.38				8,834.38	88.26	630.0	200+960.00	6
9,215.85		9,215.85			88.05	400.0	200+980.00	7
9,804.14		9,804.14			87.85	390.0	201+000.00	8
9,977.50				9,977.50	87.64	610.0	201+020.00	9
10,398.13			10,398.13		87.43	550.0	201+040.00	10
10,812.59			10,812.59		87.23	500.0	201+060.00	11
10,695.49			10,695.49		87.02	570.0	201+080.00	12
10,067.13	10,067.13				86.82	267.0	201+100.00	13
10,011.24				10,011.24	86.61	620.0	201+120.00	14
9,758.73			9,758.73		85.76	500.0	201+140.00	15
10,318.80		10,318.80			85.55	450.0	201+160.00	16
11,130.49		11,130.49			85.35	440.0	201+180.00	17
11,103.67	11,103.67				85.14	260.0	201+200.00	18
11,234.40		11,234.40			84.93	390.0	201+220.00	19
10,299.42				10,299.42	84.73	650.0	201+240.00	20
8,039.35				8,039.35	84.52	630.0	201+260.00	21

الشركة المنفذة

حمد فتيح

فريق / محمد فتيح 1978

عن الاستشاري ا.د حسن مهدي
مدير المشروع
م/محمود غريب
المكتب الفني
م/احمد عزب





الترتيب	الاجزاء والمقاييس ٢٠٠٠-٢٠٠٠ (كجم / سم ^٢)	الاجزاء والمقاييس ٢٠٠٠-٢٠٠٠ (كجم / سم ^٢)	الاجزاء والمقاييس ٢٠٠٠-٢٠٠٠ (كجم / سم ^٢)	الاجزاء والمقاييس ٢٠٠٠-٢٠٠٠ (كجم / سم ^٢)	الاجزاء والمقاييس ٢٠٠٠-٢٠٠٠ (كجم / سم ^٢)	المسبوق (م)	الاجزاء (كجم / سم ^٢)	المسافة	ملاحظة
22	6,829.61			6,829.61		84.32	510.0	201+280.00	
23	10,218.98			10,218.98		84.11	550.0	201+300.00	
24	8,466.06			8,466.06		83.90	600.0	201+320.00	
25	8,693.69				8,693.69	83.70	640.0	201+340.00	
26	8,567.94			8,567.94		83.49	590.0	201+360.00	
27	8,251.06			8,251.06		83.28	520.0	201+380.00	
28	8,252.44			8,252.44		83.08	500.0	201+400.00	
29	8,500.81			8,500.81		82.87	570.0	201+420.00	
30	9,470.53			9,470.53		83.27	510.0	201+440.00	
31	12,967.51			12,967.51		83.07	550.0	201+460.00	
32	10,951.35		10,951.35			82.86	490.0	201+480.00	
33	9,199.31	9,199.31				82.65	280.0	201+500.00	
34	8,710.47		8,710.47			82.45	350.0	201+520.00	
35	8,379.96			8,379.96		82.24	570.0	201+540.00	
36	8,372.24		8,372.24			82.03	460.0	201+560.00	
37	8,799.80		8,799.80			81.83	500.0	201+580.00	
38	9,068.39		9,068.39			81.62	500.0	201+600.00	
39	9,165.69			9,165.69		81.42	580.0	201+620.00	
40	4,621.06			4,621.06		81.21	540.0	201+640.00	
360,432.18	40,071.40	38,964.86	58,641.07	166,899.27	55,855.58	اجمالي الكمية (م)			
25,963.20	2,942.32	2,167.28	4,722.32	12,924.63	3,206.65	الكمية المنفذة من شهر سبتمبر حتى شهر يناير			

يعتمد
مهندس الهيئة العامة للطرق والكباري

عن الاستشاري ا.د. حسن مهدي
مدير المشروع
م/محمود حبيب
المكتب الفني
م/احمد عزب
14/

الشركة المنفذة

حمد فتح

1979





جدول توزيع اجهادات الصخر للقطاع من ٢٠٠+٨٧٦ الى ٢٠١+٦٤٠
تنفيذ شركة ابوعجيلة للمقاولات العامة القطاع من المحطة ٢٠٠+٨٧٦ الى المحطة ٢٠٢+٨٧٦ كم

حتى تاريخ ٢٠٢٣/٨/٢٤

الاجهادات بالمقاييسه ٢٠٠٠-٢٠٠٠ (كجم / سم)	الاجهادات بالمقاييسه ٤٠٠٠-٢٠٠٠ (كجم / سم)	الاجهادات بالمقاييسه ٨٠٠٠-٤٠٠٠ (كجم / سم)	الاجهادات بالمقاييسه ٦٠٠٠-٤٠٠٠ (كجم / سم)	الاجهادات بالمقاييسه ٧٠٠٠-٦٠٠٠ (كجم / سم)	المشوب (م)	الاجهات (كجم / سم)	المحطة	متر
0.00			0.00		89.12	590.0	200+876.01	1
2,382.75			2,382.75		89.08	560.0	200+880.00	2
9,672.89			9,672.89		88.88	600.0	200+900.00	3
9,397.29	9,397.29				88.67	250.0	200+920.00	4
8,828.23			8,828.23		88.46	500.0	200+940.00	5
8,622.69				8,622.69	88.26	630.0	200+960.00	6
9,056.30	9,056.30				88.05	400.0	200+980.00	7
9,633.59	9,633.59				87.85	390.0	201+000.00	8
9,816.77				9,816.77	87.64	610.0	201+020.00	9
10,161.19			10,161.19		87.43	550.0	201+040.00	10
10,316.01			10,316.01		87.23	500.0	201+060.00	11
10,106.96			10,106.96		87.02	570.0	201+080.00	12
9,326.54	9,326.54				86.82	267.0	201+100.00	13
9,085.07				9,085.07	86.61	620.0	201+120.00	14
8,723.87			8,723.87		85.76	500.0	201+140.00	15
9,427.85		9,427.85			85.55	450.0	201+160.00	16
10,627.76		10,627.76			85.35	440.0	201+180.00	17
10,619.76	10,619.76				85.14	260.0	201+200.00	18
10,688.55	10,688.55				84.93	390.0	201+220.00	19
9,805.55				9,805.55	84.73	650.0	201+240.00	20
7,513.81				7,513.81	84.52	630.0	201+260.00	21

عن الاستشاري أد حسن مهدي

مدير المشروع

م/محمود عزب
م/م

المكتب الفني

م/أحمد عزب
م/م

الشركة المنفذة

حمد فتح

بيع/م





جدول توزيع اجهادات الصخر للقطاع من ٢٠٠+٨٧٦ إلى ٢٠١+٦٤٠
تنفيذ شركة ابوعجيلة للمقاولات العامة القطاع من المحطة ٢٠٠+٨٧٦ كم إلى المحطة ٢٠٢+٨٧٦ كم

حتى تاريخ ٢٠٢٢/٨/٢٤

مرتبة	المحطة	الاجهاد (كجم / سم ^٢)	المسبوب (م)	الاجهاد بالمقاييسه ٧٠٠-٦٠٠ (كجم / سم ^٢)	الاجهاد بالمقاييسه ٦٠٠-٥٠٠ (كجم / سم ^٢)	الاجهاد بالمقاييسه ٥٠٠-٤٠٠ (كجم / سم ^٢)	الاجهاد بالمقاييسه ٤٠٠-٣٠٠ (كجم / سم ^٢)	الاجهاد بالمقاييسه ٣٠٠-٢٠٠ (كجم / سم ^٢)	الإجمالي
22	201+280.00	510.0	84.32		6,493.55				6,493.55
23	201+300.00	550.0	84.11		8,857.74				8,857.74
24	201+320.00	600.0	83.90		7,644.47				7,644.47
25	201+340.00	640.0	83.70	7,805.04					7,805.04
26	201+360.00	590.0	83.49		7,599.15				7,599.15
27	201+380.00	520.0	83.28		7,628.19				7,628.19
28	201+400.00	500.0	83.08		7,945.26				7,945.26
29	201+420.00	570.0	82.87		8,261.94				8,261.94
30	201+440.00	510.0	83.27		8,539.07				8,539.07
31	201+460.00	550.0	83.07		11,153.78				11,153.78
32	201+480.00	490.0	82.86			9,333.44			9,333.44
33	201+500.00	280.0	82.65					7,785.49	7,785.49
34	201+520.00	350.0	82.45				7,419.14		7,419.14
35	201+540.00	570.0	82.24		7,686.87				7,686.87
36	201+560.00	460.0	82.03			7,940.71			7,940.71
37	201+580.00	500.0	81.83			8,284.23			8,284.23
38	201+600.00	500.0	81.62			8,304.76			8,304.76
39	201+620.00	580.0	81.42		8,030.34				8,030.34
40	201+640.00	540.0	81.21		3,942.38				3,942.38
اجمالي الكمية (م ^٣)				52,648.93	153,974.64	53,918.75	36,797.58	37,129.08	334,468.98
الكمية المتفاد من شهر يوليو حتى شهر أغسطس				11,888.32	30,183.91	19,517.48	8,336.98	8,958.92	78,885.62
المتفاد في يوليو ٢٠٢٢				5,944.16	15,091.95	9,758.74	4,168.49	4,479.46	39,442.81
المتفاد في أغسطس ٢٠٢٢				5,944.16	15,091.95	9,758.74	4,168.49	4,479.46	39,442.81

يعتمد !!!
مهندس الهيئة العامة للطرق والكباري

عن الاستشاري أ.د حسن مهدي
مدير المشروع
م/محمود شريب
المكتب الفني
م/أحمد عزب
م/

الشركة المنفذة
حمد فتح
فريق /





جدول توزيع اجهادات الصخر للقطاع من ٢٠٠٨٧٦ الى ٢٠١٦٤٠
تنفيذ شركة ابو عجيله للمقاولات العامة للقطاع من المحطة ٢٠٠٨٧٦ كم الي المحطة ٢٠٢٨٧٦ كم

حتى asbuilt بتاريخ ٢٠٢٢/٦/١٣

الاجمالي	الاجهات بالمقاييس ٢٠٠٨٧٦ - ٢٠١٦٤٠ (كجم / سم)	الاجهات بالمقاييس ٢٠٠٨٧٦ - ٢٠١٦٤٠ (كجم / سم)	الاجهات بالمقاييس ٢٠٠٨٧٦ - ٢٠١٦٤٠ (كجم / سم)	الاجهات بالمقاييس ٢٠٠٨٧٦ - ٢٠١٦٤٠ (كجم / سم)	الاجهات بالمقاييس ٢٠٠٨٧٦ - ٢٠١٦٤٠ (كجم / سم)	المسحوب (م)	الاجهات (كجم / سم)	المحطة	العمود
0.00				0.00		89.12	590.0	200+876.01	1
112.38				112.38		89.08	560.0	200+880.00	2
2,663.76				2,663.76		88.88	600.0	200+900.00	3
1,435.54	1,435.54					88.67	250.0	200+920.00	4
1,064.63				1,064.63		88.46	500.0	200+940.00	5
1,920.04					1,920.04	88.26	630.0	200+960.00	6
2,125.51		2,125.51				88.05	400.0	200+980.00	7
1,834.39		1,834.39				87.85	390.0	201+000.00	8
1,879.09					1,879.09	87.64	610.0	201+020.00	9
2,578.06				2,578.06		87.43	550.0	201+040.00	10
3,143.58				3,143.58		87.23	500.0	201+060.00	11
2,954.06				2,954.06		87.02	570.0	201+080.00	12
2,223.81	2,223.81					86.82	267.0	201+100.00	13
2,473.07					2,473.07	86.61	620.0	201+120.00	14
1,698.26				1,698.26		85.76	500.0	201+140.00	15
1,254.30			1,254.30			85.55	450.0	201+160.00	16
1,565.36			1,565.36			85.35	440.0	201+180.00	17
1,349.70	1,349.70					85.14	260.0	201+200.00	18
1,103.95		1,103.95				84.93	390.0	201+220.00	19
1,023.98					1,023.98	84.73	650.0	201+240.00	20
783.13					783.13	84.52	630.0	201+260.00	21

عن الاستشاري ا.د حسن مهدي
مدير المشروع
م/محمود غريب

المكتب الفني
م/احمد عرب

عن الشركة المنفذة
م/احمد فتح
التوقيع





جدول توزيع اجهادات الصخر للقطاع من ٨٧٦+٢٠٠ الى ٦٤٠+٢٠١
تنفيذ شركة ابروجبل للمقاولات العامة القطاع من المحطة ٨٧٦+٢٠٠ كم الى المحطة ٦٤٠+٢٠١ كم

حتى التوقف بتاريخ ٢٠٢٢/٦/١٢

الاجمالي	الاجمالي بالمقاييس ٢٠٠٠+٢٠١ (كجم / سم)	الاجمالي بالمقاييس ٢٠٠٠+٢٠١ (كجم / سم)	الاجمالي بالمقاييس ٢٠٠٠+٢٠١ (كجم / سم)	الاجمالي بالمقاييس ٢٠٠٠+٢٠١ (كجم / سم)	المسبوق (م)	الاجمالي (كجم / سم)	المنطقة	العمق
626.38			626.38		84.32	510.0	201+280.00	22
729.41			729.41		84.11	550.0	201+300.00	23
1,458.37			1,458.37		83.90	600.0	201+320.00	24
2,205.69				2,205.69	83.70	640.0	201+340.00	25
2,709.16			2,709.16		83.49	590.0	201+360.00	26
3,092.92			3,092.92		83.28	520.0	201+380.00	27
2,936.12			2,936.12		83.08	500.0	201+400.00	28
2,322.45			2,322.45		82.87	570.0	201+420.00	29
773.02			773.02		83.27	510.0	201+440.00	30
236.87			236.87		83.07	550.0	201+460.00	31
236.87		236.87			82.86	490.0	201+480.00	32
236.87	236.87				82.65	280.0	201+500.00	33
236.87		236.87			82.45	350.0	201+520.00	34
236.87			236.87		82.24	570.0	201+540.00	35
236.87		236.87			82.03	460.0	201+560.00	36
236.87		236.87			81.83	500.0	201+580.00	37
236.87		236.87			81.62	500.0	201+600.00	38
236.87			236.87		81.42	580.0	201+620.00	39
236.87			236.87		81.21	540.0	201+640.00	40
54,408.78	5,245.92	5,300.72	3,767.13	29,810.02	10,285.00	الجمالي الكلية (م)		
9,068.13	874.32	883.45	627.85	4,968.34	1,714.17	المنفذ في يناير ٢٠٢٢		
9,068.13	874.32	883.45	627.85	4,968.34	1,714.17	المنفذ في فبراير ٢٠٢٢		
9,068.13	874.32	883.45	627.85	4,968.34	1,714.17	المنفذ في مارس ٢٠٢٢		
9,068.13	874.32	883.45	627.85	4,968.34	1,714.17	المنفذ في ابريل ٢٠٢٢		
9,068.13	874.32	883.45	627.85	4,968.34	1,714.17	المنفذ في مايو ٢٠٢٢		
9,068.13	874.32	883.45	627.85	4,968.34	1,714.17	المنفذ في يونيو ٢٠٢٢		

يعتمد
مهندس الهيئة العامة للطرق والكباري

المكتب الفني
م/أحمد عزب
م/أحمد عزب
م/أحمد عزب
م/أحمد عزب

عن الشركة المنفذة
م/أحمد فتوح
التوقيع





جدول توزيع اجهيزات الصخر للقطاع من ٨٧٦+ إلى ٢٠٠٠+ ٢٠١٦

حتى asbuilt بتاريخ ٢٠٢٣/١/٣

الاجمالي	الاجمالي بالعملة (كجم / سنة)	الاجمالي بالعملة (كجم / سنة)	الاجمالي بالعملة (كجم / سنة)	الاجمالي بالعملة (كجم / سنة)	الاجمالي بالعملة (كجم / سنة)	المتوسط (م)	الاجمالي (كجم / سنة)	المحددة	هينة
0.00				0.00		89.12	590.0	200+876.01	1
2,184.54				2,184.54		89.08	560.0	200+880.00	2
6,343.73				6,343.73		88.88	600.0	200+900.00	3
6,968.18	6,968.18					88.67	250.0	200+920.00	4
6,513.96				6,513.96		88.46	500.0	200+940.00	5
5,620.74					5,620.74	88.26	630.0	200+960.00	6
5,904.97		5,904.97				88.05	400.0	200+980.00	7
6,487.94		6,487.94				87.85	390.0	201+000.00	8
6,468.92					6,468.92	87.64	610.0	201+020.00	9
6,183.40				6,183.40		87.43	550.0	201+040.00	10
5,642.90				5,642.90		87.23	500.0	201+060.00	11
5,417.11				5,417.11		87.02	570.0	201+080.00	12
5,413.19	5,413.19					86.82	267.0	201+100.00	13
4,925.54					4,925.54	86.61	620.0	201+120.00	14
5,300.81				5,300.81		85.76	500.0	201+140.00	15
5,929.39			5,929.39			85.55	450.0	201+160.00	16
6,154.93			6,154.93			85.35	440.0	201+180.00	17
6,044.32	6,044.32					85.14	260.0	201+200.00	18
6,073.37		6,073.37				84.93	390.0	201+220.00	19
5,341.24					5,341.24	84.73	650.0	201+240.00	20
3,477.38					3,477.38	84.52	630.0	201+260.00	21

الشركة المنفصلة

عن الاستشاري أ.د حسن مهدي

مدير الميثاق

المكتب الطبي

م / محمود الفرب

م/أحمد عرب

19788 ت. 19788 ت.





جدول توزيع اجهادات الصخر للقطاع من ٨٧٦+٢٠٠ الى ٦٤٠+٢٠١
تنفيذ شركة ابروجيلا للمقاولات العامة القطاع من المحطة ٨٧٦+٢٠٠ كم الى المحطة ٨٧٦+٢٠٢ كم

حبي asphalt بتأريخ ٢٠٢٢/١/٢

محطة	المحطة	الاجمالي (كجم / سم ٢)	الاجمالي (كجم / سم ٢)	الاجمالي (كجم / سم ٢)	الاجمالي (كجم / سم ٢)	الاجمالي (كجم / سم ٢)	الاجمالي (كجم / سم ٢)	الاجمالي (كجم / سم ٢)
22	201+280.00	510.0	84.32	2,510.82				2,510.82
23	201+300.00	550.0	84.11	5,380.56				5,380.56
24	201+320.00	600.0	83.90	4,293.43				4,293.43
25	201+340.00	640.0	83.70	4,641.79				4,641.79
26	201+360.00	590.0	83.49	4,380.66				4,380.66
27	201+380.00	520.0	83.28	3,951.10				3,951.10
28	201+400.00	500.0	83.08	3,792.97				3,792.97
29	201+420.00	570.0	82.87	5,054.19				5,054.19
30	201+440.00	510.0	83.27	7,939.23				7,939.23
31	201+460.00	550.0	83.07	8,491.55				8,491.55
32	201+480.00	490.0	82.86	5,674.33			5,674.33	
33	201+500.00	280.0	82.65	4,498.55	4,498.55			
34	201+520.00	350.0	82.45	4,693.60		4,693.60		
35	201+540.00	570.0	82.24	4,346.00				4,346.00
36	201+560.00	460.0	82.03	4,378.58			4,378.58	
37	201+580.00	500.0	81.83	4,401.76			4,401.76	
38	201+600.00	500.0	81.62	4,095.15			4,095.15	
39	201+620.00	580.0	81.42	4,076.95				4,076.95
40	201+640.00	540.0	81.21	2,176.80				2,176.80
اجمالي الكمية (م ٢)				30,475.61	93,980.71	30,634.14	23,159.88	22,924.24
								201,174.58

يعتمد !!!
مهندس الهيئة العامة للطرق والكباري

عن الاستشاري لاد حسن مهدي
المكتب الفني
م/احمد عزب
م/محمود غريب
مدير المشروع

الشركة المنفذة
احمد فتوح
وقفا





مركز الاستشارات الهندسية
Engineering Consultation Center

معمل الخرسانة
Concrete plant



رؤية الكلية : تسعى الكلية إلى أن تكون مؤسسة تعليمية وبحثية عالية الجودة متميزة بتقديم خدمات مجتمعية لتنمية البيئة وتعسيها

نتائج اختبارات عينات من مكعبات الحجر		
خاص بعملية : القطار السريع (أكتوبر - أسوان) القطاع الثاني بطول ١٥٨ كم المسافة من ١٧٦ + ٨٠٠ : ٢٣٤ + ٨٠٠		
مقاول : شركة أبو عجيلة للمقاولات - القطاع ٨٥٠ + ٢٠٠ : ٢٥٠ + ٢٠٢ بطول ١,٥ كم		
توريد : ٨٣٦٨٨٨٦٤١٥	بتاريخ : ٢٣ / ٥ / ٢٠٢٣	رقم القيد : ١

نتائج الاختبارات

القطاع من ٢٠١ + ٦٤٠ : ٢٠١ + ٤٤٠

م	الأبعاد / سم	المحطة	منسوب	حمل الكسر / طن	إجهاد الكسر / كجم/سم ^٢
١	١٠ × ١٠ × ١٠	٢٠١ + ٤٤٠	٨٣,٢٧١	٥١	٥١٠
٢	١٠ × ١٠ × ١٠	٢٠١ + ٤٦٠	٨٣,٠٦٥	٥٥	٥٥٠
٣	١٠ × ١٠ × ١٠	٢٠١ + ٤٨٠	٨٢,٨٥٨	٤٩	٤٩٠
٤	١٠ × ١٠ × ١٠	٢٠١ + ٥٠٠	٨٢,٦٥٢	٢٨	٢٨٠
٥	١٠ × ١٠ × ١٠	٢٠١ + ٥٢٠	٨٢,٤٤٦	٣٥	٣٥٠
٦	١٠ × ١٠ × ١٠	٢٠١ + ٥٤٠	٨٢,٢٤	٥٧	٥٧٠
٧	١٠ × ١٠ × ١٠	٢٠١ + ٥٦٠	٨٢,٠٣٤	٤٦	٤٦٠
٨	١٠ × ١٠ × ١٠	٢٠١ + ٥٨٠	٨١,٨٢٨	٥٠	٥٠٠
٩	١٠ × ١٠ × ١٠	٢٠١ + ٦٠٠	٨١,٦٢٢	٥٠	٥٠٠
١٠	١٠ × ١٠ × ١٠	٢٠١ + ٦٢٠	٨١,٤١٥	٥٨	٥٨٠
١١	١٠ × ١٠ × ١٠	٢٠١ + ٦٤٠	٨١,٢٠٩	٥٤	٥٤٠

* تم توريد العينات بمعرفة م / محمود الحيني دون أدنى مسئولية على المعمل

يعتمد ،
الرأي الاستشاري على مسئولية اللجنة
مركز الاستشارات الهندسية



المشرف على المعمل

أ. د. / أسامة محمد

التوقيع : /

فنى المعمل

١ / /

التوقيع : /

التوقيع : /

رسالة الكلية : تتلزم كلية الهندسة جامعة المنيا بتقديم برامج تعليمية وفقاً للمعايير القومية لإعداد خريج متميز وقادر على المنافسة في أسواق العمل محلياً وإقليمياً وعالمياً، كما تتلزم بالتشجيع والتطوير في البحث العلمي بما يخدم البيئة والتطور التكنولوجي .



مركز الاستشارات الهندسية
Engineering Consultation Center

معمل الخرسانة
Concrete plant



رؤية الكلية : تسعى الكلية إلى أن تكون مؤسسة تعليمية وبحثية عالية الجودة متميزة بتقديم خدمات مجتمعية لتنمية البيئة وتعويضها

نتائج اختبارات عينات من مكعبات الحجر		
خاص بعملية : القطار السريع (أكتوبر - أسوان) القطاع الثاني بطول ١٥٨ كم المسافة من ٨٠٠ + ١٧٦ : ٨٠٠ + ٣٣٤		
مقاول : شركة أبو عجيلة للمقاولات - القطاع ٨٥٠ + ٢٠٠ : ٢٠٢ + ٣٥٠ بطول ١,٥ كم		
توريد : ٨٣٦٨٨٨٦٤١٥	بتاريخ : ٢٣ / ٥ / ٢٠٢٣	رقم القيد : ٢

نتائج الاختبارات

القطاع من ٨٧٦ + ٢٠٠ : ١٢٠ + ٢٠١

م	الأبعاد / سم	المحطة	منسوب	حمل الكسر / طن	إجهاد الكسر / كجم/سم ^٢
١	١٠ × ١٠ × ١٠	٢٠٠ + ٨٧٦,٠١	٨٩,١٢٤	٥٩	٥٩٠
٢	١٠ × ١٠ × ١٠	٢٠٠ + ٨٨٠	٨٩,٠٨٣	٥٦	٥٦٠
٣	١٠ × ١٠ × ١٠	٢٠٠ + ٩٠٠	٨٨,٨٧٧	٦٠	٦٠٠
٤	١٠ × ١٠ × ١٠	٢٠٠ + ٩٢٠	٨٨,٦٧	٢٥	٢٥٠
٥	١٠ × ١٠ × ١٠	٢٠٠ + ٩٤٠	٨٨,٤٦٤	٥٠	٥٠٠
٦	١٠ × ١٠ × ١٠	٢٠٠ + ٩٦٠	٨٨,٢٥٨	٦٣	٦٣٠
٧	١٠ × ١٠ × ١٠	٢٠٠ + ٩٨٠	٨٨,٠٥٢	٤٠	٤٠٠
٨	١٠ × ١٠ × ١٠	٢٠١ + ٠٠٠	٨٧,٨٤٦	٣٩	٣٩٠
٩	١٠ × ١٠ × ١٠	٢٠١ + ٠٢٠	٨٧,٦٤	٦١	٦١٠
١٠	١٠ × ١٠ × ١٠	٢٠١ + ٠٤٠	٨٧,٤٣٤	٥٥	٥٥٠
١١	١٠ × ١٠ × ١٠	٢٠١ + ٠٦٠	٨٧,٢٢٧	٥٠	٥٠٠
١٢	١٠ × ١٠ × ١٠	٢٠١ + ٠٨٠	٨٧,٠٢١	٥٧	٥٧٠
١٣	١٠ × ١٠ × ١٠	٢٠١ + ١٠٠	٨٦,٨١٥	٦٠	٢٦٧
١٤	١٠ × ١٠ × ١٠	٢٠١ + ١٢٠	٨٦,٦٠٩	٦٢	٦٢٠

* تم توريد العينات بمعرفه م / محمود الحيني دون أدنى مسئولية علي المعمل

بمعد ،
الرأي الاستشاري علي مسئولية اللجنة
مركز الاستشارات الهندسية

المشرف علي المعمل

فني المعمل

أ. د. / /

أ. د. / /

التوقيع :

التوقيع :

رسالة الكلية : تلتزم كلية الهندسة جامعة المنيا بتقديم برامج تعليمية وفقاً للمعايير القومية لإعداد خريج متميز وقادر على المنافسة في اسواق العمل محلياً وإقليمياً وعالمياً، كما تلتزم بالتنشجيع والتطوير في البحث العلمي بما يخدم البيئة والتطور التكنولوجي .



مركز الاستشارات الهندسية
Engineering Consultation Center

معمل الخرسانة
Concrete plant



رؤية الكلية : تسعى الكلية إلى أن تكون مؤسسة تعليمية وبحثية عالية الجودة متميزة بتقديم خدمات مجتمعية لتنمية البيئة وتعميرها

نتائج اختبارات عينات من مكعبات الحجر		
خاص بعملية : القطار السريع (أكتوبر - أسوان) القطاع الثاني بطول ١٥٨ كم المسافة من ٨٠٠ + ١٧٦ : ٨٠٠ + ٣٣٤		
مقاوله : شركة أبو عجيلة للمقاولات - القطاع ٨٥٠ + ٢٠٠ : ٢٠٢ + ٣٥٠ بطول ١,٥ كم		
توريد : ٨٢٤٩١١٤٩٨٤	بتاريخ : ٢٧ / ٤ / ٢٠٢٣	رقم القيد : ١

نتائج الاختبارات

القطاع من ١٤٠ + ٢٠٠ : ٢٠١ + ٤٢٠

م	الأبعاد / سم	المحطة	متسوب	حمل الكسر / طن	إجهاد الكسر / كجم/سم ^٢
١	١٠ × ١٠ × ١٠	٢٠١ + ١٤٠	٨٥,٧٥٨	٥٠	٥٠٠
٢	١٠ × ١٠ × ١٠	٢٠١ + ١٦٠	٨٥,٥٥٢	٤٥	٤٥٠
٣	١٠ × ١٠ × ١٠	٢٠١ + ١٨٠	٨٥,٣٥٤	٤٤	٤٤٠
٤	١٠ × ١٠ × ١٠	٢٠١ + ٢٠٠	٨٥,١٣٩	٢٦	٢٦٠
٥	١٠ × ١٠ × ١٠	٢٠١ + ٢٢٠	٨٤,٩٣٣	٢٩	٢٩٠
٦	١٠ × ١٠ × ١٠	٢٠١ + ٢٤٠	٨٤,٧٢٧	٦٥	٦٥٠
٧	١٠ × ١٠ × ١٠	٢٠١ + ٢٦٠	٨٤,٥٢١	٦٣	٦٣٠
٨	١٠ × ١٠ × ١٠	٢٠١ + ٢٨٠	٨٤,٣١٥	٥١	٥١٠
٩	١٠ × ١٠ × ١٠	٢٠١ + ٣٠٠	٨٤,١٠٩	٥٥	٥٥٠
١٠	١٠ × ١٠ × ١٠	٢٠١ + ٣٢٠	٨٣,٩٠٢	٦٠	٦٠٠
١١	١٠ × ١٠ × ١٠	٢٠١ + ٣٤٠	٨٣,٦٩٦	٦٤	٦٤٠
١٢	١٠ × ١٠ × ١٠	٢٠١ + ٣٦٠	٨٣,٤٩٠	٥٩	٥٩٠
١٣	١٠ × ١٠ × ١٠	٢٠١ + ٣٨٠	٨٣,٢٨٢	٥٢	٥٢٠
١٤	١٠ × ١٠ × ١٠	٢٠١ + ٤٠٠	٨٣,٠٧٨	٥٠	٥٠٠
١٥	١٠ × ١٠ × ١٠	٢٠١ + ٤٢٠	٨٢,٨٧٢	٥٧	٥٧٠

* تم توريد العينات بمعرفه م / محمود الحيني دون أدنى مسئولية على المعمل

يعتمد ،
الرأي الاستشاري على مسئولية اللجنة
مركز الاستشارات الهندسية

المشرف على المعمل

أ. د. / محمد /

التوقيع : محمد /

فنى المعمل

أ. د. / محمد /

التوقيع : محمد /

رسالة الكلية : تلتمز كلية الهندسة جامعه المنيا بتقديم برامج تعليمية وفقاً للمعايير القومية لإعداد خريج متميز وقادر على المنافسة في اسواق العمل محلياً وإقليمياً وعالمياً، كما تلتمز بالتنشجيع والتطوير في البحث العلمي بما يخدم البيئة والتطور التكنولوجي.

محضر استلام موقع

مشروع إنشاء خط القطار الكهربائي السريع (أكتوبر - أبو سمبل) من الكم 200+850 حتي الكم 202+350 بطول 1.5 كم تنفيذ شركة أبو عجيلة للمقاولات العامة والتوريدات العمومية.

انه في يوم الخميس الموافق 19 / 10 / 2023 وبناء على عقد العملية رقم 499 / 2023 / 2024 اتجاه ملوي

اجتمعت اللجنة المشكلة من السادة الاتي اسماؤهم بعد وهم :-

عن الهيئة العامة للطرق والكباري (طرف اول)

مدير عام المشروعات

1- السيد المهندس / مصطفى شعبان البدري

مهندس الإشراف بالمنطقة السادسة

2- السيد المهندس / محمود حسين

مدير المشروع الاستشاري (مكتب أ.د/حسن مهدي)

3- السيد المهندس / حاتم مهران

استشاري المساحة (XYZ)

4- السيد المهندس / محمد عبدالرحمن سالم

عن الشركة المنفذه (طرف ثاني)

مهندس عن الشركة المنفذه

1- السيد المهندس / محمد حامد ابو عجيلة

وقد قامت اللجنة بالانتقال علي الطبيعة للموقع عالية بالمعاينة الظاهرية علي الطبيعة قام الطرف الاول بتسليم الطرف الثاني الموقع خاليا من العوائق الظاهرية ولا مانع من استلام الموقع والبدء في الاعمال ويعتبر تاريخ 19 / 10 / 2023 هو تاريخ استلام الموقع .

وقفل المحضر علي ذلك .

اللجنة من الهيئة (طرف اول)



4- السيد المهندس / محمد حامد ابو عجيلة

3- السيد المهندس / محمد حامد ابو عجيلة

2- السيد المهندس / محمد حامد ابو عجيلة

1- السيد المهندس / محمد حامد ابو عجيلة

الشركة المنفذه (طرف ثاني)

1- السيد المهندس / محمد حامد ابو عجيلة

رئيس الادارة المركزية للمنطقة

السادسة ببني سويف

مهندس / طارق الجزار




$$f_{(n)}^{(k)} = \frac{1}{n} f_0^{(k)}, \quad g_{(n)}^{(k)} = \frac{1}{n} g_0^{(k)}, \quad h_{(n)}^{(k)} = \frac{1}{n} h_0^{(k)},$$

2012/ 8 / 21



الهيئة العامة للإعطاء



محاضر معالمة تربية (سماو)

المشروع القطر الكهربائي السريع (الكويت - امراء) القطاع الثاني

بطول 158 كم المسافة من (800+176 إلى 334+400)

تقديرات شركة أوبر عن حصة المعفوات القطاع من (2014-85) إلى (2014-85) 1.5م

العدد التسوي يسوم **الأحمد** الموافق ٨ / ١ / 2022 قسم المتشاري الهيئة العامة للطريق والكساري
أحة بماتة القطر 200+850 202+350

المجتمعة العامة للطرق والملاحة

[illegible]

مكتبة المكتبة العامة

مؤلفه: | محتويات: | تاريخ النشر: |

شركة دبي دبي للإسكان والمساكن العامة

[illegible]

Figure 1

تتمثل الأدلة في القطعاع لعمل معاينة للزناشوات على تسليح بدائية ونهائية (الرئيسة) (N3:136379.6301, E260172.2324) 201+660 (N3:136379.6301, E260172.2324) 201+660
(N3:136439.6664, E260168.2343) 201+900 (N3:136439.6664, E260168.2343) 201+900



Figure 1

المنطقة السادسة - بني سويف

محاضر معاينة تربية متماسكة

القطاع من كم 200+800 الي كم 202+300 بطول 1.5 كم غرب سمالوط

أولاً : عام

والكباري بالمنطقة السادسة بيني سويف بمعاينة القطاع من كم 800+200 إلى كم 300+202

بطول 1.5 كم حضور كلا من :

الاستشاري - هيئة الطرق والكباري
للإدارة العامة ١٥٠٠٠٠
هيئة الطرق والكباري ٢٠٠٠٠
شركة الهندسة ٣٠٠٠٠

1- محمد بن عبد الله
2- محمد بن عبد الله
3- محمد بن عبد الله

ثانياً : الاجراءات

1- قام الحاضرون بالمرور علي قطاع أنتره متماسكة للقطاع للوقوف علي مدي نوعية التربة

وذلك في القطاع من كم 200+850 الى كم 201+650

2- نلاحظ ما يلي :-
 ا. التربة الطماح لجة كور تربتها ملاءمة ولا يتم قطعها بغير الجلويا

جاء

-2-

ثَالِثًا : الْقَوَصِيَّاتُ

1- يتم القطع باستخدام البلور /

-2

-3

-4

رابعاً : التوقيعات

($\frac{b}{c}$)

(rel)



محضر مسافة نقل

مشروع القطار الكهربائي السريع (6 أكتوبر-اسوان) القطاع الثاني

انه في يوم الاثنين الموافق 2022/9/5 قامت اللجنة المذكورة من :-

(1) السيد المهندس / مصطفى محمد عبدالحمد مهندس المشروع الهيئة العامة للطرق والكباري

(2) السيد المهندس / محمد عبدالرحمن سالم مهندس المكتب الاستشاري (X,Y,Z)

(3) السيد المهندس / محمد حامد أبو عجيبة مدير المشروع شركة اورعجلة للمقاولات المتكاملة والتوريدات

وقد تم اللجوء بالذهاب الى مكان المقاب حيث وجد ان المسافة من قطاع (من محطة 200+800 حتى 202+300)

على مكان المقاب 3 كم وذلك بسبب تعثر وجود مداف بسبب وجود مراوغ حول القطاع

وهذا محضر منا بذلك

التوقيع



م / مصطفى محمد عبدالحمد

م / محمد عبدالرحمن سالم

م / محمد حامد أبو عجيبة

الإدارة المركزية بالمنطقة السادسة بنى سويف

اعتماد

م / طارق يوسف الجزان








	مشروع القطار الكهربائي السريع	 الهيئة العامة للنقل مكتب أ.د/حسن مهدي للإستشارات الهندسية
	إستكمال إنساناد أعمال الجسر الترابي والأعمال الصناعية بقطاعات مشروع إنشاء القطار الكهربائي السريع (أكتوبر - أبوسمبل)	
	تنفيذ شركة أبو عجيله للمقاولات العامة والتوريدات العمومية	

حصر كمية الاحلال في السفلو ابتداء من شهر سبتمبر ٢٠٢٣

Station	Total Cut Area(m2)	Cum. Cut Vol(m3)	As Built vol.cut		
				CUT VOL(m3)	Total.Qty
201+920.00	172.54	495,420.53	CUT	1,725.37	36058.01
201+940.00	117.37	498,319.63		2,899.09	
201+960.00	121.91	500,712.41		2,392.78	
201+980.00	141.36	503,345.11		2,632.70	
202+000.00	131.55	506,074.23		2,729.12	
202+020.00	123.82	508,627.92		2,553.69	
202+040.00	93.18	510,797.88		2,169.96	
202+060.00	50.98	512,239.45		1,441.57	
202+080.00	49.6	513,245.30		1,005.85	
202+100.00	43	514,171.38		926.08	
202+120.00	38.08	514,982.21		810.83	
202+140.00	0	515,362.98		380.78	
202+160.00	0	515,362.98		0.00	
202+180.00	0	515,362.98		0.00	
202+200.00	0	515,362.98		0.00	
202+220.00	73.22	516,095.23		732.24	
202+240.00	80.7	517,634.50		1,539.28	
202+260.00	97.19	519,413.44		1,778.93	
202+280.00	119.49	521,580.25		2,166.81	
202+300.00	140.13	524,176.43		2,596.18	
202+320.00	63.81	526,215.81		2,039.38	
202+340.00	66.23	527,516.19		1,300.37	
202+360.00	64.12	528,819.69		1,303.50	
202+376.01	52.46	529,753.19		933.50	

عن الاستشاري أ.د حسن مهدي
م/ احمد عزب
م/ محمود غراب
عن استشاري المساحة
م/ محمد عبدالرحمن
عن الشركة
م/ احمد خفيف
م/ احمد خفيف





ABUAGLA
609-161-199

	مشروع القطار الكهربائي السريع إستكمال أعمال الجسر الترابي لمسار القطار الكهربائي السريع الخط الثاني (الفيوم / بني سويف - أبو سمبل) (مرحلة الجسور والتأسيس والأساس) القطاع الثاني (بني مزار / منفلوط) تنفيذ شركة أبو عجيبة للمقاولات العامة والتوريدات العمومية حصر اجمال لكميات الردم	الهيئة العامة للإنشاء مكتب أد/مسن مهدي للمستشارات الهندسية
---	---	---

الهيئة العامة للإشراف
مكتب أ.د/سنه موهي
للإشراف العامة

بند رقم (١٠٣) : أعمال تحميل وتوريد ونقل أتربة مطابقة للمواصفات وتشغيلها باستخدام آلات التسيبة بسبك لا يزيد عن ٥٠ سم حتى منسوب (2٠ متر) أسفل منسوب الغرمة و بسبك لا يزيد عن ٢٥ سم اعلي من منسوب (2٠ متر) من منسوب الغرمة لاستكمال المنسوب التصميمي الخ

Station	Total Fill Area(m2)	Cum. Fill Vol(m3)	As Built vol.Fill		
			Fill VOL(m3)	Total.Qty	
201+920.00	202.61	2026.07	2026.07	100122.28	
201+940.00	227.66	6,328.78	4,302.71		
201+960.00	248.2	11,087.40	4,758.61		
201+980.00	274.47	16,314.06	5,226.67		
202+000.00	262.01	21,678.88	5,364.82		
202+020.00	243.79	26,736.89	5,058.01		
202+040.00	194.01	31,114.85	4,377.95		
202+060.00	362.48	36,679.73	5,564.88		
202+080.00	341.72	43,721.80	7,042.07		
202+100.00	314.56	50,284.61	6,562.81		
202+120.00	301.56	56,445.77	6,161.16		
202+140.00	0	59,461.36	3,015.59		
202+160.00	0	59,461.36	0.00		
202+180.00	0	59,461.36	0.00		
202+200.00	0	59,461.36	0.00		
202+220.00	317.97	62,641.01	3,179.66		
202+240.00	312.67	68,947.36	6,306.35		
202+260.00	320.6	75,280.03	6,332.66		
202+280.00	330.13	81,787.33	6,507.30		
202+300.00	335.88	88,447.44	6,660.11		
202+320.00	141.42	93,220.38	4,772.95		
202+340.00	132.47	95,959.23	2,738.85		
202+360.00	116.74	98,451.35	2492.11		
202+376.01	91.94	100,122.29	1,670.94		
اجمالي كميات الردم المصروفة سابقا					0
اجمالي كميات الردم الفعلية الحالية بعد خصم سمك خرسانه الميول					100122.28
كمية خصم سمك خرسانه الميول				911	

100122.28

Q

100122.28

911

1977/1978



608-161-153

الممسوحة ضوئياً بـ CamScanner

	مشروع القطار الكهربائي السريع		 مكتب المهندسين للمشروعات الهندسية				
	إستكمال أعمال الجسر الترابي لمسار القطار الكهربائي السريع الخط الثاني (الفيوم / بني سويف - أبو سمبل) (مرحلة الجسور والتأسيس والأساس) القطاع الثاني (بني مزار / منفلوط)						
	تنفيذ شركة أبوعجيبة للمقاولات العامة والتوريدات العمومية كميات حتي مستخلص جاري (١) جاري لعقد رقم (٢٠٢٥/٢٠٢٤/٢٠٩) بتاريخ ASBUILT 2024/4/1						
بند رقم (١-٣) : أعمال تحميل وتوريد ونقل أتربة مطابقة للمواصفات وتشغيلها باستخدام آلات التسوية بسمك لا يزيد عن ٥٠ سم حتى منسوب (-2 متر) أسفل منسوب القرمه و بسمك لايزيد عن ٢٥ سم اعلي من منسوب (-2 متر) من منسوب القرمه لاستكمال المنسوب التصميميالخ							
As Built vol.Fill							
Station	Total Fill Area(m2)	Cum. Fill Vol(m3)	FILL	Fill VOL(m3)	Total.Qty	Fill VOL(m3) ابتداء من ٢٠٢٤/٣/٢٢	اجمالي الكميات ابتداء من ٢٠٢٤/٣/٢٢
201+920.00	202.61	2026.07		2026.07	100122.28	582.22	9669.67
201+940.00	227.66	6,328.78		4,302.71		1,170.55	
201+960.00	248.2	11,087.40		4,758.61		1,162.28	
201+980.00	274.47	16,314.06		5,226.67		1,140.36	
202+000.00	262.01	21,678.88		5,364.82		1,142.87	
202+020.00	243.79	26,736.89		5,058.01		1,149.44	
202+040.00	194.01	31,114.85		4,377.95		1,134.32	
202+060.00	362.48	36,679.73		5,564.88		561.35	
202+080.00	341.72	43,721.80		7,042.07		0.00	
202+100.00	314.56	50,284.61		6,562.81		0.00	
202+120.00	301.56	56,445.77		6,161.16		0.00	
202+140.00	0	59,461.36		3,015.59		0.00	
202+160.00	0	59,461.36		0.00		0.00	
202+180.00	0	59,461.36		0.00		0.00	
202+200.00	0	59,461.36		0.00		0.00	
202+220.00	317.97	62,641.01		3,179.66		162.54	
202+240.00	312.67	68,947.36		6,306.35		325.06	
202+260.00	320.6	75,280.03		6,332.66		321.62	
202+280.00	330.13	81,787.33		6,507.30		322.02	
202+300.00	335.88	88,447.44		6,660.11		328.98	
202+320.00	141.42	93,220.38		4,772.95		166.06	
202+340.00	132.47	95,959.23		2,738.85		0.00	
202+360.00	116.74	98,451.35		2492.11		0	
202+376.01	91.94	100,122.29		1,670.94		0.00	

عن الاستشاري أد حسن مهدي
المكتب الفني
م / احمد عزب
م / محمود شبيب

مشروع النظام السريع

أحمد / حسن / محمد / علي / فهد

المساحة

مساحة عيسى بن
البحر في البحر المتوسط - أقصى الشرق

عن الشركة
م/ احمد فتح
11
1978
ABUAGLA
الجمعية العامة
609-161-109

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name [Signature]	Date	Time
Received by Employers Representative	Sign [Signature]	15-8-2022	2
UIR	C1 KP	C2 EW	C3 OT
	DD 15	MM 8	YY 22
	HH	MM	

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
From 200+876 To 202+376	200+876 TO 202+376	
	E=260126.0446 N=3137487.7094	E=260129.6912 N=3135991.0324
Inspection description[Disinfection Of Trees Cutting From st (200+876) to st (202+376)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
[Signature]	- Trees No. was checked only by xyz and under their own responsibility - you must follow specs and design dr

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	[Signature]	[Signature]				
Contractor QA/QC*	XYZ	[Signature]	15-8-2022		A	
	H.M.C	[Signature]	15-8-2022		A	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024		AWC	

* Designer

** Alignment: Bridges: Culvert Only

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name [Signature]	Sign [Signature]	Date 15-8-2022
Received by Employers Representative	UIR	C1 KP	C2 EW
		C3 OT	DD 15
		MM 8	YY 22
		HH 22	MM 22
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 202+376	
	E=260126.0446 N=3137487.7094	E=260129.6912 N=3135991.0324
Inspection description[Disinfection Of Trees Cutting From st (200+876) to st (202+376)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

تصوير وازالة الاشجار بمساحة 200+876 الى 202+376	- Trees No. was checked only by xyz and under their own responsibility - you must follow specs and design dr
--	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	[Signature]	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	[Signature]	15-8-2022		A	
	H.M.C	[Signature]	15-8-2022		A	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024		AWC	

* Designer

** Alignment: Bridges: Culvert Only

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيل للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
	20-10-2022	3								
Received by Employers Representative			C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	20	10	22		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5						

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+686 E=260126.0446 E=260172.2356 N=3137487.7094 N=3136679.1711	
Inspection description/ تطهير بعد قطع الاشجار Disinfection of crops and trees cutting from st (200+876) to st (201+686)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
---	--

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA/QC*	XYZ		20-10-2022	14:30	A	
	H.M.C		20/10/2022	15:00	A	
GARB**						
Employers Representative						

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
	أديسن مهدي	أديسن مهدي	20-10-2022	4						
Received by Employers Representative			C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	20	10	22		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5						

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+686 TO 201+846	
	E=260172.2356 N=3136679.1711	E=260170.8362 N=3136519.1841
Inspection description/		
Disinfection of crops and trees cutting from st (201+686) to st (201+846) / تم تعقيم بعد قطع الأشجار		

منطقة قطع

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time


Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
أديسن مهدي	أديسن مهدي

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	أديسن مهدي	أديسن مهدي				
Contractor QA/QC*	XYZ	أديسن مهدي	20-10-2022	16:00	A	
	H.M.C	أديسن مهدي	20/10/2022	16:30		
GARB**						
Employers Representative						



Contractor Company	Issued by Contractor	Received by Employers Representative	CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
DR. Hassan Mahdy	Name Signature Date Time	20-10-2022 5	CT C2 C3 DD MM YY HH MM	KP EW OT 20 10 22			

CODE-1		CODE-2		CODE-3		CODE-4		CODE-5	
Received by	Employers	Representative							
C1	C2	C3	C4	OT	EW	KP	UIR		
DD	MM	YY	HH	MM	YY	HH	MM		
22	10	20	10	22					

Area	Element	Item
From 200+876 To 202+376	201+966 TO 202+376	
	E=260166.4277 N=3136399.268	E=260129.6912 N=3135991.0324

From 200+876 To 202+376	E=260166.4277 N=3136399.268	E=260129.6912 N=3135991.0324
-------------------------	--------------------------------	---------------------------------

Disinfection of crops and trees cutting from st (201+966) to st (202+376), leylil' p'io as japhis

INSPECTION DETAILS	
Planned Inspection Date	Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate		☐ Checklist Attached ☐ Test Results Attached ☐ Calibration Attached	Drawing Reference ITP Reference MS Reference
---	--	--	--

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐	Drawing Reference	ITP Reference	MS Reference

Comments by: General consultant (systa) - Levels and coordinates were checked only by XYZ and under their own responsibility - you must follow spec, design drawing	Comments by: (GARB SURVEY CONSULTANT: XYZ)  Hand-drawn sketch of a building layout with dimensions and labels. The sketch shows a rectangular building with internal divisions. Dimensions are given in meters (m). Labels include 'GARB SURVEY CONSULTANT: XYZ' and 'GARB SURVEY CONSULTANT: XYZ'.
--	---

INSPECTION RESULT		Status
☒	- This work was inspected	Approval
☐		Not Attended

INSPECTION RESULT		Approval Status		Please Tick if	
Organisation	Name	Sign	Date	Time	A-AWC-R
Contractor Engineer	20/10/2022 14:30	20/10/2022 14:30	20/10/2022 14:30	20/10/2022 14:30	20/10/2022 14:30
Contractor	XYZ	20/10/2022 14:30	20/10/2022 14:30	20/10/2022 14:30	20/10/2022 14:30
QA/QC	H.M.C	20/10/2022 14:30	20/10/2022 14:30	20/10/2022 14:30	20/10/2022 14:30
GARB**					
Employers Representative	Khaded ahr	20/10/2022 14:30	20/10/2022 14:30	20/10/2022 14:30	20/10/2022 14:30

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)					
Issued by Contractor	Name	Sign	Date					
			25-10-2022					
Received by Employers Representative	Name	Sign	Time					
			6					
C1		C2	C3	DD	MM	YY	HH	MM
KP		EW	OT	25	10	22		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+466 TO 201+666	
	E=260165.8013	E=260172.0505
	N=3136899.0593	N=3136699.1703
Inspection description/		
As-Built for rock surface from st (201+466) to st (201+666)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)


	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C - you must follow spec and geo-technical report
--	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer					A-AWC-R	
Contractor QA/QC*	XYZ		25-10-2022	13:00	A	
	H.M.C		25/10/2022	13:00	A	
GARB**						
Employers Representative	Khaled ali		23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
			29-10-2022	7						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	29	10	28		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	200+876 TO 201+466		
	E=260126.0446	E=260165.8013	
	N=3137487.7094	N=3136899.0593	
Inspection description[الرفع المساحي + المعاينة للطرح المقصود (المسوح الأول) As-Built for rock surface from st (200+876) to st (201+466)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate





Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. (xyz))

Comments by: General consultant (systra)

 (as built)	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C. - you must follow specs and design drawings.
---	--

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer					A-AWC-R	
Contractor QA/QC*	XYZ		29-10-2022	12:00	A	
	H.M.C		29/10/2022		A	
GARB**						
Employers Representative	Khaleed ali		23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	مكتب أديان مهدي للإستشارات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
	أديان مهدي	[Signature]	2-11-2022	8						
Received by Employers Representative	[Signature]	[Signature]	C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	2	11	22		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+036 TO 201+086	
	E=260137.1186 N=3137328.0971	E=260140.5793 N=3137278.217
<u>Inspection description/</u> As-Built for rock surface from st (201+036) to st (201+086)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
2/11/2022	

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

[Signature]

- Levels and coordinates were checked only by xyz and under their own responsibility
 - This work was inspected only by xyz and H.M.C
 - you must follow spec and geo-technical report

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	أديان مهدي	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	[Signature]	2-11-2022	17:30	A	
	H.M.C	[Signature]	2/11/2022	13:30	A	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عبيدة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	محمد أبو بكر	Date	6-11-2022						
	Sign		Time	10						
Received by Employers Representative	UIR		C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	6	11	2022		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+156 TO 201+246	
	E=260145.4242	E=260151.6535
	N=3137208.3848	N=3137118.6007
<u>Inspection description:</u> As-Built for rock surface from st (201+156) to st (201+246)		

الرفع المساحي + معاينة سطح صخري (المنسوب الثالث)

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. (xyz))	Comments by: General consultant (systra)
	- Levels and Coordinates were checked only by xyz and under their own responsibility. - This work was inspected only by xyz and H.M.C. you must follow specs and geo-technical report

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	محمد أبو بكر						
Contractor QA\QC*	XYZ		6-11-2022	14:00	A		
	H.M.C		6/11/2022	14:30	A		
GARB**							
Employers Representative	Khaled Ali		23/9/2024				

مختبرية في
الاستشارة الهندسية
خاصة بمقاولات الهندسة

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name أبو عجلة	Sign أبو عجلة	Date 7-12-2022																
Received by Employers Representative			Time 13																
		UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>EW</td> <td>OT</td> <td>7</td> <td>12</td> <td>23</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	EW	OT	7	12	23		
C1	C2	C3	DD	MM	YY	HH	MM												
KP	EW	OT	7	12	23														
CODE-1	CODE-2	CODE-3	CODE-4																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+286 TO 201+386	
	E=260154.422 N=3137078.6966	E=260161.1582 N=3136978.9239
<u>Inspection description</u> As-Built for rock surface from st (201+286) to st (201+386)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT: (xyz))	Comments by: General consultant (systra)
	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C. - you must follow specs and geo-technical report

INSPECTION RESULT						Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	Approval Status	
Contractor Engineer	أبو عجلة	أبو عجلة				
Contractor QA/QC*	XYZ	أبو عجلة	7-12-2022	14:00	A	
	H.M.C	أبو عجلة	7/12/2022	14:30	A	
GARB**						
Employers Representative	Khaled ali	أبو عجلة	23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR ,Hassan Mahdy (H.M.C)
Issued by Contractor	Name Sign	Date	Time
Received by Employers Representative	Sign	13-12-2022	14
	UIR	C1 KP	C2 EW
		C3 OT	DD 13
		MM 12	YY 22
		HH	MM
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+386 TO 201+426	
	E=260161.1582 N=3136978.9239	E=260163.6041 N=3136938.9988
Inspection description/		
الرفع المساحي + معاينة سطح صخره (المستوي الثالث) As-Built for rock surface from st {201+386} to st {201+426}		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)



- Levels and coordinates were checked only by xye and under their own responsibility
- This work was inspected only by xye and H.M.C
- you must follow specs and geo-technical report

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer					A-AWC-R	
Contractor QA\QC*	XYZ		13-12-2022	12:16	A	
	H.M.C		13/12/2022	12:17	A	
GARB**						
Employers Representative	Khaled ah.		23/12/2022			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)			
Issued by Contractor	Name	Sign	Date	Time			
	13-12-2022	16					
Received by Employers Representative	C1	C2	C3	DD	MM	YY	HH
	13	12	23				
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+036	
	E=260126.0446 N=3137487.7094	E=260137.1186 N=3137328.0971
Inspection description/		
As-Built for rock surface from st (200+876) to st (201+036)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C - you must follow spec and geotechnical rep.

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer						
Contractor QA/QC*	XYZ		13-12-2022	13:30	A	
	H.M.C		13/12/2022	14:00	A	
GARB**						
Employers Representative	Phaked ali		23/12/2022		A	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR ,Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
			2023-1-3	17						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	3	1	23		
CODE-1		CODE-2	CODE-3	CODE-4		CODE-5				

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	200+876 TO 201+666		
	E=260126.0446	E=260172.0505	
	N=3137487.7094	N=3136699.1703	
Inspection description/			
As-Built for cut from st (200+876) to st (201+666)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
2023/1/3	

COMPLIANCE EVIDENCE Must be Included as appropriate


Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
	- Levels and coordinates were checked only by XYZ and under their own responsibility - you must follow specs and design drawings

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor	XYZ		3-1-2023	14:00	A	
QA/QC*	H.M.C		3/1/2023	19:00		
GARB**						
Employers Representative	Khaled ali		23/9/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name  Sign 	Date	Time
Received by Employers Representative	UIR	13-6-2023	18
		C1 KP	C2 EW
		C3 OT	DD 13
		MM 6	YY 23
		HH	MM
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+660	
	E=260126.0446 N=3137487.7094	E=260171.9793 N=3136705.1798
Inspection description		
As-Built for cut from st (200+876) to st (201+660)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time



Planned Inspection Date	Planned Inspection Time
12/6/2023	

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

- Levels and coordinates were checked only by xyz and under their own responsibility

- you must follow spec and design dwg.

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA/QC*	XYZ		13-6-2023	9:00	A	
	H.M.C		13/6/2023			
GARB**						
Employers Representative	Khaled ali		23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله والمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name Sign 24-8-2023	Date	Time 19
Received by Employers Representative	Sign 23	Time	

CODE -1	CODE -2	CODE -3	CODE -4	CODE -5
---------	---------	---------	---------	---------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+840 E=260126.0446 N=3137487.7094	E=260170.9813 N=3136525.1923
Inspection description: As-Built for cut from st (200+876) to st (201+840)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
24/8/2023	

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

as built
قطاع الصنع

- Levels and coordinates were checked only by xyz and under their own responsibility
- you must follow specs and design dwg.

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	محمد زكريا	محمد زكريا			A-AWC-R	
Contractor QA/QC*	XYZ	محمد زكريا	26-8-2023	10:00	A	
	H.M.C	محمد زكريا	26/8/2023	10:15	A	
GARB**						
Employers Representative	Khaled ali	محمد زكريا	23/8/2023		A	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name وليد فهد محمد	Date	9-11-2023
Received by Employers Representative	Sign وليد فهد محمد	REQ.NUM	20
Received by Employers Representative	UIR	C1 KP	C2 SU
		C3 OT	DD 9
		MM 11	YY 23
		HH	MM
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description/ تشييد قاع إحلل from st (202+220) to st (202+300)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))	Comments by: General consultant (systra)
	- levels and coordinates were checked only by xyz and under their own responsibility - No objection according to the attached reports and lab. results.

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد فهد محمد	وليد فهد محمد	19-11-2023	10:00	(A)	
Contractor QA/QC*	XYZ	محمد عبد الله	9/11/2023	11:00	A	
Employers Representative	Khaled ali		23/9/2024			

* Designer

** Alignment: Bridges; Culvert Only

UNIVERSAL INSPECTION REQUEST



مكتب أد/حسن مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عبيدة للمقاولات 2023	Designer Company*	DR ,Hassan Mahdy (H.M.C)															
Issued by Contractor	Name [Signature] [Stamp: ABU ABIDA]	Date	REQ. NUM 22															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>21</td> <td>11</td> <td>23</td> <td>2</td> <td>30</td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	21	11	23	2	30
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT	21	11	23	2	30											
CODE-1	CODE-2	CODE-3	CODE-4															
CODE-5																		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+000 TO 202+120	
	E=260164.6561 N=3136365.3242	E=260156.5571 N=3136245.6007
<u>Inspection description/</u> from st (202+000) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was checked only by xyz and H.M. - you must follow speed and design drawing and geo-technical report

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	[Signature]	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	[Signature]	21-11-2023	3:15	(A)	
	H.M.C	[Signature]	21/11/2023	3:00	A	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/11/2024		Any	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown:

Contractor Company	أبو عجمية للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	REQ. NUM							
			22-11-2023	23							
Received by Employers Representative	UIR		C1	C2	C3	DD	MM	YY	HH	MM	
			KP	SU	OT	22	11	23			
CODE-1			CODE-2			CODE-3			CODE-4		
CODE-5			CODE-6			CODE-7			CODE-8		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+220 TO 202+300		
	E=260147.6147	E=260139.0278	
	N=3136146.003	N=3136066.4661	
<u>Inspection description/</u>			
منطقة ردم منسوب (-9.5) متر from st (202+220) to st (202+300)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time



Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
	- No objection, according to the attached reports and Lab. results. - you must follow specs and design drawings

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد عوريجي						
Contractor QA/QC*	XYZ		22-11-2023	3:45	(A)		
	H.M.C		22/11/2023	11:00	A		
GARB**							
Employers Representative	Fhaled ali		23/10/2024				


RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours The Work described below will be complete and ready for inspection at planned time shown											
Contractor Company	شركة المقاولات العامة 				Designer Company*	DR .Hassan Mahdy (H.M.C)					
Issued by Contractor	Name	Sign	Date		REQ.NUM						
			25-11-2023		24						
Received by Employers Representative			UIR	C1	C2	C3	DD	MM	YY	HH	MM
				AP	SU	OT	25	11	23		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
From 200+876 To 202+376	202+000 TO 202+020	
	E=260164.6561	E=260163.5058
	N=3136365.3242	N=3136345.3573
<u>Inspection description:</u> من طبقة ردم منسوب (13) متر from st (202+000) to st (202+020)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (systra)) 	Comments by: General consultant (systra) - No objection, according to the attached reports and lab. results. - you must follow specs and design drawings
--	--

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد محمد						
Contractor QA/QC*	XYZ		25-11-2023	12:30	(A)		
	H.M.C		25/11/2023	11:00	A		
GARB**							
Employers Representative	Khaled ali		23/9/2024				

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name 	Sign 	Date 28-11-2023																
Received by Employers Representative	UIR	REQ NUM 25																	
		<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>28</td> <td>11</td> <td>23</td> <td>11</td> <td>00</td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	28	11	23	11	00	
C1	C2	C3	DD	MM	YY	HH	MM												
KP	SU	OT	28	11	23	11	00												
CODE-1	CODE-2-109	CODE-3	CODE-4	CODE-5															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300 E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description from st (202+220) to st (202+300) طبقة ردم منسوب (-9) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time


Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)



- No objection, according to the attached reports and lab. results
- you must follow specs and design dng.

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمد				A-AWC-R	
Contractor QA/QC*	XYZ	عبد الله الدلاوي	28/11/2023	3:30	A	
	H.M.C	عبد الله الدلاوي	28/11/2023	11:00	A	
GARB**						
Employers Representative	Khaled ali		23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	Name		Sign	Designer Company*	DR .Hassan Mahdy (H.M.C)				
Issued by Contractor	29-11-2023		REQ.NUM		26				
Received by Employers Representative	C1		C2	C3	DO	MM	YY	HH	MM
	KP		SU	OT	29	11	23		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5	

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+060 TO 202+080		
	E=260160.9658 N=3136305.4382	E=260159.576 N=3136285.4865	
Inspection description[from st (202+060) to st (202+080) طبقة ردم منسوب (-11) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))	Comments by: General consultant (systra)
 المهندس خالد علي - الهندس العام	- No objection, according to the attached reports and lab. results. - you must follow specs and design draw

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	Waleed Elmaghrabi	Waleed Elmaghrabi	29-11-2023	1:15	(A)	
Contractor QA/QC*	XYZ	Khaled Ali	29-11-2023	12:45	A	
GARB**						
Employers Representative	Khaled Ali	Khaled Ali	29/11/2023		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name وليد محمود محمد	Date	29-11-2023															
Received by Employers Representative	Sign [Signature]	REQ.NUM	27															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>29</td> <td>11</td> <td>23</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	29	11	23		
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT	29	11	23													
CODE-1	CODE-2	CODE-3	CODE-4															
CODE-5	CODE-6	CODE-7	CODE-8															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+080 TO 202+120	
	E=260159.576 N=3136285.4865	E=260156.5571 N=3136245.6007
Inspection description[منطقة ردم منسوب (-10.5) متر from st (202+080) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSANTANT.(xyz))

Comments by: General consultant (systra)

-No objection, according to the attached reports and lab. results
-you must follow specs and design dwg

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمود محمد	[Signature]	29-11-2023	11:30	(A)	
Contractor QA/QC*	H.M.C	[Signature]	29-11-2023	12:30	(A)	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	157137 أبو عزة للتقانات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)					
Issued by Contractor	Name م.د/حسن مهدي	Date	30-11-2023					
Received by Employers Representative	Sign م.د/حسن مهدي	REQ.NUM	28					
UIR	C1 KP	C2 SU	C3 OT	DD 30	MM 11	YY 23	HH	MM

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+000 TO 202+020 E=260164.6561 N=3136365.3242	E=260163.5058 N=3136345.3573
Inspection description: ردم طبقة ردم منسوب (-12.5) متر from st (202+000) to st (202+020)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT: XYZ)	Comments by: General consultant (systra)
م.د/حسن مهدي	-No objection, according to the attached reports and lab. results. -you must follow spec and design draw

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	م.د/حسن مهدي	م.د/حسن مهدي	30-11-2023	13:00	A	
Contractor QA/QC*	XYZ	م.د/حسن مهدي	30/11/2023	12:30pm	A	
GARB**						
Employers Representative	Khaled Ali	م.د/حسن مهدي	23/9/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 57537	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name [Signature]	Sign [Signature]	Date 2-12-2023
Received by Employers Representative	UIR	REQ.NUM 29	
		C1 KP	C2 SU
		C3 OT	DD 2
		MM 12	YY 23
		HH 23	MM 23
CODE-1	CODE-2	CODE-3	CODE-4
CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300 E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description[from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (-8.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (sysra)

تم استلام نتائج التحليلات
من مختبر أديس
البيانات

- No objection, according to the attached reports and lab. results.
- you must follow specs and design dr

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمد	[Signature]				
Contractor QA/QC*	XYZ	عبد الرحمن الوالد	21/12/2023	3:15	A	
	H.M.C	أحمد مصطفى	21/12/23	3:00	AWC	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/12/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name 157537	Sign	Date 3-12-2023
Received by Employers Representative		UIR	REQ.NUM 30
		C1 KP	C2 SU
		C3 OT	DD
		MM	YY 23
		HH	MM

CODE-1

CODE-2

CODE-3

CODE-4

CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+100	
	E=260160.9658 N=3136305.4382	E=260158.1064 N=3136265.5406
Inspection description		
from st (202+060) to st (202+100) طبقة ردم ملسوب (-10.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))	Comments by: General consultant (systra)
 مهندس: أحمد مصطفى السريحي - أحمد أناني	- No objection, according to the attached reports and lab. results. - you must follow specs and design d.

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA\QC*	XYZ		3-12-2023	4:15	(A)	
	H.M.C		3/12/2023	2:30pm	AWC	
GARB**						
Employers Representative	Khaled ali		28/9/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة البترول العالمية		Designer Company*	DR. Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	وليد عيسى	Date	5-12-2023							
	Sign		REQ. NUM	31							
Received by Employers Representative	Signature	Sign	Date	C1	C2	C3	DD	MM	YY	HH	MM
				KP	SU	OT				23	
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+220 TO 202+300		
	E=260147.6147	E=260139.0278	
	N=3136146.003	N=3136066.4661	
Inspection description/			
من تسليم طبقة ردم منسوب (8-متر) from st (202+220) to st (202+300)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT (-xyz))

Comments by: General consultant (systra)

 مهندسون استشاريون - الهندسة المدنية	- No objection, according to the attached reports and lab. results. - you must follow specs and design dwg.
--	--

INSPECTION RESULT

					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد عيسى					
Contractor QA/QC*	XYZ	محمد ابراهيم	6-12-2023	10:30	(A)	
	H.M.C	شوربلة النسي	5/12/2023	4:15Pm	Awc	
GARB**						
Employers Representative	Khaleel ali		23/9/2024		Awc	



UNIVERSAL INSPECTION REQUEST



مكتب أ.أ.إ.م.م.م.
للإشراف الهندسية



الهيئة العامة للإشراف الهندسي



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR. Hassan Mahdy (H.M.C)					
Issued by Contractor	Name	Sign	Date	REQ. NUM					
	13-12-2023	35							
Received by Employers Representative	UIR	G1	C2	C3	DD	MM	YY	HH	MM
		XP	SU	OT	13	12	23	3	00
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5	

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+060 TO 202+120		
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007	
Inspection description/ منطقة ردم طلبة (9- متر) from st (202+060) to st (202+120)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT. (xyz))	Comments by: General consultant (systra)
	- No objection, according to the attached reports and lab. results. - you must follow specs and design drawings.

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	أبو عجيبة للمقاولات العامة		13-12-2023	4:00	(A)		
Contractor QA/QC*	XYZ		13-12-2023	3:00	Awc		
GARB**							
Employers Representative	Khaled ali		23/9/2024		Awc		

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



شركة أديس مهدي
للإستشارات الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة			Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM							
	أبو عجلة	أبو عجلة	16-12-2023	36							
Received by Employers Representative	Signature	Signature	UIR	G1	G2	G3	DD	MM	YY	HH	MM
				XP	SU	OT			23		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	200+220 TO 202+300		
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661	
Inspection description:			
من تسليم طبقة ردم مسلوب (7-متر) from st (202+220) to st (202+300)			

INSPECTION DETAILS The following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT: xyz)

أبو عجلة
أبو عجلة
أبو عجلة

Comments by: General consultant (systra)

- No objection, according to the attached reports and lab. results.
- you must follow specs and design diry.

INSPECTION RESULT

					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	أبو عجلة	أبو عجلة				
Contractor QA/QC*	XYZ	أبو عجلة	16-12-2023	3:15	A	
	H.M.C	أبو عجلة	16/12/2023	3:00	A	
GARB**						
Employers Representative	Khaled ali	أبو عجلة	29/12/24		Awc	



UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للطرق
والبنية التحتية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	وليد فلاح	وليد فلاح	17-12-2023	37						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT				23	

EXPLANATION OF WORK TO BE INSPECTED			
Area	Element		Item
From 200+876 To 202+376	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007	
Inspection description:			
من (8.5) متر from st (202+060) to st (202+120)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by (GARB SURVEY CONSULTANT xyz)	Comments by: General consultant (systra)
استاذ المهندس مستوى التفتيش الكيفي الذي	- No objection, according to the attached reports and lab. results. - you must follow specs and design dwg

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد فلاح	وليد فلاح				تم العمل
Contractor QA/QC*	XYZ		17-12-2023	13:00	A	OK
	H.M.C	محمد بن عبد الله	17-12-2023	11:00	AWC	OK
GARB**						
Employers Representative	Khaled ali		20/12/24		AWC	



UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإشراف الهندسية



المكتب الهندسي للإشراف



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown:

Contractor Company			Designer Company*	DR. Hassan Mahdy (H.M.C)																
Issued by Contractor	Name	Sign	Date	REQ. NUM																
			19-12-2023	38																
Received by Employers Representative			<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>AP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>YY</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	AP	SU	OT			YY			
C1	C2	C3	DD	MM	YY	HH	MM													
AP	SU	OT			YY															
CODE-1	CODE-2 2603-1615-199	CODE-3	CODE-4	CODE-5																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+576	202+220 TO 202+300	
	E=260147.5147	E=260139.0278
	N=3136146.003	N=3136066.4661
Inspection description (from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (7,0-)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	M5 Reference	



Comments by: (GARB SURVEY CONSULTANT: XYZ)

تم فحص القطاع ووافق عليه
مستوى تشتت الكثبان للترسيب - الخط الذي

Comments by: General consultant (systra)

- No objection, according to the attached reports and lab. results.
- you must follow specs and design drawings

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA/QC*	XYZ		19-12-2023	3:30	A	
	H.M.C		19-12-2023	11:30	A	
GARB**						
Employers Representative	Khaled ali		23/9/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date							
	وليد محمود محمد		20-12-2023							
Received by Employers Representative		REQ.NUM	39							
		C1	C2	C3	DD	MM	YY	HH	MM	
		KP	SU	OT				23		

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description/		
من (8-) متر from st (202+060) to st (202+120) طبقة ردم منسوب		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
	- No objection, according to the attached reports and Lab. results. - You must follow specs and design draw

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمود محمد				A-AWC-R	
Contractor QA/QC*	XYZ		20-12-2023	3:40	A	
	H.M.C		20-12-2023	1:45	A	
GARB**						
Employers Representative	Khaled ali		23/9/2024		A	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للغذاء والدواء
Saudi Food & Drug Authority



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name Sign 21-12-2023	Date	REQ.NUM 40															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>21</td> <td>12</td> <td>23</td> <td>11</td> <td>30</td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	21	12	23	11	30
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT	21	12	23	11	30											
CODE-1	CODE-2	CODE-3	CODE-4															
CODE-5	CODE-6	CODE-7	CODE-8															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description: from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (6-متر)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT: xyz)	Comments by: General consultant (systra)
	- No objection, according to the attached reports and lab. results. - you must follow specs and design d.

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمد	وليد محمد				
Contractor QA/QC*	XYZ	عبد الرحمن العرابي	21-12-2023	11:00	A	
	H.M.C	محمد بن عبد الله العرابي	21/12/23	11:30	A	
GARB**						
Employers Representative	Khaled ali		23/12/2023		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب المدققين
للإشراف الهندسية



الهيئة العامة للتأهيل
والإشراف الهندسي



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name وليد محمود محمد	Sign 	Date 23-12-2023	REQ.NUM 41																
Received by Employers Representative			<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>23</td> <td></td> <td></td> </tr> </table>		C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			23		
C1	C2	C3	DD	MM	YY	HH	MM													
KP	SU	OT			23															
CODE-1		CODE-2	CODE-3	CODE-4	CODE-5															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
<u>Inspection description</u> from st (202+220) to st (202+300) تسليم طبقة ردم ملسوب (-5.5) متر		

INSPECTION DETAILS The following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
	- No objection, according to the attached reports and lab. results. - you must follow specs and design dr.

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود محمد	وليد محمود				
Contractor QA/QC*	XYZ	عبدالله العبدالله	23/12/2023	1:00	A	
	H.M.C	محمد علي النور	23/12/2023	12:00	A	
GARB**						
Employers Representative	Khaled ali		23/12/2023		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للمستشارات الهندسية



الهيئة العامة للإعانة
والتطوير العمراني



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name وليد محمود	Date	23-12-2023																
Received by Employers Representative	Sign [Signature]	REQ.NUM	43																
		<table border="1"> <tr> <td>G1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>23</td> <td>12</td> <td>23</td> <td></td> <td></td> </tr> </table>	G1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	23	12	23			
G1	C2	C3	DD	MM	YY	HH	MM												
KP	SU	OT	23	12	23														
CODE-1	CODE-2	CODE-3	CODE-4																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description/ منسوب (7.5-) متر from st (202+060) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT. (xyz))	Comments by: General consultant (systra)
[Signature]	- No objection, according to the attached reports and lab. results. - you must follow specs and design data

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود	[Signature]				
Contractor QA/QC*	XYZ	[Signature]	23-12-2023	4:15	A	
	H.M.C	[Signature]	23/12/23	4:00	AWC	
GARB**						
Employers Representative	Khaled Ali	[Signature]	23/12/2023		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أراضين مهدي
للإستشارات الهندسية



الهيئة العامة للإعتماد
والتقنين



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	المشروعات العامة		Designer Company*	DR. Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ. NUM						
	ولي محمد	[Signature]	25-12-2023	44						
Received by Employers Representative			C1	C2	C3	DO	MM	YY	HH	MM
			KP	SU	OT			23		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description:		
من (7) متر طبقه ردم منسوب (202+060) to st (202+120)		

INSPECTION DETAILS The following will be ready at the Planned inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT. xyz)

Comments by: General consultant (systra)

[Signature]

- No objection, according to the attached reports and lab. results.
- you must follow specs and design data

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	ولي محمد	[Signature]				
Contractor QA/QC*	XYZ	[Signature]	25-12-2023	4:13	A	
	H.M.C	[Signature]	25-12-2023	4:10	AWC	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أديسن مهندسي
الاستشارات الهندسية



الهيئة العامة للطرق
والمواصلات



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أيم جلوبل للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	وليد محمود محمد	[Signature]	28-12-2023	46						
Received by Employers Representative		[Signature]	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT				23	

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
From 200+876 To 202+376	201+980 E=260165.727 N=3136385.3	
Inspection description: منطقة ردم منسوب (-14) متر from st (201+980)		

INSPECTION DETAILS The Following will be ready at the Planned inspection Time	
Planned inspection Date	Planned inspection Time


COMPLIANCE EVIDENCE Must be included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))	Comments by: General consultant (systra)
[Signature]	- No objection, according to the attached reports and lab. results. - you must follow specs and design drawings

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود محمد	[Signature]				
Contractor QA/QC*	XYZ	[Signature]	28-12-2023	12:00	A	[Signature]
	H.M.C	[Signature]	28-12-2023	11:00		
GARB**						
Employers Representative	Khaled Ali	[Signature]	23/9/2024		ANC	

UNIVERSAL
INSPECTION
REQUEST








RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours
The Work described below will be complete and ready for inspection at planned time shown

Contractor Company

Name

Designer Company*

Date

DR. Hassan Mahdy
(H.M.C)

28-12-2023

Issued by Contractor

Sign

REQ.NUM

47

Received by Employers Representative

Sign

C1 C2 C3 DO MM YY HH MM

KP SU OT 23

EXPLANATION OF WORK TO BE INSPECTED

Area

Element

Item

From 200+876 To 202+376

202+060 TO 202+120
E=260160.9658
N=3136305.4382

E=260156.5571
N=3136245.6007

Inspection description:
from st (202+060) to st (202+120) طبقة ردم منسوب (-6.5) متر

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date

Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐

Test Results Attached ☐

Calibration Attached ☐

Other as indicated ☐

Drawing Reference

ITP Reference

MS Reference

Comments by: (GARB SURVEY CONSATANT: xyz)

Comments by: General consultant (systra)

No objection, according to the attached reports and lab. results.

you must follow specs and design dng.

INSPECTION RESULT

Approval Status

Please Tick if Not Attend

Organisation

Name

Sign

Date

Time

Contractor Engineer

XYZ

H.M.C

28-12-2023

13:00

GARB**

Employers Representative

23/9/2024



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	157537 مكتب المهندس مهدي للإستشارات الهندسية	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name وليد محجور محمد	Sign 	Date 2-1-2024																
Received by Employers Representative	Sign 	REQ.NUM 48																	
		<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>IP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	IP	SU	OT			24			
C1	C2	C3	DD	MM	YY	HH	MM												
IP	SU	OT			24														
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300 E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description/ من تسليم طبقة ردم مسسوب (-4.5) متر from st (202+220) to st (202+300)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz)) 	Comments by: General consultant (systra) -No objection, according to the attached reports and Lab. results. -you must follow specs and design drawings
--	--

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محجور محمد					
Contractor QA/QC*	XYZ H.M.C		2-1-2024	10:40	A	
GARB**						
Employers Representative	Khaled ali		23/1/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company			Designer Company*	DR. Hassan Mahdy (H.M.C)																
Issued by Contractor	Name	Sign	Date	REQ. NUM																
			2-1-2024	49																
Received by Employers Representative			<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			24			
C1	C2	C3	DD	MM	YY	HH	MM													
KP	SU	OT			24															
CODE-1		CODE-2		CODE-3	CODE-4	CODE-5														

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+060 TO 202+120		
	E=260160.9658	E=260156.5571	
	N=3136305.4382	N=3136245.6007	
<u>Inspection description</u> from st (202+060) to st (202+120) طبقة ردم منسوب (-6) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))	Comments by: General consultant (systra)
	- No objection, according to the attached reports and lab. results - you must follow specs and design drawings

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer							
Contractor QA/QC*	XYZ		2-1-2024	11:40	A		
	H.M.C		2-1-2024	11:50	AWC		
GARB**							
Employers Representative	Khaleed ali		23/1/2024		AWC		

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة المهندسين مهدي للإستشارات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name وليد محمور	Sign 	Date 2-1-2024																
Received by Employers Representative	UIR	REQ NUM 50																	
		<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			24			
C1	C2	C3	DD	MM	YY	HH	MM												
KP	SU	OT			24														
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+960 TO 202+000	
	E=260166.717 N=3136405.271	E=260164.6561 N=3136365.1247
<u>Inspection description</u> from st (201+960) to st (202+000) طبقة ردم منسوب (-13.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. (xyz)) 	Comments by: General consultant (systra) -No objection, according to the attached reports and lab. results. -you must follow specs and design dr
---	--

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمور					
Contractor QA\QC*	XYZ	عبد الرحمن الشرايحي	2-1-2024	11:15	A	
	H.M.C	محمود محمد	2-1-2024	11:00	AUC	
GARB**						
Employers Representative	Khaled ali		23/9/2024		AUC	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



المهنة العامة الإستشارية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	[Signature]		6-1-2024	51						
Received by Employers Representative	[Signature]	UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT				20	

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+960 TO 202+000		
	E=260166.717 N=3136405.271	E=260164.6561 N=3136365.3242	
<u>Inspection description</u> from st (201+960) to st (202+000) طبقه ردم منسوب (-13) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: [GARB SURVEY CONSATANT. (xyz)]	Comments by: General consultant (systra)
[Signature]	- No objection, according to the attached reports and Lab. results. - you must follow specs and design drag

INSPECTION RESULT

					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمدي	[Signature]				
Contractor QA/QC*	XYZ	عبد الرحمن العرابي	6-1-2024	4:20	A	يرجى إعادة المعاينة قبل العمل [Signature]
	H.M.C	محمود عولمة	6/1/2023	4:15	AWC	
GARB**						
Employers Representative	Khaled ali	[Signature]	29/9/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أمان مهدي
للإشراف الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name	Sign	Date	REQ.NUM
	وليد عمار	وليد عمار	6-1-2024	52
Received by Employers Representative	UIR		C1 C2 C3 DD MM YY HH MM	
			KP SU OT	24
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description/		
من (202+060) to st (202+120) طبقة ردم منسوب (5.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
تم الاستعراض والتوقيع على التقرير مفتوحه الفشار الكهربي السريع - لفت الذرق	- No objection, according to the attached reports and lab results. - you must follow spec and design

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد عمار	وليد عمار			A-AWC-R	
Contractor QA/QC*	XYZ	عبد الرحمن الدواوي	6-1-2024	5:00	A	
	H.M.C	محمد عمار	6/1/2024	4:40	Awc	
GARB**						
Employers Representative	Khaled ali		23/9/2024		Anrc	

UNIVERSAL INSPECTION REQUEST



مكتب أ.أ.أ. من مهاي
للإشراف الهندسية



الهيئة العامة للإشراف
على الطرق



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours													
The Work described below will be complete and ready for inspection at planned time shown													
Contractor Company	أ.أ.أ. من مهاي للمقاولات العامة 57577				Designer Company*	DR. Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign			Date	REQ. NUM							
	[Signature]			10-1-2024	53								
Received by Employers Representative	[Signature]	[Signature]	[Signature]	[Signature]	UIR	C1	C2	C3	DD	MM	YY	HH	MM
					KP	SU	OT				28		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5					

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
<u>Inspection description:</u> متر (5-) من from st (202+060) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	



Comments by: (GARB SURVEY CONSALTANT. (xyz))	Comments by: General consultant (systra)
[Signature] م.أ.أ. من مهاي م.أ.أ. من مهاي	-No objection, according to the attached reports and lab. results. -you must follow specs and design dwg

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد الحويهد	[Signature]					
Contractor QA/QC*	XYZ	عبد الرحمن العرياني	10-1-2024	12:30	A	[Signature]	
	H.M.C	محمد العرياني	10-1-2024	12:00	A		
GARB**							
Employers Representative	Khaled chi	[Signature]	23/9/2024		Awc		



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name:  Sign: 	Date	REQ.NUM
Received by Employers Representative	UIR	10-1-2024	54
		C1 C2 C3 DD MM YY HH MM	
		KP SU OT	23
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+300 TO 202+376	
	E=260139.0278 N=3136066.4661	E=260129.6912 N=3135991.0324
Inspection description/		
from st (202+300) to st (202+376)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time


Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))

Comments by: General consultant (systra)





- levels and coordinates were checked only by xyz and under their own responsibility

- you must follow specs and designing and geo-technical report.


- This work was inspected only by xyz and H.M.C

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمود				A-AWC-R	
Contractor QA/QC*	XYZ		10-1-2024	10:30	A	
	H.M.C		10-1-2024	10:30	AWC	
GARB**						
Employers Representative	Khaled ali		23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name:  Sign: 	Date	REQ. NUM
Received by Employers Representative	UIR	15-1-2024	55
		C1 C2 C3 DD MM YY HH MM	
		KP SU OT	20
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+300 TO 202+340 E=260139.0278 E=260134.2574 N=3136066.4661 N=3136026.7517	
Inspection description/ منسوب (8.5-) متر from st (202+300) to st (202+340)		


INSPECTION DETAILS The following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT - (xyz))  تم فحص الموقع من قبل المهندس محمد صالح - الهندس الذي	Comments by: General consultant (systra) -you must follow specs and design drug- -you must do leveling and lining the compacted side slope of filling layer
---	--

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	علي محمد					
Contractor QA/QC*	XYZ	عبد الرحمن العزبان	16-1-2024	8:30	A	
	H.M.C	محمد علي	15/1/2024	4:30pm	A	
GARB**						
Employers Representative	Khaled ali		26/1/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أ.إ.ص.ن مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name:  Sign: 	Date	REQ. NUM						
Received by Employers Representative	UIR	15-1-2024	56						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT			24		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+220 TO 202+300		
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661	
Inspection description/			
from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (4) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	


Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)



-you must follow specs and design by
-you must do leveling and lining
the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود محمد		16-1-2024			
Contractor QA/QC*	XYZ	عبد الرحمن الزقراوي	16-1-2024	9:18	A	
	H.M.C	محمد علي	15/1/2024	5:10	A	
GARB**						
Employers Representative	Khaled ali		16/1/2024		AWC	



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name [Signature] Sign [Signature]	Date	REQ. NUM
Received by Employers Representative	UIR	16-1-2024	57
		C1 C2 C3 DD MM YY HH MM	
		KP SU OT	21
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description/		
منطقة ردم منسوب (4.5) متر from st (202+060) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT - xyz)	Comments by: General consultant (systra)
تم استلام الموقع في 16/1/2024 مستوى القاع الكبريتي السريع - القاع الثاني	- you must follow specs and design durg. - you must do landing and lining the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد عمار	[Signature]				
Contractor QA\QC*	XYZ	[Signature]	16-1-2024	3:30	A	
	H.M.C	[Signature]	16/1/2024	3:00	AWC	
GARB**						
Employers Representative	Khaled ali	[Signature]	16/1/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name: 157537 Sign: وليد خلافة	Date	17-1-2024						
Received by Employers Representative	UIR	REQ.NUM	58						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT	17	1	24	4	00
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description/		
from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (3.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: GARB SURVEY CONSATANT (xyz)	Comments by: General consultant (systra)
تم اكتشاف خلل في التسليم في المنطقة المذكورة - القيد 157537	-you must follow specs and design dng -you must do leveling and lining the compacted side slope & filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليده خلافة					
Contractor	XYZ	عليه الرحمه الهادي	17-1-2024	5:10	A	
QA/QC*	H.M.C	عليه الرحمه الهادي	17/1/2024	4:00	A	
GARB**						
Employers Representative	Khaled ali		17/1/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أديان مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR. Hassan Mahdy (H.M.C)					
Issued by Contractor	Name	137537	Sign	Date	REQ. NUM				
	وليد محمد			20-1-2024	59				
Received by Employers Representative	UIR	C1	C2	C3	DO	MM	YY	HH	MM
		KP	SU	OT				24	
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5	

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+300 TO 202+360	
	E=260139.0278 N=3136066.4661	E=260131.7531 N=3136006.9091
Inspection description		
منسوب (8-متر) from st (202+300) to st (202+360) تسليم طبقة ردم منسوب		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: GARB SURVEY CONSATANT. (xyz)	Comments by: General consultant (systra)
مستشار الاستشارات العامة	- you must follow specs and design dwg.
مستشار الاستشارات العامة	- you must do leveling and lining
مستشار الاستشارات العامة	the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمد					
Contractor QA/QC*	XYZ	عبد الرحمن الزباري	20/1/2024	10:00	A	
	H.M.C	محمود علي	20/1/2024	09:00	A	
GARB**						
Employers Representative	Khaled ali		20/1/2024		Amr	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name: <u>علي محمد</u> Sign: <u>علي محمد</u>	Date	REQ.NUM
Received by Employers Representative	UIR	18-1-2024	60
		C1 C2 C3 DD MM YY HH MM	
		KP SU OT	24
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+920 TO 202+000	
	E=260168.4582 N=3136445.233	E=260164.6561 N=3136365.3242
Inspection description:		
منسوب (12.5) متر from st (201+920) to st (202+000)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
تم العمل على الخطأ في التصميم	- you must follow specs and design drawing
تمت الموافقة على التصميم	- you must do leveling and lining
	- the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	علي محمد	علي محمد				
Contractor QA/QC*	XYZ	علي محمد	20-1-2024	11:15	A	
	H.M.C	علي محمد	20-1-2024	3:45	A	
GARB**						
Employers Representative	Khaled ali	علي محمد	20/1/2024	Amrc		

UNIVERSAL INSPECTION REQUEST



مكتب أ.د. حسن مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR. Hassan Mahdy (H.M.C)
Issued by Contractor	Name: Sign:	Date	18-1-2024
Received by Employers Representative	UIR	C1 KP	C2 SU
		C3 OT	DO MM
			YY 23
			HH MM
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+020 TO 202+060 E=260163.5058 N=3136345.3573	E=260160.9658 N=3136305.4382
Inspection description/ منسوب (12.5-) متر from st (202+020) to st (202+060)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT: xyz)	Comments by: General consultant (systra)
	- you must follow specs and design dwg - you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	ر.ب. محمود محمد				A-AWC-R	
Contractor QA/QC*	XYZ		21-1-2024	5:15	A	
	H.M.C		21-1-2024	5:00	A	
GARB**						
Employers Representative	Ali Khaled		20/1/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name: Sign:	Date	REQ. NUM
Received by Employers Representative	UIR	21-1-2024	62
		C1 C2 C3 DD MM YY HH MM	
		KP SU OT	24

CODE-1

CODE-2

CODE-3

CODE-4

CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+300 TO 202+376 E=260139.0278 E=260129.6912 N=3136066.4661 N=3135991.0324	
Inspection description: منسوب (7.5) متر from st (202+300) to st (202+376) تسليم طبقة ردم منسوب (7.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

-you must follow specs and design dng
-you must do leveling and lining
the compacted side slope & filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود	وليد محمود				
Contractor QA/QC*	XYZ	عبد الرحمن الابرار	21-1-2024	5:20	A	
	H.M.C	شودا	21-1-2024	5:28	A	
GARB**						
Employers Representative	Khaled ali	كhaled ali	21/1/2024		A	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجمية للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name:  Sign: 	Date	22-1-2024																
Received by Employers Representative	UIR	REQ.NUM	63																
		<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>20</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			20			
C1	C2	C3	DD	MM	YY	HH	MM												
KP	SU	OT			20														
CODE-1	CODE-2	CODE-3	CODE-4																
CODE-5																			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+920 TO 202+040	
	E=260168.4582 N=3136445.233	E=260162.2757 N=3136325.3952
Inspection description:		
منسوب (12-) متر from st (201+920) to st (202+040)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. (xyz))


Comments by: General consultant (systra)



-you must follow specs and design dwg
-you must do leveling and lining
the compacted side slope of filling layer

INSPECTION RESULT

Approval
StatusPlease Tick if
Not Attend

Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمد					
Contractor QA/QC*	XYZ عبد الرحمن الخياط		23-1-2024	9:00	A	
	H.M.C فواز العبدوي		22-1-2024	5:15	AWC	
GARB**						
Employers Representative	Khaled ali		23/1/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ. NUM						
	وليد محمود	وليد علاف	27-1-2024	65						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT				23	
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+875 To 202+376	201+920 TO 202+060		
	E=260168.4582	E=260160.9658	
	N=3136445.233	N=3136305.4382	
Inspection description/			
من 200+875 إلى 202+376 من st (201+920) إلى st (202+060) طبقة ردم منسوب (-11.5) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)





-you must follow specs and design drawing
 -you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time		A-AWC-R	
Contractor Engineer	وليد علاف	وليد محمود					
Contractor QA/QC*	XYZ	أحمد محمد	27-1-24	5:00		A	
	H.M.C	محمود محمد	27-1-24	4:15		A	
GARB**							
Employers Representative	Khaled ali		27/1/2024			A	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	REQ.NUM							
	رئيس محوّر	رئيس ملاف	30-1-2024	66							
Received by Employers Representative			UIR	C1	C2	C3	DD	MM	YY	HH	MM
				KP	SU	OT			24		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED


Area	Element		Item
From 200+876 To 202+376	202+300 TO 202+376		
	E=260139.0278	E=260129.6912	
	N=3136066.4661	N=3135991.0324	
<u>Inspection description:</u> from st (202+300) to st (202+376) تسليم طبقة ردم منسوب (6.5-) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
	-you must follow specs and design dng -you must do leveling and lining the compacted sube slp & filling layer

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد محوّر	وليد ملاف				يتم صيانة القطر قبل التورب	
Contractor QA/QC*	XYZ	محمد رافع	30-1-2024	4:00	(A)		
	H.M.C	محمد منتصر فوزي	30-1-24	12:30	AWC		
GARB**							
Employers Representative	Khated ali		30/1/2024				

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
			12-2-2024	67						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT			27		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+920 TO 202+060		
	E=260168.4582 N=3136445.233	E=260160.9658 N=3136305.4382	
Inspection description(			
from st (201+920) to st (202+060) طبقة ردم ملسوب (11- متر			

INSPECTION DETAILS The Following will be ready at the Planned inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))	Comments by: General consultant (systra)
	- you must follow specs and design - you must do leveling and lining the compacted grade slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA/QC*	XYZ		12-2-2024	3:30	A	
	H.M.C		12/2/24	3:20	A	
GARB**						
Employers Representative	Khaleel ali		12/2/2024			

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



شركة سايسترا
للخدمات الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	وليد محمود	وليد عارف	18-2-2024	68						
Received by Employers Representative	[Stamp]	UIR	C1	C2	C3	DD	MM	YY	HH	MM
			ICP	SU	OT				24	
CODE-3		CODE-2	CODE-3	CODE-4		CODE-5				

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+300 TO 202+376		
	E=260139.0278	E=260129.6912	
	N=3136066.4661	N=3135991.0324	
Inspection description:			
منسوب (6-) متر from st (202+300) to st (202+376)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT - xyz)	Comments by: General consultant (systra)
	- you must follow specs and design durg - you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد محمود	وليد عارف					
Contractor QA/QC*	XYZ	عبد الرحمن الطرابي	19-2-2024	11:30	A		
	H.M.C	محمد مشهور فوزي	19-2-2024	12:00	A		
GARB**							
Employers Representative	rehaled ale	[Signature]	19/2/2024		Arre		

UNIVERSAL INSPECTION REQUEST



مكتب أديان مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	REQ.NUM							
	وليد محمود	وليد محمود	22-2-2024	69							
Received by Employers Representative	[Signature]	[Signature]	UIR	C1	C2	C3	DD	MM	YY	HH	MM
				KP	SU	OT			24		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+920 TO 202+060		
	E=260168.4582 N=3136445.233	E=260160.9658 N=3136305.4382	
Inspection description/			
من (10.5-) متر طبقة ردم منسوب (201+920) to st (202+060)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))

مستشار الاستشارات العامة
للمقاولات العامة

Comments by: General consultant (systra)

-you must follow specs and design
-you must do leveling and lining
the compacted side slope & filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود	وليد محمود				
Contractor QA/QC*	XYZ	عبد الرحمن الوفاوي	24-2-2024	3:30	A	
	H.M.C	محمد منعم فوزي	24-2-2024	11:00	A	
GARB**						
Employers Representative	Khaled ali	[Signature]	24/2/2024		Amr	

UNIVERSAL INSPECTION REQUEST



مكتب أديسن مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أديسن مهدي للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	وليد طاي و وليد محمد		23-3-2024	74						
Received by Employers Representative	UIR		C1	C2	C3	DO	MM	YY	HH	MM
			KP	SU	OT			24		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+920 TO 202+060		
	E=260168.4582 N=3136445.233	E=260160.9658 N=3136305.4382	
Inspection description/			
منطقة ردم منسوب (10- متر) from st (201+920) to st (202+060)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
تم اتمام العمل في المنطقة (الطريق) - انظر المرفق	- you must follow specs and design drawings - you must do leveling and Ginning the compacted side slope of filling layer

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد طاي و وليد محمد						
Contractor QA/QC*	XYZ	محمد مشهور	23-3-2024	12:15	A		
	H.M.C	محمد مشهور	23/3/2024	12:00	A		
GARB**							
Employers Representative	Khaled ali		23/3/2024		Amir		

UNIVERSAL INSPECTION REQUEST



مكتب أ.د. حسن مهدي
للإستشارات الهندسية



الهيئة العامة للإعانة
SHARER



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name: Sign:	Date	31-3-2024						
Received by Employers Representative	UIR	REQ. NUM	75						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT			24		
CODE -1	CODE -2	CODE -3	CODE -4	CODE -5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+920 TO 202+060 E=260168.4582 N=3136445.233	E=260160.9658 N=3136305.4382
Inspection description: منطقة ردم منسوب (9.5) متر from st (201+920) to st (202+060)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))

Comments by: General consultant (systra)

تم التأكد من أن العمل جاهز للتحقق من قبل المهندس الاستشاري (xyz) في تاريخ 31/3/2024.

-you must follow specs and design data
-you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود محمد					
Contractor QA/QC*	XYZ عبد الرحمن الطرطوسي		1-4-2024	12:00	A	
	H.M.C	محمود علي	31-3-2024	11:00	A	
GARB**						
Employers Representative	Khakdali		1/4/2024		Done	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name:  Sign: 	Date	REQ.NUM						
Received by Employers Representative	UIR	1-4-2024	76						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT			24		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description(		
منسوب (3-متر) from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (3-متر)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate




Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))

Comments by: General consultant (systra)

تأكد من التسليم طبقاً للمواصفات - القياسات
- you must follow specs and design dra
- you must do leveling and lining
the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	أبو عجلة					
Contractor QA/QC*	XYZ		1-4-2024	11:30	A	
	H.M.C		1-4-2024	11:00	A	
GARB**						
Employers Representative	Khaled ali		1/4/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours																							
The Work described below will be complete and ready for inspection at planned time shown																							
Contractor Company	157537 أبو عجيله للمقاولات العامة			Designer Company*	DR .Hassan Mahdy (H.M.C)																		
Issued by Contractor	Name Sign Date Time 1-4-2024 77																						
Received by Employers Representative	UIR Sign			<table border="1" style="width: 100%; border-collapse: collapse;"> <tr> <td>C1</td><td>C2</td><td>C3</td><td>DD</td><td>MM</td><td>YY</td><td>HH</td><td>MM</td></tr> <tr> <td>KP</td><td>SU</td><td>OT</td><td></td><td></td><td>24</td><td></td><td></td></tr> </table>				C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			24		
C1	C2	C3	DD	MM	YY	HH	MM																
KP	SU	OT			24																		
CODE-1 CODE-2 CODE-3 CODE-4 CODE-5																							

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
From 200+876 To 202+376	201+920 TO 202+376	
	E=260168.4582	E=260129.6912
	N=3136445.233	N=3135991.0324
<u>Inspection description:</u> As-Built for Fill from st (201+920) to st (202+376)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time	
Planned Inspection Date	Planned Inspection Time
1/4/2024	

COMPLIANCE EVIDENCE Must be included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA/QC*	XYZ		2-4-2024	9:00	A	
	H.M.C		2-4-2024	9:30	A	
GARB**						
Employers Representative						
