

قائمة الكميات الواردة بالمستخلص جاري (1)

اسناد أعمال الجسر الترابي للخط الأول لمشروع القطار الكهربائي السريع
(العين السخنة - العاصمة الإدارية - العلمين - مطروح) (قطاع وادي النطرون / برج العرب)
أعمال ردم لتنفيذ المسافة من الكم 322+920 إلى الكم 323+320 بطول 0.40 كم (بالأمر المباشر).

بند (1-1):

- بالمتر المكعب أعمال تحميل وتوريد ونقل اترية مطابقة للمواصفات وتشغيلها باستخدام الات التسوية بسمك لا يزيد عن 50 سم حتي منسوب -2 متر وبسمك لا يزيد عن 25 سم لاستكمال المنسوب التصميمي لتشكيل الجسر والاكتاف (نسبه تحمل كاليفورنيا لا تقل عن 15%) ورشها بالمياه الاصولية للوصول إلى نسبة الرطوبة المطلوبة والدمك الجيد بالهراسات للوصول إلى أقصى كثافة جافة (95% من الكثافة الجافة القصوى) ويتم التنفيذ طبقاً للمناسيب التصميمية والقطاعات العرضية النموذجية والرسومات التفصيلية المعتمدة والبند بجميع مشتملاته طبقاً لأصول الصناعة ومواصفات الهيئة العامة للطرق والكباري وتعليمات المهندس المشرف.
- مسافة النقل حتي 2 كم ويتم حساب علاوه 1.4 جنيه لكل 1 كم بالزيادة او النقصان.
 - السعر يشمل عمل تشوينات وتخليط واختبارات ونقل لموقع العمل حتي مسافة 2 كم .
 - السعر يشمل قيمة المادة المحجرية

السعر خلال شهر مايو طبقاً للمفاوضة الخاصة بتاريخ 18/12/2023

تنفيذ : "شركة إيجيبت ستون للتعدين والتوريدات"

عقد رقم (1124/2023/2024)

مقدار العمل السابق :		0.0	3م
مسلسل	الموقع الكيلومتری		الكمية (م3)
	من الكم	الى الكم	
1	322+920	323+320	21,324.00
	اجمالي الكمية الهندسي (م3)		21,324.00
	الاجمالي خلال فترة المستخلص الحالية (م3)		21,324.00

مهندس الهيئة
م / احمد جلال عبد السلام
احمد جلال

مهندس الاستشاري
مكتب أ.د. خالد فنديل
م / هشام محمد نصيري
KK

مهندس الاستشاري
مكتب XYZ
م / احمد عواد
عبد رزاق

مهندس الشركة
م / عبدالفتاح الشناوي
م / رانيا
EGYPT
STO
قطاع المقاولات

قائمة الكميات الواردة بالمستخلص جاري (1)

اسناد أعمال الجسر الترابي للخط الأول لمشروع القطار الكهربائي السريع
(العين السخنة - العاصمة الإدارية - العلمين - مطروح) (قطاع وادي النطرون / برج العرب)
أعمال ردم لتنفيذ المسافة من الكم 322+920 إلى الكم 323+320 بطول 0.40 كم (بالأمر المباشر).

علاوة بند (1-1) علاوة مسافة النقل 142 كم .

السعر خلال شهر مايو طبقاً للمفاوضة الخاصة بتاريخ 18/12/2023

تنفيذ : "شركة إيجيبت ستون للتعيين والتوريدات"

عقد رقم (1124/2023/2024)

مقدار العمل السابق :	0.0	3م
----------------------	-----	----

الكمية (م3)	الطول (متر)	الموقع الكيلومري		مسلسل
		من الكم	إلى الكم	
17,059.20	400	322+920	323+320	1
17,059.20	اجمالي الكمية الهندسي (م3)			
17,059.20	الاجمالي خلال فترة المستخلص الحالية (م3)			

مهندس الهيئة
م / أحمد جلال عبد السلام
i احمد جلال

مهندس الاستشاري
مكتب أ.د/ خالد قنديل
م / هشام محمد صبري



مهندس الاستشاري
مكتب XYZ
م / أحمد عواد



مهندس الشركة
م / عبدالفتاح الشناوي
م / هشام محمد صبري



قائمة الكميات الواردة بالمستخلص جاري (1)

اسناد أعمال الجسر الترابي للخط الأول لمشروع القطار الكهربائي السريع
(العين السخنة - العاصمة الإدارية - العلمين - مطروح) (قطاع وادي النطرون / برج العرب)
أعمال ردم لتنفيذ المسافة من الكم 322+920 إلى الكم 323+320 بطول 0.40 كم (بالأمر المباشر).

علاوة بند (1-1) علاوة مسافة النقل 135 كم .

السعر خلال شهر مايو طبقاً للمفاوضة الخاصة بتاريخ 18/12/2023

تنفيذ : "شركة إيجيبت ستون للتعيين والتوريدات"

عقد رقم (1124/2023/2024)

مقدار العمل السابق :				
م3		0.0		
الكمية (م3)	الطول (متر)	الموقع الكيلومتری		مسلسل
		من الكم	الى الكم	
4,264.80	400	322+920	323+320	1
4,264.80	اجمالي الكمية الهندسي (م3)			
4,264.80	الاجمالي خلال فترة المستخلص الحالية (م3)			

مهندس الهيئة
م / أحمد جلال عيد السلام
أحمد جلال

مهندس الاستشاري
مكتب أ.د/ خالد قنديل
م / هشام محمد صبري

مهندس الاستشاري
مكتب XYZ
م / أحمد عواد

مهندس الشركة
م / عبدالفتاح الشناوي
عبدالقادر شناوي





قائمة الكميات الواردة بالمستخلص جاري (1)

اسناد أعمال الجسر الترابي للخط الأول لمشروع القطار الكهربائي السريع
(العين السخنة - العاصمة الإدارية - العلمين - مطروح) (قطاع وادي النطرون / برج العرب)
أعمال ردم لتنفيذ المسافة من الكم 322+920 إلى الكم 323+320 بطول 0.40 كم (بالأمر المباشر).

علاوة بند (1-1) علاوة تحصيل رسوم الكارثة والموازن طبقاً للالحة الشركة الوطنية.

السعر خلال شهر مايو طبقاً للمفاوضة الخاصة بتاريخ 18/12/2023

تنفيذ : "شركة إيجيبت ستون للتعيين والتوريدات"

عقد رقم (1124/2023/2024)

مقدار العمل السابق :	0.0	3م
----------------------	-----	----

الكمية (م3)	الطول (متر)	الموقع الكيلومتر		مسلسل
		من الكم	إلى الكم	
21,324.00	400	322+920	323+320	1
21,324.00	اجمالي الكمية الهندسي (م3)			
21,324.00	الاجمالي خلال فترة المستخلص الحالية (م3)			

مهندس الهيئة
م / أحمد جلال عبد السلام
محمد جلال

مهندس الاستشاري
مكتب أ.د/ خالد قنديل
م / هشام محمد صبري



مهندس الاستشاري
مكتب XYZ
م / أحمد عواد



مهندس الشركة

م / عبدالفتاح الشناوي
عبد الفتاح الشناوي



محضر مسافة نقل

التاريخ: ٢٠٢٤ / ٢ / ١٤

اسم المشروع: القطار الكهربى السريع القطاع الرابع (الاسكندرية)
قام استشاري الهيئة العامة للطرق والكباري بقياس مسافة النقل من المحجر الى الموقع والعكس
لشركة: "إيجيبت ستون للتعيين والتوريدات"
وبحضور كلا من:-

مدير المشروع (الشركة المنفذة)
استشاري المشروع (أ.د/ خالد قنديل)
الاستشاري العام (ميسرا)

1- م/ عبدالفتاح الشناوي
2- م/ هشام محمد صبري
3- م/ كريم بدوي

وكانت الاحداثيات كالتالى:-

اسم المحجر	الشرق (E)	الشمال (N)	المسافة
محجر الكابتن (رمل)	28° 44' 30.8"	30° 34' 15.7"	135 KM

ملاحظات:-

في حالة تغيير المصدر يتم قياس واعتماد مسافة النقل الجديدة

مدير المشروع
(المالك)
م/ أحمد جلال
أحمد جلال

الاستشاري العام (ميسرا)
م/ كريم بنوي

H.B

مدير المشروع
(مكتب د. خالد قنديل)
م/ هشام محمد صبري

أ.د/ خالد قنديل

مدير المشروع: م/ هشام محمد صبري
مشروع: القطار الكهربى
القطاع الرابع (الاسكندرية)

مدير المشروع
(المقاول)
م/ عبدالفتاح الشناوي
عبدالفتاح الشناوي

قطاع المقاولات
EGYPT
STONE
FOR PROJECTS & SERVICES

محضر مسافة نقل

التاريخ: ١١ / ٩ / 2024

اسم المشروع: القطار الكهربى السريع القطاع الرابع (الاسكندرية)
قام استشارى الهيئة العامة للطرق والكبارى بقياس مسافة النقل من المحجر الى الموقع والعكس
لشركة: "إيجيبت ستون للتعدين والتوريدات"
وبحضور كلا من:-

مدير المشروع (الشركة المنفذة)
استشارى المشروع (أ.د/ خالد قنديل)
الاستشارى العام (سيمترا)

1- م/ عبدالفتاح الشناوى
2- م/ هشام محمد صبرى
3- م/ كريم بدوى

وكانت الاحداثيات كالتالى:-

اسم المحجر	الشرقى (E)	الشمال (N)	المسافة
محجر السيوى (تربة)	29° 48' 26.1"	30° 32' 19.6"	142 KM

ملاحظات:-

في حالة تغيير المصدر يتم قياس واعتماد مسافة النقل الجديدة

مدير المشروع
(المالك)
م/ أحمد جلال

الاستشارى العام
(سيمترا)
م/ كريم بدوى

مدير المشروع
(مكتب د. خالد قنديل)
م/ هشام محمد صبرى

مدير المشروع
(المقاول)
م/ عبدالفتاح الشناوى

مدير المشروع (أ.د/ خالد قنديل)
م/ هشام محمد صبرى
مشروع: القطار الكهربى
القطاع الرابع (الاسكندرية)



المنطقة الخامسة - غرب الدلتا
القطار الكهربائي السريع

السيد المهندس / رئيس قطاع التنفيذ و المناطق

تحية طيبة وبعد ،،،

بالإحالة إلى مشروع القطار الكهربائي السريع القطاع الرابع
(العين السخنة - العاصمة الإدارية - العلمين - مطروح).

نتشرف بأن نرسل لسيادتكم المقايضة المعدلة لبنود أعمال الجسر الترابي لمشروع
القطار الكهربائي السريع أعمال ردم قطاع (وادي النظرون - برج العرب) لتنفيذ
المسافة من الكم 322+920 إلى الكم 323+320 بطول 0.40 كم (بالأمر المباشر).
تنفيذ شركة "إيجيبت ستون للتعيين والتوريدات".
وذلك طبقاً للأسعار بعد المفاوضة.

برجاء من سيادتكم التفضل بالموافقة والتوجيه بالازم.

و تفضلوا بقبول فائق الاحترام ،،،

أحمد جلال

رئيس الإدارة المركزية

منطقة غرب الدلتا

الاسكندرية - مرسى مطروح

عميد مهندس //

"هاني محمد محمود طه"

محضر استلام موقع عملية

العملية:

اسناد أعمال الجسر الترابي للخط الأول لمشروع القطار الكهربائي السريع (العين السخنة - العاصمة الإدارية - العلمين - مطروح) (قطاع وادي النطرون / برج العرب) أعمال ردم لتنفيذ المسافة من الكم 322+920 إلى الكم 323+320 بطول 0.40 كم (بالأمر المباشر).

تنفيذ: شركة "إيجيبت ستون للتعدين والتوريدات"

استشاري المشروع: المكتب الاستشاري الهندسي (أ.د/خالد قنديل)

إشراف: المنطقة الخامسة - منطقة غرب الدلتا

طبقاً للعقد رقم (1124-2023-2024) بتاريخ (2024/02/07)

أنه في يوم الخميس الموافق 2024/02/08 اجتمع كل من:

- | | |
|---|---|
| 1- السيد المهندس / محمد حسني فياض | مدير عام المشروعات - الهيئة العامة للطرق والكباري |
| 2- السيد المهندس / أحمد جلال عبد السلام | مهندس العملية - الهيئة العامة للطرق والكباري |
| 3- السيد المهندس / هشام محمد صبري | استشاري المشروع (أ.د/خالد قنديل) |
| 4- السيد المهندس / عبدالفتاح الشناوي | مدير مشروع - شركة إيجيبت ستون للتعدين والتوريدات |

وذلك للمرور على مسار العملية المذكورة عالية لاستلام الموقع.
وقد تبين أن الموقع خالي من العوائق الظاهرية ويسمح بالبدء في التنفيذ وبناءً عليه يعتبر تاريخ 2024/02/08 هو تاريخ استلام الموقع وبدء أعمال الإشراف بالعملية.
واقفل المحضر علي ذلك ووقع الحضور.

التوقيعات:

4- السيد/فتح إشتار

3- السيد/محمد جلال

2- السيد/محمد جلال

1- السيد/محمد جلال

رئيس الإدارة المركزية

منطقة غرب الدلتا

الاسكندرية - مرسى مطروح

عميد مهندس /

"هاني محمد محمود طه"



٢٠٢٤/٣/١٧

محضر مسافة نقل

التاريخ: ٢٠٢٤ / ٢ / ٢٠

اسم المشروع: القطر الكهربى السرى القطار الرابى (الاسكندرية)
قام استشارى الهيئة العامة للطرق والكبارى بقاء مسافة النقل من المحجر الى الموقع والعكس
شركة: "إجىبىب سئون للتعدىن والتورىدات"
وبحضور كلا من:-

مذبر المشروع (الشركة المنفذة)
استشارى المشروع (أ.د/ خالد قندىل)
الاستشارى العام (مىسترا)

١- م/ عبدالفتاح الشناوى
٢- م/ هشام محمد صبرى
٣- م/ كرىم بدوى

وكانت الأحداثىات كالتالى:-

اسم المحجر	الشرق (E)	الشمل (N)	المسافة
محجر الكابتن (رمل)	28° 44' 30.8"	30° 34' 15.7"	135 KM

ملاحظات:-

فى حالة تغىىر المصدر يتم قىاس واعتماد مسافة النقل الجدىدة

مذبر المشروع
(الملاك)
م/ أحمد جلال
أحمد جلال

الاستشارى العام (مىسترا)
م/ كرىم بدوى

٢٠٢٤

مذبر المشروع
(مكتب د. خالد قندىل)
م/ هشام محمد صبرى

مذبر المشروع
(المقاول)
م/ عبدالفتاح الشناوى
عبدالفتاح الشناوى

المكتب الاستشارى
(أ.د/ خالد قندىل)
مذبر المشروع: م/ هشام محمد صبرى
مشروع: القطار الكهربائى السرى
القطاع الرابى (الاسكندرية)

قطاع المقاولان
EGYPT STONE
FOR TRADING & SUPPLY

محضر مسافة نقل

التاريخ: ١١ / ٩ / 2024

اسم المشروع: القطار الكهربى السريع القطاع الرابع (الاسكندرية)
قام استشاري الهيئة العامة للطرق والكبارى بقياس مسافة النقل من المحجر الى الموقع والعكس
لشركة: "إيجيبت ستون للتعيين والتوريدات"
وبحضور كلا من:-

مدير المشروع (الشركة المنفذة)
استشاري المشروع (أ.د/ خالد قنديل)
الاستشاري العام (سيسترا)

1- م/ عبدالفتاح الشناوي
2- م/ هشام محمد صبرى
3- م/ كريم بدوي

وكانت الاحداثيات كالتالى:-

المسافة	الشمال (N)	الشرق (E)	اسم المحجر
142 KM	30° 32' 19.6"	29° 48' 26.1"	محجر السيوي (تربة)

ملاحظات:-

في حالة تغيير المصدر يتم قياس واعتماد مسافة النقل الجديدة

مدير المشروع
(المالك)
م/ أحمد جلال
أحمد جلال

الاستشاري العام
(سيسترا)
م/ كريم بدوي

١٤١٣

مدير المشروع
(مكتب د. خالد قنديل)
م/ هشام محمد صبرى

مدير المشروع
(المقاول)
م/ عبدالفتاح الشناوي
عبدالفتاح الشناوي

المكتب الاستشاري الهندسي
(أ.د/ خالد قنديل)
مدير المشروع: م/ هشام محمد صبرى
مشروع: القطار الكهربائي السريع
القطاع الرابع (الاسكندرية)

قطاع المقاولان
EGYPT
STONE
FOR SURVEY & MEASUREMENT

MATERIAL INSPECTION REQUEST



Contractor Company	EGYPT STONE FOR MINING AND SUPPLIES		Designer Company	(KK) Engineering Consulting Office																	
Issued by Contractor	Name	Sign	Data/ Serial Number	Time																	
	Eng. Abdelfattah El-Shennawy		21-12-2023 ES-M.I.036	04:00 PM																	
Received by ER	Eng. Gaber Ibrahim	MIR	<table border="1"> <tr> <td>CL</td> <td>CD</td> <td>CS</td> <td>DO</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>W322</td> <td>EW</td> <td>CS</td> <td>21</td> <td>12</td> <td>2023</td> <td>04</td> <td>00</td> </tr> </table>	CL	CD	CS	DO	MM	YY	HH	MM	W322	EW	CS	21	12	2023	04	00		
CL	CD	CS	DO	MM	YY	HH	MM														
W322	EW	CS	21	12	2023	04	00														

CODE-1	S1 to S21 Station Reference	D1 to S1 Depot Reference	Kp XXX Note For Kilometer point only Start Km is used
CODE-2	Work Activity		
CODE-3	Sub Element of Activity		

Description of Materials	(Fill Layer Stockpile for Soil)				
Location to be Used	From St. (W322+040) to St. (W322+240) (-4.5) .				
MAR Approval No	ES M.A.006	Date	20-12-2023		
Supplier Name	EL Sewey – EL Captin				
Test Requirement	F.D.T[ASTM D 1556]	Specification	EARTHWORK SPECIFICATIONS & TESTING REPORT (CG21-41.2) VERSION 2 BY CIVECON GROUP		
Reference Photos	No	Other			
Item	Description	Unit	Quantity	Arrival Date	Note
1	Sand Cone Test.	NUMBER	4	21/12/2023	
2					
3					
4					

Comments by: Eng. Hesham Sabry (kk)

Comments by: Eng. Gaber Ibrahim

1. تم استلام SAND CONE
2. تم تحقيق نسبة الدمك المطلوبة.

1-F.D.T was carried- out by company Lab. Attendances of material engineer for both contractor and GARB Consultant.
2-Results report attached and acceptable with project specifications.
3-Final approval is subject to above-mentioned comments.

APPROVAL STATUS

Organisation	Name	Sign	Date	A-AWC-R
Contractor	Eng. Abdelfattah El-Shennawy			
QA/QC *	Eng. Hesham Sabry		25/12/2023	A
GARB**	Eng. Ahmed Galal			
Employers Representative	Eng. Gaber Ibrahim		23-12-2023	A.W.C

* Designer

** Alignment / Bridges: Culvert Only

Section - 4 From Wadi El Nnatroun To Borg Elarab
"From Station 322+100 To Station 323+450"

Density of Soil In-Place By the Sand-Cone Method (ASTM D1556)

Request No. :	ES M.I.036	Station:	322+340 TO 322+240
Date :	22-Dec-2023	Aggregate Source :	EL Sewey - EL Captin
Sample type :	SOIL	LAYER:	-4.5

MDD gm/cm ³	OMC %	Sand Density
2.140	7.40	1.45

STA. & REF. TO CENTER		322+050	322+120	322+180	322+230			
WT. OF WET SOIL	gms	2434.0	2178.0	2367.0	2597.0			
WT. OF INITIAL SAND+CONE	gms	9847.0	10320.0	10157.0	9958.0			
WT. OF RESIDUAL SAND	gms	7152.0	7182.0	7162.0	7152.0			
WT. OF SAND TO FILL CONE+HOLE	gms	2895.0	3138.0	3015.0	2806.0			
WT. OF SAND TO FILL CONE	gms	1161.0	1141.0	1141.0	1141.0			
WT. OF SAND TO FILL HOLE	gms	1554.0	2027.0	1874.0	1665.0			
GROSS VOL. OF HOLE	ccs	1071.7	1397.9	1252.4	1148.3			
CONTAINER No.	n	5	2	3	4			
WEIGHT OF CAN	gms	40.0	42.0	48.0	41.0			
WT. OF CAN+WET SOIL	gms	143.3	146.0	142.4	146.3			
WT. OF CAN+DRY SOIL	gms	132.4	133.6	131.3	133.6			
WT. OF WATER	gms	10.9	12.3	11.2	12.8			
WT. OF WET SOIL	gms	2.3	2.2	2.3	2.3			
WATER CONTENT	%	8.3	9.2	8.5	9.6			
DRY UNIT WT. OF SOIL	gm/cc	2.10	2.11	2.12	2.10			
COMPACTION	%	97.7	98.2	98.7	97.7			
REMARKS		accepted	accepted	accepted	accepted			

مهندس الاستشاري

مهندس المواد (الشركة)



MATERIAL INSPECTION REQUEST



Contractor Company	EGYPT STONE FOR MINING AND SUPPLIES		Designer Company	(KK) Engineering Consulting Office																	
Issued by Contractor	Name	Sign	Date/ Serial Number	Time																	
	Eng. Abdelfattah El-Shennawy		26-12-2023 ES-M.I.044	04:00 PM																	
Received by ER	Eng. Gaber Ibrahim	MIR	<table border="1"> <tr> <td>CE</td> <td>EW</td> <td>CS</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>W322</td> <td>EW</td> <td>CS</td> <td>26</td> <td>12</td> <td>2023</td> <td>04</td> <td>00</td> </tr> </table>			CE	EW	CS	DD	MM	YY	HH	MM	W322	EW	CS	26	12	2023	04	00
CE	EW	CS	DD	MM	YY	HH	MM														
W322	EW	CS	26	12	2023	04	00														

CODE - 1	S1 to S21 Station Reference	D1 to S3 Depot Reference	Kp XXX Note For Kilometer point only Start Km is used
CODE - 2	Work Activity		
CODE - 3	Sub Element of Activity		

Description of Materials	(Fill Layer Stockpile for Soil)				
Location to be Used	From St. (W323+040) to St. (W323+120) (-4) .				
MAR Approval No	ES M.A.008	Date	23-12-2023		
Supplier Name	EL Sewey – EL Captin				
Test Requirement	F.D.T(ASTM D 1556)	Specification	EARTHWORK SPECIFICATIONS & TESTING REPORT (CG21-41.2) VERSION 2 BY CIVECON GROUP		
Reference Photos	No	Other			
Item	Description	Unit	Quantity	Arrival Date	Note
1	Sand Cone Test.	NUMBER	2	26/12/2023	
2					
3					
4					

Comments by: Eng. Hesham Sabry (kk)	Comments by: Eng. Gaber Ibrahim
1. تم استلام SAND CONE 2. تم تحقيق نسبة الدمك المطلوبة.	1-F.D.T was carried-out . Attendances of material engineer for both contractor and GARB Consultant. 2-Results report attached and acceptable with project specifications. 3-Final approval is subject to above-mentioned comments.

APPROVAL STATUS				
Organisation	Name	Sign	Date	A-AWC-R
Contractor	Eng. Abdelfattah El-Shennawy			
QA/QC *	Eng. Hesham Sabry		27/12/2023	A
GARB**	Eng. Ahmed Galal			
Employers Representative	Eng. Gaber Ibrahim			A.W.C

* Designer

** Alignment / Bridges/ Culvert Only

27-12-2023

Section - 4 From Wadi El Nhatroun To Borg Elarab
"From Station 322+100 To Station 323+450"

Density of Soil In-Place By the Sand-Cone Method (ASTM D1556)


Request No. :	E3 M.I.044		Station:	323+040	TO	323+120						
Date :	27-Dec-2023		aggregate Source :	EL Saway - EL Captin								
Sample type :	SOIL		LAYER:	+4								
<table><tr><td>MDD gm/cm³</td><td>OMC %</td><td>Sand Density</td></tr><tr><td>2.152</td><td>6.40</td><td>1.45</td></tr></table>							MDD gm/cm ³	OMC %	Sand Density	2.152	6.40	1.45
MDD gm/cm ³	OMC %	Sand Density										
2.152	6.40	1.45										
STA. & REF. TO CENTER	323+040	323+120										
WT.OF WET SOIL	gms	2414.0	2587.0									
WT. OF INITIAL SAND+CONC.	gms	9947.0	9987.0									
WT. OF RESIDUAL SAND	gms	7152.0	7152.0									
WT. OF SAND TO FILL CONE+HOLE	gms	2095.0	2835.0									
WT.OF SAND TO FILL CONE	gms	1141.0	1141.0									
WT.OF SAND TO FILL HOLE	gms	1554.0	1694.0									
GROSS VOL. OF HOLE	ccs	1071.7	1188.3									
CONTAINER No.	n	1	2									
WEIGHT OF CAN	gms	40.0	40.0									
WT. OF CAN+WET SOIL	gms	142.7	144.0									
WT. OF CAN+DRY SOIL	gms	132.5	135.5									
WT. OF WATER	gms	10.2	9.3									
WT. OF WET SOIL	gms	2.3	2.2									
WATER CONTENT	%	7.7	6.9									
DRY UNIT WT. OF SOIL	gm/cc	2.09	2.07									
COMPACTION	%	97.2	96.3									
REMARKS		accepted	accepted									

مهندس الاستشاري



مهندس المواد (الشركة)

MATERIAL INSPECTION REQUEST



Contractor Company	EGYPT STONE FOR MINING AND SUPPLIES		Designer Company	(KK) Engineering Consulting Office							
Issued by Contractor	Name	Sign	Date/ Serial Number	Time							
	Eng. Abdelfattah El-Shennawy		26-12-2023 ES-M.I.045	04:00 PM							
Received by ER	Eng. Gaber Ibrahim		MIR	C1	C2	C3	DD	MM	YY	HH	MM
				W323	EW	CS	26	12	2023	04	00

CODE-1	51 to 521 Station Reference	01 to 53 Depot Reference	Kp XXX Note For Kilometer point only Start Km is used
CODE-2	Work Activity		
CODE-3	Sub Element of Activity		

Description of Materials	(Fill Layer Stockpile for Soil)		
Location to be Used	From St. (W323+120) to St. (W323+240) (-4) .		
MAR Approval No	ES M.A.009	Date	24-12-2023
Supplier Name	EL Sewey – EL Captin		
Test Requirement	F.D.T(ASTM D 1556)	Specification	EARTHWORK SPECIFICATIONS & TESTING REPORT (CG21-41.2) VERSION 2 BY CIVECON GROUP
Reference Photos	No	Other	

Item	Description	Unit	Quantity	Arrival Date	Note
1	Sand Cone Test.	NUMBER	3	26/12/2023	
2					
3					
4					

Comments by: Eng. Hesham Sabry (kk)	Comments by: Eng. Gaber Ibrahim
1. SAND CONE تم استلام 2. تم تحقيق نسبة الدمك المطلوبة.	1-F.D.T was carried-out . Attendances of material engineer for both contractor and GARB Consultant. 2-Results report attached and acceptable with project specifications. 3-Final approval is subject to above-mentioned comments.

APPROVAL STATUS				
Organisation	Name	Sign	Date	A-AWC-R
Contractor	Eng. Abdelfattah El-Shennawy			
QA/QC *	Eng. Hesham Sabry		27/12/2023	A
GARB**	Eng. Ahmed Galal			
Employers Representative	Eng. Gaber Ibrahim		27-12-2023	A.W.C

* Designer

** Alignment / Bridges: Culvert Only

Section - 4 From Wadi El Nnatroun To Borg Elarab
"From Station 322+100 To Station 323+450"

Density of Soil In-Place By the Sand-Cone Method (ASTM D1556)

Request No. :	ES M.I.045	Station:	323+120 TO 323+240
Date :	27-Dec-2023	aggregate Source :	EL Seway - EL Captin
Sample type :	SOIL	LAYER:	-4

MDD gm/cm ³	OMC %	Sand Density
2.144	7.80	1.45

STA. & REF. TO CENTER	323+140	323+190	323+220					
WT. OF WET SOIL	gms	2404.0	2587.2	2767.0				
WT. OF INITIAL SAND+CONE	gms	9852.0	9987.0	10124.0				
WT. OF RESIDUAL SAND	gms	7152.0	7152.0	7152.0				
WT. OF SAND TO FILL CONE+HOLE	gms	2700.0	2835.0	2972.0				
WT. OF SAND TO FILL CONE	gms	1141.0	1141.0	1141.0				
WT. OF SAND TO FILL HOLE	gms	1559.0	1694.0	1831.0				
GROSS VOL. OF HOLE	ccs	1076.2	1169.3	1262.8				
CONTAINER No.	n	1	2	3				
WEIGHT OF CAN	gms	40.0	45.0	42.0				
WT. OF CAN+WET SOIL	gms	142.7	144.5	144.5				
WT. OF CAN+DRY SOIL	gms	132.5	136.5	135.5				
WT. OF WATER	gms	10.2	8.3	9.3				
WT. OF WET SOIL	gms	2.2	2.2	2.2				
WATER CONTENT	%	7.7	6.9	6.9				
DRY UNIT WT. OF SOIL	gm/ccs	2.08	2.07	2.1				
COMPACTION	%	96.9	96.6	96.3				
REMARKS		accepted	accepted	accepted				

مهندس الاستشاري


مهندس المواد (الشركة)

خالد فؤاد



MATERIAL APPROVAL REQUEST



Contractor Company	Alexandria Company for Construction and Paving Roads			Designer Company				(KK) Engineering Consulting Office			
Issued by Contractor	Name	Sign		Date/serial Number				Time			
	Eng. Abdelfattah El-Shennawy			04-01-2024 (ES M.A.017)				10:30 AM			
Received by ER	Eng. Gaber Ibrahim		MAR	CI	CC	CS	DD	MM	YY	HH	MM
				W322	EW	CS	04	01	24	10	30

CODE -1	S1 to S21 Station Reference	D1 to S3 Depot Reference	Kp XXX Note For Kilometer point only Start Km is used
CODE -2	Work Activity		
CODE -3	Sub Element of Activity		

Description of Materials	Stock Pile for Soil (Fill Layer) .		
Location to be Used	Station Stock Pile (322).		
Sample only	Yes	Materials Type	Fill layer
Supplier Name	El Sewy – EL Captin	Data Sheet provided	Yes attached
Reference in BoQ		Specification	EARTHWORK SPECIFICATIONS & TESTING REPORT (CG21-41.2) VERSION 2 BY CIVECON GROUP
Prequalification reference		Test Samples Results	Approved
Reference Photos	No	Other	
Comments by: Eng. Hesham Sabry (kk)		Comments by: Eng. Gaber Ibrahim	
1-تم اجراء الاختبارات المعملية بعمل (كوميصل) وتم تحقيق النتائج المطلوبة طبقا لمواصفات المشروع.		1- All tests were carried-out by Comibassal Lab. Depended on samples Submitted by material engineer for both contractor and GARB Consultant. 2-Results report attached and acceptable with the project specifications. 3-Final approval is subject to above-mentioned comments.	

APPROVAL STATUS				
Organisation	Name	Sign	Date	A-AWC-R
Contractor	Eng. Abdelfattah El-Shennawy			
QA/QC *	Eng. Hesham Sabry		31/1/2024	A
GARB**	Eng. Ahmed Galal			
Employers Representative	Eng. Gaber Ibrahim		09-01-2024	A.W.C

* Designer

** Alignment/Bridges: Culvert only



COMIBASSAL International Controllers Internal inspection and laboratories sector

Accredited by : Egyptian General Authority for Petroleum under No. 34/29-11-2011

SOIL REPORTS FOR ELECTRIC EXPRESS TRAIN PROJECT

Contractor :

شركة ايجبت ستون للمقاولات

Date :

09/01/2024

QC :

137





COMIBASSAL International Controllers

Internal inspection and laboratories sector

Accredited by : Egyptian General Authority for Petroleum under No. 34/ES-11-2011

I- Introduction

General Consultant : SYSTRA
Consultant : DR/Khaled Kandil
Contractor : شركة ايجبت ستون للمقاولات
Sample : Upper Embankment (Ferma).
Station : From stored materials.
Date of Test : 04/01/2024
QC : 137

II- Sample description:

Gravel and Sand

III- Required tests and Results

Required Tests		Results
1- Grain size analysis and classification	Grain size analysis	As showed in appendix
	Classification	A-1-a
2- Modified compaction (Proctor test)	MDD	2.163
	OMC	7.0%
3- Liquid limit, plastic limit and plasticity index	LL	NP
	PL	NP
	PI	NP
4- California bearing ratio (CBR)	CBR ratio	30%

IV- Notes

- 1- Samples were brought by : Consultant.
- 2- Samples are responsible from the Person who brought it.
- 3- The results are applying only for the present report.

LAB DIRECTOR

Eng / Eman kandil



Geotechnical consultant

For Dr. H -
Dr. Mohamed Mostafa Badry



COMIBASSAL International Controllers Internal inspection and laboratories sector

Accredited by : Egypton General Authority for Petroleum under No. 34/29-11-2011

APPENDIX





COMIBASSAL International Controllers


Internal inspection and laboratories sector

Accredited by : Egypt General Authority for Petroleum under No. 34/29-11-2011

PARTICLE SIZE DISTRIBUTION ANALYSIS ASTM C-136 / AASHTO T27

	WEIGHT RETAINED (gm)	CUMULATIVE WEIGHT RETAINED (gm)	CUMULATIVE PERCENTAGE RETAINED (%)	CUMULATIVE PERCENTAGE PASSING (%)	STANDARD SPECIFICATION LIMITS
2	0.00	0.00	0.00	100.0	
1 1/2	110.00	110.00	1.10	98.9	
1	863.00	973.00	9.73	90.3	
3/4	690.00	1663.00	16.63	83.4	
1/2	1351.00	3014.00	30.14	69.9	
3/8	667.00	3681.00	36.81	63.2	
No.4	1246.00	4921.00	49.21	50.8	
No.10	33.00	33.00	6.60	47.4	
No.40	160.00	160.00	32.00	34.5	
No.200	393.90	393.90	78.78	10.8	

Total sample weight = 10000.00 pass No.4= 5079.0 Total fine aggregates weight = 500 gm
% 50.8

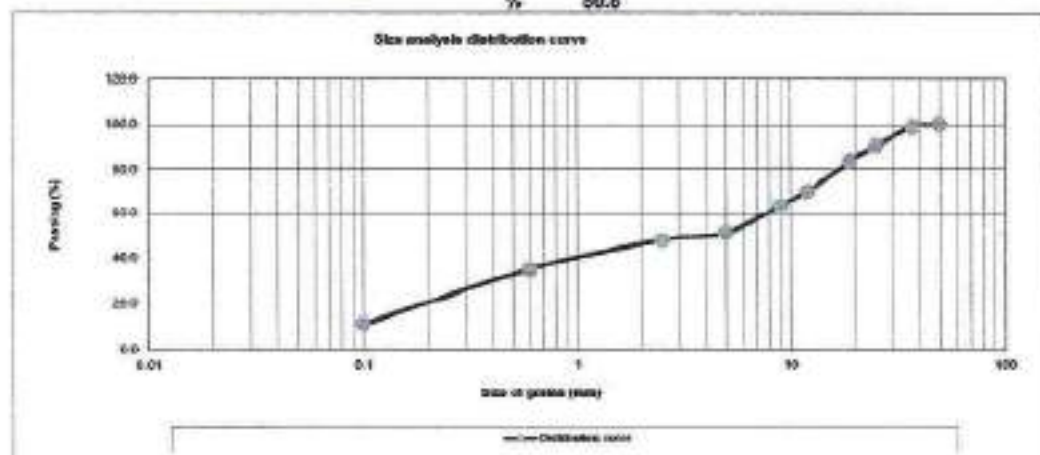

Soil classification: A - 1- a sample is non-plastic





COMIBASSAL International Controllers

Internal inspection and laboratories sector

Accredited by : Egypt General Authority for Petroleum under No. 34/29-11-2011

Modified Proctor Test Report

ASTM - D 1557

Mould Number :- 3
 Volume of mould = 2165 cm³
 Weight of mould = 5821 g
 G.S = 2.59 g/cm³


A- Density Calculations :-

	1	2	3	4	5
Weight of wet soil+mould (g)	10410	10630	10830	10720	10610
Weight of mould (g)	5821	5821	5821	5821	5821
Weight of wet soil (g)	4589	4809	5009	4899	4789
Volume of mould (cm ³)	2165	2165	2165	2165	2165
Wet density (g/cm ³)	2.120	2.221	2.314	2.263	2.212
Dry density (g/cm ³)	2.036	2.105	2.163	2.080	2.001
Zero-air Void curve			2.194	2.109	2.034

B- Moisture Calculations :-

Weight of wet soil+container (g)	250.0	250.0	250.0	250.0	250.0
Weight of dry soil+container (g)	241.4	238.5	236.0	232.6	229.0
Weight of container (g)	31.0	30.0	35.0	35.0	30.0
moisture content (%)	4.1	5.5	7.0	8.8	10.6

C- Dry density-Moisture relationship:-

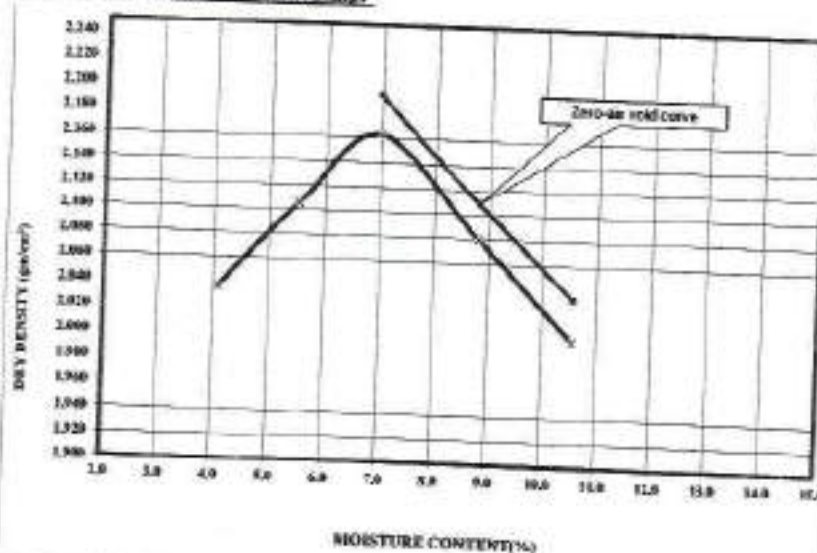

M.D.D= 2.163 g/cm³
 O.M.C= 7 %






COMIBASSAL International Controllers

Internal inspection and laboratories sector

Accredited by : Egypt General Authority for Petroleum under No. 34/29-11-2011

Report Of CBR Test - ASTM - D 1883

NO OF BLOWS	56				
MOULD NO	4				
WT OF MOULD+SOIL	10420				
WT OF MOULD	5394				
WT OF SOIL	5026				
VOLUME OF MOULD	2188				
WET DENSITY	2.297				
	MC before soaking		Weight of Rammer	4.54Kg	
TIN NO	1		MDD	Kg/m3	2.163
WT OF WET SOIL+TIN	250.00		OMC	%	7.000
WT OF DRY SOIL+TIN	237				
WT OF WATER	13.00				
WT OF TIN	35				
WT OF DRY SOIL	202				
MOISTURE CONTENT	6.4				
DRY DENSITY	2.158		Capacity (KN)	50	
Pen	Reading (Div)	Bearing (KN)	CBR		
mm	56	56	standar	56	
0.00	0	0.0	0.0		
0.64	69	0.7	4.5		
1.27	120	1.2	8.5		
1.91	194	1.9	12.0		
2.54	282	2.6	14.5	20	
3.17	350	3.4	16.3		
3.81	451	4.4	18.0		
4.45	535	5.2	19.3		
5.08	620	6.1	20.5	30	
5.71	722	7.1	21.9		
6.35	810	7.9	23.3		

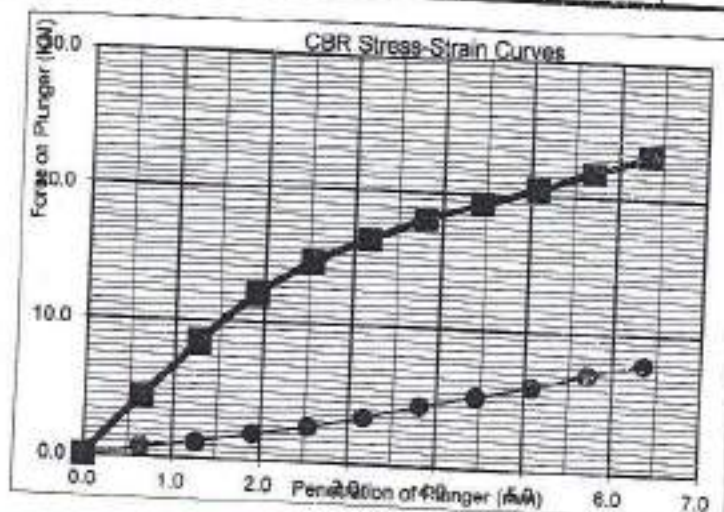



COMIBASSAL International Controllers

Internal inspection and laboratories sector

Accredited by : Egypt General Authority for Petroleum under No. 34/29-11-2011

Report :	113 -I - Center
Date :	09/01/2024

CHEMICAL ANALYSIS

General Consultant :	SYSTRA
Consultant :	DR/ Khaled Kandil
Contractor :	شركة ايجيبت ستون
Project :	Electric express train
Sample :	Upper Embankment Ferra
Station :	From Stored Materials
Date of Test :	4-1-2024

Temperature : 22 °C

Humidity : 45%

ANALYSIS	RESULTS	TEST METHOD
ORGANIG MATTER	NEGATIVE	ASTM D 2974



LAB DIRECTOR
CH/ Mostafa Asker

Mostafa

