

المسوحة ضوئياً - CamScanner



استشاري أبحاث التربة والاساسات :
أ.د.م. هشام محمد حلمي

مشروع :
قطار اسوان الكهربائي السريع - القطاع الثاني

تقرير بنتائج إختبارات صلاحية أترية للتأسيس

مقدمة : تم إعداد هذا التقرير بناء على طلب شركة / ابو عجيبة

وذلك لتحديد خصائص ومدي صلاحية عينة تراب للإستخدام في / طبقات الردم لجسر القطار الكهربائي

مصدر العينة : عند المحطة / تشوينة يمين المسار 202+220

- المنسوب: وقد تم توريد العينة بمعرفة 1- م/ محمود الحيني رقم الهاتف =01030344342

- تنبيه هام : العينة مسئولية من أحضرها

- تاريخ توريد العينة : 2023/12/11

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بني مزار - منفوط)

وقد تم عمل الإختبارات الآتية :

- 1- التدرج الحبيبي
- 2- حد السيولة واللدونة
- 3- إختبار البروكتور
- 4- إختبار CBR
- 5- إختبار المواد العضوية

وكانت نتائج الإختبارات كالآتي :

م	نوع الإختبار	النتائج	حدود القبول والرفض طبقا للمواصفات
1	تصنيف العينة	A-1-b	(A-1-a) - (A-1-b) - (A-2-4)
2	نسبة العار من مخل 200	12.9%	لا تزيد عن (15 %)
3	مجال اللدونة	NP	(A-1-a or A-1-b = 6 max) (A-2-4 = 10 max)
4	أقصى كثافة جافة (البروكتور) yd max	2.171 gm/cm3	لا تقل عن 1.88 gm/cm3
5	نسبة المياه الأصلية	6.4%	--
6	قيمة CBR المغمورة	38.2%	لا تقل عن 20%
8	المواد العضوية	لا يوجد	لا تزيد عن 1%

و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي صالحة للتأسيس عليها



مهندس المعمل
م/م
التوقيع

فني المعمل
م/م
التوقيع

Coarse & Fine Aggregate Grading - ASTM C136 & AASHTO T27

202+220	الموقع : تشوين يمين العمار	16/12/2023	التاريخ :
---------	----------------------------	------------	-----------

نتائج الاختبار :-

رقم المنخل (mm)	رقم المنخل (inch)	وزن المحجوز على كل منخل	وزن المحجوز التراكمي	المحجوز %	المر %
127	5"	0	0	0%	100%
101.6	4"	0	0	0.00%	100.00%
76.2	3"	0	0	0.00%	100.00%
63.5	2.5"	0	0	0.00%	100.00%
50.8	2"	462	462	5.78%	94.22%
37.5	1.5"	348	810	10.14%	89.86%
25	1"	797	1607	20.11%	79.89%
19	3/4"	413	2020	25.28%	74.72%
12.7	1/2"	522	2542	31.81%	68.19%
9.5	3/8"	376	2918	36.52%	63.48%
4.75	# 4	312	3230	40.43%	59.57%
	المر من منخل # 4	4760		59.57%	
	وزن العينة الكلي	7990			
	وزن عينة الناعم	500			
2.36	# 10	54	54	46.9%	53.1%
0.425	# 40	145	199	64.1%	35.9%
0.075	# 200	193	392	87.1%	12.9%

NP	السيولة و اللدونة
A-1-b	التصنيف

ملاحظات :



م. حيدر بن عبد الله

مهندس المعمل
م. /
التوقيع

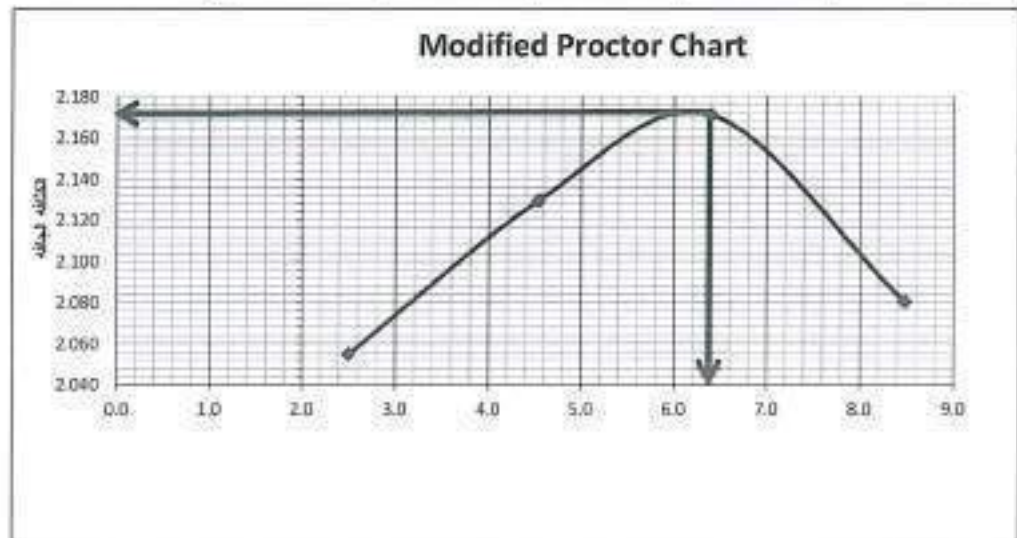
Modified Proctor : ASTM D1557

نوع العينة:	عينة من التشون
تصنيف العينة:	A-1-b
نتائج الاختبار:	
وزن القالب:	5731
حجم القالب:	2140

القيمة القصوى جافه	2.171
القيمة الاسمي	6.4

رقم الاختبار	1	2	3	4
وزن القالب + العينة رطبه	10238.0	10495	10674	10560
وزن القالب الرطبه	4507.0	4764	4943	4829
الكثافه الرطبه	2.105	2.226	2.310	2.257

رقم المحطه	1	2	3	4	5	6	7	8
وزن المحطه	52.3	55.1	25.9	25.5	54.6	52.3	30.4	31.7
وزن المحطه + العينه رطبه	150.0	150.0	150.0	150.0	150.0	150.0	150.0	150.0
وزن المحطه + العينه جافه	147.7	147.6	144.3	144.9	144.3	144.1	140.8	140.8
وزن المياه	2.3	2.4	5.7	5.1	5.7	5.9	9.2	9.4
وزن العينه جافه	95.4	92.5	118.4	119.4	89.7	91.8	110.4	108.9
المحتوى المائي %	2.4	2.6	4.8	4.3	6.4	6.4	8.3	8.6
معدل المحتوى المائي %	2.5	4.5	6.4	8.5				
الكثافه الجافه	2.055	2.129	2.171	2.080				



ملاحظات:



مهندس المعمل
محمد بن محمد
التوقيع
لل

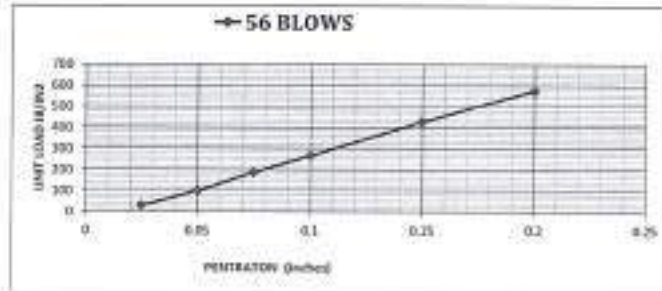
المعمل
محمد بن محمد
التوقيع

اختبار نسبة تحمل كاتيلورنيا (ASTM D1883(C.B.R))

A-1-b		تصنيف العينة	
56	حد الضربات	56	حد الضربات
5	رقم الجقنة	2131	حجم قالب (سم ³)
51.3	وزن الجقنة	5280	وزن القالب (جم)
180	وزن الجقنة + العينة رطبة جم	10134	وزن قالب + وزن العينة رطبة (جم)
144.2	وزن الجقنة + العينة جافة جم	4845	وزن العينة رطبة (جم)
8.8	وزن الماء جم	2.276	الكتلة الرطبة (جم/سم ³)
80.9	وزن العينة جافة جم	2.137	الكثافة جافة (جم/سم ³)
6.4%	المحتوى المائي %	2.171	كثافة الهواء (جم/سم ³)
		88.4%	نسبة الدمك
		0.39%	نسبة الإفراش
			غير قابلة للتفكك

حساب نسبة تحمل كاتيلورنيا

7.62	5.08	3.81	2.54	1.95	1.27	0.635	الاختبار (ان) بالمسم
0.3	0.2	0.15	0.1	0.075	0.05	0.025	الاختبار (ان) بالمليمتر
1369.0	780	581.0	360.0	255.0	134.0	39.0	الفرادة kg
3017.276	1719.12	1280.524	793.44	562.02	295.336	85.956	الفرادة بالباوند
1006.215	573.3	427.035	264.6	187.425	98.49	28.665	المعدل (lb/ft ²)



38.2%	قيمة C.B.R
-------	------------

ملاحظة: تم طرح القالب في الماء لمدة 96 ساعة طبقاً لمواصفة المشروع



في الموقع
م. محمد صالح عبيد
مهندس

مهندس مشرف في محمد البنا
شوقي
4/



التاريخ : 2024-9-22

اسم المشروع : مشروع القطار الكهربائي السريع قطاع (أكتوبر - أبو سجيل)
الموضوع : اعتماد الهيئة العامة للطرق والكبارى لطلبات استلام الأعمال الخاصة بالمشروع
الشركة المنفذة : ابوعجيلة للمقاولات العامة والتوريدات العمومية في المسافة
من (200+876) الى (202+376) بطول 1.5 كم.

عقد رقم : - (2023-2022-1968) بتاريخ 2023-5-17

- (2023-2023-142) بتاريخ 2023-8-3

- (2023-2023-143) بتاريخ 2023-8-3

- (2023-2023-499) بتاريخ 2023-10-12

- (2023-2023-1021) بتاريخ 2024-1-18

- (2023-2023-1229) بتاريخ 2024-2-26

- (2024-2024-209) بتاريخ 2024-8-21

تم الإطلاع ظاهريا على طلبات الفحص الخاصة بالمشروع المذكور عاليه والمرفقة بمستخلصات
المذكورة عالية لعدد (77) طلبات فحص وذلك بعد مراجعتها وتوقيعها من استشارى المساحة (XYZ)
واستشارى ضبط الجودة (مكتب أ.د حسن مهدي) وعليه تم اعتمادها

وتنقسم الى :

- (53) طلبات فحص لأعمال الردم .
- (14) طلبات فحص لأعمال الحفر .
- (4) طلبات فحص لأعمال التطهير .

عن الاستشاري (أ.د حسن مهدي)
مشروع القطار السريع

مهندس الاستشاري
أ.د حسن مهدي

يعتمد،،،

مهندس الهيئة العامة للطرق والكبارى

مهندس الهيئة العامة للطرق والكبارى

البرنامج الزمني

أعمال الجسر الترابي لمسار القطار الكهربائي السريع الخط الثاني (القيوم / بني سويف - أبوسمبل) (مرحلة الجسور والتأسيس والأساس)
القطاع الثاني (بني مزار / منفلووط)

من المحطة ٢٠٠+٨٥٠ الى المحطة ٢٠٢+٣٥٠ بطول ١,٥ كم رقم العقد (٢٠٢٤/٢٠٢٣/١٢٢٩)
أعمال ردم من منسوب ١١م الي - ٩م من منسوب القرمة

تاريخ استلام الموقع ٢٠٢٤/٣/٣

مدة تنفيذ العملية ٨ شهور

تاريخ نهو الاعمال ٢٠٢٤/١١/٢

رقم البند	بيان الاعمال	الوحدة	الكمية	مارس ٢٠٢٤	أبريل ٢٠٢٤	مايو ٢٠٢٤	يونيو ٢٠٢٤	يوليو ٢٠٢٤	أغسطس ٢٠٢٤	سبتمبر ٢٠٢٤	أكتوبر ٢٠٢٤	نوفمبر ٢٠٢٤
٢	أعمال الحفر											
	المتفد في سبتمبر ٢٠٢٣											
١-٥-٢	بالمتر المكعب اعمال حفر باستخدام المعدات الميكانيكية في السفو وتسوية السطح بالآلات التسوية والرش بالمياه الاصلوية للوصول الى نسبة الرطوبة المطلوبة والدمك الجيد بالهراسات للوصول الى أقصى كثافة جافة (95% من الكثافة الجافة القصوى) ومحمل على البند تحميل ونقل الأتربة الزائدة لمسافة ١,٥ كم من محور الطريق والغلة تشمل استخدام المعية في تثبيت السفو واعداد مدقات على السفو لحركة المعدات ويتم التنفيذ طبقاً للمناسيب التصميمية والقطاعات العرضية النموذجية والرسومات التفصيلية المعتمدة والبند بجميع مشتملاته طبقاً لأصول الصناعة ومواصفات الهيئة العامة للطرق والكباري وتعليمات المهندس المشرف علاوة ١ جنيه / كم لمسافة نقل ناتج الحفر وتصيح ١,١ جنيه / كم ابتداءً من ٢٠٢٣/٥/٤.	م³	٣٦٠٥٨		٧,٢١١,٦٠	٧,٢١١,٦٠	٧,٢١١,٦٠	٧,٢١١,٦٠	٧,٢١١,٦٠			
	المتفد في سبتمبر ٢٠٢٣											
١-٣	أعمال تحميل وتوريد ونقل أتربة مطابقة للمواصفات وتشغيلها باستخدام آلات التسوية بسمك لا يزيد عن ٥٠ سم حتى منسوب (2٠ متر) اسفل منسوب القرمة و بسمك لايزيد عن ٢٥سم اعلي من منسوب (2٠ متر) من منسوب القرمة لاستكمال المنسوب التصميمي للشكيل الجسر والأكتاف (نسبة تحمل كاليفورنيا لا تقل عن ١٥%) ورشها بالمياه الاصلوية للوصول الى نسبة الرطوبة المطلوبة والدمك الجيد بالهراسات للوصول الى أقصى كثافة جافة (٩٥% من الكثافة الجافة القصوى) ويتم التنفيذ طبقاً للمناسيب التصميمية والقطاعات العرضية النموذجية والرسومات التفصيلية المعتمدة والبند بجميع مشتملاته طبقاً لأصول الصناعة ومواصفات الهيئة العامة للطرق والكباري وتعليمات المهندس المشرف - في حالة طلب جهاز الإشراف زيادة نسبة الدمك عن ٩٥% يحسب زيادة ١ جنيه على زيادة نسبة الدمك لكل ١% - مسافة النقل حتى ٢ كم و يتم احتساب علاوة ١,٤ جنيه لكل كم بالزيادة او النقصان و تصبح ١,٥ جنيه لكل كم اعتباراً من ٢٠٢٣/٥/٤. -السعر يشمل عمل تشوينات و تخليط و اختبارات و نقل لموقع العمل حتى مسافة ٢ كم. - والبند لا يشمل القيمة المحجربة.	م³	٤٩٩٢٠						٩,٩٨٤,٠٠	٩,٩٨٤,٠٠	٩,٩٨٤,٠٠	٩,٩٨٤,٠٠

مهندس الشركة المنفذة

م/ احمد فتحي

التوقيع / الم/ احمد فتحي

عن الاستشاري ا.د حسن مهدي

م/ احمد عزب م/محمود غريب

التوقيع / م/ احمد عزب
التوقيع / م/محمود غريب

يعتمد

مهندس الهيئة العامة للطرق والكباري

التوقيع

شركة أبو عبيدة للمقاولات العامة والتوريدات العمومية
ب من 103-103-809

نفس الشركة المتقلة
احمد فتح
يقع / احمد فتح



الهيئة العامة
للطرق والكباري
محافظة القاهرة



هيكل تنظيمي للعاملين بمشروع القطار السريع شركة أبوعجيلة للمقاولات العامة

التاريخ : ٢٠٢٤-٩-٢٢

اسم المشروع : مشروع القطار السريع (أكتوبر-أبوسمبل)

رقم العقد: (٢٠٢٤/٢٠٢٣/١٢٢٩)

مسلسل	الاسم	الوظيفة	عدد سنوات الخبرة	رقم التليفون
1	محمد حامد يحي	مدير المشروع	10	01009742637
2	احمد احمد محمود	مدير المكتب الفني	5	01017199596
3	نادي عادل	مدير ضبط الجودة	5	01019930593
4	ربيع توحيد	مدير السلامة الوقائية	10	01114562154
5	وليد محمود محمد	مهندس التنفيذ	5	01090254469
6	محمد عماد الدين محمد	مهندس صيانة (ميكانيكا وكهرباء)	5	01559856322
7	احمد قاسم	مهندس التخطيط والبرمجة الزمنية	5	01223691236
8	احمد السيد احمد	مراقب تنفيذ (فني مواد)	5	01002612002
	محمد نادي			01063768307
9	عبدالعال رجب	حساب كميات	5	01029734478
10	حسين محمد جبريل	مساح	7	01064950832
	محمد جمال		7	01033806848
11	محمد ابوغنيمه	فني سلامة مرورية	5	01092355765
	محمد حسين		5	01022245866

يعتمد
مهندس الهيئة العامة للطرق والكباري

م/ احمد عزب
م/ محمود عويب
التوقيع /

عن الاستشاري ا.د حسن مهدي
م/ احمد عزب
م/ محمود عويب
التوقيع /

مهندس الشركة المنفذة

م/ احمد فتوح

التوقيع /



محضر استلام موقع

مشروع إنشاء خط القطار الكهربائي السريع (أكتوبر - أبوسمبل) من الكم 200+850 حتي الكم 202+350 بطول 1.5 كم
تنفيذ شركة أبو عجيبة للمقاولات العامة والتوريدات العمومية.

انه في يوم الاحد الموافق 3 / 3 / 2024 وبناء على عقد العملية رقم 1229 / 2023 / 2024

اجتمعت اللجنة المشكلة من السادة الاتي اسماؤهم بعد وهم :-

عن الهيئة العامة للطرق والكباري (طرف اول)

مدير عام المشروعات

مهندس الإشراف بالمنطقة السادسة

عن الاستشاري (مكتب أ.د/حسن مهدي)

استشاري المساحة (XYZ)

1-السيد المهندس / مصطفى شعبان البديري

2-السيد المهندس / محمود حسين

3- السيد المهندس / أحمد عزب

4- السيد المهندس / محمد عبدالرحمن سالم

عن الشركة المنفذه (طرف ثاني)

مهندس عن الشركة المنفذه

1-السيد المهندس / محمد حامد أبو عجيبة

وقد قامت اللجنة بالانتقال على الطبيعة للموقع عالية بالمعاينة الظاهرية على الطبيعة قام الطرف الاول بتسليم الطرف الثاني
الموقع خاليا من العوائق الظاهرية ولا مانع من استلام الموقع والبدء في الاعمال ويعتبر تاريخ 3 / 3 / 2024 هو تاريخ استلام
الموقع .

وقبل المحضر على ذلك .



اللجنة من الهيئة (طرف اول)



الشركة المنفذه (طرف ثاني)



رئيس الادارة المركزية للمنطقة

السادسة ببني سويف

مهندس / طارق الجزار



مكتب أ.د/حسن مهدي
للإستشارات الهندسية

SYSTRA



مشروع القطار السريع (6 أكتوبر / أبو سمبل)
القطاع الثاني بطول 158 كم من 176+700 كم الى 334+800
تنفيذ شركة : أبو عجيبة للمقاولات العامة بطول 1.5 كم
من كم 200+876 الى كم 202+376

محضر إجمال

اسم الشركة : أبو عجيبة للمقاولات العامة والتوريدات العمومية

القطاع: (201+920) الى (202+376)

أنه في يوم الثلاثاء الموافق 26 / 9 / 2023 قامت اللجنة المكونة من السادة :-

- 1- السيد المهندس/ حاتم مهران مدير المشروع
- 2- السيد المهندس/ محمود عبدالرحيم الحينى مكتب أ.د / حسن مهدي
- 3- السيد المهندس/ محمد حامد ابو عجيبة شركة أبو عجيبة للمقاولات العامة

قامت اللجنة بالمعاينة الظاهرية وأخذ عينات وإجراء اختبارات صلاحية للقطاع من (201+920) احداثي (260168.4582E, 3136445.233N) الى (202+376) احداثي (260129.6912E, 3135991.0324N) وطبقاً لنتيجة العينة المرفقة تبين أن التربة غير صالحة

للتأسيس (سفو) ويلزم إزالتها وذلك حسب توصيات استشاري التربة وتوصيات سيفكون جروب .

ملحوظات : ...
التوقيع :
التوقيعات :-

لجنة
مجلس
مجلس

عن مكتب أ.د حسن مهدي
مدير المشروع
م. محمود عثمان
م. محمد عثمان
م. محمد عثمان

عن الشركة المنفذة
م. محمد عثمان
م. محمد عثمان
م. محمد عثمان

تقرير نتائج اختبارات صلاحية أترية للتأسيس

وذلك لتحديد خصائص ومدى صلاحية حبة تراب كارض طبيعية تصلح للتأسيس

مصدر العينة : عذ المحطة / ٢٠١٩ + ٢٠٢٠ (أرض طبيعية)

- المندوب: وقد تم تزويد العينة بمعرفة م/ محمود الحبيسي . (مهندس اشراف د/ حسن المهدي) رقم الهاتف ٠١١٥٩٤٠٠١٠٨

تاریخ: ۲۰۲۳/۹/۲۱

اسم المشروع : مشروع القطار الكهربائي السريع (القطاع الثاني) - (بنى مزار - منفلوط)

- التوصيف الظاهري للعينة : كتابان رمالية ناعمة (سقو)

وقد تم عمل الاختبارات الآتية :

- ١- التدرج الحبيبي
- ٢- حد السيولة واللدونة
- ٣- اختبار البرونكتور
- ٤- اختبار CBR
- ٥- اختبار المواد العضوية

وكانت نتائج الاختبارات كالآتي :

م	نوع الاختبار	النتائج	ملاحظات
1	تصنيف العيلة	A-3	
2	نسبة الماء من منخل 200	4.6%	
3	مجال اللدونة	عديمة اللدونة	
4	أقصى كثافة جافة (البركتور) $\gamma_d \max$	1.858 gm/cm ³	
5	نسبة المياه الأمولية	10.13 %	
6	قيمة CBR المغمورة	8.50 %	
8	المواد العضوية	لا يوجد	

- و بمقارنة نتائج العينة بمواصفات مشروع القطار السريع فهي غير صالحة للتأسيس عليها او للاستخدام في طبقات الردم



असिमासि
असिमासि

مهندس المعمول
م/ محمد بن عبد الله
التوقيع

Coarse & Fine Aggregate Grading - ASTM C136 & AASHTO T27

التاريخ :	26/09/2023	الموقع : St =201+920	ارض طبيعية
-----------	------------	----------------------	------------

نتائج الاختبار :-

رقم المنخل (mm)	رقم المنخل (inch)	وزن المحجوز على كل منخل	وزن المحجوز التراكمي	المحجوز %	العار %
127	5"	0	0	0%	100%
101.6	4"	0	0	0.00%	100.00%
76.2	3"	0	0	0.00%	100.00%
63.5	2.5"	0	0	0.00%	100.00%
50.8	2"	0	0	0.00%	100.00%
37.5	1.5"	0	0	0.00%	100.00%
25	1"	0	0	0.00%	100.00%
19	3/4"	0	0	0.00%	100.00%
12.7	1/2"	0	0	0.00%	100.00%
9.5	3/8"	0	0	0.00%	100.00%
4.75	# 4	0	0	0.00%	100.00%
	العار من منخل # 1	500			100.00%
	وزن العينة الكلي	500			
	وزن عينة الناعم	500			
2.36	# 10	0	0	0.0%	100.0%
0.425	# 40	63	63	12.6%	87.4%
0.075	# 200	414	477	95.4%	4.6%
السيولة و اللدونة		N.P			
التصنيف		A-3			

ملاحظات : توصيف العينة : كحبات رملية ناعمة (Sand Dunes)



امه حسن عبيد
المهندس

مهندس المعماري
د. محمد في محمد البنا
التوقيع
م. طه كمال

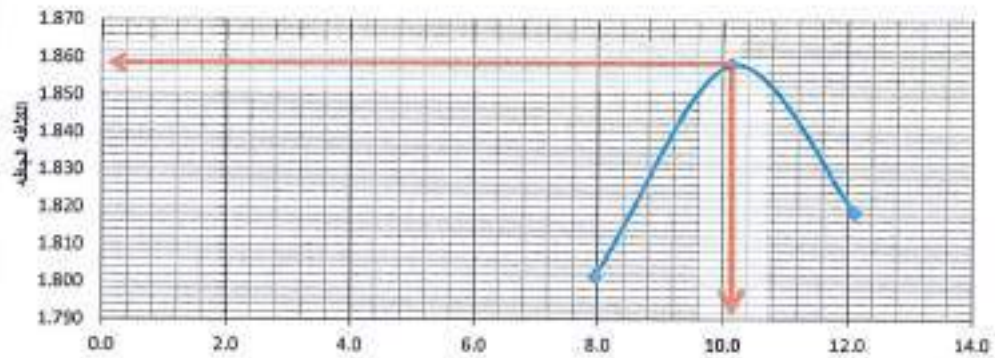
Modified Proctor : ASTM D1557

نوع العينة:	عينة قشبان رملية
تصنيف العينة:	A-3
نتائج الاختبار:	
وزن قالب:	5731
حجم القالب:	2140
الوزن الجاف:	1.858
الماء المضاف:	10.13

رقم الاختبار	1	2	3
وزن القالب + العينة رطبة	9893.0	10110	10094
وزن التربة الرطبة	4162.0	4379	4383
كثافة الرطبة	1.945	2.046	2.039

رقم البقعة	1	2	3	4	5	6
وزن البقعة	53.65	55.31	54.35	54.15	55.14	53.4
وزن القالب + العينة رطبة	150.0	150.0	150.0	150.0	150.0	150.0
وزن البقعة + العينة جافة	142.81	143.12	141.22	141.16	139.81	139.5
وزن المياه	7.2	6.9	8.8	8.8	10.2	10.5
وزن العينة جافة	88.96	87.61	86.87	87.01	84.67	86.1
المحتوى المائي %	8.1	7.8	10.1	10.2	12.0	12.2
متوسط المحتوى المائي %	8.0	10.1	12.1			
كثافة الجافة	1.801	1.858	1.818			

Modified Proctor Chart



ملاحظات:



احمد حسن عطيه
احمد حسن عطيه

مهندس المعمل
د. محمد فني محمد البنا
التوقيع
محمد فني

محضر مسافة نقل

مشروع القطار الكهربائي السريع (6 أكتوبر-اسوان) القطاع الثاني

انه في يوم الاثنين الموافق 2022/9/5 قامت اللجنة المذكورة من :-

(1) السيد المهندس / مصطفى محمد عبدالحمد مهندس المشروع الهيئة العامة للطرق والكباري

(2) السيد المهندس / محمد عبدالرحمن سالم مهندس المكتب الاستشاري (X,Y,Z)

(3) السيد المهندس / محمد حامد أبو عجيبة مدير المشروع شركة اورعجلة للمقاولات المتكاملة والتوريدات

وقد تم اللجوء بالذهاب الى مكان المقاب حيث وجد ان المسافة من قطاع (من محطة 200+800 حتى 202+300)

على مكان المقاب 3 كم وذلك بسبب تعذر وجود مدال بسبب وجود مراوغ حول القطاع

وهذا محضر منا بذلك

التوقيع



م / مصطفى محمد عبدالحمد

م / محمد عبدالرحمن سالم

م / محمد حامد أبو عجيبة

الإدارة المركزية بالمنطقة السادسة بنى سويف

اعتماد

م / طارق يوسف الجزان



محضر معاينة مسافة نقل توريد تربة صالحة من محجر (أبو هشيمة)

مشروع القطار السريع (6 أكتوبر / أبو سمبل)
القطاع الثاني بطول 158 كم من 700+176 كم الى 800+334
تنفيذ شركة : أبو عجيبة للمقاولات العامة بطول 1.5 كم
من كم 876+200 الى كم 376+202

بالإشارة الي التكاليف الصادر من الهيئة العامة للطرق والكباري لصالح شركة أبو عجيبة
للمقاولات العامة و التوريدات العمومية بشأن تنفيذ الجسر الترابي والأعمال الصناعية
بمشروع القطار الكهربائي السريع (أكتوبر - أسوان) في المسافة الكيلومترية 876+200
الي العلامة الكيلومترية 376+202

بناءً علي تعليمات السيد المهندس / رئيس قطاع التنفيذ والمناطق بالتوريد من محاجر
خارجية مرخصة بصفة مؤقتة لحين اعتماد وترخيص محاجر اخري اقرب للقطاع

فقد اجتمعت اللجنة يوم الاثنين الموافق 2023/8/28 قامت اللجنة المشكلة من :-

- | | |
|---|--|
| (1) السيد المهندس / محمد السيد شعبان | مهندس الاشراف بالهيئة |
| (2) السيد المهندس / حاتم مهران | مدير المشروع |
| (3) السيد المهندس / محمد عبدالرحمن سالم | مهندس المكتب الاستشاري (X,Y,Z) |
| (4) السيد المهندس / محمد حامد أبو عجيبة | مدير المشروع شركة أبو عجيبة للمقاولات المتكاملة والتوريدات |

وقامت اللجنة بالذهاب الي مكان محجر (أبو هشيمة) حيث وجد ان المسافة من القطاع (من محطة 876+200 حتى
876+202) حتي مكان المحجر (49 كم) وذلك بسبب تعذر وجود محجر قريب علي ان يتم التوريد بعد عمل اختبارات
الصلحية اللازمة والتأكد من صلاحية مواد المحجر للتوريد .

Easting	Northing	Longitude (E)	Latitude (N)	Station	الشركة	
260126.0446	3137487.7094	30° 33' 10.74 "	28° 20' 30.11 "	200+876	البداية	أبو عجيبة
260129.6907	3135991.0284	30° 33' 11.98 "	28° 19' 41.52 "	202+376	النهاية	للمقاولات العامة
270048.623	3178136.045	30° 38' 45.6 "	28° 42' 36.3 "	-	-	محجر أبو هشيمة

- هذا المحضر اعتماد مؤقت لحين اعتماد محجر بجوار القطاع ، ولا يعد إثبات لتوريد أية كميات من المحجر المذكور ، ويجب
علي استشاري ضبط الجودة متابعة وحصر أي كميات يتم توريدها من المحجر المذكور ومتابعة صلاحية المحجر بصفة دورية
مستمرة ومقارنتها بصلاحية المواد المشونة لتوريدها علي القطاع .

وأقفل المحضر علي ذلك :-

أ.د/حسن مهدي
مدير المشروع
م.م/حاتم مهران
م.م/محمد عبدالرحمن سالم
م.م/محمد حامد أبو عجيبة

استشاري المساحة (X,Y,Z)
م.م/محمد عبدالرحمن سالم

عن الشركة المنفذة
م.م/محمد حامد أبو عجيبة

يعتمد...
مهندس الهيئة العامة للطرق والكباري

م.م/حاتم مهران
م.م/محمد عبدالرحمن سالم
م.م/محمد حامد أبو عجيبة

م.م/حاتم مهران
م.م/محمد عبدالرحمن سالم
م.م/محمد حامد أبو عجيبة

اسم المشروع : مشروع انشاء خط القطار الكهربائي السريع (أكتوبر - أبوسمبل)
الموضوع : اعتماد الهيئة العامة للطرق والكباري لطلبات استلام الاعمال الخاصة بالمشروع
الشركة المنفذة : شركة أبو عجيبة للمقاولات العامة والتوريدات العمومية من الكم 200+850
حتى الكم 202+350 .

محضر استلام بوفيات مائية

انه في يوم الاحد الموافق 1 / 4 / 2024 تم عمل مستخلص جاري (1) اعمال ردم من
منسوب -11م الي -9م من منسوب الفرمة والبونات المائية المقدمه من الشركة المصرية
للتعدين الى شركة أبو عجيبة للمقاولات العامة علي كامل مسئولية الشركة المنفذة وتفرغ ارقامها
في بيان موقع من مسئول الشركة.
وبيانها كالآتي :-

1- محجر ابو هشيمة بواقع عدد 942 بون مائي.

وتم الاطلاع عليها من قبل استشاري المشروع ومهندس الاشراف من الهيئة واستلام البيان
الموقع من الشركة وارجاع اصل البونات المائية للشركة وعلي مسئوليتها الكاملة من صحتها
وعدها وخلافه لحين إعادة تقديمها للهيئة اثناء مراجعة وعمل المستخلص الختامي للعملية.
وعلي ذلك جري التوقيع.

1- مهندس الشركة المنفذة

2- عن الاستشاري (مكتب أ.د/حسن مهدي)

3- الهيئة -مهندس الإشراف. م/محمود محمد حسين

التوقيع/

التوقيع/ 
السيد المهندس / أحمد عزب محمد
609-161-199
التوقيع/ 

م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارطة	رسوم المرور والميزان (جنيه)	المحجر
107	2023/08/19	1659184	2673-5926	60			سلطان أبو هشيمة
108	2023/08/19	15786087	5728-7138	60			سلطان أبو هشيمة
109	2023/08/20	67776508	5127-8731	60			سلطان أبو هشيمة
110	2023/08/20	67776520	6874-5472	60			سلطان أبو هشيمة
111	2023/08/20	15786057	2546-5241	60			سلطان أبو هشيمة
112	2023/08/21	67776511	9637-2564	60			سلطان أبو هشيمة
113	2023/08/21	67776702	9271-7932	60			سلطان أبو هشيمة
114	2023/08/21	15783768	4823-3418	60			سلطان أبو هشيمة
115	2023/08/21	15783709	2533-1482	60			سلطان أبو هشيمة
116	2023-08-21	22418424	2789-9254	60			سلطان أبو هشيمة
117	2023-08-21	22417567	7391-5268	60			سلطان أبو هشيمة
118	2023-08-21	22419695	1932-9164	60			سلطان أبو هشيمة
119	2023-08-21	22417554	22417554	60			سلطان أبو هشيمة
120	2023/08/22	67776852	4958-1478	60			سلطان أبو هشيمة
121	2023/08/22	67776840	2673-5926	60			سلطان أبو هشيمة
122	2023/08/22	15780909	5748-7182	60			سلطان أبو هشيمة
123	2023/08/22	15780739	7548-7184	60			سلطان أبو هشيمة
124	2023-08-22	22417594	1658-9287	60			سلطان أبو هشيمة
125	2023-08-22	22417564	1658-6287	60			سلطان أبو هشيمة
126	2023-08-22	24602410	5973-7489	60			سلطان أبو هشيمة
127	2023/08/23	67776846	5728-7138	60			سلطان أبو هشيمة
128	2023/08/23	67776903	6497-6854	60			سلطان أبو هشيمة
129	2023/08/23	15797899	5748-7138	60			سلطان أبو هشيمة
130	2023/08/23	15765731	7159-3657	60			سلطان أبو هشيمة
131	2023-08-23	21279793	5973-7489	60			سلطان أبو هشيمة
132	2023-08-23	22417578	5973-7489	60			سلطان أبو هشيمة
133	2023/08/24	67776514	2546-5241	60			سلطان أبو هشيمة
134	2023/08/24	67776505	4823-3418	60			سلطان أبو هشيمة
135	2023/08/24	1686159	3967-8437	60			سلطان أبو هشيمة
136	2023/08/24	15798649	8291-1679	60			سلطان أبو هشيمة
137	2023-08-24	22419884	7489-5973	60			سلطان أبو هشيمة
138	2023-08-24	22419735	7489-5973	60			سلطان أبو هشيمة
139	2023-08-24	6751433	8263-6394	60			سلطان أبو هشيمة
140	2023/08/26	67776708	2533-1482	60			سلطان أبو هشيمة
141	2023/08/26	67776711	5748-7182	60			سلطان أبو هشيمة
142	2023/08/26	15798369	2533-1482	60			سلطان أبو هشيمة
143	2023/08/26	15787824	7138-5748	60			سلطان أبو هشيمة
144	2023/08/27	67776849	7548-7184	60			سلطان أبو هشيمة
145	2023/08/27	67776714	5748-7138	60			سلطان أبو هشيمة
146	2023/08/27	15787924	5589-5784	60			سلطان أبو هشيمة
147	2023/08/27	15795948	2533-1482	60			سلطان أبو هشيمة
148	2023-08-27	5440053	5362-4927	60			سلطان أبو هشيمة
149	2023-08-27	5442196	8341	20			سلطان أبو هشيمة
150	2023-08-27	13195149	8193-4973	60			سلطان أبو هشيمة
151	2023/08/28	67776502	7159-3657	60			سلطان أبو هشيمة
152	2023/08/28	67776837	8291-1679	60			سلطان أبو هشيمة
153	2023/08/28	15797349	3967-8437	60			سلطان أبو هشيمة
154	2023/08/28	15783149	6853-9672	60			سلطان أبو هشيمة
155	2023-08-28	18999009	3651	20			سلطان أبو هشيمة
156	2023/08/29	67776705	2533-1482	60			سلطان أبو هشيمة
157	2023/08/29	67776699	7138-5748	60			سلطان أبو هشيمة
158	2023/08/29	15783141	4973-8193	60			سلطان أبو هشيمة
159	2023/08/29	1686159	7413-6925	60			سلطان أبو هشيمة

مهندس اشراف الهيئة
م/محمود حسين

عن مكتب الاستشاري أ.د/حسن مهدي
م/أحمد علي عزالدين السريع
م/أحمد علي عزالدين السريع

مهندس اشراف الهيئة
م/محمود حسين
م/أحمد علي عزالدين السريع
م/أحمد علي عزالدين السريع

مكتب أ.د. إحسان مهدي
للإستشارات الهندسية

م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارثة	رسوم المرور والميزان (جنيه)	المحجر
54	2023/08/08	67776665	2673-5926	60			سلطان أبو هشيمة
55	2023/08/08	67776659	5728-7138	60			سلطان أبو هشيمة
56	2023/08/08	1687394	4823-3418	60			سلطان أبو هشيمة
57	2023/08/08	1659781	2533-1482	60			سلطان أبو هشيمة
58	2023/08/09	67776638	6497-6854	60			سلطان أبو هشيمة
59	2023/08/09	67776641	2546-5241	60			سلطان أبو هشيمة
60	2023/08/09	1687956	5748-7182	60			سلطان أبو هشيمة
61	2023/08/09	16893428	7548-7148	60			سلطان أبو هشيمة
62	2023-08-09	22417176	9271-1687	60			سلطان أبو هشيمة
63	2023-08-09	22416941	5317-8651	60			سلطان أبو هشيمة
64	2023-08-09	22417689	3257-2756	60			سلطان أبو هشيمة
65	2023-08-09	22417136	5391-8953	60			سلطان أبو هشيمة
66	2023-08-09	22417151	7316-9865	60			سلطان أبو هشيمة
67	2023/08/10	67776635	2533-1482	60			سلطان أبو هشيمة
68	2023/08/10	67776632	5748-7182	60			سلطان أبو هشيمة
69	2023/08/10	1687237	5748-7138	60			سلطان أبو هشيمة
70	2023/08/10	1659375	7159-3657	60			سلطان أبو هشيمة
71	2023-08-10	22417170	8614-7142	60			سلطان أبو هشيمة
72	2023-08-10	22416954	1687-9271	60			سلطان أبو هشيمة
73	2023-08-10	22417141	1687-9271	60			سلطان أبو هشيمة
74	2023-08-10	22417131	4156-3286	60			سلطان أبو هشيمة
75	2023/08/11	16893413	8291-1679	60			سلطان أبو هشيمة
76	2023/08/11	1686948	2533-1482	60			سلطان أبو هشيمة
77	2023-08-11	22417688	9752-1648	60			سلطان أبو هشيمة
78	2023-08-11	22416914	3864-8465	60			سلطان أبو هشيمة
79	2023-08-11	22417190	8764-6249	60			سلطان أبو هشيمة
80	2023-08-11	22417599	1758-5469	60			سلطان أبو هشيمة
81	2023/08/12	67776629	7548-7184	60			سلطان أبو هشيمة
82	2023/08/12	67776626	5748-7138	60			سلطان أبو هشيمة
83	2023/08/12	1686771	7138-5748	60			سلطان أبو هشيمة
84	2023/08/12	1686773	5589-5784	60			سلطان أبو هشيمة
85	2023/08/13	67776623	7138-5748	60			سلطان أبو هشيمة
86	2023/08/13	67776548	7159-3657	60			سلطان أبو هشيمة
87	2023/08/13	1686397	3967-8437	60			سلطان أبو هشيمة
88	2023/08/13	1659153	6853-9674	60			سلطان أبو هشيمة
89	2023/08/14	67776551	8291-1679	60			سلطان أبو هشيمة
90	2023/08/14	67776544	5589-5784	60			سلطان أبو هشيمة
91	2023/08/14	6754795	4973-8193	60			سلطان أبو هشيمة
92	2023/08/14	6754962	7413-6925	60			سلطان أبو هشيمة
93	2023/08/15	67776563	3967-8437	60			سلطان أبو هشيمة
94	2023/08/15	67776596	6853-9672	60			سلطان أبو هشيمة
95	2023/08/15	1656852	7163-2139	60			سلطان أبو هشيمة
96	2023/08/15	1656175	6391-2854	60			سلطان أبو هشيمة
97	2023/08/16	67776557	4973-8193	60			سلطان أبو هشيمة
98	2023/08/16	67776620	7413-6925	60			سلطان أبو هشيمة
99	2023/08/16	1659375	4659-4679	60			سلطان أبو هشيمة
100	2023/08/16	1656823	6874-5472	60			سلطان أبو هشيمة
101	2023/08/17	67776554	7163-2139	60			سلطان أبو هشيمة
102	2023/08/17	67776675	6391-2854	60			سلطان أبو هشيمة
103	2023/08/17	1659369	9637-2564	60			سلطان أبو هشيمة
104	2023/08/17	1684085	7958-1478	60			سلطان أبو هشيمة
105	2023/08/19	67776614	4659-4679	60			سلطان أبو هشيمة
106	2023/08/19	67776617	7239-5639	60			سلطان أبو هشيمة

مهندس اشرف الهيئة
م/محمود حسين

عن مكتب الاستشاري: أ.د/ حسن مهدي
م/ احمد عزب
المستشار السري

157537
هندسة الشركة المتحدة
م/ محمد جمال محمد
109-108-107

مكتب أ.د/حسن مهدي
للإستشارات الهندسية

مشروع إنشاء القطار الكهربائي (أكتوبر - أسوان)
القطاع الثاني (بني مزار - منفلووط) من الكم 200+850 الى الكم 202+350 بطول 1.5 كم
تنفيذ : شركة أبو عجيبة للمقاولات العامة والتوريدات العمومية
عقد رقم (2024-2023-1229)



م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارثة	رسوم المرور والميزان (جنيه)	المحجر
1	2023/08/01	67776931	3967-8437	60			سلطان أبو هشيمة
2	2023/08/01	67776937	6853-9672	60			سلطان أبو هشيمة
3	2023/08/01	16578697	6853-9672	60			سلطان أبو هشيمة
4	2023/08/01	16576573	4973-8193	60			سلطان أبو هشيمة
5	2023-08-01	22418474	1758-5419	60			سلطان أبو هشيمة
6	2023-08-01	22418237	5198-6814	60			سلطان أبو هشيمة
7	2023-08-01	22418212	9449-2983	60			سلطان أبو هشيمة
8	2023-08-01	22416980	2514-1687	60			سلطان أبو هشيمة
9	2023/08/02	67776934	4973-8193	60			سلطان أبو هشيمة
10	2023/08/02	67776940	7413-6925	60			سلطان أبو هشيمة
11	2023/08/02	1684271	7413-6925	60			سلطان أبو هشيمة
12	2023/08/02	1684085	7163-2139	60			سلطان أبو هشيمة
13	2023-08-02	22417194	7142-8614	60			سلطان أبو هشيمة
14	2023/08/03	67776943	7163-2139	60			سلطان أبو هشيمة
15	2023/08/03	67776946	6391-2139	60			سلطان أبو هشيمة
16	2023/08/03	1686781	6391-2854	60			سلطان أبو هشيمة
17	2023/08/03	1659752	4659-4679	60			سلطان أبو هشيمة
18	2023-08-03	22417672	4523-7419	60			سلطان أبو هشيمة
19	2023-08-03	22417691	7698-6912	60			سلطان أبو هشيمة
20	2023-08-03	22417198	7316-9865	60			سلطان أبو هشيمة
21	2023-08-03	22417669	7142-8614	60			سلطان أبو هشيمة
22	2023/08/04	67776723	4659-4679	60			سلطان أبو هشيمة
23	2023/08/04	67776726	7239-5639	60			سلطان أبو هشيمة
24	2023/08/04	1683562	7239-5639	60			سلطان أبو هشيمة
25	2023/08/04	1682383	6874-5472	60			سلطان أبو هشيمة
26	2023/08/05	67776729	5127-8731	60			سلطان أبو هشيمة
27	2023/08/05	67776732	6874-5472	60			سلطان أبو هشيمة
28	2023/08/05	1686982	9637-2564	60			سلطان أبو هشيمة
29	2023/08/05	1687582	7958-1478	60			سلطان أبو هشيمة
30	2023-08-05	22417155	7435-3127	60			سلطان أبو هشيمة
31	2023-08-05	22417210	1687-9271	60			سلطان أبو هشيمة
32	2023-08-05	22417152	6381-1265	60			سلطان أبو هشيمة
33	2023-08-05	22417667	3257-2756	60			سلطان أبو هشيمة
34	2023-08-05	22417167	5312-5341	60			سلطان أبو هشيمة
35	2023/08/06	67776899	9637-2564	60			سلطان أبو هشيمة
36	2023/08/06	67776653	9271-7932	60			سلطان أبو هشيمة
37	2023/08/06	1687672	2673-5926	60			سلطان أبو هشيمة
38	2023/08/06	1687192	5728-7138	60			سلطان أبو هشيمة
39	2023-08-06	22417153	9154-3267	60			سلطان أبو هشيمة
40	2023-08-06	22417297	1483-1785	60			سلطان أبو هشيمة
41	2023-08-06	22417113	4157-8726	60			سلطان أبو هشيمة
42	2023-08-06	22416915	8729-8217	60			سلطان أبو هشيمة
43	2023-08-06	22417133	1973-2945	60			سلطان أبو هشيمة
44	2023/08/07	67776672	7958-1478	60			سلطان أبو هشيمة
45	2023/08/07	67776668	4823-3418	60			سلطان أبو هشيمة
46	2023/08/07	1687352	6497-6854	60			سلطان أبو هشيمة
47	2023/08/07	1687482	2546-5241	60			سلطان أبو هشيمة
48	2023-08-07	22417692	246-9784	60			سلطان أبو هشيمة
49	2023-08-07	22417144	5837-1754	60			سلطان أبو هشيمة
50	2023-08-07	22417661	2568-9123	60			سلطان أبو هشيمة
51	2023-08-07	22416970	3864-8465	60			سلطان أبو هشيمة
52	2023-08-07	22417160	8249-7192	60			سلطان أبو هشيمة
53	2023-08-07	22417682	9417-3529	60			سلطان أبو هشيمة

مهندس اشراف الهيئة
م/محمود حسين

عن مكتب الاستشاري أ.د/ حسن مهدي
م/ أحمد عزب
م/ محمد حسن



م/ محمد علي بن محمد
الشيخ

١٥٧٥٣٧

٢٠١٩-١٠-١٨

عن مكتب الاستشاري: أ.د/ حسن مهدي
م/ احمد عذب

م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارثة	رسوم المرور والميزان (جنيه)	المحجر
213	2023/09/05	67776821	5464-3972	60			سلطان أبو هشيمة
214	2023/09/05	67776577	9695-8576	60			سلطان أبو هشيمة
215	2023/09/05	67777002	6953-5392	60			سلطان أبو هشيمة
216	2023/09/05	67776586	3729-7285	60			سلطان أبو هشيمة
217	2023/09/05	67776590	6874-5472	60			سلطان أبو هشيمة
218	2023/09/05	67776647	9637-2564	60			سلطان أبو هشيمة
219	2023/09/05	15797825	7548-7184	60			سلطان أبو هشيمة
220	2023/09/05	15797867	5748-7138	60			سلطان أبو هشيمة
221	2023-09-05	22419682	5391-8953	60			سلطان أبو هشيمة
222	2023-09-05	22418236	3742-9478	60			سلطان أبو هشيمة
223	2023-09-05	22418406	1483-1785	60			سلطان أبو هشيمة
224	2023/09/06	67776948	8553-4713	60			سلطان أبو هشيمة
225	2023/09/06	67777087	9892-7561	60			سلطان أبو هشيمة
226	2023/09/06	67777084	5695-2867	60			سلطان أبو هشيمة
227	2023/09/06	67777081	5993-7534	60			سلطان أبو هشيمة
228	2023/09/06	677770899	2365-1729	60			سلطان أبو هشيمة
229	2023/09/06	67776560	9271-7932	60			سلطان أبو هشيمة
230	2023/09/06	67776584	7958-1478	60			سلطان أبو هشيمة
231	2023/09/06	15766856	7159-3657	60			سلطان أبو هشيمة
232	2023/09/06	15765743	8241-1679	60			سلطان أبو هشيمة
233	2023-09-06	24602428	2183-4689	60			سلطان أبو هشيمة
234	2023-09-06	13196624	5923	20			سلطان أبو هشيمة
235	2023-09-06	22418604	7352-6971	60			سلطان أبو هشيمة
236	2023-09-06	21279760	6438-8465	60			سلطان أبو هشيمة
237	2023-09-06	18998557	7435-3127	60			سلطان أبو هشيمة
238	2023/09/07	67777078	1684-4638	60			سلطان أبو هشيمة
239	2023/09/07	67776839	2983-4312	60			سلطان أبو هشيمة
240	2023/09/07	67777072	4622-3692	60			سلطان أبو هشيمة
241	2023/09/07	67776848	1867-3657	60			سلطان أبو هشيمة
242	2023/09/07	67777066	3564-8316	60			سلطان أبو هشيمة
243	2023/09/07	67776581	2673-5926	60			سلطان أبو هشيمة
244	2023/09/07	67776587	5728-7138	60			سلطان أبو هشيمة
245	2023/09/07	15787824	2533-1482	60			سلطان أبو هشيمة
246	2023/09/07	15797249	7138-5748	60			سلطان أبو هشيمة
247	2023-09-07	18998591	3651	20			سلطان أبو هشيمة
248	2023-09-07	22419700	2694-7365	60			سلطان أبو هشيمة
249	2023-09-07	24602570	3259-1257	60			سلطان أبو هشيمة
250	2023-09-07	22419618	6482-4597	60			سلطان أبو هشيمة
251	2023-09-07	18998627	7348-7381	60			سلطان أبو هشيمة
252	2023/09/08	67776893	5589-5782	60			سلطان أبو هشيمة
253	2023/09/08	67776816	3967-8437	60			سلطان أبو هشيمة
254	2023-09-08	13196734	1936-1785	60			سلطان أبو هشيمة
255	2023/09/09	67777063	3729-7285	60			سلطان أبو هشيمة
256	2023/09/09	67777060	8919-5736	60			سلطان أبو هشيمة
257	2023/09/09	67777057	9886-7524	60			سلطان أبو هشيمة
258	2023/09/09	67777054	8714-5371	60			سلطان أبو هشيمة
259	2023/09/09	67777051	7172-44852	60			سلطان أبو هشيمة
260	2023/09/09	67776578	6497-6854	60			سلطان أبو هشيمة
261	2023/09/09	67776575	2546-5241	60			سلطان أبو هشيمة
262	2023/09/09	67776813	6853-9672	60			سلطان أبو هشيمة
263	2023/09/09	67776856	4973-8193	60			سلطان أبو هشيمة
264	2023/09/10	67777048	8231-9258	60			سلطان أبو هشيمة
265	2023/09/10	67777045	8553-4713	60			سلطان أبو هشيمة

مهندس اشراف الهيئة
م/محمود حسين

عن مكتب الاستشاري أ.د/ حسن مهدي
م/ احمد محمد شحات السريخ
م/ احمد محمد شحات السريخ



م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارثة	رسوم المرور والميزان (جنيه)	المحجر
266	2023/09/10	67777042	7419-8627	60			سلطان أبو هشيمة
267	2023/09/10	67776685	3762-8691	60			سلطان أبو هشيمة
268	2023/09/10	67776688	7968-1692	60			سلطان أبو هشيمة
269	2023/09/10	67776572	4823-3418	60			سلطان أبو هشيمة
270	2023/09/10	67776569	2533-1482	60			سلطان أبو هشيمة
271	2023/09/10	67776858	7413-6925	60			سلطان أبو هشيمة
272	2023/09/10	67776864	7163-2139	60			سلطان أبو هشيمة
273	2023-09-10	13196766	1936-1785	60			سلطان أبو هشيمة
274	2023/09/11	67776802	1282-7137	60			سلطان أبو هشيمة
275	2023/09/11	67776805	7214-9365	60			سلطان أبو هشيمة
276	2023/09/11	67776808	3692-4622	60			سلطان أبو هشيمة
277	2023/09/11	67776811	1692-7968	60			سلطان أبو هشيمة
278	2023/09/11	67776814	8691-3762	60			سلطان أبو هشيمة
279	2023/09/11	67776566	5748-7182	60			سلطان أبو هشيمة
280	2023/09/11	67776819	7548-7138	60			سلطان أبو هشيمة
281	2023-09-11	13196751	1936-1785	60			سلطان أبو هشيمة
282	2023-09-11	21278015	7591-2158	60			سلطان أبو هشيمة
283	2023-09-11	18997924	3651	20			سلطان أبو هشيمة
284	2023-09-11	13196774	1639-1785	60			سلطان أبو هشيمة
285	2023/09/12	67776823	9253-3285	60			سلطان أبو هشيمة
286	2023/09/12	67776817	7285-3729	60			سلطان أبو هشيمة
287	2023/09/12	67776820	2867-8392	60			سلطان أبو هشيمة
288	2023/09/12	67776826	8691-3762	60			سلطان أبو هشيمة
289	2023/09/12	67776829	7916-7848	60			سلطان أبو هشيمة
290	2023/09/12	67776843	3967-8237	60			سلطان أبو هشيمة
291	2023/09/12	67776783	6853-9672	60			سلطان أبو هشيمة
292	2023/09/12	67776870	6391-2854	60			سلطان أبو هشيمة
293	2023/09/12	67776880	4659-4679	60			سلطان أبو هشيمة
294	2023-09-12	18998080	2179-9274	60			سلطان أبو هشيمة
295	2023-09-12	21278095	7381-7271	60			سلطان أبو هشيمة
296	2023-09-12	18998062	5746-7912	60			سلطان أبو هشيمة
297	2023/09/13	67776564	2867-8392	60			سلطان أبو هشيمة
298	2023/09/13	67776567	6574-8739	60			سلطان أبو هشيمة
299	2023/09/13	67776570	9253-3285	60			سلطان أبو هشيمة
300	2023/09/13	67776573	2365-2381	60			سلطان أبو هشيمة
301	2023/09/13	67776786	4973-8193	60			سلطان أبو هشيمة
302	2023/09/13	67776789	7413-6925	60			سلطان أبو هشيمة
303	2023/09/13	67776894	2673-5926	60			سلطان أبو هشيمة
304	2023-09-13	18997994	9274-4965	60			سلطان أبو هشيمة
305	2023-09-13	18998106	6493-3789	60			سلطان أبو هشيمة
306	2023-09-13	13196609	1936-1785	60			سلطان أبو هشيمة
307	2023-09-13	13196794	1936-1785	60			سلطان أبو هشيمة
308	2023-09-13	13196796	1856-1896	60			سلطان أبو هشيمة
309	2023-09-13	18998091	9612-7698	60			سلطان أبو هشيمة
310	2023/09/14	67776576	4713-8553	60			سلطان أبو هشيمة
311	2023/09/14	67776579	7285-3729	60			سلطان أبو هشيمة
312	2023/09/14	67776582	8576-9695	60			سلطان أبو هشيمة
313	2023/09/14	67776585	8739-9749	60			سلطان أبو هشيمة
314	2023/09/14	67776588	1692-7968	60			سلطان أبو هشيمة
315	2023/09/14	67776798	7163-2139	60			سلطان أبو هشيمة
316	2023/09/14	67776792	6391-2854	60			سلطان أبو هشيمة
317	2023/09/14	67776777	5728-7138	60			سلطان أبو هشيمة
318	2023/09/14	67776780	6497-6854	60			سلطان أبو هشيمة

مهندس اشراف الهيئة
م/محمود حسين

عن مكتب الاستشاري أ.د/ حسن مهدي

م/ احمد عزب
الاستشار السريخ
أ.د/ حسن مهدي
م/ احمد عزب

مهندس الشركة
م/ محمد عيسى عيسى
أ.د/ حسن مهدي
م/ احمد عزب
م/ محمد عيسى عيسى

م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارثة	رسوم المرور والموزان (جنيه)	المحجر
319	2023-09-14	18998188	7912-5746	60			سلطان أبو هشيمة
320	2023/09/15	67776834	2546-5248	60			سلطان أبو هشيمة
321	2023/09/15	67776831	4823-3418	60			سلطان أبو هشيمة
322	2023-09-15	13196619	1936-1785	60			سلطان أبو هشيمة
323	2023-09-15	6674609	1982-7376	60			سلطان أبو هشيمة
324	2023-09-15	18998294	4735-4973	60			سلطان أبو هشيمة
325	2023/09/16	67776558	6158-8357	60			سلطان أبو هشيمة
326	2023/09/16	67776645	9186-4847	40			سلطان أبو هشيمة
327	2023/09/16	67776772	7189-6463	60			سلطان أبو هشيمة
328	2023/09/16	67776597	1282-7137	60			سلطان أبو هشيمة
329	2023/09/16	67776600	7214-9365	60			سلطان أبو هشيمة
330	2023/09/16	67776795	4659-4679	60			سلطان أبو هشيمة
331	2023/09/16	67776801	7239-5639	60			سلطان أبو هشيمة
332	2023/09/16	67776828	2533-1482	60			سلطان أبو هشيمة
333	2023/09/16	67776825	5748-7182	60			سلطان أبو هشيمة
334	2023-09-16	8423361	9396-9783	60			سلطان أبو هشيمة
335	2023-09-16	21278101	7381-7348	60			سلطان أبو هشيمة
336	2023-09-16	22418480	3529-9417	60			سلطان أبو هشيمة
337	2023-09-16	13196666	1936-1785	60			سلطان أبو هشيمة
338	2023-09-16	13196637	1936-1785	60			سلطان أبو هشيمة
339	2023-09-16	8423360	1859-7163	60			سلطان أبو هشيمة
340	2023-09-16	18998271	1982-2786	60			سلطان أبو هشيمة
341	2023/09/17	67776603	3692-4622	60			سلطان أبو هشيمة
342	2023/09/17	67776606	1692-7968	60			سلطان أبو هشيمة
343	2023/09/17	67776609	8691-3762	60			سلطان أبو هشيمة
344	2023/09/17	67776612	7285-3729	60			سلطان أبو هشيمة
345	2023/09/17	67776673	2867-8392	60			سلطان أبو هشيمة
346	2023/09/17	67776804	6874-5472	60			سلطان أبو هشيمة
347	2023/09/17	67776807	9637-2564	60			سلطان أبو هشيمة
348	2023/09/17	67776822	7548-7184	60			سلطان أبو هشيمة
349	2023-09-17	8423391	8465-2475	60			سلطان أبو هشيمة
350	2023-09-17	8423515	2378-2359	60			سلطان أبو هشيمة
351	2023-09-17	8423395	4361-3184	60			سلطان أبو هشيمة
352	2023-09-17	8423513	6379-8246	60			سلطان أبو هشيمة
353	2023-09-17	8423532	7356-2681	60			سلطان أبو هشيمة
354	2023-09-17	8423541	2987-1836	60			سلطان أبو هشيمة
355	2023-09-17	18998196	4678-7562	60			سلطان أبو هشيمة
356	2023-09-17	8423367	4356-7892	60			سلطان أبو هشيمة
357	2023-09-17	8423537	2756-3257	60			سلطان أبو هشيمة
358	2023-09-17	8423510	9648-7518	60			سلطان أبو هشيمة
359	2023-09-17	24602407	5869-1736	60			سلطان أبو هشيمة
360	2023-09-17	22418416	1265-6381	60			سلطان أبو هشيمة
361	2023-09-17	22417593	5973-7489	60			سلطان أبو هشيمة
362	2023-09-17	13196650	1936-1785	60			سلطان أبو هشيمة
363	2023-09-17	22418485	5312-5341	60			سلطان أبو هشيمة
364	2023/09/18	67776615	9253-3285	60			سلطان أبو هشيمة
365	2023/09/18	67776618	8691-3762	60			سلطان أبو هشيمة
366	2023/09/18	67776552	7916-7848	60			سلطان أبو هشيمة
367	2023/09/18	67776555	7139-8423	60			سلطان أبو هشيمة
368	2023/09/18	67776594	6397-4727	60			سلطان أبو هشيمة
369	2023/09/18	67776810	9271-7932	60			سلطان أبو هشيمة
370	2023/09/18	67776644	7958-1478	60			سلطان أبو هشيمة
371	2023-09-18	189978806	1826-2319	60			سلطان أبو هشيمة

مهندس اشراف الهيئة
م/محمود حسين

عن مكتب الاستشاري أ.د/ حسن مهدي

م/احمد عزب
شركة انقصار السريع
م/محمود حسين

مهندس الاستشارات
م/محمد جاسم أبو عجيبة
شركة أبو عجيبة للمقاولات العامة والتوريدات العمومية
ب.ع. 101-198

م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارثة	رسوم المرور والميزان (جنيه)	المحجر
372	2023-09-18	18997809	6942-9853	60			سلطان أبو هشيمة
373	2023-09-18	8423588	4937-6983	60			سلطان أبو هشيمة
374	2023-09-18	18997849	1217-8729	60			سلطان أبو هشيمة
375	2023-09-18	18997811	1736-5869	60			سلطان أبو هشيمة
376	2023-09-18	18997819	4378-4965	60			سلطان أبو هشيمة
377	2023-09-18	8423583	6381-1295	60			سلطان أبو هشيمة
378	2023-09-18	8423552	4973-8193	60			سلطان أبو هشيمة
379	2023-09-18	8423599	2645-2716	60			سلطان أبو هشيمة
380	2023-09-18	18997805	1754-5837	60			سلطان أبو هشيمة
381	2023-09-18	8423573	2593-4378	60			سلطان أبو هشيمة
382	2023-09-18	8423566	4637-5319	60			سلطان أبو هشيمة
383	2023-09-18	8423581	8439-8612	60			سلطان أبو هشيمة
384	2023-09-18	18997801	8476-2943	60			سلطان أبو هشيمة
385	2023-09-18	18997830	1854-1654	60			سلطان أبو هشيمة
386	2023-09-18	8423554	9271-7932	60			سلطان أبو هشيمة
387	2023-09-18	8423551	1948-7653	60			سلطان أبو هشيمة
388	2023-09-18	8423563	6721-9657	60			سلطان أبو هشيمة
389	2023-09-18	8423546	6874-5472	60			سلطان أبو هشيمة
390	2023-09-18	8423358	2179-9274	60			سلطان أبو هشيمة
391	2023-09-18	8423572	1687-8317	60			سلطان أبو هشيمة
392	2023-09-18	8423560	7215-5248	60			سلطان أبو هشيمة
393	2023-09-18	18997823	8975-2931	60			سلطان أبو هشيمة
394	2023-09-18	18997817	6573-1843	60			سلطان أبو هشيمة
395	2023-09-18	18997821	2645-7698	60			سلطان أبو هشيمة
396	2023-09-18	18997804	5329-8314	60			سلطان أبو هشيمة
397	2023-09-18	8423548	9637-2564	60			سلطان أبو هشيمة
398	2023-09-18	8423565	6713-4895	60			سلطان أبو هشيمة
399	2023-09-18	8423575	2819-1824	60			سلطان أبو هشيمة
400	2023-09-18	8423586	9417-3529	60			سلطان أبو هشيمة
401	2023-09-18	18997820	7921-5216	60			سلطان أبو هشيمة
402	2023-09-18	8423595	1986-2975	60			سلطان أبو هشيمة
403	2023-09-18	8423570	1896-1856	60			سلطان أبو هشيمة
404	2023-09-18	18997825	9173-7135	60			سلطان أبو هشيمة
405	2023/09/19	67776542	2867-8392	60			سلطان أبو هشيمة
406	2023/09/19	67776561	6574-8739	60			سلطان أبو هشيمة
407	2023/09/19	67776546	9253-3285	60			سلطان أبو هشيمة
408	2023/09/19	67776549	2365-2381	60			سلطان أبو هشيمة
409	2023/09/19	67776621	15062-4263	20			سلطان أبو هشيمة
410	2023/09/19	67776655	2673-5926	60			سلطان أبو هشيمة
411	2023/09/19	67776681	5728-7138	60			سلطان أبو هشيمة
412	2023-09-19	18997865	7352	20			سلطان أبو هشيمة
413	2023-09-19	22417811	5216-8921	60			سلطان أبو هشيمة
414	2023-09-19	13196673	1936-1785	60			سلطان أبو هشيمة
415	2023-09-19	18997835	3248-3176	60			سلطان أبو هشيمة
416	2023-09-19	18997878	9417-3529	60			سلطان أبو هشيمة
417	2023-09-19	8423600	9271-2599	60			سلطان أبو هشيمة
418	2023-09-19	18997864	1982-2789	60			سلطان أبو هشيمة
419	2023-09-19	18997856	9518-8945	60			سلطان أبو هشيمة
420	2023-09-19	18997848	7359-2459	60			سلطان أبو هشيمة
421	2023-09-19	13196683	7653-2979	60			سلطان أبو هشيمة
422	2023-09-19	18997854	5973-7489	60			سلطان أبو هشيمة
423	2023-09-19	18997837	7142-8614	60			سلطان أبو هشيمة
424	2023-09-19	18997885	1843-6573	60			سلطان أبو هشيمة

مهندس اشراف الهيئة
م/محمود حسين

عن مكتب الاستشاري ا.د/ حسن مهدي
م/ احمد عزب



[illegible]

م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارثة	رسوم المرور والموزان (جنيه)	المحجر
478	2023/09/25	67776731	1282-7137	60			سلطان أبو هشيمة
479	2023/09/25	67776898	7214-9365	60			سلطان أبو هشيمة
480	2023/09/25	67776887	7138-5748	60			سلطان أبو هشيمة
481	2023/09/25	67776890	5589-5784	60			سلطان أبو هشيمة
482	2023/09/26	67776667	8691-3762	60			سلطان أبو هشيمة
483	2023/09/26	67776754	7189-6463	60			سلطان أبو هشيمة
484	2023/09/26	67776757	9186-4847	60			سلطان أبو هشيمة
485	2023/09/26	67776649	3692-4622	60			سلطان أبو هشيمة
486	2023/09/26	67776652	1692-7968	60			سلطان أبو هشيمة
487	2023/09/26	67776658	8691-3762	60			سلطان أبو هشيمة
488	2023/09/26	67776664	7285-3729	60			سلطان أبو هشيمة
489	2023/09/26	67776670	2867-8392	60			سلطان أبو هشيمة
490	2023/09/27	67776677	9253-3285	60			سلطان أبو هشيمة
491	2023/09/27	67776680	8691-3762	60			سلطان أبو هشيمة
492	2023/09/27	67776760	6158-8357	60			سلطان أبو هشيمة
493	2023/09/27	67776763	1692-7968	60			سلطان أبو هشيمة
494	2023/09/27	67776683	7916-7848	60			سلطان أبو هشيمة
495	2023/09/27	67776686	7139-8423	60			سلطان أبو هشيمة
496	2023/09/27	67776689	6397-4727	60			سلطان أبو هشيمة
497	2023/09/27	67776692	2867-8392	60			سلطان أبو هشيمة
498	2023-09-27	6754657	2642-9127	60			سلطان أبو هشيمة
499	2023-09-27	13196727	1936-1785	60			سلطان أبو هشيمة
500	2023-09-27	22419638	5312-5341	60			سلطان أبو هشيمة
501	2023-09-27	22419798	3698-1853	60			سلطان أبو هشيمة
502	2023-09-27	22417644	7894-7416	60			سلطان أبو هشيمة
503	2023/09/28	67776766	8739-9749	60			سلطان أبو هشيمة
504	2023/09/28	67776769	8576-9695	60			سلطان أبو هشيمة
505	2023/09/28	67776695	6574-8739	60			سلطان أبو هشيمة
506	2023/09/28	67776698	2365-2381	60			سلطان أبو هشيمة
507	2023/09/28	67776701	15062-4263	60			سلطان أبو هشيمة
508	2023/09/28	67776704	9258-3285	60			سلطان أبو هشيمة
509	2023/09/28	67776707	5837	20			سلطان أبو هشيمة
510	2023/09/28	67776929	1428-7148	60			سلطان أبو هشيمة
511	2023/09/28	67776926	1482-2533	60			سلطان أبو هشيمة
512	2023-09-28	16556218	6254-4221	60			سلطان أبو هشيمة
513	2023-09-29	16558594	1428-5631	60			سلطان أبو هشيمة
514	2023/09/30	67776922	7182-5748	60			سلطان أبو هشيمة
515	2023/09/30	67776919	5784-5589	60			سلطان أبو هشيمة
516	2023/09/30	67776916	7138-5748	60			سلطان أبو هشيمة
517	2023/09/30	67776913	5784-5589	60			سلطان أبو هشيمة
518	2023/09/30	67776910	1679-8291	60			سلطان أبو هشيمة
519	2023/09/30	67776907	7138-5748	60			سلطان أبو هشيمة
520	2023/09/30	67776904	7138-5748	60			سلطان أبو هشيمة
521	2023-09-30	16558532	8341-9157	60			سلطان أبو هشيمة
522	2023-09-30	16558599	4791	20			سلطان أبو هشيمة
523	2023/10/01	67776748	1282-7137	60			سلطان أبو هشيمة
524	2023/10/01	67776751	7214-9365	60			سلطان أبو هشيمة
525	2023/10/01	67776745	3692-4622	60			سلطان أبو هشيمة
526	2023/10/01	67776742	1692-7968	60			سلطان أبو هشيمة
527	2023/10/02	67776739	7285-3729	60			سلطان أبو هشيمة
528	2023/10/02	67776736	2867-8392	60			سلطان أبو هشيمة
529	2023/10/02	67776733	9253-3285	60			سلطان أبو هشيمة
530	2023/10/02	67776947	8691-3762	60			سلطان أبو هشيمة

م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارثة	رسوم المرور والميزان (جنيه)	المحجر
531	2023/10/03	67777086	7916-7848	60			سلطان أبو هشيمة
532	2023/10/03	67777083	7139-8423	60			سلطان أبو هشيمة
533	2023/10/03	67777080	6397-4727	60			سلطان أبو هشيمة
534	2023/10/03	67777098	2867-8392	60			سلطان أبو هشيمة
535	2023-10-03	16556651	1572-3756	60			سلطان أبو هشيمة
536	2023/10/04	67777077	6574-8739	60			سلطان أبو هشيمة
537	2023/10/04	67777074	9253-3285	60			سلطان أبو هشيمة
538	2023/10/04	67777071	2365-2381	60			سلطان أبو هشيمة
539	2023/10/04	67777068	15062-4263	60			سلطان أبو هشيمة
540	2023/10/05	67776945	6156-8357	60			سلطان أبو هشيمة
541	2023/10/05	67776715	1282-7137	60			سلطان أبو هشيمة
542	2023/10/05	67776691	4622-3692	60			سلطان أبو هشيمة
543	2023/10/05	67776694	9365-7214	60			سلطان أبو هشيمة
544	2023-10-06	24602544	5619-9123	60			سلطان أبو هشيمة
545	2023-10-06	20440321	1842-8348	60			سلطان أبو هشيمة
546	2023-10-06	5886304	2348-3898	60			سلطان أبو هشيمة
547	2023-10-06	16558666	8341	20			سلطان أبو هشيمة
548	2023/10/07	67776697	7137-1282	60			سلطان أبو هشيمة
549	2023/10/07	67776700	6463-7189	60			سلطان أبو هشيمة
550	2023/10/07	67776703	4847-9186	60			سلطان أبو هشيمة
551	2023/10/07	67776706	8357-6158	60			سلطان أبو هشيمة
552	2023-10-07	16558688	5923	20			سلطان أبو هشيمة
553	2023-10-07	20440210	3248-5177	60			سلطان أبو هشيمة
554	2023-10-07	22416923	9154-3267	60			سلطان أبو هشيمة
555	2023/10/08	67776580	7968-1692	60			سلطان أبو هشيمة
556	2023/10/08	67776583	9749-8739	60			سلطان أبو هشيمة
557	2023/10/08	67776897	32285-9253	60			سلطان أبو هشيمة
558	2023/10/08	67776648	8739-6574	60			سلطان أبو هشيمة
559	2023/10/08	67776651	8392-2867	60			سلطان أبو هشيمة
560	2023-10-08	22418430	2139-7163	60			سلطان أبو هشيمة
561	2023-10-08	22416925	3928-6417	60			سلطان أبو هشيمة
562	2023-10-08	22416916	8614-7142	60			سلطان أبو هشيمة
563	2023-10-08	22418423	6438-8465	60			سلطان أبو هشيمة
564	2023-10-08	22418602	4378-4965	60			سلطان أبو هشيمة
565	2023-10-08	6751810	7163-1859	60			سلطان أبو هشيمة
566	2023/10/09	67776657	4727-6397	60			سلطان أبو هشيمة
567	2023/10/09	67776663	8423-7139	60			سلطان أبو هشيمة
568	2023/10/09	67776666	7848-7916	60			سلطان أبو هشيمة
569	2023/10/09	67776669	3762-8691	60			سلطان أبو هشيمة
570	2023-10-09	2895288	3798-2348	60			سلطان أبو هشيمة
571	2023-10-09	22417283	7238-5824	60			سلطان أبو هشيمة
572	2023-10-09	22416921	5341-5312	60			سلطان أبو هشيمة
573	2023-10-09	22416920	1687-9271	60			سلطان أبو هشيمة
574	2023/10/10	67776884	6953-5392	60			سلطان أبو هشيمة
575	2023/10/10	67777017	3729-7258	60			سلطان أبو هشيمة
576	2023/10/10	67776682	3729-7285	60			سلطان أبو هشيمة
577	2023/10/10	67776803	3285-9253	60			سلطان أبو هشيمة

م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارثة	رسوم المرور والميزان (جنيه)	المحجر
578	2023-10-10	22416928	7921-5216	60			سلطان أبو هشيمة
579	2023/10/11	67776815	2381-2365	60			سلطان أبو هشيمة
580	2023/10/11	67776886	5394-7563	60			سلطان أبو هشيمة
581	2023/10/11	67777065	7137-1282	60			سلطان أبو هشيمة
582	2023/10/11	67777059	4123-1256	60			سلطان أبو هشيمة
583	2023-10-11	8424540	9673-5428	60			سلطان أبو هشيمة
584	2023-10-11	22416810	9362-6315	60			سلطان أبو هشيمة
585	2023-10-11	22419185	1658-6287	60			سلطان أبو هشيمة
586	2023/10/12	67777053	3729-7285	60			سلطان أبو هشيمة
587	2023/10/12	67777047	8919-5736	60			سلطان أبو هشيمة
588	2023/10/12	67777041	8231-9258	60			سلطان أبو هشيمة
589	2023/10/12	67776710	447-8517	60			سلطان أبو هشيمة
590	2023-10-12	6751195	6482-6581	60			سلطان أبو هشيمة
591	2023-10-12	22417553	5973-7489	60			سلطان أبو هشيمة
592	2023-10-12	24602629	6287-1658	60			سلطان أبو هشيمة
593	2023-10-12	22419204	1658-6287	60			سلطان أبو هشيمة
594	2023-10-12	8424160	5198-6814	60			سلطان أبو هشيمة
595	2023-10-12	22419859	5973-7489	60			سلطان أبو هشيمة
596	2023/10/13	67776501	9695-8576	60			سلطان أبو هشيمة
597	2023/10/13	67776513	8553-4713	60			سلطان أبو هشيمة
598	2023/10/13	67776510	5695-2864	60			سلطان أبو هشيمة
599	2023/10/13	67776504	2365-1729	60			سلطان أبو هشيمة
600	2023-10-13	22417539	5973-7489	60			سلطان أبو هشيمة
601	2023-10-13	2895442	2348-3798	60			سلطان أبو هشيمة
602	2023/10/14	67777075	2983-4312	60			سلطان أبو هشيمة
603	2023/10/14	67777069	1867-3657	60			سلطان أبو هشيمة
604	2023/10/14	67776892	3729-7285	60			سلطان أبو هشيمة
605	2023/10/14	67776857	9886-7524	60			سلطان أبو هشيمة
606	2023-10-14	13196978	5923	20			سلطان أبو هشيمة
607	2023-10-14	20439865	9752-1648	60			سلطان أبو هشيمة
608	2023/10/15	67776769	7172-44852	60			سلطان أبو هشيمة
609	2023/10/15	67776882	8553-4713	60			سلطان أبو هشيمة
610	2023/10/15	67776776	3762-8691	60			سلطان أبو هشيمة
611	2023/10/15	67776842	4622-3692	60			سلطان أبو هشيمة
612	2023-10-15	8425835	9173-7135	60			سلطان أبو هشيمة
613	2023/10/16	67776785	7137-1282	60			سلطان أبو هشيمة
614	2023/10/16	67776773	4847-9186	60			سلطان أبو هشيمة
615	2023/10/16	67776598	7968-1692	60			سلطان أبو هشيمة
616	2023/10/16	67776604	3285-9253	60			سلطان أبو هشيمة
617	2023-10-16	8425890	5428-9673	60			سلطان أبو هشيمة
618	2023/10/17	67776788	8392-2867	60			سلطان أبو هشيمة
619	2023/10/17	67776794	8423-7139	60			سلطان أبو هشيمة
620	2023/10/17	67776800	3762-8691	60			سلطان أبو هشيمة
621	2023/10/17	67777023	2983-4312	60			سلطان أبو هشيمة

مهندس اشراف الهيئة
م/محمود حسين

عن مكتب الاستشاري أ/د/ حسن مهدي
م/ احمد عزب



م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارثة	رسوم المرور والميزان (جنيه)	المحجر
622	2023/10/18	67776676	3285-9253	60			سلطان أبو هشيمة
623	2023/10/18	67776610	2381-2365	60			سلطان أبو هشيمة
624	2023/10/18	67776809	3729-7285	60			سلطان أبو هشيمة
625	2023/10/18	67777008	7138-5748	60			سلطان أبو هشيمة
626	2023-10-18	13196833	5362-4927	60			سلطان أبو هشيمة
627	2023-10-18	13196851	5879-6437	60			سلطان أبو هشيمة
628	2023/10/19	67776889	4519-8289	60			سلطان أبو هشيمة
629	2023/10/19	67777062	9658-8274	60			سلطان أبو هشيمة
630	2023/10/19	67777056	3729-7285	60			سلطان أبو هشيمة
631	2023/10/19	67777050	8374-3714	60			سلطان أبو هشيمة
632	2023-10-19	6751184	9272-2179	60			سلطان أبو هشيمة
633	2023-10-20	16556761	9362-6315	60			سلطان أبو هشيمة
634	2023/10/21	67777044	6374-9683	60			سلطان أبو هشيمة
635	2023/10/21	67777038	8413-6983	60			سلطان أبو هشيمة
636	2023/10/21	67776713	5464-3972	60			سلطان أبو هشيمة
637	2023/10/21	67776901	3729-7285	60			سلطان أبو هشيمة
638	2023-10-21	13196871	1428-5631	60			سلطان أبو هشيمة
639	2023-10-21	13196875	4613-1854	60			سلطان أبو هشيمة
640	2023-10-21	16556781	8724-9328	60			سلطان أبو هشيمة
641	2023/10/22	67776507	9892-7561	60			سلطان أبو هشيمة
642	2023/10/22	67776519	5993-7534	60			سلطان أبو هشيمة
643	2023/10/22	67776836	1684-4638	60			سلطان أبو هشيمة
644	2023/10/22	67776845	4622-3692	60			سلطان أبو هشيمة
645	2023-10-22	20441491	3267-4921	60			سلطان أبو هشيمة
646	2023/10/23	67776851	3564-8316	60			سلطان أبو هشيمة
647	2023/10/23	67776854	8919-5736	60			سلطان أبو هشيمة
648	2023/10/23	67776863	8714-5371	60			سلطان أبو هشيمة
649	2023/10/23	67776869	8231-9258	60			سلطان أبو هشيمة
650	2023-10-23	16556744	8629-9426	60			سلطان أبو هشيمة
651	2023-10-23	16555634	7524-4179	60			سلطان أبو هشيمة
652	2023-10-23	20441482	8721-9752	60			سلطان أبو هشيمة
653	2023-10-23	22418486	3127-7435	60			سلطان أبو هشيمة
654	2023-10-23	22418246	7519-5316	60			سلطان أبو هشيمة
655	2023-10-23	22419808	1658-6287	60			سلطان أبو هشيمة
656	2023/10/24	67776896	7419-8627	60			سلطان أبو هشيمة
657	2023/10/24	67776779	7968-1692	60			سلطان أبو هشيمة
658	2023/10/24	67776782	9365-7214	60			سلطان أبو هشيمة
659	2023/10/24	67776646	6463-7189	60			سلطان أبو هشيمة
660	2023-10-24	16555729	4937-6983	60			سلطان أبو هشيمة
661	2023-10-24	16555839	6398-3581	60			سلطان أبو هشيمة
662	2023/10/25	67776592	8357-6158	60			سلطان أبو هشيمة
663	2023/10/25	67776601	9749-8739	60			سلطان أبو هشيمة
664	2023/10/25	67776607	8739-6574	60			سلطان أبو هشيمة
665	2023/10/25	67776791	4727-6397	60			سلطان أبو هشيمة

[illegible]

م/ احمد شعري الشماوي المسترشد

م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارثة	رسوم المرور والميزان (جنيه)	المحجر
710	2023-11-12	21279093	7831-8236	60			سلطان أبو هشيمة
711	2023-11-12	22418945	1824-2952	60			سلطان أبو هشيمة
712	2023-11-12	21279292	8614-7145	60			سلطان أبو هشيمة
713	2023-11-13	21279277	7142-8614	60			سلطان أبو هشيمة
714	2023-11-14	5440981	8193-8346	60			سلطان أبو هشيمة
715	2023-11-14	21279135	7142-8614	60			سلطان أبو هشيمة
716	2023-11-15	21279177	6832-1592	60			سلطان أبو هشيمة
717	2023-11-15	21279759	5312-5341	60			سلطان أبو هشيمة
718	2023-11-16	18997617	6432-3512	60			سلطان أبو هشيمة
719	2023-11-16	18997646	3971-8547	60			سلطان أبو هشيمة
720	2023-11-17	18997688	4726-9417	60			سلطان أبو هشيمة
721	2023-11-17	22419743	7941-2386	60			سلطان أبو هشيمة
722	2023-11-17	22419841	4381	20			سلطان أبو هشيمة
723	2023-11-17	24602597	3529-9417	60			سلطان أبو هشيمة
724	2023-11-17	21279272	6439-1829	60			سلطان أبو هشيمة
725	2023-11-18	22419680	1265-6381	60			سلطان أبو هشيمة
726	2023-11-19	18997268	2134-7439	60			سلطان أبو هشيمة
727	2023-11-19	18997267	2195-4628	60			سلطان أبو هشيمة
728	2023-11-19	18997235	7831-8276	60			سلطان أبو هشيمة
729	2023-11-19	22418320	5317-8651	60			سلطان أبو هشيمة
730	2023-11-19	22419689	2467-7389	60			سلطان أبو هشيمة
731	2023-11-19	24602518	5619-9123	60			سلطان أبو هشيمة
732	2023-11-19	22418976	4965-4378	60			سلطان أبو هشيمة
733	2023-11-20	18997288	8217-8729	60			سلطان أبو هشيمة
734	2023-11-20	18997402	7261	20			سلطان أبو هشيمة
735	2023-11-20	18997412	1654-1854	60			سلطان أبو هشيمة
736	2023-11-21	18997300	6381-1265	60			سلطان أبو هشيمة
737	2023-11-21	18997435	9413-6519	60			سلطان أبو هشيمة
738	2023-11-21	5885331	2348-2134	60			سلطان أبو هشيمة
739	2023-11-21	18997437	9479-2983	60			سلطان أبو هشيمة
740	2023-11-22	18997508	9752-8721	60			سلطان أبو هشيمة
741	2023-11-23	18997558	5619-736	60			سلطان أبو هشيمة
742	2023-11-23	22419785	4628-2195	60			سلطان أبو هشيمة
743	2023-11-23	24599404	9645-8169	60			سلطان أبو هشيمة
744	2023-11-23	22418405	3412-7382	60			سلطان أبو هشيمة
745	2023-11-23	5442770	4613-4971	60			سلطان أبو هشيمة
746	2023-11-24	22419775	7482-5619	60			سلطان أبو هشيمة
747	2023-11-24	13197064	2596	20			سلطان أبو هشيمة
748	2023-11-24	22418482	5854	20			سلطان أبو هشيمة
749	2023-11-24	22419151	3671-8926	60			سلطان أبو هشيمة
750	2023-11-24	22418490	5391-8953	60			سلطان أبو هشيمة
751	2023-11-25	24602498	2789-9254	60			سلطان أبو هشيمة
752	2023-11-25	24601403	7462-2579	60			سلطان أبو هشيمة
753	2023-11-25	18997581	9674-8548	60			سلطان أبو هشيمة

مهندس اشراف الهيئة
م/محمود حسين

عن مكتب الاستشاري أ.د. حسن مهدي
م/ احمد عتيق النصار السريع
م/ محمد عبد الله النصار

مهندس الشركة
م/ محمد عبد الله النصار
م/ محمد عبد الله النصار
م/ محمد عبد الله النصار
م/ محمد عبد الله النصار



مكتب أ.د/حسن مهدي
للإستشارات الهندسية

مشروع إنشاء القطار الكهربائي (أكتوبر - أسوان)
القطاع الثاني (إبني مزار - منفلووط) من الكم 200+850 الى الكم 202+350 بطول 1.5 كم
تنفيذ : شركة أبوعجيلة للمقاولات العامة والتوريدات العمومية
عقد رقم (1229-2023-2024)



م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارثة	رسوم المرور والميزان (جنيه)	المحجر
798	2023-12-04	18996796	9271-1687	60			سلطان أبوهشيمة
799	2023-12-04	18996766	7381-7348	60			سلطان أبوهشيمة
800	2023-12-04	20440272	1658-6287	60			سلطان أبوهشيمة
801	2023-12-04	22417242	1658-6287	60			سلطان أبوهشيمة
802	2023-12-04	22417286	8945-5398	60			سلطان أبوهشيمة
803	2023-12-04	22416932	7894-7516	60			سلطان أبوهشيمة
804	2023-12-04	22417597	6438-8465	60			سلطان أبوهشيمة
805	2023-12-04	5441116	8132-6983	60			سلطان أبوهشيمة
806	2023-12-04	21277906	5943-9427	60			سلطان أبوهشيمة
807	2023-12-04	18996785	9154-3267	60			سلطان أبوهشيمة
808	2023-12-04	18996771	1265-6381	60			سلطان أبوهشيمة
809	2023-12-04	18996797	7489-5973	60			سلطان أبوهشيمة
810	2023-12-04	18996776	5973-7489	60			سلطان أبوهشيمة
811	2023-12-04	21277907	7942-1564	60			سلطان أبوهشيمة
812	2023-12-04	18996780	2479-8465	60			سلطان أبوهشيمة
813	2023-12-04	18996791	6713-4895	60			سلطان أبوهشيمة
814	2023-12-04	18996768	9362-6331	60			سلطان أبوهشيمة
815	2023-12-04	18996798	5428-9673	60			سلطان أبوهشيمة
816	2023-12-04	18996800	7142-8614	60			سلطان أبوهشيمة
817	2023-12-05	21277914	7698-6912	60			سلطان أبوهشيمة
818	2023-12-05	24602496	5782	20			سلطان أبوهشيمة
819	2023-12-05	22418410	7413-6925	60			سلطان أبوهشيمة
820	2023-12-05	24602434	4378-4965	60			سلطان أبوهشيمة
821	2023-12-05	22417600	5312-5341	60			سلطان أبوهشيمة
822	2023-12-05	18998461	5973-7489	60			سلطان أبوهشيمة
823	2023-12-05	18996769	9426-8629	60			سلطان أبوهشيمة
824	2023-12-05	18996763	6439-5724	60			سلطان أبوهشيمة
825	2023-12-05	21277928	3652-4791	60			سلطان أبوهشيمة
826	2023-12-05	21277911	3257-2756	60			سلطان أبوهشيمة
827	2023-12-05	21277920	9637-2564	60			سلطان أبوهشيمة
828	2023-12-05	21277933	7942-1564	60			سلطان أبوهشيمة
829	2023-12-05	18996772	4791-3652	60			سلطان أبوهشيمة
830	2023-12-05	21277910	9865-7316	60			سلطان أبوهشيمة
831	2023-12-05	21278506	3127-7435	60			سلطان أبوهشيمة
832	2023-12-05	21277929	1265-6381	60			سلطان أبوهشيمة
833	2023-12-05	21277925	9154-3267	60			سلطان أبوهشيمة
834	2023-12-05	21277934	2479-8465	60			سلطان أبوهشيمة
835	2023-12-05	21277926	1859-7163	60			سلطان أبوهشيمة
836	2023-12-05	21277932	8614-7142	60			سلطان أبوهشيمة
837	2023-12-05	21278505	2983-9479	60			سلطان أبوهشيمة
838	2023-12-05	21277918	2983-9479	60			سلطان أبوهشيمة
839	2023-12-05	21278964	9634-4351	60			سلطان أبوهشيمة
840	2023-12-05	21277917	6832-1592	60			سلطان أبوهشيمة
841	2023-12-05	18997446	3698-1853	60			سلطان أبوهشيمة

مهندس اشراف الهيئة
م/محمود حسين

عن مكتب الاستشاري أ.د/حسن مهدي
م/احمد عزب
م/احمد عزب



مكتب أ.د/حسن مهدي
للإستشارات الهندسية

مشروع إنشاء القطار الكهربائي (أكتوبر - أسوان)
القطاع الثاني (بني مزار - منفلووط) من الكم 200+850 الى الكم 202+350 بطول 1.5 كم
تنفيذ : شركة أبوعجيبة للمقاولات العامة والتوريدات العمومية
عقد رقم (2024-2023-1229)



م	التاريخ	رقم البون	رقم العربية	الكمية	رقم الكارثة	رسوم المرور والميزان (جنيه)	المحجر
930	2023-12-31	22417310	1658-6287	60			سلطان أبوهشيمة
931	2023-12-31	22417205	7238-5824	60			سلطان أبوهشيمة
932	2023-12-31	22417092	5619-736	60			سلطان أبوهشيمة
933	2023-12-31	22417358	7896	60			سلطان أبوهشيمة
934	2023-12-31	22417270	1363-7415	60			سلطان أبوهشيمة
935	2023-12-31	22417941	2819-6754	60			سلطان أبوهشيمة
936	2023-12-31	22417067	2756-3257	60			سلطان أبوهشيمة
937	2023-12-31	22417375	5398-8945	60			سلطان أبوهشيمة
938	2023-12-31	22417037	3652-4791	60			سلطان أبوهشيمة
939	2023-12-31	22417072	7214-1864	60			سلطان أبوهشيمة
940	2023-12-31	22417081	2195-2167	60			سلطان أبوهشيمة
941	2023-12-31	22417265	5128-9236	60			سلطان أبوهشيمة
942	2023-12-31	22417010	6731-4181	60			سلطان أبوهشيمة
				55280			
							الإجمالي

مهندس اشراف الهيئة
م/محمود حسين

عن مكتب الاستشاري أ.د/ حسن مهدي
م/ احمد عزب
الموقع
أ.د/ حسن مهدي
م/ احمد عزب
م/ محمود حسين



	مشروع القطار الكهربائي السريع	
	إستكمال أعمال الجسر الترابي لمسار القطار الكهربائي السريع الخط الثاني (الفيوم / بني سويف - أبو سمبل) (مرحلة الجسور والتأسيس والأساس) القطاع الثاني (بني مزار / منفلوط) تنفيذ شركة أبو عجيبة للمقاولات العامة والتوريدات العمومية حصر اجمال لكميات الردم	

الهيئة العامة للإشراف
مكتب أ.د/سن مهدي
للإشراف الهندسية

بند رقم (١٠٣) : أعمال تحميل وتوريد ونقل أتربة مطابقة للمواصفات وتشغيلها باستخدام آلات التوسية بسك لا يزيد عن ٥٠ سم حتى منسوب (2٠ متر) أسفل منسوب الغرمة و بسك لا يزيد عن ٢٥ سم اعلي من منسوب (2٠ متر) من منسوب الغرمة لاستكمال المنسوب التصميمي الخ

Station	Total Fill Area(m2)	Cum. Fill Vol(m3)	As Built vol.Fill	
			Fill VOL(m3)	Total.Qty
201+920.00	202.61	2026.07	2026.07	100122.28
201+940.00	227.66	6,328.78	4,302.71	
201+960.00	248.2	11,087.40	4,758.61	
201+980.00	274.47	16,314.06	5,226.67	
202+000.00	262.01	21,678.88	5,364.82	
202+020.00	243.79	26,736.89	5,058.01	
202+040.00	194.01	31,114.85	4,377.95	
202+060.00	362.48	36,679.73	5,564.88	
202+080.00	341.72	43,721.80	7,042.07	
202+100.00	314.56	50,284.61	6,562.81	
202+120.00	301.56	56,445.77	6,161.16	
202+140.00	0	59,461.36	3,015.59	
202+160.00	0	59,461.36	0.00	
202+180.00	0	59,461.36	0.00	
202+200.00	0	59,461.36	0.00	
202+220.00	317.97	62,641.01	3,179.66	
202+240.00	312.67	68,947.36	6,306.35	
202+260.00	320.6	75,280.03	6,332.66	
202+280.00	330.13	81,787.33	6,507.30	
202+300.00	335.88	88,447.44	6,660.11	
202+320.00	141.42	93,220.38	4,772.95	
202+340.00	132.47	95,959.23	2,738.85	
202+360.00	116.74	98,451.35	2492.11	
202+376.01	91.94	100,122.29	1,670.94	
اجمالي كميات الردم المصروفة سابقا				
اجمالي كميات الردم الفعلية الحالية بعد خصم سمك خرسانه الميول				100122.28
كمية خصم سمك خرسانه الميول				911

100122.28

0

100122-28

كمية خصم سمك خرسانه المبول

911

157A03-

عن الاستشاري أ.د حسن مهدي
ع / احمد عزاب
ع / محمود عزاب

Logo of the Italian Association of Agricultural Engineers (AIAA). The logo is a square with a blue border. Inside, the text "AIAA" is written in a stylized, bold, blue font. Below "AIAA", the word "ASSOCIAZIONE" is written in a smaller, blue font. At the bottom, the text "INGEGNERI AGRARI" is written in a blue font. The logo is partially obscured by a blue line.

	مشروع القطار الكهربائي السريع		 الهيئة العامة للغمرات بني مزار / منفطوط تحت إشراف مهندسين مصريين				
	إستكمال أعمال الجسر الترابي لمسار القطار الكهربائي السريع الخط الثاني (الفيوم / بني سويف - أبو سماعيل) (مرحلة الجسور والتأسيس والأساس) القطاع الثاني (بني مزار / منفطوط)						
	تنفيذ شركة أبو عجيبة للمقاولات العامة والتوريدات العمومية كميات حتي مستخلص جاري (١) جاري لعقد رقم (٢٠٢٥/٢٠٢٤/٢٠٩) بتاريخ ASBUILT 2024/4/1						
بند رقم (١-٣) : أعمال تحميل وتوريد ونقل أتربة مطابقة للمواصفات وتشغيلها باستخدام آلات التسوية بسمك لا يزيد عن ٥٠ سم حتى منسوب (-2 متر) أسفل منسوب القرمه و بسمك لايزيد عن ٢٥ سم اعلي من منسوب (-2 متر) من منسوب القرمه لاستكمال المنسوب التصميميالخ							
As Built vol.Fill							
Station	Total Fill Area(m2)	Cum. Fill Vol(m3)	FILL	Fill VOL(m3)	Total.Qty	Fill VOL(m3) ابتداء من ٢٠٢٤/٣/٢٢	اجمالي الكميات ابتداء من ٢٠٢٤/٣/٢٢
201+920.00	202.61	2026.07		2026.07	100122.28	582.22	9669.67
201+940.00	227.66	6,328.78		4,302.71		1,170.55	
201+960.00	248.2	11,087.40		4,758.61		1,162.28	
201+980.00	274.47	16,314.06		5,226.67		1,140.36	
202+000.00	262.01	21,678.88		5,364.82		1,142.87	
202+020.00	243.79	26,736.89		5,058.01		1,149.44	
202+040.00	194.01	31,114.85		4,377.95		1,134.32	
202+060.00	362.48	36,679.73		5,564.88		561.35	
202+080.00	341.72	43,721.80		7,042.07		0.00	
202+100.00	314.56	50,284.61		6,562.81		0.00	
202+120.00	301.56	56,445.77		6,161.16		0.00	
202+140.00	0	59,461.36		3,015.59		0.00	
202+160.00	0	59,461.36		0.00		0.00	
202+180.00	0	59,461.36		0.00		0.00	
202+200.00	0	59,461.36		0.00		0.00	
202+220.00	317.97	62,641.01		3,179.66		162.54	
202+240.00	312.67	68,947.36		6,306.35		325.06	
202+260.00	320.6	75,280.03		6,332.66		321.62	
202+280.00	330.13	81,787.33		6,507.30		322.02	
202+300.00	335.88	88,447.44		6,660.11		328.98	
202+320.00	141.42	93,220.38		4,772.95		166.06	
202+340.00	132.47	95,959.23		2,738.85		0.00	
202+360.00	116.74	98,451.35		2492.11		0	
202+376.01	91.94	100,122.29	1,670.94	0.00			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name [Signature]	Date	Time
Received by Employers Representative	Sign [Signature]	15-8-2022	2
UIR	C1 KP	C2 EW	C3 OT
	DD 15	MM 8	YY 22
	HH	MM	

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
From 200+876 To 202+376	200+876 TO 202+376	
	E=260126.0446 N=3137487.7094	E=260129.6912 N=3135991.0324
Inspection description[Disinfection Of Trees Cutting From st (200+876) to st (202+376)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
[Signature]	- Trees No. was checked only by xyz and under their own responsibility - you must follow specs and design dr

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	[Signature]	[Signature]					
Contractor QA/QC*	XYZ	[Signature]	15-8-2022		A		
	H.M.C	[Signature]	15-8-2022		A		
GARB**							
Employers Representative	Khaled ali	[Signature]	23/9/2024				

* Designer

** Alignment: Bridges: Culvert Only

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name [Signature]	Sign [Signature]	Date 15-8-2022
Received by Employers Representative		Time 2	
		UIR	
		C1 KP	C2 EW
		C3 OT	DD 15
		MM 8	YY 22
		HH	MM
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 202+376	
	E=260126.0446 N=3137487.7094	E=260129.6912 N=3135991.0324
Inspection description[Disinfection Of Trees Cutting From st (200+876) to st (202+376)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

تصوير وازالة الحما
بواسطة فريق العمل

- Trees No. was checked only by xyz and under their own responsibility
- you must follow specs and design dr

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	[Signature]	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	[Signature]	15-8-2022		A	
	H.M.C	[Signature]	15-8-2022		A	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024		AWC	

* Designer

** Alignment: Bridges: Culvert Only

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيل للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
	20-10-2022	3								
Received by Employers Representative			C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	20	10	22		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5						

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+686 E=260126.0446 E=260172.2356 N=3137487.7094 N=3136679.1711	
Inspection description/ تطهير بعد قطع الاشجار Disinfection of crops and trees cutting from st (200+876) to st (201+686)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
---	--

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA/QC*	XYZ		20-10-2022	14:30	A	
	H.M.C		20/10/2022	15:00	A	
GARB**						
Employers Representative						

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
	أديسن مهدي	أديسن مهدي	20-10-2022	4						
Received by Employers Representative			C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	20	10	22		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5						

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+686 TO 201+846	
	E=260172.2356 N=3136679.1711	E=260170.8362 N=3136519.1841
Inspection description/		
Disinfection of crops and trees cutting from st (201+686) to st (201+846) / تم تعقيم بعد قطع الأشجار		

منطقة قطع

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
أديسن مهدي	أديسن مهدي

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	أديسن مهدي	أديسن مهدي				
Contractor QA/QC*	XYZ	أديسن مهدي	20-10-2022	16:00	A	
	H.M.C	أديسن مهدي	20/10/2022	16:30		
GARB**						
Employers Representative						



المملكة العربية السعودية
الجمهورية العربية السورية



الجمهورية العربية السورية
الجمهورية العربية السورية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours
The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	Name	Sign	Date	Designer Company*	Time	RECEIVED BY EMPLOYERS REPRESENTATIVE RECEIVED BY CONTRACTOR ISSUED BY CONTRACTOR NAME SIGN DATE DESIGNER COMPANY* TIME											
						CODE-1 CODE-2 CODE-3 CODE-4 CODE-5											

EXPLANATION OF WORK TO BE INSPECTED			
Area	Element	Item	Inspection description
From 200+876 To 202+376	201+966 TO 202+376		Disinfection of crops and trees cutting from st (201+966) to st (202+376)

INSPECTION DETAILS			
Planned Inspection Date		Planned Inspection Time	
COMPLIANCE EVIDENCE Must be included as appropriate			
☐ Checklist Attached ☐ Test Results Attached ☐ Calibration Attached ☐ Other as indicated	☐ MS Reference ☐ MS Reference		

Comments by: (GARBB SURVEY CONSULTANT (XYZ))	Comments by: General consultant (systa)
--	---

INSPECTION RESULT			
Organisation Name Sign Date Time Status Approval Please Tick if Not Attend	Contractor Engineer Name Sign Date Time Status Approval Please Tick if Not Attend	Contractor XYZ H.M.C. QA/QC* Sign Date Time Status Approval Please Tick if Not Attend	Employers Representative Name Sign Date Time Status Approval Please Tick if Not Attend

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)					
Issued by Contractor	Name	Sign	Date					
			25-10-2022					
Received by Employers Representative	Name	Sign	Time					
			6					
C1		C2	C3	DD	MM	YY	HH	MM
KP		EW	OT	25	10	22		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+466 TO 201+666	
	E=260165.8013	E=260172.0505
	N=3136899.0593	N=3136699.1703
Inspection description/		
As-Built for rock surface from st (201+466) to st (201+666)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)


	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C - you must follow spec and geo-technical report
--	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer					A-AWC-R	
Contractor QA/QC*	XYZ		25-10-2022	13:00	A	
	H.M.C		25/10/2022	13:00	A	
GARB**						
Employers Representative	Khaled ali		23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
			29-10-2022	7						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	29	10	28		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+466	
	E=260126.0446	E=260165.8013
	N=3137487.7094	N=3136899.0593
Inspection description[الرفع المساحي + المعاينة للطرح المقصود (المسوح الأول) As-Built for rock surface from st (200+876) to st (201+466)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate






Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. (xyz))

Comments by: General consultant (systra)

	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C. - you must follow spec and design drawings.
---	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer					A-AWC-R	
Contractor QA/QC*	XYZ		29-10-2022	12:00	A	
	H.M.C		29/10/2022		A	
GARB**						
Employers Representative	Khaleed ali		23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	مكتب أديسن مهدي للإستشارات الهندسية		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
			2-11-2022	8						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	2	11	22		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+036 TO 201+086	
	E=260137.1186 N=3137328.0971	E=260140.5793 N=3137278.217
<u>Inspection description/</u> As-Built for rock surface from st (201+036) to st (201+086)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
2/11/2022	

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

مكتب أديسن مهدي للإستشارات الهندسية

- Levels and coordinates were checked only by xyz and under their own responsibility
 - This work was inspected only by xyz and H.M.C
 - you must follow spec and geo-technical report

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	مكتب أديسن مهدي للإستشارات الهندسية	مكتب أديسن مهدي للإستشارات الهندسية			A-AWC-R	
Contractor QA/QC*	XYZ	مكتب أديسن مهدي للإستشارات الهندسية	2-11-2022	17:30	A	
	H.M.C	مكتب أديسن مهدي للإستشارات الهندسية	2/11/2022	13:30	A	
GARB**						
Employers Representative	Khaled ali	مكتب أديسن مهدي للإستشارات الهندسية	23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عبيدة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
	محمد أبو بكر		6-11-2022	10						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	6	11	2022		
CODE-1		CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+156 TO 201+246	
	E=260145.4242 N=3137208.3848	E=260151.6535 N=3137118.6007
<u>Inspection description:</u> As-Built for rock surface from st (201+156) to st (201+246)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))

Comments by: General consultant (systra)

- Levels and Coordinates were checked only by xyz and under their own responsibility.

- This work was inspected only by xyz and H.M.C.

you must follow specs and geo-technical report

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	محمد أبو بكر				A-AWC-R	
Contractor QA\QC*	XYZ		6-11-2022	14:00	A	
	H.M.C		6/11/2022	14:30	A	
GARB**						
Employers Representative	Khaled Ali		23/11/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أ.م.م. مهدي أمان		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	Time							
	أ.م.م. مهدي أمان	أ.م.م. مهدي أمان	24-11-2022	12							
Received by Employers Representative	Sign	Date	Time	C1	C2	C3	DO	MM	YY	HH	MM
				KP	EW	OT	24	11	22		

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
From 200+876 To 202+376	201+076 TO 201+156	
	E=260139.8871 N=3137288.193	E=260145.4242 N=3137208.3848
<u>Inspection description</u> As-Built for rock surface from st (201+076) to st (201+156)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. xyz)	Comments by: General consultant (systra)
أ.م.م. مهدي أمان	- Levels and Coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and you must follow specs and geo-technical report

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	أ.م.م. مهدي أمان	أ.م.م. مهدي أمان					
Contractor QA/QC*	XYZ	أ.م.م. مهدي أمان	24-11-2022	12:00	A		
	H.M.C	أ.م.م. مهدي أمان	24/11/2022	12:30	A		
GARB**							
Employers Representative	Khaled di	أ.م.م. مهدي أمان	23/9/2024				

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name أبو عجلة	Sign أبو عجلة	Date 7-12-2022																
Received by Employers Representative			Time 13																
		UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>EW</td> <td>OT</td> <td>7</td> <td>12</td> <td>23</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	EW	OT	7	12	23		
C1	C2	C3	DD	MM	YY	HH	MM												
KP	EW	OT	7	12	23														
CODE-1	CODE-2	CODE-3	CODE-4																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+286 TO 201+386	
	E=260154.422 N=3137078.6966	E=260161.1582 N=3136978.9239
<u>Inspection description</u> As-Built for rock surface from st (201+286) to st (201+386)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT: (xyz))	Comments by: General consultant (systra)
	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C. - you must follow specs and geo-technical report

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	أبو عجلة	أبو عجلة					
Contractor QA/QC*	XYZ	أبو عجلة	7-12-2022	14:00	A		
	H.M.C	أبو عجلة	7/12/2022	14:30	A		
GARB**							
Employers Representative	Khaled ali	أبو عجلة	23/9/2024				

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR ,Hassan Mahdy (H.M.C)
Issued by Contractor	Name Sign 13-12-2022	Date	Time 14
Received by Employers Representative	UIR	C1 KP	C2 EW
		C3 OT	DD 13
		MM 12	YY 22
		HH	MM
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+386 TO 201+426	
	E=260161.1582 N=3136978.9239	E=260163.6041 N=3136938.9988
Inspection description: الرفع المساحي + معاينة سطح صخره (المستوي الثالث) As-Built for rock surface from st (201+386) to st (201+426)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
	- Levels and coordinates were checked only by systra and under their own responsibility - This work was inspected only by systra and H.M.C - you must follow specs and geo-technical report

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer							
Contractor QA/QC*	XYZ		13-12-2022	12:16	A		
	H.M.C		13/12/2022	12:17	A		
GARB**							
Employers Representative	Khaled al.		23/12/2022				

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)					
Issued by Contractor	Name	Sign	Date	Time					
	13-12-2022	16							
Received by Employers Representative	C1	C2	C3	DD	MM	YY	HH	MM	
									13
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5	

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+036	
	E=260126.0446 N=3137487.7094	E=260137.1186 N=3137328.0971
Inspection description: As-Built for rock surface from st (200+876) to st (201+036)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSANTANT.(xyz))	Comments by: General consultant (systra)
	- Levels and coordinates were checked only by xyz and under their own responsibility - This work was inspected only by xyz and H.M.C - you must follow spec and geotechnical rep.

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer					A-AWC-R	
Contractor QA/QC*	XYZ		13-12-2022	13:30	A	
	H.M.C		13/12/2022	14:00	A	
GARB**						
Employers Representative	Phaked ali		23/12/2022		A	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR ,Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	Time						
			2023-1-3	17						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	EW	OT	3	1	23		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED


Area	Element		Item
From 200+876 To 202+376	200+876 TO 201+666		
	E=260126.0446	E=260172.0505	
	N=3137487.7094	N=3136699.1703	
Inspection description/			
As-Built for cut from st (200+876) to st (201+666)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
2023/1/3	

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
	- Levels and coordinates were checked only by XYZ and under their own responsibility - you must follow specs and design drawings

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor	XYZ		3-1-2023	19:00	A	
QA/QC*	H.M.C		3/1/2023	19:00		
GARB**						
Employers Representative	Khaled ali		23/9/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name  Sign 	Date	Time
Received by Employers Representative	UIR	13-6-2023	18
		C1 KP	C2 EW
		C3 OT	DD 13
		MM 6	YY 23
		HH	MM
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+660 E=260126.0446 N=3137487.7094	E=260171.9793 N=3136705.1798
Inspection description		
As-Built for cut from st (200+876) to st (201+660)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time



Planned Inspection Date	Planned Inspection Time
12/6/2023	

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)


- Levels and coordinates were checked only by xyz and under their own responsibility

- you must follow spec and design dwg.

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA/QC*	XYZ		13-6-2023	9:00	A	
	H.M.C		13/6/2023			
GARB**						
Employers Representative	Khaled Ali		23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله والمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name Sign 24-8-2023	Date	Time 19
Received by Employers Representative	Sign 23	Time	

CODE -1	CODE -2	CODE -3	CODE -4	CODE -5
---------	---------	---------	---------	---------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	200+876 TO 201+840 E=260126.0446 N=3137487.7094	E=260170.9813 N=3136525.1923
Inspection description: As-Built for cut from st (200+876) to st (201+840)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
24/8/2023	

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

as built
قطاع الضلع
القطاع الذي

- Levels and coordinates were checked only by xyz and under their own responsibility
- you must follow specs and design dwg.

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	محمد بن عبد الله	محمد بن عبد الله			A-AWC-R	
Contractor QA/QC*	XYZ	محمد بن عبد الله	26-8-2023	10:00	A	
	H.M.C	محمد بن عبد الله	26/8/2023	10:15	A	
GARB**						
Employers Representative	Khaled ali	محمد بن عبد الله	23/8/2023		A	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name وليد فاضل Sign [Signature]	Date	9-11-2023
Received by Employers Representative	UIR	REQ.NUM	20
		C1 KP	C2 SU
		C3 OT	DD 9
		MM 11	YY 23
		HH	MM
CODE-1		CODE-2	CODE-3
		CODE-4	CODE-5

EXPLANATION OF WORK TO BE INSPECTED


Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description/ تشييد قاع إحلال from st (202+220) to st (202+300)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))	Comments by: General consultant (systra)
	- levels and coordinates were checked only by xyz and under their own responsibility - No objection according to the attached reports and lab. results.

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد فاضل	[Signature]	19-11-2023	10:00	(A)		
Contractor QA/QC*	XYZ	[Signature]	9/11/2023	11:00	A		
GARB**							
Employers Representative	Khaled ali	[Signature]	23/9/2024				

* Designer

** Alignment: Bridges; Culvert Only

UNIVERSAL INSPECTION REQUEST



مكتب أ.د. حسن مهدي
للإشراف الهندسية



الهيئة العامة للغذاء والدواء
Saudi Food & Drug Authority



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name وليد محمد محمود	Date	18-11-2023
Received by Employers Representative	Sign [Signature]	REQ. NUM	21
UIR	C1 KP	C2 SU	C3 QT
	DD 18	MM 11	YY 23
CODE-1	CODE-2	CODE-3	CODE-4
	CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+280 TO 202+300	
	E=260141.2938 N=3136086.3373	E=260139.0278 N=3136066.4661
Inspection description:		
من (10-متر) تسليم طبقة (10-متر) from st (202+280) to st (202+300)		

INSPECTION DETAILS The Following will be ready at the Planned inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))

مكتب أ.د. حسن مهدي
للإشراف الهندسية

Comments by: General consultant (systra)

- No objection, according to the attached reports and lab. results.
- you must follow specs and design dwg.

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمد محمود	[Signature]	18/11/2023	10:10	A	يقم صيانة
Contractor QA/QC*	XYZ	[Signature]	18-11-2023	13:30	A	العمل قبل
	H.M.C	محمود محمد	18/11/2023	11:30	AWC	العمل قبل
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عبيدة للمقاولات 2023	Designer Company*	DR ,Hassan Mahdy (H.M.C)
Issued by Contractor	Name Signature Signature	Date	REQ. NUM
Received by Employers Representative	Signature	20-11-2023	22
UIR	C1 C2 C3 DD MM YY HH MM		
	KP SU OT 21 11 23 2 30		
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+000 TO 202+120	
	E=260164.6561 N=3136365.3242	E=260156.5571 N=3136245.6007
Inspection description/		
تسليم قاع إحلال from st (202+000) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSANTANT (xyz))	Comments by: General consultant (systra)
تسليم قاع إحلال	- Levels and coordinates were checked only by xyz and under their own responsibility
تسليم قاع إحلال	- This work was checked only by xyz and H.M.
	- you must follow speed and design drawing and geo-technical report

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	Signature	Signature			A-AWC-R	
Contractor QA/QC*	XYZ	Signature	21-11-2023	3:15	(A)	
	H.M.C	Signature	21/11/2023	3:00	A	
GARB**						
Employers Representative	Khaleel ali	Signature	23/11/2024		Any	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown:

Contractor Company	أبو عجمية للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name:  Sign: 	Date	REQ. NUM						
Received by Employers Representative	UIR	21-11-2023	23						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT	22	11	23		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED


Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description/		
منطقة ردم منسوب (-9.5) متر from st (202+220) to st (202+300)		



INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
	- No objection, according to the attached reports and Lab. results. - you must follow specs and design drawings

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد محمد						
Contractor QA/QC*	XYZ		22-11-2023	3:45	(A)		
	H.M.C		22/11/2023	11:00	A		
GARB**							
Employers Representative	Fhaled ali		23/11/2023				

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإشراف الهندسية



الهيئة العامة للإشراف
على الطرق



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	شركة المقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name	Sign	Date	REQ.NUM
	أحمد محمد	أحمد محمد	25-11-2023	24
Received by Employers Representative	شركة المقاولات العامة		UIR	
			C1 C2 C3 DO MM YY HH MM	
			KP SU OT 25 11 23	

CODE-1 CODE-2 CODE-3 CODE-4 CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+000 TO 202+020	
	E=260164.6561 E=260163.5058	
	N=3136365.3242 N=3136345.3573	
Inspection description/		
منطقة ردم منسوب (13) متر from st (202+000) to st (202+020)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (systa))



Comments by: General consultant (systa)

- No objection, according to the attached reports and lab. results.
- you must follow specs and design drawings

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	أحمد محمد	أحمد محمد			A-AWC-R	
Contractor QA/QC*	XYZ	أحمد محمد	25-11-2023	12:30	(A)	
	H.M.C	أحمد محمد	25/11/2023	11:00	A	
GARB**						
Employers Representative	Khaled ali	أحمد محمد	23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name 	Sign 	Date 28-11-2023
Received by Employers Representative	UIR	C1 KP	C2 SU
		C3 OT	DD 28
		MM 11	YY 23
		HH 11	MM 00

CODE-1

CODE-2-109

CODE-3

CODE-4

CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300 E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description from st (202+220) to st (202+300) طبقة ردم منسوب (-9) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time


Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)



- No objection, according to the attached reports and lab. results
- you must follow specs and design dng.

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمد				A-AWC-R	
Contractor QA/QC*	XYZ	عبد الله الدلاوي	28/11/2023	3:30	A	
	H.M.C	عبد الله الدلاوي	28/11/2023	11:00	A	
GARB**						
Employers Representative	Khaled ali		23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	Name		Sign	Designer Company*	DR .Hassan Mahdy (H.M.C)				
Issued by Contractor	29-11-2023		REQ.NUM		26				
Received by Employers Representative	C1		C2	C3	DO	MM	YY	HH	MM
	KP		SU	OT	29	11	23		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5	

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+060 TO 202+080		
	E=260160.9658 N=3136305.4382	E=260159.576 N=3136285.4865	
Inspection description[			
from st (202+060) to st (202+080) طبقة ردم منسوب (-11) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))	Comments by: General consultant (systra)
 المهندس خالد علي - الهندس العام	- No objection, according to the attached reports and lab. results. - you must follow specs and design draw

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	Waleed Elmaghrabi	Waleed Elmaghrabi				
Contractor QA/QC*	XYZ	Khaled Ali	29-11-2023	11:15	(A)	
	H.M.C	Khaled Ali	29-11-2023	12:45	A	
GARB**						
Employers Representative	Khaled Ali	Khaled Ali	29/11/2023		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)					
Issued by Contractor	Name وليد محمود محمد	Date	29-11-2023					
Received by Employers Representative	Sign [Signature]	REQ.NUM	27					
UIR	C1 KP	C2 SU	C3 OT	DD 29	MM 11	YY 23	HH	MM
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5				

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+080 TO 202+120 E=260159.576 N=3136285.4865	E=260156.5571 N=3136245.6007
Inspection description: منطقة ردم منسوب (10.5) متر from st (202+080) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSANTANT.(xyz))

Comments by: General consultant (systra)

-No objection, according to the attached reports and lab. results
-you must follow specs and design dwg

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمود محمد	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	[Signature]	29-11-2023	11:30	(A)	
	H.M.C	[Signature]	29-11-2023	12:30	A11	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024			

UNIVERSAL INSPECTION REQUEST



مكتب أ.د/حسن مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
SYSTRA



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	157137 أبو عجلة للتقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name وليد محمد Sign [Signature] Date 30-11-2023	REQ. NUM	28
Received by Employers Representative	UIR	C1 KP	C2 SU
		C3 OT	DD 30
		MM 11	YY 23
		HH	MM

CODE-1

CODE-2

CODE-3

CODE-4

CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+000 TO 202+020 E=260164.6561 N=3136365.3242	E=260163.5058 N=3136345.3573
Inspection description: ردم طبقة ردم منسوب (-12.5) متر from st (202+000) to st (202+020)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (XYZ)) [Signature] [Stamp]	Comments by: General consultant (systra) - No objection, according to the attached reports and lab. results. - you must follow spec and design draw
---	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمد	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	[Signature]	30-11-2023	13:00	A	
	H.M.C	[Signature]	30/11/2023	12:30pm	A	
GARB**						
Employers Representative	Khaled Ali	[Signature]	23/9/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 57537	Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name [Signature]	Date	2-12-2023																
Received by Employers Representative	Sign [Signature]	REQ.NUM	29																
UIR		<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>2</td> <td>12</td> <td>23</td> <td></td> <td></td> </tr> </table>		C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	2	12	23		
C1	C2	C3	DD	MM	YY	HH	MM												
KP	SU	OT	2	12	23														
CODE-1	CODE-2	CODE-3	CODE-4																
CODE-5	CODE-6	CODE-7	CODE-8																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description[from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (-8.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (sysra)

تم استلام نتائج الاختبار
من مختبر اختبار التربة - أ.أ.أ.أ.

- No objection, according to the attached reports and lab. results.
- you must follow specs and design dr

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمد	[Signature]				
Contractor QA/QC*	XYZ	عبد الرحمن الوالد	21/12/2023	3:15	A	
	H.M.C	أحمد مصطفى	21/12/23	3:00	AWC	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/12/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name 157537 Sign 	Date	REQ.NUM 30															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>23</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			23		
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT			23													

CODE-1

CODE-2

CODE-3

CODE-4

CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+100 E=260160.9658 N=3136305.4382	E=260158.1064 N=3136265.5406
Inspection description منطقة ردم مسوب (-10.5) متر from st (202+060) to st (202+100)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz)) 	Comments by: General consultant (systra) - No objection, according to the attached reports and lab. results. - you must follow specs and design d.
---	--

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA\QC*	XYZ		3-12-2023	4:15	(A)	
	H.M.C		3/12/2023	2:30 PM	AWC	
GARB**						
Employers Representative	Khaled ali		28/9/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown.

Contractor Company	شركة البترول العالمية		Designer Company*	DR. Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	وليد عيسى	Date	5-12-2023							
	Sign	وليد عيسى	REQ. NUM	31							
Received by Employers Representative	Signature	Sign	Date	C1	C2	C3	DD	MM	YY	HH	MM
				KP	SU	OT				23	
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147	E=260139.0278
	N=3136146.003	N=3136066.4661
Inspection description/		
من تسليم طبقة ردم منسوب (8-متر) from st (202+220) to st (202+300)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT (-xyz))

مكتب أدريس مهدي
للإستشارات الهندسية

Comments by: General consultant (systra)

- No objection, according to the attached reports and lab. results.
- you must follow specs and design dwg.

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد عيسى	وليد عيسى				
Contractor QA/QC*	XYZ	محمد إدريس	6-12-2023	10:30	(A)	
	H.M.C	شعوبه الخبي	5/12/2023	4:15Pm	AWC	
GARB**						
Employers Representative	Khaleel ali	Khaleel ali	23/9/2024		AWC	




RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours The Work described below will be complete and ready for inspection at planned time shown										
Contractor Company	أبو عجيبة للمقاولات العامة				Designer Company*	DR .Hassan Mahdy (H.M.C)				
Issued by Contractor	Name	Sign	Date	REQ. NUM						
	وليد زكريا	وليد زكريا	7-12-2023	32						
Received by Employers Representative	UIR		C1	C2	C3	DD	MM	YY	HH	MM
			XP	SU	OT			23		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED			
Area	Element		Item
From 200+876 To 202+376	200+876 TO 202+120		
	E=260160.9658	E=260156.5571	
	N=3136305.4382	N=3136245.6007	
<u>Inspection description/</u> from st (202+060) to st (202+120) طبقة ردم ملمسوب (10-) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time	
Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as Indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz)) 	Comments by: General consultant (systra) -No objection, according to the attached reports and lab. results. -you must follow specs and design drug
---	--

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد زكريا	وليد زكريا	7-12-2023	1:30	(A)		
	XYZ	أحمد محمد					
Contractor QA/QC*	H.M.C	محمود علي	7/12/2023	12:15	A		
GARB**							
Employers Representative	Khaled ali	Khaled ali	23/12/2024	AWC			



Page 1 of 4

UNIVERSAL INSPECTION REQUEST



مكتب أ.إ.إ. من مهاب
للإستشارات الهندسية



شركة أ.إ.إ. من مهاب
للإستشارات الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR. Hassan Mahdy (H.M.C)
Issued by Contractor	Name	Sign	Date	REQ.NUM
	د. محمد د. محمد	د. محمد د. محمد	16-12-2023	36
Received by Employers Representative	UIR	G1 KP	G2 SU	G3 OT
				23
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description: تسليم طبقة ردم مسلوب (7-متر) from st (202+220) to st (202+300)		

INSPECTION DETAILS The following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARIB SURVEY CONSULTANT (xyz))

تسليم الطبقة الردم مسلوب (7-متر) من st (202+220) إلى st (202+300)

Comments by: General consultant (systra)

- No objection, according to the attached reports and lab. results.
- you must follow specs and design dwg.

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	د. محمد د. محمد	د. محمد د. محمد				
Contractor QA/QC*	XYZ	عبد الرحمن العرابي	16-12-2023	3:15	A	
	H.M.C	م. محمد د. محمد	16/12/2023	3:00	A	
GARB**						
Employers Representative	Khaled ali	د. محمد د. محمد	28/12/2024		Awc	



UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للطرق
والبنية التحتية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR. Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ. NUM						
	وليد فلاح	وليد فلاح	17-12-2023	37						
Received by Employers Representative		UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT				23	
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007	
Inspection description:			
من (202+060) to st (202+120) طبقة ردم ملسوب (8.5) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by (GARB SURVEY CONSULTANT xyz)

Comments by: General consultant (systra)

استاذ المهندس
مستوى التفتيش الكافي إلى الحد
-315

-No objection, according to the attached reports and lab. results.
-you must follow specs and design dwg

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد فلاح	وليد فلاح			A-AWC-R	
Contractor QA/QC*	XYZ		17-12-2023	13:00	A	
	H.M.C		17-12-2023	11:00	Amc	
GARB**						
Employers Representative	Khaled ali		20/12/24		Amc	



UNIVERSAL INSPECTION REQUEST



مكتب المدعى
للإشراف الهندسية



المكتب الهندسي
للإشراف الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company			Designer Company*	DR. Hassan Mahdy (H.M.C)																
Issued by Contractor	Name	Sign	Date	REQ. NUM																
			19-12-2023	38																
Received by Employers Representative			<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>AP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>YY</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	AP	SU	OT			YY			
C1	C2	C3	DD	MM	YY	HH	MM													
AP	SU	OT			YY															
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+576	202+220 TO 202+300	
	E=260147.5147	E=260139.0278
	N=3136146.003	N=3136066.4661
Inspection description (from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (7.0) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time


Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	M5 Reference	

Comments by: (GARB SURVEY CONSULTANT: XYZ)

Comments by: General consultant (systra)

 تم فحص المخطط ووافق عليه المهندس مسؤول قسم التخطيط الهندسي - المكتب الهندسي	- No objection, according to the attached reports and lab. results. - you must follow specs and design drawings
--	---

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer					A-AWC-R	
Contractor QA/QC*	XYZ		19-12-2023	3:30	A	
	H.M.C		19-12-2023	11:30	A	
GARB**						
Employers Representative	Khaled ali		23/9/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)				
Issued by Contractor	Name	Sign	Date				
	وليد محمود محمد		20-12-2023				
Received by Employers Representative		REQ.NUM	39				
C1	C2	C3	DD	MM	YY	HH	MM
	KP	SU	OT			23	

CODE-1	CODE-2	CODE-3	CODE-4	CODE-5
--------	--------	--------	--------	--------

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description/		
من (8-) متر from st (202+060) to st (202+120) طبقة ردم منسوب		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

- No objection, according to the attached reports and Lab. results.
- You must follow specs and design draw

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمود محمد				A-AWC-R	
Contractor QA/QC*	XYZ		20-12-2023	3:40	A	
	H.M.C		20-12-2023	1:45	A	
GARB**						
Employers Representative	Khaled ali		23/9/2024		A	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name Sign 21-12-2023	Date	REQ.NUM 40															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>21</td> <td>12</td> <td>23</td> <td>11</td> <td>30</td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	21	12	23	11	30
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT	21	12	23	11	30											
CODE-1	CODE-2	CODE-3	CODE-4															
CODE-5	CODE-6	CODE-7	CODE-8															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description: from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (6-متر)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT: xyz)	Comments by: General consultant (systra)
	- No objection, according to the attached reports and lab. results. - you must follow specs and design d.

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمد	وليد محمد				
Contractor QA/QC*	XYZ	عبد الرحمن العرابي	21-12-2023	11:00	A	
	H.M.C	محمد بن عبد الله العرابي	21/12/23	11:30	A	
GARB**						
Employers Representative	Khaled ali		23/12/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب المهندس
للإشراف الهندسية



الهيئة العامة للطرق
والمواصلات



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name وليد محمود محمد	Sign 	Date 23-12-2023	REQ.NUM 41																
Received by Employers Representative			<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>23</td> <td></td> <td></td> </tr> </table>		C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			23		
C1	C2	C3	DD	MM	YY	HH	MM													
KP	SU	OT			23															
CODE-1		CODE-2	CODE-3	CODE-4	CODE-5															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
<u>Inspection description</u> from st (202+220) to st (202+300) تسليم طبقة ردم ملسوب (-5.5) متر		

INSPECTION DETAILS The following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
	- No objection, according to the attached reports and lab. results. - you must follow specs and design dr.

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود محمد					
Contractor QA/QC*	XYZ		23/12/2023	1:00	A	
	H.M.C		23/12/2023	12:00	A	
GARB**						
Employers Representative	Khaled ali		23/12/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أراضين مهدي
للإستشارات الهندسية



الهيئة العامة للإعتماد
والتأهيل



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	المشروعات العامة		Designer Company*	DR. Hassan Mahdy (H.M.C)																
Issued by Contractor	Name وليد محمود	Sign [Signature]	Date 25-12-2023	REQ. NUM 44																
Received by Employers Representative	[Signature]		<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DO</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>23</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DO	MM	YY	HH	MM	KP	SU	OT			23			
C1	C2	C3	DO	MM	YY	HH	MM													
KP	SU	OT			23															
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description:		
من 200+876 إلى 202+376 طبقاً من st (202+060) إلى st (202+120)		

INSPECTION DETAILS The following will be ready at the Planned inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT. xyz) Comments by: General consultant (systra)

	- No objection, according to the attached reports and lab. results. - you must follow specs and design data
--	--

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمود	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	[Signature]	25-12-2023	4:13	A	
	H.M.C	[Signature]	25-12-2023	4:10	AWC	
GARB**						
Employers Representative	Khaled Ali	[Signature]	23/9/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أديسن مهندسي
الاستشارات الهندسية



الهيئة العامة للطرق
والمواصلات



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أ.م. عجيلان للاستشارات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	وليد محمود محمد	[Signature]	28-12-2023	46						
Received by Employers Representative		[Signature]	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT				23	

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
From 200+876 To 202+376	201+980 E=260165.727 N=3136385.3	
Inspection description: منطقة ردم منسوب (-14) متر from st (201+980)		

INSPECTION DETAILS The Following will be ready at the Planned inspection Time	
Planned inspection Date	Planned inspection Time


COMPLIANCE EVIDENCE Must be included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))	Comments by: General consultant (systra)
[Signature]	- No objection, according to the attached reports and lab. results. you must follow specs and design drawings

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود محمد	[Signature]				
Contractor QA/QC*	XYZ	[Signature]	28-12-2023	12:00	A	[Signature]
	H.M.C	[Signature]	28-12-2023	11:00		
GARB**						
Employers Representative	Khaled Ali	[Signature]	23/9/2024		ANC	

UNIVERSAL
INSPECTION
REQUEST








RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours
The Work described below will be complete and ready for inspection at planned time shown

Contractor Company

Name

Designer Company*

Date

DR. Hassan Mahdy
(H.M.C)

28-12-2023

Issued by Contractor

Sign

REQ.NUM

47

Received by Employers Representative

Sign

C-1 C-2 C-3 DO MM YY HH MM

KP SU OT 23

EXPLANATION OF WORK TO BE INSPECTED

Area

Element

Item

From 200+876 To 202+376

202+060 TO 202+120
E=260160.9658
N=3136305.4382

E=260156.5571
N=3136245.6007

Inspection description:
from st (202+060) to st (202+120) طبقة ردم منسوب (-6.5) متر

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date

Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐

Test Results Attached ☐

Calibration Attached ☐

Other as indicated ☐

Drawing Reference

ITP Reference

MS Reference

Comments by: (GARB SURVEY CONSULTANT: xyz)

Comments by: General consultant (systra)

No objection, according to the attached reports and lab. results.

you must follow specs and design dmy.

INSPECTION RESULT

Approval Status

Please Tick if Not Attend

Organisation

Name

Sign

Date

Time

A-AWC-R

Contractor Engineer

XYZ

H.M.C

28-12-2023

1:00

A

GARB**

Employers Representative

23/9/2024

Ame



UNIVERSAL INSPECTION REQUEST



مكتب المهندس
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	157533 مكتب المهندس للإستشارات الهندسية		Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name وليد محجور محمد	Sign 	Date 2-1-2024	REQ.NUM 48																
Received by Employers Representative	 UIR		<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			24			
C1	C2	C3	DD	MM	YY	HH	MM													
KP	SU	OT			24															
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
<u>Inspection description/</u> from st (202+220) to st (202+300) تسليم طبقة ردم مسسوب (-4.5) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))

Comments by: General consultant (systra)

تم تسليم طبقة ردم مسسوب (-4.5) متر
مستوفى القياسات التسريبية - الفحص الذي

-No objection, according to the attached reports and lab. results.
-you must follow specs and design draw

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محجور محمد					
Contractor QA/QC*	XYZ H.M.C	عبدالله بن عبدالمجيد محمود بن محمد	2-1-2024 2-1-2024	10:40 10:30	A A	
GARB**						
Employers Representative	Khaled ali		23/1/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company			Designer Company*	DR. Hassan Mahdy (H.M.C)																
Issued by Contractor	Name	Sign	Date	REQ. NUM																
			2-1-2024	49																
Received by Employers Representative			UIR																	
			<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			24			
C1	C2	C3	DD	MM	YY	HH	MM													
KP	SU	OT			24															
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description		
from st (202+060) to st (202+120) طبقة ردم منسوب (-6) متر		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARBSURVEYCONSANTANT.(xyz))	Comments by: General consultant (systra)
	- No objection, according to the attached reports and lab. results - you must follow specs and design drawings

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time			
Contractor Engineer	وليد محمد						
Contractor QA/QC*	XYZ		2-1-2024	11:40	A		
	H.M.C		2-1-2024	11:50	AWC		
GARB**							
Employers Representative	Khaled ali		2/1/2024				

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company			Designer Company*	DR .Hassan Mahdy (H.M.C)																
Issued by Contractor	Name	Sign	Date	REQ NUM																
			2-1-2024	50																
Received by Employers Representative			UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			24		
C1	C2	C3	DD	MM	YY	HH	MM													
KP	SU	OT			24															
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5																

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+960 TO 202+000		
	E=260166.717	E=260164.6561	
	N=3136405.271	N=3136365.1247	
<u>Inspection description</u> from st (201+960) to st (202+000) طبقة ردم منسوب (-13.5) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. (xyz))

Comments by: General consultant (systra)

-No objection, according to the attached reports and lab. results.

-you must follow specs and design dr

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA\QC*	XYZ		2-1-2024	11:15	A	
	H.M.C		2-1-2024	11:00	AUC	
GARB**						
Employers Representative	Khaled ali		23/9/2024		AUC	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



المهنة العامة الإستشارية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	[Signature]		6-1-2024	51						
Received by Employers Representative	[Signature]	UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT				20	
CODE-1		CODE-2	CODE-3	CODE-4		CODE-5				

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+960 TO 202+000		
	E=260166.717 N=3136405.271	E=260164.6561 N=3136365.3242	
<u>Inspection description</u> from st (201+960) to st (202+000) طلبة ردم منسوب (-13) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: [GARB SURVEY CONSATANT. (xyz)]	Comments by: General consultant (systra)
[Signature]	- No objection, according to the attached reports and Lab. results.
[Signature]	- you must follow specs and design drag

INSPECTION RESULT

					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمدي	[Signature]				
Contractor QA/QC*	XYZ	عبد الرحمن العرابي	6-1-2024	4:20	A	[Signature]
	H.M.C	محمود عولمة	6/1/2023	4:15	AWC	
GARB**						
Employers Representative	Khaled ali	[Signature]	29/9/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للاستشارات الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	[Signature]		6-1-2024	52						
Received by Employers Representative	[Stamp]	UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT				24	
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+060 TO 202+120		
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007	
Inspection description/			
from st (202+060) to st (202+120) طبقة ردم منسوب (5.5) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))

تم الاستعراض وفقاً للمواصفات
المرفقة مع التقرير.

Comments by: General consultant (systra)

- No objection, according to the attached reports and lab results.
- you must follow spec and design

INSPECTION RESULT

					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	علي محمد	[Signature]				
Contractor QA/QC*	XYZ	[Signature]	6-1-2024	5:00	A	
	H.M.C	[Signature]	6/1/2024	4:40	Awc	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024		Anrc	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإشراف الهندسية



الهيئة العامة للإشراف
على الطرق



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة 157577	Designer Company*	DR. Hassan Mahdy (H.M.C)						
Issued by Contractor	Name: Sign:	Date	10-1-2024						
Received by Employers Representative	UIR	REQ. NUM	53						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT			28		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120 E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description: من (5- متر from st (202+060) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSALTANT. (xyz)) 	Comments by: General consultant (systra) - No objection, according to the attached reports and lab. results. - you must follow specs and design dwg
--	---

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد الحويج					
Contractor QA/QC*	XYZ	عبد الرحمن العرياني	10-1-2024	12:30	A	
	H.M.C	محمد المكي	10-1-2024	12:00	A	
GARB**						
Employers Representative	Khaled chi		23/9/2024		Awc	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 137537	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name: <u>وليد محمد</u> Sign: <u>[Signature]</u>	Date	10-1-2024
Received by Employers Representative	UIR	C1 KP	C2 SU
		C3 OT	DD MM YY HH MM
			23
CODE-1	CODE-2	CODE-3	CODE-4

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+300 TO 202+376	
	E=260139.0278 N=3136066.4661	E=260129.6912 N=3135991.0324
Inspection description/		
from st (202+300) to st (202+376)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))

Comments by: General consultant (systra)

تم التحقق من المستويات والارتفاعات فقط بواسطة XYZ والمسئولية تقع على عاتقهم فقط.

- levels and coordinates were checked only by xyz and under their own responsibility
- you must follow specs and design dng. and geo-technical report.


- This work was inspected only by xyz and H.M.C

INSPECTION RESULT

Organisation	Name	Sign	Date	Time	Approval Status	Please Tick if Not Attend
Contractor Engineer	وليد محمد	[Signature]			A-AWC-R	
Contractor QA/QC*	XYZ	[Signature]	10-1-2024	10:30	A	
	H.M.C	[Signature]	10-1-2024	10:30	AWC	
GARB**						
Employers Representative	Khaled ali	[Signature]	23/9/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name:  Sign: 	Date	REQ. NUM
Received by Employers Representative	UIR	15-1-2024	55
		C1 C2 C3 DD MM YY HH MM	
		KP SU OT	20

CODE-1

CODE-2

CODE-3

CODE-4

CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+300 TO 202+340	
	E=260139.0278 N=3136066.4661	E=260134.2574 N=3136026.7517
Inspection description/		
from st (202+300) to st (202+340) ردم منسوب (8.5) متر		


INSPECTION DETAILS The following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT - (xyz))	Comments by: General consultant (systra)
	-you must follow specs and design drug- -you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	علي محمد					
Contractor QA/QC*	XYZ	عبد الرحمن العزاد	16-1-2024	8:30	A	
	H.M.C	محمد علي	15/1/2024	4:30pm	H	
GARB**						
Employers Representative	Khaled ali		26/1/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أ.إ.ص.م
للإستشارات الهندسية





الهيئة العامة للإستشارات
والإستشارات الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR. Hassan Mahdy (H.M.C)						
Issued by Contractor	Name:  Sign: 	Date	REQ. NUM						
Received by Employers Representative	UIR	15-1-2024	56						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT			24		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300 E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description/ تسليم طبقة ردم منسوب (4) متر from st (202+220) to st (202+300)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	


Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)



-you must follow specs and design by
-you must do leveling and lining
the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود محمد		16-1-2024			
Contractor QA/QC*	XYZ	عبد الرحمن الزينادي	16-1-2024	9:18	A	
	H.M.C	محمد علي	15/1/2024	5:16	A	
GARB**						
Employers Representative	Khaled ali		16/1/2024		AWC	



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name [Signature] Sign [Signature]	Date	REQ.NUM 57															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>24</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			24		
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT			24													
CODE-1	CODE-2	CODE-3	CODE-4															

EXPLANATION OF WORK TO BE INSPECTED


Area	Element	Item
From 200+876 To 202+376	202+060 TO 202+120	
	E=260160.9658 N=3136305.4382	E=260156.5571 N=3136245.6007
Inspection description/		
منطقة ردم منسوب (4.5) متر from st (202+060) to st (202+120)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT-xyz)	Comments by: General consultant (systra)
 مشروع القمم الكبريتي السريع - القمم الثاني	- you must follow specs and design durg. - you must do landing and lining the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد عمار	[Signature]				
Contractor QA\QC*	XYZ	[Signature]	16-1-2024	3:30	A	
	H.M.C	[Signature]	16/1/24	3:00	Awc	
GARB**						
Employers Representative	Khaled ali	[Signature]	16/1/2024		Awc	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name: 157537 Sign: وليد خلافة وليد محمود	Date	REQ.NUM 58															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td>17</td> <td>1</td> <td>2024</td> <td>4</td> <td>00</td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT	17	1	2024	4	00
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT	17	1	2024	4	00											
CODE-1	CODE-2	CODE-3	CODE-4															

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300 E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description/ منسوب (3.5-) متر from st (202+220) to st (202+300)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time
-------------------------	-------------------------

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: GARB SURVEY CONSATANT (xyz)	Comments by: General consultant (systra)
تم اكتشاف خلل في التسوية والتسوية المطلوبة - القيد 157537	-you must follow specs and design dng -you must do leveling and lining the compacted side slope & filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليده خلافة وليد محمود					
Contractor QA/QC*	XYZ	عليه الرحمه الهادي	17-1-2024	5:10	A	
	H.M.C	عليه الرحمه الهادي	17/1/2024	4:00	A	
GARB**						
Employers Representative	Khaled Ali		17/1/2024		AWC	

UNIVERSAL INSPECTION REQUEST



مكتب أديان مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR. Hassan Mahdy (H.M.C)					
Issued by Contractor	Name	137537	Sign	Date	REQ. NUM				
	وليد محمد		20-1-2024		59				
Received by Employers Representative	UIR	C1	C2	C3	DO	MM	YY	HH	MM
		KP	SU	OT			24		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5	

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+300 TO 202+360		
	E=260139.0278 N=3136066.4661	E=260131.7531 N=3136006.9091	
Inspection description			
منسوب (8-متر) from st (202+300) to st (202+360) تسليم طبقة ردم منسوب			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: GARB SURVEY CONSATANT. (xyz)	Comments by: General consultant (systra)
مستشار الاستشارات العامة	- you must follow specs and design dng.
مستشار الاستشارات العامة	- you must do leveling and Cinning
مستشار الاستشارات العامة	the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمد					
Contractor QA/QC*	XYZ	عبد الرحمن الزباري	20/1/2024	10:00	A	
	H.M.C	محمود محمد	20/1/2024	9:00	A	
GARB**						
Employers Representative	Khaled ali		20/1/2024		Amr	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)
Issued by Contractor	Name: <u>علي محمد</u> Sign: <u>علي محمد</u>	Date	REQ.NUM
Received by Employers Representative	UIR	18-1-2024	60
		C1 C2 C3 DD MM YY HH MM	
		KP SU OT	24
CODE-1	CODE-2	CODE-3	CODE-4
			CODE-5

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+920 TO 202+000	
	E=260168.4582 N=3136445.233	E=260164.6561 N=3136365.3242
Inspection description:		
منسوب (12.5) متر from st (201+920) to st (202+000)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
تم العمل على الحفر والردم في المنطقة المذكورة في المخطط	- you must follow specs and design dwg - you must do leveling and lining - the compacted side slope of filling layer

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	علي محمد	علي محمد	20-1-2024	11:15	A	
Contractor QA/QC*	XYZ	علي محمد	20-1-2024	3:45	A	
GARB**						
Employers Representative	Khaled ali	علي محمد	20/1/2024	Amrc		

UNIVERSAL INSPECTION REQUEST



مكتب أ.د/حسن مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والتصميم



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة 157537	Designer Company*	DR. Hassan Mahdy (H.M.C)
Issued by Contractor	Name: Sign:	Date	REQ.NUM
Received by Employers Representative	UIR	18-1-2024	61
		C1 C2 C3 DO MM YY HH MM	
		KP SU OT	23
CODE-1	CODE-2	CODE-3	CODE-4
CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+020 TO 202+060	
	E=260163.5058 N=3136345.3573	E=260160.9658 N=3136305.4382
Inspection description/		
منسوب (12.5-) متر from st (202+020) to st (202+060)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT: xyz)	Comments by: General consultant (systra)
	- you must follow specs and design dr - you must do leveling and lining - the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	ر.ب. محمود					
Contractor QA/QC*	XYZ		21-1-2024	5:15	A	
	H.M.C		21-1-2024	5:00	A	
GARB**						
Employers Representative	Ali K		20/1/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	REQ. NUM							
			21-1-2024	62							
Received by Employers Representative			UIR	C1	C2	C3	DD	MM	YY	HH	MM
				KP	SU	OT				24	
CODE-1		CODE-2	CODE-3	CODE-4		CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+300 TO 202+376		
	E=260139.0278	E=260129.6912	
	N=3136066.4661	N=3135991.0324	
Inspection description(			
منسوب (7.5) متر from st (202+300) to st (202+376) تسليم طبقة ردم منسوب (7.5) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)

	-you must follow specs and design dng -you must do leveling and lining the compacted side slope & filling layer
--	---

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمد					
Contractor QA/QC*	XYZ	عبد الرحمن الابرار	21-1-2024	5:10	A	
	H.M.C	شودا	21-1-2024	5:28	A	
GARB**						
Employers Representative	Khaled ali		21/1/2024			

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجمية للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)															
Issued by Contractor	Name [Signature]	Date	22-1-2024															
Received by Employers Representative	Sign [Signature]	REQ.NUM	63															
Received by Employers Representative	UIR	<table border="1"> <tr> <td>C1</td> <td>C2</td> <td>C3</td> <td>DD</td> <td>MM</td> <td>YY</td> <td>HH</td> <td>MM</td> </tr> <tr> <td>KP</td> <td>SU</td> <td>OT</td> <td></td> <td></td> <td>20</td> <td></td> <td></td> </tr> </table>	C1	C2	C3	DD	MM	YY	HH	MM	KP	SU	OT			20		
C1	C2	C3	DD	MM	YY	HH	MM											
KP	SU	OT			20													
CODE-1	CODE-2	CODE-3	CODE-4															
CODE-5																		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+920 TO 202+040	
	E=260168.4582 N=3136445.233	E=260162.2757 N=3136325.3952
Inspection description:		
منسوب (12-) متر from st (201+920) to st (202+040)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT. (xyz))

Comments by: General consultant (systra)



-you must follow specs and design dwg
-you must do leveling and lining
the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	علي محمد	[Signature]				
Contractor QA/QC*	XYZ	[Signature]	23-1-2024	9:00	A	
	H.M.C	[Signature]	22-1-2024	5:15	AWC	
GARB**						
Employers Representative	Khaled	[Signature]	23/1/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	REQ. NUM							
	وليد محمود	وليد علاف	27-1-2024	65							
Received by Employers Representative			UIR	C1	C2	C3	DD	MM	YY	HH	MM
				KP	SU	OT			23		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+875 To 202+376	201+920 TO 202+060		
	E=260168.4582	E=260160.9658	
	N=3136445.233	N=3136305.4382	
Inspection description/			
من 200+875 إلى 202+376 من st (201+920) إلى st (202+060) طبقة ردم منسوب (-11.5) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))

Comments by: General consultant (systra)



-you must follow specs and design dng
-you must do leveling and lining
the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time		A-AWC-R	
Contractor Engineer	وليد علاف	وليد محمود					
Contractor QA/QC*	XYZ	أحمد محمد	27-1-24	5:00		A	
	H.M.C	محمود محمد	27-1-24	4:15		A	
GARB**							
Employers Representative	Khaled ali		27/1/2024			A	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيله للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	REQ. NUM							
	رئيس محوري	رئيس علف	30-1-2024	66							
Received by Employers Representative			UIR	C1	C2	C3	DD	MM	YY	HH	MM
				KP	SU	OT				24	
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+300 TO 202+376		
	E=260139.0278	E=260129.6912	
	N=3136066.4661	N=3135991.0324	
<u>Inspection description:</u> from st (202+300) to st (202+376) تسليم طبقة ردم منسوب (6.5-) متر			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
	-you must follow specs and design drug -you must do leveling and lining the compacted sube slp & filling layer

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد علف	وليد علف				يتم صيانة القطر قبل التورب	
Contractor QA/QC*	XYZ	محمد رافع	30-1-2024	4:00	(A)		
	H.M.C	محمد منتصر قزوه	30-1-24	12:30	AWC		
GARB**							
Employers Representative	Khated ali		30/1/2024				

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



شركة أديس مهدي
للإستشارات الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	وليد محمود	وليد عارف	18-2-2024	68						
Received by Employers Representative	[Stamp]	UIR	C1	C2	C3	DD	MM	YY	HH	MM
			KP	SU	OT			24		
CODE-3		CODE-2	CODE-3	CODE-4		CODE-5				

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	202+300 TO 202+376		
	E=260139.0278	E=260129.6912	
	N=3136066.4661	N=3135991.0324	
<u>Inspection description:</u>			
منسوب (6-) متر from st (202+300) to st (202+376)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT - xyz)

تم استلام العمل (الطريق) من قبل فريق العمل
في الموقع بتاريخ 18/2/2024 - انظر المرفق

Comments by: General consultant (systra)

- you must follow specs and design durg
- you must do leveling and lining
the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود	وليد عارف				
Contractor QA/QC*	XYZ	عبد الرحمن العلي	19-2-2024	11:30	A	
	H.M.C	محمد مشهور	19-2-2024	12:00	A	
GARB**						
Employers Representative	rehaled ale	[Signature]	19/2/2024		Arre	

UNIVERSAL INSPECTION REQUEST



مكتب أ.إ.ص. مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)							
Issued by Contractor	Name	Sign	Date	REQ.NUM							
	وليد محمود	وليد محمود	22-2-2024	69							
Received by Employers Representative	[Signature]	[Signature]	UIR	C1	C2	C3	DD	MM	YY	HH	MM
				KP	SU	OT			24		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5			

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+920 TO 202+060		
	E=260168.4582 N=3136445.233	E=260160.9658 N=3136305.4382	
Inspection description/			
منطقة ردم منسوب (10.5-) متر from st (201+920) to st (202+060)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))

مستشار الاستشارات العامة
للمقاولات العامة
أبو عجلة للمقاولات العامة

Comments by: General consultant (systra)

-you must follow specs and design
-you must do leveling and lining
the compacted side slope & filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود	وليد محمود				
Contractor QA/QC*	XYZ	عبد الرحمن الوفاوي	24-2-2024	3:30	A	
	H.M.C	محمد منعم فوزي	24-2-2024	11:00	A	
GARB**						
Employers Representative	Khaled ali	[Signature]	24/2/2024		Amr	

UNIVERSAL INSPECTION REQUEST



مكتب أديسن مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والبحوث



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أديسن مهدي للمقاولات العامة		Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name	Sign	Date	REQ.NUM						
	وليد طاي و وليد محمد		23-3-2024	74						
Received by Employers Representative	UIR		C1	C2	C3	DO	MM	YY	HH	MM
			KP	SU	OT			24		
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5		

EXPLANATION OF WORK TO BE INSPECTED

Area	Element		Item
From 200+876 To 202+376	201+920 TO 202+060		
	E=260168.4582 N=3136445.233	E=260160.9658 N=3136305.4382	
Inspection description:			
منطقة ردم منسوب (10- متر) from st (201+920) to st (202+060)			

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))	Comments by: General consultant (systra)
تم اتمام العمل في المنطقة (الطريق) - انظر المرفق	- you must follow specs and design drawings - you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT						Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R		
Contractor Engineer	وليد طاي و وليد محمد						
Contractor QA/QC*	XYZ	عليه الرحمه (الطاي)	23-3-2024	12:15	A		
	H.M.C	محمد مشهور فوزي	23/3/2024	12:00	A		
GARB**							
Employers Representative	Khaled ali		23/3/2024		Amr		

UNIVERSAL INSPECTION REQUEST



مكتب أ.أ.أ. مهندسي
للإستشارات الهندسية



الهيئة العامة للإعانة
والتطوير



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجيبة للمقاولات العامة 157537	Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name: Sign:	Date	REQ. NUM						
Received by Employers Representative	UIR	31-3-2024	75						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT			24		
CODE -1	CODE -2	CODE -3	CODE -4	CODE -5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	201+920 TO 202+060 E=260168.4582 N=3136445.233	E=260160.9658 N=3136305.4382
Inspection description منطقة ردم منسوب (9.5) متر from st (201+920) to st (202+060)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be included as appropriate

Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSULTANT (xyz))

Comments by: General consultant (systra)

تم التأكد من أن العمل جاهز للتحقق من قبل المهندس الاستشاري (xyz) في تاريخ 31-3-2024.

-you must follow specs and design draw
-you must do leveling and lining the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	وليد محمود محمد					
Contractor QA/QC*	XYZ عبد الرحمن الطرناوي		1-4-2024	12:00	A	
	H.M.C	محمود علي	31-3-2024	11:00	A	
GARB**						
Employers Representative	Khakhdali		1/4/2024		Done	

UNIVERSAL INSPECTION REQUEST



مكتب أدريس مهدي
للإستشارات الهندسية



الهيئة العامة للإستشارات
والمصممات الهندسية



RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours

The Work described below will be complete and ready for inspection at planned time shown

Contractor Company	أبو عجلة للمقاولات العامة	Designer Company*	DR .Hassan Mahdy (H.M.C)						
Issued by Contractor	Name:  Sign: 	Date	REQ.NUM						
Received by Employers Representative	UIR	1-4-2024	76						
		C1	C2	C3	DD	MM	YY	HH	MM
		KP	SU	OT			24		
CODE-1	CODE-2	CODE-3	CODE-4	CODE-5					

EXPLANATION OF WORK TO BE INSPECTED

Area	Element	Item
From 200+876 To 202+376	202+220 TO 202+300	
	E=260147.6147 N=3136146.003	E=260139.0278 N=3136066.4661
Inspection description(		
منسوب (3-متر) from st (202+220) to st (202+300) تسليم طبقة ردم منسوب (3-متر)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time

Planned Inspection Date	Planned Inspection Time

COMPLIANCE EVIDENCE Must be Included as appropriate



Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT (xyz))

Comments by: General consultant (systra)

تأكد من التسليم طبقاً للمواصفات - القياسات
- you must follow specs and design dra
- you must do leveling and lining
the compacted side slope of filling layer

INSPECTION RESULT

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer	أبو عجلة					
Contractor QA/QC*	XYZ		1-4-2024	11:30	A	
	H.M.C		1-4-2024	11:00	A	
GARB**						
Employers Representative	Khaled ali		1/4/2024		AWC	

RECEIPT of NOTIFICATION - Minimum Notice Period not less than 24 Hours									
The Work described below will be complete and ready for inspection at planned time shown									
Contractor Company	157537 157537			Designer Company*	DR .Hassan Mahdy (H.M.C)				
Issued by Contractor	Name Sign			Date	1-4-2024				
Received by Employers Representative	Name Sign			Time	77				
CI C2 C3				DD	MM	YY	HH	MM	
KP SU OT						24			
CODE-1		CODE-2		CODE-3		CODE-4		CODE-5	

EXPLANATION OF WORK TO BE INSPECTED		
Area	Element	Item
From 200+876 To 202+376	201+920 TO 202+376	
	E=260168.4582 E=260129.6912 N=3136445.233 N=3135991.0324	
Inspection description: As-Built for Fill from st (201+920) to st (202+376)		

INSPECTION DETAILS The Following will be ready at the Planned Inspection Time	
Planned Inspection Date	Planned Inspection Time
1/4/2024	

COMPLIANCE EVIDENCE Must be included as appropriate			
Checklist Attached ☐	Test Results Attached ☐	Calibration Attached ☐	Other as indicated ☐
Drawing Reference	ITP Reference	MS Reference	

Comments by: (GARB SURVEY CONSATANT.(xyz))	Comments by: General consultant (systra)
1 2	

INSPECTION RESULT					Approval Status	Please Tick if Not Attend
Organisation	Name	Sign	Date	Time	A-AWC-R	
Contractor Engineer						
Contractor QA/QC*	XYZ		2-4-2024	9:00	A	
	H.M.C		2-4-2024	9:30	A	
GARB**						
Employers Representative						
