



السيد المهندس / رئيس قطاع التنفيذ والمناطق

تحية طيبة وبعد...

الموضوع بخصوص: مشروع كويري دوران للخلف عند كم ٨٠٠ + ٢٤ ضمن
وادي النظرون/العلمين بطول ١٣٥ كم

تنفيذ شركة: يوني بيلد للصناعة والمقاولات

رقم العقد: (٢٠٢٣/٢٠٢٢/٩١٩) - تاريخ العقد: ٢٠٢٢/١٢/٦

قيمة العقد: ٧٢,٢٧٩ مليون جنيه فقط (اثنان وسبعون مليون ومائتان تسعة وسبعون ألف جنيه لا غير)

نسبة التنفيذ: ٩٥ %

بالاحالة إلى المشروع عاليه وبخصوص كتاب الشركة والذي تطلب فيه مد أمر الإسناد ليصبح قيمته ٨٦,١٢٤,٧٩٠ جنيه فقط (ستة وثمانون مليون ومائة وأربعة وعشرون ألف وسبعائة وتسعون جنيه لا غير) بنسبة زياده ١٩,٢ % عن العقد الأصلي وذلك طبقا للوحات التصميمية والتنفيذ على الطبيعه فإنه قد تم زيادة كميات بعض بنود العقد وإستحداث بند وهي:

رقم البند	البيان	الوحدة	كمية المقاييسه المعدل رقم ١	كمية المقاييسه المجدده
١٣	بالمتر المكعب خرسانة عادية للأساسات وأسفل البلاطات الانتقائية والقدمات السفلية للميول...	م ^٣	٢٤٢	٢٩٨
٢٩	بالمتر المكعب أعمال حفر باستخدام المعدات الميكانيكية في التربة المتماسكة عدا التربة الصخرية...	م ^٣	١٥٠٠٠	٥٢٠٠٠
٣٠	بالمتر المكعب أعمال توريد وتشغيل أتربة صالحه للردم من المحاجر المعتمدة مطابقة للمواصفات...	م ^٣	٢٥٠٠٠	٤٣٠٠٠
٣١	بالمتر المكعب أعمال توريد وفرش طبقة الأساس من الأحجار الصلبة المترججه ناتج تكسير الكسارات والمطابقة للمواصفات...	م ^٣	٣٠٠٠	٥٣٠٠
٣٢	بالمتر المسطح أعمال توريد ورش طبقة تشريب من البيتومين السائل متوسط التطاير ٣٠٠ MC بمعدل من (١,٢) كجم...	م ^٢	١٥٠٠	١٠٠٠٠
٣٤	بالمتر المسطح أعمال توريد ورش طبقة لاصقه من البيتومين السائل سريع التطاير ٣٠٠ RC بمعدل ٠,٤ كجم/م ^٢ ...	م ^٢	١٥٠٠	٢٥٥٠٠
٣٥	بالمتر المسطح أعمال توريد وفرش طبقة رابطة من الخرسانة الاسفلتية بسمك ٦ سم...	م ^٢	١٠٠٠	١٣٠٠٠
٣٦	بالمتر المسطح أعمال توريد وفرش طبقة رابطة من الخرسانة الاسفلتية بسمك ٥ سم...	م ^٢	١٠٠٠	١٣٠٠٠
٣٧	بالمتر الطولي توريد وإنشاء حاجز من الخرسانه العاليه نيوجرسي وجه واحد بارتفاع ٨٠ سم اعلى الفرشه طبقا للرسومات على ان يكون وجه الخرسانه FAIR FACE ...	م ^ط	١٥٠	١٦٥٠
٣٨	بالمتر المسطح أعمال توريد وصب خرسانة عادية سمك ١٥ سم لحماية الأكتاف والميول الجانبية...	م ^٢	١٠٠٠	١٤٤٠٠
البند المستحدثه				
١	بالمتر المسطح أعمال توريد وفرش طبقة رابطة من الخرسانة الاسفلتية بسمك ٧ سم...	م ^٢	-	١٠٠٠٠

نتشرف أن نرفق لسيداتكم طية المقاييسه المجدده للكميات طبقا لأسعار المفاوضه .

برجاء التكرم بالاحاطة والتوجيه باللائم نحو مد أمر الإسناد.

وتفضلوا بقبول فائق الاحترام ...

• تحرير افي: ٢٠٢٣/٩/٢٦

• مرفق: (٥)

مهندس العمليه

م/ أحمد الشاعر

مدير علم المشروعات

م / السيد عبد المجيد

رئيس الإدارة المركزية للمنطقه الثالثه عشر

بالبجيره وكفر الشيخ

لواء . أ. ح . مهندس / أحمد باسم حسن . الكرذاني

السيد اللواء.أ.ح. / رئيس الإدارة المركزية للمنطقة الثالثة عشر بالبحيرة وكفر الشيخ

تحية طيبة وبعد...

الموضوع بخصوص : مشروع كوبرى دوران للخلف عدد كم ٨٠٠ + ٢٤ ضمن أعمال تطوير طريق وادى التطرون/الطين بطول ١٣٥ كم

تنفيذ شركة : يوني بيلد للصناعة والمقاولات

رقم العقد : (٢٠٢٣ / ٢٠٢٢ / ٩١٩)

تاريخ العقد : ٢٠٢٢ / ١٢ / ٦

قيمة العقد : ٧٢,٢٧٩ مليون جنيه فقط (اثنان وسبعون مليون ومئتان تسعة وسبعون ألف جنيهها لاغير)

نتشرف بإحاطة سيادتكم علما طبقا للوحات التصميمية والتنفيذ على الطبيعة فإنه قد تم زيادة كميات بعض بنود العقد وإستحداث بند وهي:

رقم البند	البيان	الوحدة	كمية المقايضة المعطى رقم ١	كمية المقايضة المجدد
١٣	بالمتر المكعب خرسانة عادية للأساسات وأسفل البلاطات الانتقالية والقضبان المقلية للميول..	م ^٣	٢٤٢	٣٩٨
٢٩	بالمتر المكعب أعمال حفر باستخدام المعدات الميكانيكية في التربة المتمسكة عدا التربة الصخرية..	م ^٣	١٥٠٠٠	٥٢٠٠٠
٣٠	بالمتر المكعب أعمال توريد وتشغيل أتربة صالحة للردم من المحاجر المضادة مطابقة للمواصفات..	م ^٣	٢٥٠٠٠	٤٣٠٠٠
٣١	بالمتر المكعب أعمال توريد وفرش طبقة الأسفلت من الأحجار الصلبة المتدرجة ناتج تكسير الكسرات والمطابقة للمواصفات..	م ^٣	٣٠٠٠	٥٣٠٠
٣٣	بالمتر المسطح أعمال توريد ورش طبقة تشريب من البيتومين السفل متوسط التطاير ٣٠ Mc بمعدل من (١.٢) كجم..	م ^٢	١٥٠٠	١٠٠٠٠
٣٤	بالمتر المسطح أعمال توريد ورش طبقة لاصقة من البيتومين السفل سريع التطاير ٣٠٠ RC بمعدل ٠.٤ كجم/م ^٢ ..	م ^٢	١٥٠٠	٢٥٥٠٠
٣٥	بالمتر المسطح أعمال توريد وفرش طبقة رابطة من الخرسانة الاسفلتية بسمك ٦ سم..	م ^٢	١٠٠٠	١٣٠٠٠
٣٦	بالمتر المسطح أعمال توريد وفرش طبقة رابطة من الخرسانة الاسفلتية بسمك ٥ سم..	م ^٢	١٠٠٠	١٣٠٠٠
٣٧	بالمتر الطولى توريد وإنشاء حبلز من الخرسانة العالية نيوجرس وجه واحد بارتفاع ٨٠ سم اعلى الفرشه طبقا للمواصفات على ان يكون وجه الخرسانة FAIR FACE ..	م ^ط	١٥٠	١٦٥٠
٣٨	بالمتر المسطح أعمال توريد وقطب خرسانة عادية سمك ١٥ سم لحماية الاكتاف والميول الجذبية..	م ^٢	١٠٠٠	١٤٤٠٠
البند المستحدث				
١	بالمتر المسطح أعمال توريد وفرش طبقة رابطة من الخرسانة الاسفلتية بسمك ٧ سم..	م ^٢	-	١٠٠٠٠

مرفق لسيدتكم طية :-

- المقايضة المجدد للكميات طبقا لأسعار المفوضه
- القيمة : ٨٦,١٢٤,٧٩٠ جنيها فقط (ستة وثمانون مليون ومئة وأربعة وعشرون ألف وسبعمائة وتسعون جنيها لاغير)
- نسبة زياده ١٩.٢ % عن العقد الأصلي.

يرجاء التكرم بالإحاطة والتوجيه بمد أمر الإصدار.

وتفضلوا بقبول فائق الاحترام ...

شركة يوني بيلد للصناعة

والمقاولات

مهندس / حسام عباس

مقارنة مجتمعة للكيفيات طبقاً لأسعار المقايضة

أضال كويري نوران للخلب حذ كم ٨٠٠+٢٤ ضمن أصال غلور عروق وادي الثعرون / الطمون بطول ١٣ كم

تقليد شركة يولي بيك للصناعة والمطويات

[illegible]

المكتب الاستشاري بحرم بالقوي
القوي
و / محمد كمال

فشرقة الخلقاء (يولي بيد الخلقاء والملاويان)
التوقيف
م. أ. د. ع. م. م.



تلقب شركة يوني بيك للصناعة والمقاولات

Handwritten signature and stamp.



المقايضة مواد و التكاليف طبقا لأسعار المقايضة

أعمال كبرى في نوران الخلفاء على كم 114800 ضمن أعمال تطوير طريق وادي اللطرون / العلمين بطول 13 كم
تقديراً لخدمة بولاني بيك للتسليم والمساكنات

شركة بولي بيلد للصناعة والمكاولات					
م	بيان الأصل	الوحدة	كمية المقايسة	الكلنة بعد المقايضة	إجمالي القيمة
٢٩	بالمتر المسطح أصل تخطيط بالهوية الدائلة بنظام القيسق (EXTRUDER) بسبك لا يقل عن ٢.٥ سم وطبقة لمراسلات القياسية البترطكية وتطبيقات المكناس المشرف	٢٥	١	٢٥٥	٢٥٥
٣٠	بالقد توريد وتركيب عرائس أرضية (عفن أفقي) من مادة البوليستر بياض وحساب عليها مادة U.V.5 سطح التماس ١٠٠% اسم وطبقة بطون + سم وقطر الحادون عند القاعدة ١٧ سم وقطر عند القاعدة ١٥ سم ووسط التماس سطوي وتعمل على راسي ١ طن دون عس أو تقيير في القفل طبقة التثبيت القياسي وحمل أقصى وزن للباور لا يقل عن ٤٠٠٠ كجم مزودة بالدرع حماية بالورق ٣١ خدمة مثل سطح مستطيل ١٥٠٠٠ سم من التواء وبعد لفافات شدة التماس مطبقة . لمراسلات (ASTM E 800) ويتم استخدام مادة الصلابة لتثبيت التماس تتصل فوق التماس بالارض لا تقل عن ١٢ سمسم. وبما التخليد طبقة أصول الصلابة والرمومات القياسية فستعداة وإزالة جميع مشتات طبقة لمراسلات الجهة خدمة التشر والتقير والتطبيقات المكناس المشرف على فراغات في السطح التماس لتمام على سطح الأرض للتثبيت.	عدد	١	٣٩	٣٩
٣١	بالقد توريد وتركيب عرائس ساج يتم تركيبها على السطح الخرساني الموجود طبقة الترسبات وبتطبيق مساحات طبقة بعد ٢ سمسم والتأكد بشدة توريد العرائس بالورق الملصق طبق مع مراعاة أصول الصناعة من حيث المسافات القياسية والمراجع العرائس من سطح العمايز طبقة الترسبات الترسيمية وثان ما يتم تهيؤ العمل كما يلي أصول الصناعة والمواصفات وتطبيقات المكناس المشرف	عدد	٥٠٥	١٠	٥٠٥٠

ثالثها : اعملي صرفك المظري

٤	توريد وتركيب مواسير LSPVC لتأدية التيارات الكهربائية لخط ١ بوسطة خلاصة بكتابات الاستشارة والمسر بشكل جميع ما يلزم لإنهاء العمل حتى يتم وضعه وحسب أصول الصيانة وتعليمات المهندسين المشرفين.	م.ب.م	٢٨٤٠	١٨٠	٤٢١٥٠٠
٥	بالمسح الطولي لتوريد وتركيب مواسير التصفيف PVC قطر (٤ بوصة) وإل ما يلزم للسير الأسفلتي لخواصا طبقا لأصول الصيانة وتعليمات المهندسين المشرفين.	م.ب.م	٥٥	٢٨٠	١٥٤٠٠
٦	بالمسح الطولي لتوريد وتركيب مواسير التصفيف PVC قطر (٦ بوصة) وإل ما يلزم للسير الأسفلتي لخواصا طبقا لأصول الصيانة وتعليمات المهندسين المشرفين.	م.ب.م	٩٢	٣٥٠	٨٧٤٠
٧	بالمسح الطولي لخرقة صرف مطر داخل محطة التحويل من مادة GEP بالإضافة طبقا لقرصات الهندسة مع عمل جراجات والسور بشكل جزئي فائقة بدون خيز فائقة لتسريب المياه وتوريد المواد من GEP كما هو موضح بالقرصات ورسمة المراسم من PVC في حدود الصرف طبقا لتعليمات المهندسين المشرفين .	م.ب.م	٥	٤٩٠٠	٢٤٥٠٠

ثَلَاثًا: الْأَعْمَالُ الْكَلْبِيَّةُ

١٠	١١	١٢	١٣	١٤	١٥	١٦	١٧	١٨	١٩	٢٠	٢١	٢٢	٢٣	٢٤	٢٥	٢٦	٢٧	٢٨	٢٩	٣٠	٣١	٣٢	٣٣	٣٤	٣٥	٣٦	٣٧	٣٨	٣٩	٤٠	٤١	٤٢	٤٣	٤٤	٤٥	٤٦	٤٧	٤٨	٤٩	٥٠	٥١	٥٢	٥٣	٥٤	٥٥	٥٦	٥٧	٥٨	٥٩	٦٠	٦١	٦٢	٦٣	٦٤	٦٥	٦٦	٦٧	٦٨	٦٩	٧٠	٧١	٧٢	٧٣	٧٤	٧٥	٧٦	٧٧	٧٨	٧٩	٨٠	٨١	٨٢	٨٣	٨٤	٨٥	٨٦	٨٧	٨٨	٨٩	٩٠	٩١	٩٢	٩٣	٩٤	٩٥	٩٦	٩٧	٩٨	٩٩	١٠٠									
١	٢	٣	٤	٥	٦	٧	٨	٩	١٠	١١	١٢	١٣	١٤	١٥	١٦	١٧	١٨	١٩	٢٠	٢١	٢٢	٢٣	٢٤	٢٥	٢٦	٢٧	٢٨	٢٩	٣٠	٣١	٣٢	٣٣	٣٤	٣٥	٣٦	٣٧	٣٨	٣٩	٤٠	٤١	٤٢	٤٣	٤٤	٤٥	٤٦	٤٧	٤٨	٤٩	٥٠	٥١	٥٢	٥٣	٥٤	٥٥	٥٦	٥٧	٥٨	٥٩	٦٠	٦١	٦٢	٦٣	٦٤	٦٥	٦٦	٦٧	٦٨	٦٩	٧٠	٧١	٧٢	٧٣	٧٤	٧٥	٧٦	٧٧	٧٨	٧٩	٨٠	٨١	٨٢	٨٣	٨٤	٨٥	٨٦	٨٧	٨٨	٨٩	٩٠	٩١	٩٢	٩٣	٩٤	٩٥	٩٦	٩٧	٩٨	٩٩	١٠٠

رایحه : القیو، المصنعة

١	بالمر المستخرج اعلى التوريد و فرش طبقة رابطة من الخرسانة الاسفلتية بسك ٧ سم بعد الدمك واستلام اعمال طبقة تجميع تكسير الكسرات و التهيؤ من الصلب ٧٠-٨٠ وازالة شوكية التمر بوسوس او ما يلائها و القذبة لتعمل اجزاء التجارب الصخرية والتمكينة على السطوح وعلى التواء المستقيمة ويتم التفتيش طبقة التفتيشات الخرسانية المرصبة والرسومات التفصيلية المعتمدة والى ما يجرى من مشكلات طبقة لاصول الصخرية ومواسمات الجهة الخاصة للخرق والتكوير وتطبيقات المعاسير المشرف والصخر يشمل الزيادة في قيمة التكلفة المعبورة لمحدود منطقة ولاي التفرير والتي لقرتها المناطق المشرفة في	٦٤	١٠٠٠٠	١٧٧	١٧٧٠٠٠٠
	الإجمالي				٨٦,١٧٤,٧٩٠

ملاحظات:

- ١- في حالة المرور على ممتلكات تصعد الشركة الوطنية للبناء والتنمية وإدارة الطرق بصفاء قيمة لتعميد رسوم الشارة والنوازلين طبقاً للوحة الشركة الوطنية للتقاني =
- أ- أحصل التوريب الاحرية يتم اخذها مبلغ ١٣ جنيه لكل متر مكعب ختمسي.
- ب- أحصل طبقات الاسفل يتم اخذها مبلغ ٢٥ جنيه لكل متر مكعب ختمسي.
- ج- أحصل طبقات الاسفلت يتم اخذها مبلغ ٣٠ جنيه لكل متر مكعب ختمسي.
- ٢- يحق للشركة صرف قيمة التخفيضات نتيجة تلافى بنود الصنف الذي تشكل في ممتلكاتها مواد معجزة بعد موافقة السلطة المختصة.
- ٣- يحق للشركة صرف قروض الأسفار سواء (بالقرعة / التفاضل) للشارع المردود عليها بالصنف (الحديد بجميع انواعه - الاسمنت - البوليسترين - البوليلا) طبقاً لائحة الشركة الوطنية للأسفار المردود و لتعميد والامضاء طبقاً لنسب التوفيق المعتمدة من الشركة من تاريخ امر الاسفار

الشركة المسجلة (برني بيك للمصاحف والمقالات) المكتب الاستشاري (بحرم بالموم)

والله اعلم

١٠٠

م. لا محمد المصطفى

10

1. *Algebra*

100

الأسعار الصاعدة من الجهد

1932

وہ جو ان کے لئے ہے

والمز

شماره ۱۰۰

101

571

المجلس الأعلى للثقافة

100



وزارة النقل
الهيئة العامة للطرق والكباري
القياس: ١٢٤٠٦ / ٢٠٢٣ / الكباري
التاريخ: ٢٠٢٤ / ٠١ / ٠٣ م

مذكرة

للمعرض على السيد اللواء مهندس / رئيس مجلس الإدارة

بخصوص: إضافة مدة قدرها (٦) شهر لعملية مشروع كوبري دوران للخلف عند كم ٨٠٠+٢٤ ضمن أعمال
تطوير طريق وادي النطرون / العلمين

الموضوع:

- أسندت الهيئة العامة للطرق والكباري المشروع عاليه إلى يوني بيلد للصناعة والمقاولات بالعقد رقم (٢٠٢٣/٢٠٢٢/٩١٩)
- تاريخ بدء العمل في ٢٠٢٢/١٢/١١
- تاريخ النهو طبقاً للتعاقد: ٢٠٢٣/١٢/١٠
- ورد كتاب السيد المهندس / رئيس الإدارة المركزية . المنطقة الثالثة عشر (البحيرة وكفر الشيخ) بطلب إضافة مدة قدرها (٦) شهور للمشروع عاليه بناء على دراسة طلب الشركة المنفذه بإضافة المدة طبقاً لما ورد بالكتاب الدوري رقم (٣-٢٧٨١٥) بخصوص قرار مجلس الوزراء رقم (٢٥٤) بتاريخ ٢٠٢٣/٨/٣٠ نظراً للأسباب والمبررات على النحو الوارد بكتاب الشركة (مرفق).
- بالدراسة تبين تأثير الشركة بالإرتفاع المبالغ فيه لأسعار الخامات الأساسية (حديد - أسمنت . . . الخ) وإرتفاع أسعار قطع غيار المعدات وعدم توافرها بالأسواق مما أثر على معدلات سير العمل طبقاً للبرنامج الزمني للمشروع .

المطالب:

التكرم باتخاذ ماترونه سيادتكم مناسباً نحو الموافقة على طلب المنطقة المشرفة بإضافة مدة قدرها (٦) شهور للمشروع عاليه دون فرض غرامات تأخير أو فوائد ليصبح تاريخ النهو الفعلي ٢٠٢٤/٦/٩ كون أسباب التأخير خارجة عن إرادة الشركة

والأمر مفوض لسيادتكم ..

التوقيع

مهندس / أيمن محمد متولى

رئيس الإدارة المركزية

لتنفيذ وصيانة الكباري

التوقيع

الأستاذ / تامر بدرت محمد

مدير عام العقود والفتاوى واللوائح

التوقيع

مهندس / محمد زهران

رئيس قطاع التنفيذ والمناطق

التوقيع

لواء مهندس / ماجد محمد عبد الحميد متولى

نائب رئيس الهيئة العامة للطرق والكباري

التوقيع

لواء مهندس / حسام الدين محمد طنب

رئيس الهيئة العامة للطرق والكباري

رأى السيد الأستاذ / مدير عام العقود والفتاوى واللوائح

١) نرى جواز المرافعة بالما استرجع إليه الجانب الفني

وتمتاً بقرار السيد الأستاذ / مدير عام العقود والفتاوى واللوائح

التمديد لمدة ٦ شهور في سائر المناطق

رأى السيد المهندس / رئيس قطاع التنفيذ والمناطق

رحمته بسم المواقف ٢٠٢٣/١٢/١٠

رأى السيد اللواء مهندس / نائب رئيس مجلس الإدارة

أمانة على رأي لفتاوى

قرار السيد اللواء مهندس / رئيس مجلس الإدارة

وأما استمارة ذلك مع نسخ العاليه لكل الجهة المقررة (١٦٠٠)

مع عدم إرجاعها لمصلحة جهة الجهة المستفيدة - مع عدم تأخير

مما له ذلك . ج. أ. م. م.


DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	450/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	بلاطة إنشائية محور 7
DATE OF CASTING	20-Aug-2023	SPECIFIED STRENGTH	400 kg/cm ²
POURED QUANTITY	22 m	NO. OF CUBES MADE	
CONCRETE SLUMP	200 mm	date of test	23-Aug-2023
TARGET SLUMP	200:230mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3		
Age of Test (Days)	3	3	3		
Average Dimension (mm)	150	150	150		
Weight (g)	8530	8674	8611		
Density (kg/m ³)	2527	2570	2551		
Failure Load (kN)	903	826	817		
Comp. Strength Kg/cm ²	409	374	370		
Mode of Failure	A	A	A		
Average 28 Days	385				
Ratio %	96				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983



Remarks :


Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant
			




DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY _____ :	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD _____ :	BS 1881
CONSULTANT	ACE	Cement Content/Type	450/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE _____ :	بلاطة 2222ية محور 7
DATE OF CASTING	16-Sep-2023	SPECIFIED STRENGTH _____ :	400 kg/cm ²
POURED QUANTITY	25 m	NO. OF CUBES MADE _____ :	
CONCRETE SLUMP	200 mm	date of test	23-Sep-2023
TARGET SLUMP	200:230mm	CONCRETE TEMP (°C) _____ :	25

Specimen Reference	1	2	3			
Age of Test (Days)	7	7	7			
Average Dimension (mm)	150	150	150			
Weight (g)	8345	8367	8451			
Density (kg/m ³)	2473	2479	2504			
Failure Load (kN)	869	880	876			
Comp. Strength Kg/cm ²	394	399	397			
Mode of Failure	A	A	A			
Average 28 Days	397					
Ratio %	99					

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983 Unsatisfactory



Remarks :

Density measurement is carried out in accordance with BS


1881:Part 114 in the as received condition for moist specimens and in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking









Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant

BOX SECTION AX-5 : AX-7

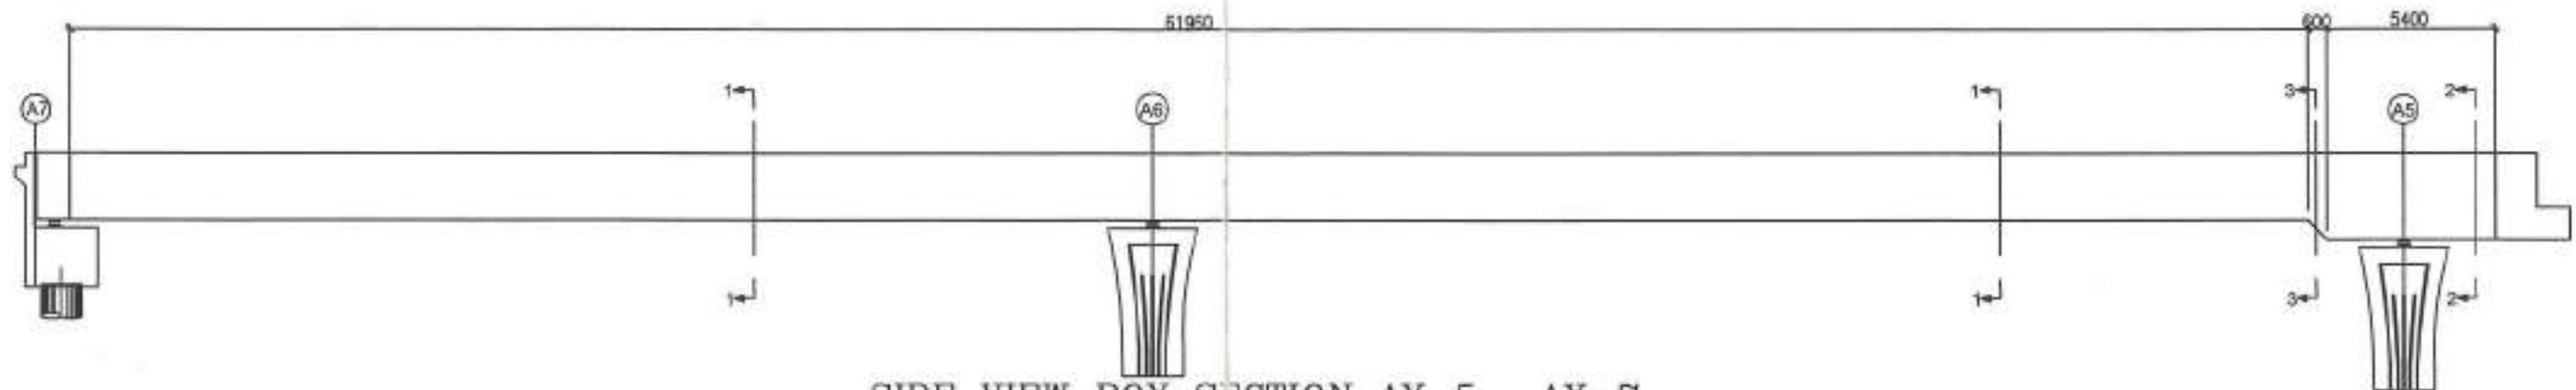

SIDE VIEW BOX SECTION AX-5 : AX-7

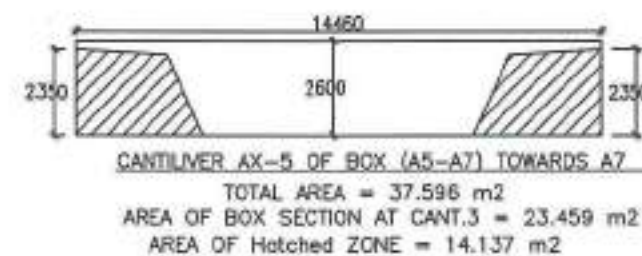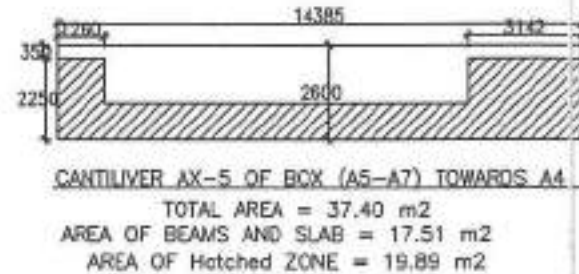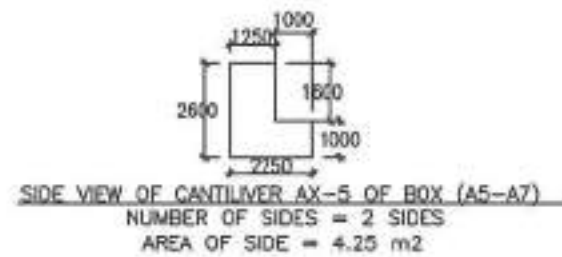


المكتب الهندسي

١٤/١٠/٢٠١٩

المكتب الهندسي

١٤/١٠/٢٠١٩




DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY _____ :	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD _____ :	BS 1881
CONSULTANT	ACE	Cement Contn/Type	450/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE _____ :	بلاطة متقاطعة محور 7
DATE OF CASTING	20-Aug-2023	SPECIFIED STRENGTH _____ :	400 kg/cm ²
POURED QUANTITY	22 m	NO. OF CUBES MADE _____ :	
CONCRETE SLUMP	200 mm	date of test	23-Aug-2023
TARGET SLUMP	200:230mm	CONCRETE TEMP (°C) _____ :	25

Specimen Reference	1	2	3			
Age of Test (Days)	3	3	3			
Average Dimension (mm)	150	150	150			
Weight (g)	8530	8674	8611			
Density (kg/m ³)	2527	2570	2551			
Failure Load (kN)	903	826	817			
Comp. Strength Kg/cm ²	409	374	370			
Mode of Failure	A	A	A			
Average 28 Days	385					
Ratio %	96					

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983



Remarks :


Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant





DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	450/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	بلاطة انتقالية محور 7
DATE OF CASTING	16-Sep-2023	SPECIFIED STRENGTH	400 kg/cm ²
POURED QUANTITY	25 m	NO. OF CUBES MADE	
CONCRETE SLUMP	200 mm	date of test	23-Sep-2023
TARGET SLUMP	200:230mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3			
Age of Test (Days)	7	7	7			
Average Dimension (mm)	150	150	150			
Weight (g)	8345	8367	8451			
Density (kg/m ³)	2473	2479	2504			
Failure Load (kN)	869	880	876			
Comp. Strength Kg/cm ²	394	399	397			
Mode of Failure	A	A	A			
Average 28 Days	397					
Ratio%	99					

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983



Remarks :

Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant



DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	450/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	كويتا
DATE OF CASTING	20-Sep-2023	SPECIFIED STRENGTH	400 kg/cm ²
POURED QUANTITY	3	NO. OF CUBES MADE	
CONCRETE SLUMP	200 mm	date of test	27-Sep-2023
TARGET SLUMP	200-230mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3		
Age of Test (Days)	7	7	7		
Average Dimension (mm)	150	150	150		
Weight (g)	8364	8414	8404		
Density (kg/m ³)	2478	2493	2490		
Failure Load (kN)	866	875	846		
Comp. Strength Kg/cm ²	393	397	384		
Mode of Failure	A	A	A		
Average 28 Days	391				
Ratio %	98				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983



Remarks :

Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and
in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC-Engineer	QC Consultant



المهندسون الاستشاريون العرب
مصر - بالقاهرة



UNIBUILD
INDUSTRIES & CONSTRUCTION

DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	450/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	كويتا
DATE OF CASTING	21-Sep-2023	SPECIFIED STRENGTH	400 kg/cm ²
POURED QUANTITY	3	NO. OF CUBES MADE	
CONCRETE SLUMP	200 mm	date of test	28-Sep-2023
TARGET SLUMP	200:230mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3		
Age of Test (Days)	7	7	7		
Average Dimension (mm)	150	150	150		
Weight (g)	8421	8394	8451		
Density (kg/m ³)	2495	2487	2504		
Failure Load (kN)	844	838	849		
Comp. Strength Kg/cm ²	383	380	385		
Mode of Failure	A	A	A		
Average 28 Days	382				
Ratio %	96				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983



Remarks :

Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and
in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant

DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	450/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	كويسم
DATE OF CASTING	24-Sep-2023	SPECIFIED STRENGTH	400 kg/cm ²
POURED QUANTITY	3	NO. OF CUBES MADE	
CONCRETE SLUMP	200 mm	date of test	1-Oct-2023
TARGET SLUMP	200:230mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3		
Age of Test (Days)	7	7	7		
Average Dimension (mm)	150	150	150		
Weight (g)	8421	8364	8328		
Density (kg/m ³)	2495	2478	2468		
Failure Load (kN)	887	857	869		
Comp. Strength Kg/cm ²	402	389	394		
Mode of Failure	A	A	A		
Average 28 Days	395				
Ratio%	99				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER BS Unsatisfactory





Remarks :


Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC-Engineer	QC Consultant
			




DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	450/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	بلاطة الكتلية محور 7
DATE OF CASTING	20-Aug-2023	SPECIFIED STRENGTH	400 kg/cm ²
POURED QUANTITY	22 m	NO. OF CUBES MADE	
CONCRETE SLUMP	200 mm	date of test	17-Sep-2023
TARGET SLUMP	240:230mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3		
Age of Test (Days)	28	28	28		
Average Dimension (mm)	150	150	150		
Weight (g)	8470	8452	8514		
Density (kg/m ³)	2510	2504	2523		
Failure Load (kN)	1079	1089	1056		
Comp. Strength Kg/cm ²	489	494	479		
Mode of Failure	A	A	A		
Average 28 Days	487				
Ratio %	122				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983



Remarks :


Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant




DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	450/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	بلاطة التقوية محور 7
DATE OF CASTING	20-Aug-2023	SPECIFIED STRENGTH	400 kg/cm ²
POURED QUANTITY	22 m	NO. OF CUBES MADE	
CONCRETE SLUMP	200 mm	date of test	23-Aug-2023
TAPE	100:230mm	CONCRETE TEMP (°C)	25

Specimen	1	2	3		
Age of Test (Days)	3	3	3		
Average Dimension (mm)	150	150	150		
Weight (g)	8530	8574	8611		
Density (kg/m ³)	2827	2870	2881		
Failure Load (kN)	903	826	817		
Comp. Strength (Kgf/cm ²)	409	374	370		
Mode of Failure	A	A	A		
Average 28 Days	385				
%	96				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory **MODES OF FAILURE AS PER BS 1881: Unsatisfactory**



Remarks :



Density measurement is carried out in accordance with BS


1881:Part 114 in the as received condition for moist specimens and in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant

مع التأكيد ان هذه النتائج استوفت
مطلوب




DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Contn/Type	350/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	أبواب مرسى
DATE OF CASTING	2-Sep-2023	SPECIFIED STRENGTH	250 kg/cm ²
POURED QUANTITY	45	NO. OF CUBES MADE	
CONCRETE SLUMP	200 mm	date of test	9-Sep-2023
TARGET SLUMP	200:230mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3		
Age of Test (Days)	7	7	7		
Average Dimension (mm)	150	150	150		
Weight (g)	8367	8371	8362		
Density (kg/m ³)	2479	2480	2478		
Failure Load (kN)	527	565	526		
Comp. Strength Kg/cm ²	239	256	238		
Mode of Failure	A	A	A		
Average 28 Days	244				
Ratio%	97.80				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER B: Unsatisfactory



Remarks :

Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant

DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	350/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	لجوجيرسي
DATE OF CASTING	18-Sep-2023	SPECIFIED STRENGTH	250 kg/cm ²
POURED QUANTITY	10	NO. OF CUBES MADE	
CONCRETE SLUMP	200 mm	date of test	25-Sep-2023
TARGET SLUMP	200-230mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3			
Age of Test (Days)	7	7	7			
Average Dimension (mm)	150	150	150			
Weight (g)	8374	8365	8396			
Density (kg/m ³)	2481	2479	2488			
Failure Load (kN)	545	573	526			
Comp. Strength Kg/cm ²	247	260	238			
Mode of Failure	A	A	A			
Average 28 Days	248					
Ratio %	99.37					

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER B: Unsatisfactory



Remarks :


Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and
in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant



DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES


Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	350/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	جسر
DATE OF CASTING	19-Sep-2023	SPECIFIED STRENGTH	250 kg/cm ²
POURED QUANTITY	10	NO. OF CUBES MADE	
CONCRETE SLUMP	200 mm	date of test	26-Sep-2023
TARGET SLUMP	160-230mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3			
Age of Test (Days)	7	7	7			
Average Dimension (mm)	150	150	150			
Weight (g)	8388	8405	8354			
Density (kg/m ³)	2485	2490	2475			
Failure Load (kN)	509	527	547			
Comp. Strength Kg/cm ²	231	239	248			
Mode of Failure	A	A	A			
Average 28 Days	239					
Ratio %	95.68					

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER B: Unsatisfactory



Remarks :

Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and

in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant



المهندسون الاستشاريون العرب
معهم - بلخوم



UNIBUILD
INDUSTRIES & CONSTRUCTION


DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	350/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	جسر
DATE OF CASTING	20-Sep-2023	SPECIFIED STRENGTH	250 kg/cm ²
POURED QUANTITY	13	NO. OF CUBES MADE	
CONCRETE SLUMP	200 mm	date of test	27-Sep-2023
TARGET SLUMP	200:230mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3		
Age of Test (Days)	7	7	7		
Average Dimension (mm)	150	150	150		
Weight (g)	8378	8390	8351		
Density (kg/m ³)	2482	2486	2474		
Failure Load (kN)	560	517	530		
Comp. Strength Kg/cm ²	254	234	240		
Mode of Failure	A	A	A		
Average 28 Days	243				
Ratio%	97.13				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983



Remarks :


Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant




DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	350/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	جسر
DATE OF CASTING	21-Sep-2023	SPECIFIED STRENGTH	250 kg/cm ²
POURED QUANTITY	18	NO. OF CUBES MADE	
CONCRETE SLUMP	200 mm	date of test	28-Sep-2023
TARGET SLUMP	230:230mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3		
Age of Test (Days)	7	7	7		
Average Dimension (mm)	150	150	150		
Weight (g)	8354	8382	8395		
Density (kg/m ³)	2475	2484	2487		
Failure Load (kN)	578	511	544		
Comp. Strength Kg/cm ²	262	232	247		
Mode of Failure	A	A	A		
Average 28 Days	247				
Ratio %	98.71				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983



Remarks :

Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC-Engineer	QC Consultant


DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	350/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	أبواب حديدية
DATE OF CASTING	23-Sep-2023	SPECIFIED STRENGTH	250 kg/cm ²
POURED QUANTITY	13	NO. OF CUBES MADE	
CONCRETE SLUMP	200 mm	date of test	30-Sep-2023
TARGET SLUMP	200:230mm	CONCRETE TEMP. (°C)	25

Specimen Reference	1	2	3		
Age of Test (Days)	7	7	7		
Average Dimension (mm)	150	150	150		
Weight (g)	8376	8366	8355		
Density (kg/m ³)	2482	2479	2476		
Failure Load (kN)	552	570	535		
Comp. Strength Kg/cm ²	250	258	243		
Mode of Failure	A	A	A		
Average 28 Days	250				
Ratio %	100.16				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER B: Unsatisfactory



Remarks :


Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and in the saturated condition for laboratory cured specimens.

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant



DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Contn/Type	350/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	جسر
DATE OF CASTING	24-Sep-2023	SPECIFIED STRENGTH	250 kg/cm ²
POURED QUANTITY	13	NO. OF CUBES MADE	
CONCRETE SLUMP	200 mm	date of test	1-Oct-2023
TARGET SLUMP	200:230mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3		
Age of Test (Days)	7	7	7		
Average Dimension (mm)	150	150	150		
Weight (g)	8361	8408	8361		
Density (kg/m ³)	2477	2491	2477		
Failure Load (kN)	504	542	510		
Comp. Strength Kg/cm ²	228	246	231		
Mode of Failure	A	A	A		
Average 28 Days	235				
Ratio %	94.05				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983



Remarks :


Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant




DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	350/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	جسر
DATE OF CASTING	2-Sep-2023	SPECIFIED STRENGTH	150 kg/cm ²
POURED QUANTITY	13	NO. OF CUBES MADE	
CONCRETE SLUMP	200 mm	date of test	30-Sep-2023
TARGET SLUMP	200:230mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3		
Age of Test (Days)	28	28	28		
Average Dimension (mm)	150	150	150		
Weight (g)	8369	8370	8355		
Density (kg/m ³)	2480	2480	2476		
Failure Load (kN)	592	579	585		
Comp. Strength Kg/cm ²	268	262	265		
Mode of Failure	A	A	A		
Average 28 Days	265				
Ratio%	106.14				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983



Remarks :

Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant



المهندسون الاستشاريون العرب
مكرم - بالقوم



UNIBUILD
INDUSTRIES & CONSTRUCTION

DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY _____ :	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD _____ :	BS 1881
CONSULTANT	ACE	Cement Content/Type	350/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE _____ :	جسر دائري
DATE OF CASTING	25-Sep-2023	SPECIFIED STRENGTH _____ :	250 kg/cm ²
POURED QUANTITY	13	NO. OF CUBES MADE _____ :	
CONCRETE SLUMP	200 mm	date of test	2-Oct-2023
TARGET SLUMP	200:230mm	CONCRETE TEMP (°C) _____ :	25

Specimen Reference	1	2	3		
Age of Test (Days)	7	7	7		
Average Dimension (mm)	150	150	150		
Weight (g)	8402	8391	8347		
Density (kg/m ³)	2489	2486	2473		
Failure Load (kN)	572	502	575		
Comp. Strength Kg/cm ²	259	228	261		
Mode of Failure	A	A	A		
Average 28 Days	249				
Ratio %	99.67				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983



Remarks :

Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and
in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant

DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	275/GFC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	جسر
DATE OF CASTING	6-Sep-2023	SPECIFIED STRENGTH	200 kg/cm ²
POURED QUANTITY	22	NO. OF CUBES MADE	
CONCRETE SLUMP	150 mm	date of test	13-Sep-2023
TARGET SLUMP	1400:170mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3		
Age of Test (Days)	7	7	7		
Average Dimension (mm)	150	150	150		
Weight (g)	8264	8236	8314		
Density (kg/m ³)	2449	2440	2463		
Failure Load (kN)	422	410	438		
Comp. Strength Kg/cm ²	191	186	199		
Mode of Failure	A	A	A		
Average 28 Days	192				
Ratio %	96				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER B: Unsatisfactory



Remarks :

Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and

in the saturated condition for laboratory cured specimens

Note : T Indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant




DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	275/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	جسر
DATE OF CASTING	7-Sep-2023	SPECIFIED STRENGTH	200 kg/cm ²
POURED QUANTITY	18	NO. OF CUBES MADE	
CONCRETE SLUMP	150 mm	date of test	14-Sep-2023
TARGET SLUMP	1400:170mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3		
Age of Test (Days)	7	7	7		
Average Dimension (mm)	150	150	150		
Weight (g)	8314	8236	8324		
Density (kg/m ³)	2463	2440	2466		
Failure Load (kN)	431	420	440		
Comp. Strength Kg/cm ²	195	190	199		
Mode of Failure	A	A	A		
Average 28 Days	195				
Ratio %	98				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER BS Unsatisfactory



Remarks :

Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and
in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant

DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	275/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	جسر
DATE OF CASTING	16-Sep-2023	SPECIFIED STRENGTH	200 kg/cm ²
FOURED QUANTIT	18	NO. OF CUBES MADE	
CONCRETE SLUMP	150 mm	date of test	23-Sep-2023
TARGET SLUMP	1400:170mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3		
Age of Test (Days)	7	7	7		
Average Dimension (mm)	150	150	150		
Weight (g)	8254	8246	8314		
Density (kg/m ³)	2446	2443	2463		
Failure Load (kN)	428	431	451		
Comp. Strength Kg/cm ²	194	195	204		
Mode of Failure	A	A	A		
Average 28 Days	198				
Ratio %	99.0				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983





Remarks :

Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and
in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant
			



المهندسون الإستشاريون العرب
مصر - بالقاهرة



UNIBUILD
INDUSTRIES & CONSTRUCTION

DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	275/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	جسر
DATE OF CASTING	17-Sep-2023	SPECIFIED STRENGTH	200 kg/cm ²
POURED QUANTITY	25	NO. OF CUBES MADE	
CONCRETE SLUMP	150 mm	date of test	24-Sep-2023
TARGET SLUMP	1400:170mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3		
Age of Test (Days)	7	7	7		
Average Dimension (mm)	150	150	150		
Weight (g)	8324	8364	8264		
Density (kg/m ³)	2466	2478	2449		
Failure Load (kN)	427	451	433		
Comp. Strength Kg/cm ²	194	204	196		
Mode of Failure	A	A	A		
Average 28 Days	198				
Ratio %	99.1				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983



Remarks :

Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and
in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant


DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	275/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	جسر
DATE OF CASTING	18-Sep-2023	SPECIFIED STRENGTH	200 kg/cm ²
POURED QUANTITY	36	NO. OF CUBES MADE	
CONCRETE SLUMP	150 mm	date of test	25-Sep-2023
TARGET SLUMP	1400:170mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3		
Age of Test (Days)	7	7	7		
Average Dimension (mm)	150	150	150		
Weight (g)	8391	8314	8258		
Density (kg/m ³)	2486	2463	2447		
Failure Load (kN)	462	425	441		
Comp. Strength Kg/cm ²	209	193	200		
Mode of Failure	A	A	A		
Average 28 Days	201				
Ratio %	100.3				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER B: Unsatisfactory



Remarks :

Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant




DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	275/OPC
OWNER	الهيئة العامة للطرق والمواصلات	STRUCTURE TYPE	جسر
DATE OF CASTING	19-Sep-2023	SPECIFIED STRENGTH	200 kg/cm ²
POURED QUANTITY	27	NO. OF CUBES MADE	
CONCRETE SLUMP	150 mm	date of test	26-Sep-2023
TARGET SLUMP	1400:170mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3			
Age of Test (Days)	7	7	7			
Average Dimension (mm)	150	150	150			
Weight (g)	8339	8356	8283			
Density (kg/m ³)	2471	2476	2454			
Failure Load (kN)	433	435	426			
Comp. Strength Kg/cm ²	196	197	193			
Mode of Failure	A	A	A			
Average 28 Days	196					
Ratio%	97.8					

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983



Remarks :

Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant



DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	275/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	جسر
DATE OF CASTING	26-Sep-2023	SPECIFIED STRENGTH	206 kg/cm ²
POURED QUANTITY	27	NO. OF CUBES MADE	
CONCRETE SLUMP	150 mm	date of test	27-Sep-2023
TARGET SLUMP	1400:170mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3		
Age of Test (Days)	7	7	7		
Average Dimension (mm)	150	150	150		
Weight (g)	8355	8328	8329		
Density (kg/m ³)	2476	2468	2468		
Failure Load (kN)	444	428	447		
Comp. Strength Kg/cm ²	201	194	203		
Mode of Failure	A	A	A		
Average 28 Days	199				
Ratio %	99.7				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER B: Unsatisfactory



Remarks :

Density measurement is carried out in accordance with BS


1881:Part 114 in the as received condition for moist specimens and

in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant




DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	27S/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	جسر
DATE OF CASTING	21-Sep-2023	SPECIFIED STRENGTH	200 kg/cm ²
POURED QUANTITY	27	NO. OF CUBES MADE	
CONCRETE SLUMP	150 mm	date of test	28-Sep-2023
TARGET SLUMP	1400:170mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3		
Age of Test (Days)	7	7	7		
Average Dimension (mm)	150	150	150		
Weight (g)	8318	8272	8272		
Density (kg/m ³)	2465	2451	2451		
Failure Load (kN)	431	459	441		
Comp. Strength Kg/cm ²	195	203	200		
Mode of Failure	A	A	A		
Average 28 Days	201				
Ratio%	100.6				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER B: Unsatisfactory



Remarks :


Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC-Engineer	QC Consultant




DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	275/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	جسر
DATE OF CASTING	23-Sep-2023	SPECIFIED STRENGTH	200 kg/cm ²
POURED QUANTITY	27	NO. OF CUBES MADE	
CONCRETE SLUMP	150 mm	date of test	30-Sep-2023
TARGET SLUMP	1400:170mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3		
Age of Test (Days)	7	7	7		
Average Dimension (mm)	150	150	150		
Weight (g)	8284	8323	8253		
Density (kg/m ³)	2455	2466	2445		
Failure Load (kN)	463	427	425		
Comp. Strength Kg/cm ²	210	194	193		
Mode of Failure	A	A	A		
Average 28 Days	199				
Ratio%	99.4				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983



Remarks :


Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant





DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	275/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	جسر
DATE OF CASTING	24-Sep-2023	SPECIFIED STRENGTH	200 kg/cm ²
POURED QUANTITY	41	NO. OF CUBES MADE	
CONCRETE SLUMP	150 mm	date of test	1-Oct-2023
TARGET SLUMP	140-170mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3		
Age of Test (Days)	7	7	7		
Average Dimension (mm)	150	150	150		
Weight (g)	8288	8277	8324		
Density (kg/m ³)	2456	2452	2466		
Failure Load (kN)	438	438	445		
Comp. Strength Kg/cm ²	199	199	202		
Mode of Failure	A	A	A		
Average 28 Days	200				
Ratio %	99.8				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER BS Unsatisfactory



Remarks :

Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC-Engineer	QC Consultant

DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	275/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	جسر
DATE OF CASTING	28-Aug-2023	SPECIFIED STRENGTH	200 kg/cm ²
POURED QUANTITY	36	NO. OF CUBES MADE	
CONCRETE SLUMP	150 mm	date of test	25-Sep-2023
TARGET SLUMP	1400:170mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3		
Age of Test (Days)	28	28	28		
Average Dimension (mm)	150	150	150		
Weight (g)	8363	8319	8360		
Density (kg/m ³)	2478	2465	2477		
Failure Load (kN)	491	497	498		
Comp. Strength Kg/cm ²	223	225	226		
Mode of Failure	A	A	A		
Average 28 Days	225				
Ratio %	112.3				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983



Remarks :

Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant



DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES


Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	275/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	جول
DATE OF CASTING	29-Aug-2023	SPECIFIED STRENGTH	200 kg/cm ²
POURED QUANTITY	36	NO. OF CUBES MADE	
CONCRETE SLUMP	150 mm	date of test	26-Sep-2023
TARGET SLUMP	1400:170mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3		
Age of Test (Days)	28	28	28		
Average Dimension (mm)	150	150	150		
Weight (g)	8258	8337	8361		
Density (kg/m ³)	2447	2470	2477		
Failure Load (kN)	470	484	500		
Comp. Strength Kg/cm ²	213	219	227		
Mode of Failure	A	A	A		
Average 28 Days	220				
Ratio%	109.9				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER B: Unsatisfactory



Remarks :

Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and

in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant




DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY _____	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD _____	BS 1881
CONSULTANT	ACE	Cement Contn/Type	275OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE _____	جسر
DATE OF CASTING	36-Aug-2023	SPECIFIED STRENGTH _____	200 kg/cm ²
POURED QUANTITY	38	NO. OF CUBES MADE _____	
CONCRETE SLUMP	150 mm	date of test	27-Sep-2023
TARGET SLUMP	1400:170mm	CONCRETE TEMP (°C) _____	25

Specimen Reference	1	2	3		
Age of Test (Days)	28	28	28		
Average Dimension (mm)	150	150	150		
Weight (g)	8349	8363	8286		
Density (kg/m ³)	2474	2478	2455		
Failure Load (kN)	527	522	540		
Comp. Strength Kg/cm ²	239	237	245		
Mode of Failure	A	A	A		
Average 28 Days	240				
Ratio %	120.1				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER B Unsatisfactory



Remarks :

Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and in the saturated condition for laboratory cured specimens

Note : T Indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant



DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Concn/Type	275/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	جسر
DATE OF CASTING	3-Sep-2023	SPECIFIED STRENGTH	200 kg/cm ²
POURED QUANTITY	27	NO. OF CUBES MADE	
CONCRETE SLUMP	150 mm	date of test	1-Oct-2023
TARGET SLUMP	1400:170mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3		
Age of Test (Days)	28	28	28		
Average Dimension (mm)	150	150	150		
Weight (g)	8344	8337	8339		
Density (kg/m ³)	2472	2470	2471		
Failure Load (kN)	501	475	521		
Comp. Strength Kg/cm ²	227	215	236		
Mode of Failure	A	A	A		
Average 28 Days	226				
Ratio %	113.1				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983



Remarks :

Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant



المهندسون الاستشاريون العرب
مقدم - بالقرن



UNIBUILD
INDUSTRIES & CONSTRUCTION


DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	275/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	جسر
DATE OF CASTING	4-5-2023	SPECIFIED STRENGTH	200 kg/cm ²
POURED QUANTITY	27	NO. OF CUBES MADE	
CONCRETE SLUMP	150 mm	date of test	2-Oct-2023
TARGET SLUMP	1400:170mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3		
Age of Test (Days)	28	28	28		
Average Dimension (mm)	150	150	150		
Weight (g)	8357	8269	8279		
Density (kg/m ³)	2476	2450	2453		
Failure Load (kN)	507	515	516		
Comp. Strength Kg/cm ²	230	233	234		
Mode of Failure	A	A	A		
Average 28 Days	232				
Ratio%	116.2				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983




Remarks :

Density measurement is carried out in accordance with BS 1881: Part 114 in the as received condition for moist specimens and in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant



DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY _____ :	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD _____ :	BS 1881
CONSULTANT	ACE	Cement Conen/Type	275/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE _____ :	جسر
DATE OF CASTING	25-Sep-2023	SPECIFIED STRENGTH _____ :	200 kg/cm ²
POURED QUANTITY	41	NO. OF CUBES MADE _____ :	
CONCRETE SLUMP	150 mm	date of test	2-Oct-2023
TARGET SLUMP	1400:170mm	CONCRETE TEMP (°C) _____ :	25

Specimen Reference	1	2	3		
Age of Test (Days)	7	7	7		
Average Dimension (mm)	150	150	150		
Weight (g)	8290	8328	8286		
Density (kg/m ³)	2456	2468	2455		
Failure Load (kN)	431	426	433		
Comp. Strength Kg/cm ²	195	193	196		
Mode of Failure	A	A	A		
Average 28 Days	195				
Ratio%	97.5				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER B: Unsatisfactory



Remarks :


Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant




DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES
Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content Type	275/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	جسر
DATE OF CASTING	28-Aug-2023	SPECIFIED STRENGTH	200 kg/cm ²
POURED QUANTITY	76	NO. OF CUBES MADE	
CONCRETE SLUMP	150 mm	date of test	4-Sep-2023
TARGET SLUMP	1400:170mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3			
Age of Test (Days)	7	7	7			
Average Dimension (mm)	150	150	150			
Weight (g)	8214	8314	8456			
Density (kg/m ³)	2434	2463	2505			
Failure Load (kN)	420	411	386			
Comp. Strength Kg/cm ²	190	186	175			
Mode of Failure	A	A	A			
Average 28 Days	184					
Ratio %	92					

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER B Unsatisfactory




Remarks :

Density measurement is carried out in accordance with BS 1881:Part 114 in the as received condition for moist specimens and in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant



DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES


Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Conten/Type	275/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	جول
DATE OF CASTING	29-Aug-2023	SPECIFIED STRENGTH	200 kg/cm2
POURED QUANTITY	36	NO. OF CUBES MADE	
CONCRETE SLUMP	150 mm	date of test	5-Sep-2023
TARGET SLUMP	1400:170mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3		
Age of Test (Days)	7	7	7		
Average Dimension (mm)	150	150	150		
Weight (g)	8124	8361	8451		
Density (kg/m³)	2407	2477	2504		
Failure Load (kN)	394	405	455		
Comp. Strength Kg/cm²	179	184	206		
Mode of Failure	A	A	A		
Average 28 Days	189				
Ratio%	95				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER B: Unsatisfactory



Remarks :

Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant



DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES


Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	275/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	جسر
DATE OF CASTING	3-Sep-2023	SPECIFIED STRENGTH	200 kg/cm ²
POURED QUANTITY	27	NO. OF CUBES MADE	
CONCRETE SLUMP	150 mm	date of test	16-Sep-2023
TARGET SLUMP	1400:170mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3		
Age of Test (Days)	7	7	7		
Average Dimension (mm)	150	150	150		
Weight (g)	8254	8314	8264		
Density (kg/m ³)	2446	2463	2449		
Failure Load (kN)	421	451	400		
Comp. Strength kg/cm ²	191	204	181		
Mode of Failure	A	A	A		
Average 28 Days	192				
Ratio%	96				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1983

Satisfactory MODES OF FAILURE AS PER B: Unsatisfactory



Remarks :

Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant



DETERMINATION OF COMPRESSIVE STRENGTH OF CONCRETE CUBES


Test Standard BS 1881

CLIENT	UNIBUILD	SAMPLED BY	UNIBUILD
PROJECT	Alameen Bridge	SAMPLING METHOD	BS 1881
CONSULTANT	ACE	Cement Content/Type	275/OPC
OWNER	الهيئة العامة للطرق والكباري	STRUCTURE TYPE	جسر
DATE OF CASTING	5-Sep-2023	SPECIFIED STRENGTH	160 kg/cm ²
POURED QUANTITY	36	NO. OF CUBES MADE	
CONCRETE SLUMP	150 mm	date of test	12-Sep-2023
TARGET SLUMP	1400:170mm	CONCRETE TEMP (°C)	25

Specimen Reference	1	2	3		
Age of Test (Days)	7	7	7		
Average Dimension (mm)	150	150	150		
Weight (g)	8236	8314	8210		
Density (kg/m ³)	2440	2463	2433		
Failure Load (kN)	412	436	415		
Comp. Strength Kg/cm ²	187	198	188		
Mode of Failure	A	A	A		
Average 28 Days	191				
Ratio%	95				

MODES OF FAILURE AS PER BS 1881 : Part 116 : 1993

Satisfactory MODES OF FAILURE AS PER B: Unsatisfactory



Remarks :

Density measurement is carried out in accordance with BS

1881:Part 114 in the as received condition for moist specimens and in the saturated condition for laboratory cured specimens

Note : T indicates tensile cracking

Remarks : Specified Loading Rate Range = 4.5kN/S to 9.0 kN/S or (6.8kN/S)

Lab Technician	Lab Incharge	QC Engineer	QC Consultant



تقرير فني عن تجربة تحميل

كوبري دوران (U2) بطريق وادي النطرون - العلمين - الكيلو
(٢٤+٨٠٠)

بإجمالي باكيتين بين محاور

A2 - A3 & A3 - A4

المالك

الهيئة العامة للطرق والكباري والنقل البري

إستشاري المالك

المهندسون الإستشاريون العرب

محرم باخوم

تنفيذ

شركة يوني بيلد



Report No. BR-24-8-2

مارس ٢٠٢٤





المحتويات

٣	١- المقدمة.....
٣	٢- برنامج إجراء التجربة.....
٤	٣- أجهزة القياس المستخدمة.....
٤	٣-١- أجهزة قياس الترخيم.....
٤	٣-٢- أجهزة قياس الإنفعال.....
٦	٤- توصيف واختبار ونتائج تجربة تحميل الباكية A2-A3.....
٦	٤-١- وصف الكوبري.....
٦	٤-٢- موقع التجربة.....
٧	٤-٣- طريقة التحميل.....
٩	٤-٤- نتائج تجربة التحميل.....
١٣	٤-٥- ملخص نتائج التجربة.....
١٣	٤-٥-١- نتائج الإنفعال.....
١٣	٤-٥-٢- نتائج الترخيم.....
١٤	٥- توصيف واختبار ونتائج تجربة تحميل الباكية A3-A4.....
١٤	٥-١- وصف الكوبري.....
١٤	٥-٢- موقع التجربة.....
١٥	٥-٣- طريقة التحميل.....
١٧	٥-٤- نتائج تجربة التحميل.....
٢١	٥-٥- ملخص نتائج التجربة.....
٢١	٥-٥-١- نتائج الإنفعال.....
٢١	٥-٥-٢- نتائج الترخيم.....
٢٢	ملحق (أ): شهادة المعايرة لجهاز محطة الرصد.....
٢٣	ملحق (ب): شهادة اختبار مقاييس الإنفعال.....
٢٦	ملحق (ج): مواصفات جهاز مبين قراءات الإنفعال.....



ر.م. الكرم



تقرير فني عن تجارب تحميل

كوبري دوران (U2) بطريق وادي النطرون - العلمين - الكيلو (٢٤+٨٠٠)

بإجمالي باكيتين بين محاور

A2 - A3 & A3 - A4

١- المقدمة

هذا التقرير مقدم بناءً على تكليف شركة بوني بيلد - لوحدة أبحاث الخرسانة المسلحة بكلية الهندسة - جامعة عين شمس، بإجراء تجارب تحميل للباكيات بين محاور A2-A3 و A3-A4 وذلك طبقاً للرسومات والمعلومات الموضحة في خطاب إستشاري المشروع. وقد قام أعضاء وحدة أبحاث الخرسانة المسلحة بكلية الهندسة - جامعة عين شمس - بعمل معاينة للموقع وإعطاء التوجيهات اللازمة لعمل التجهيزات الخاصة بالتجربة، وقد تم إستلام التجهيزات وإجراء تجربة التحميل يوم الاثنين الموافق ٢٠٢٤/٠٣/٠٤، وذلك في حضور مهندس الشركة وإستشاري المالك.

ويشتمل هذا التقرير بالإضافة للمقدمة، على برنامج إجراء التجربة، أجهزة القياس المستخدمة، وصف الكوبري، موقع التجربة، طريقة التحميل، نتائج التجربة وملخص لهذه النتائج، ومرفق في المخرجات شهادات معايرة الأجهزة المستخدمة في تسجيل القراءات.

٢- برنامج إجراء التجربة

بعد معاينة الموقع ودراسة متطلبات إجراء التجارب الواردة من المكتب الإستشاري للمالك والتي تتضمن قياس الترخيم أسفل الباكيتين A2-A3 و A3-A4 وقياس إنفعال الخرسانة أعلى هذه الباكيات. وقد تم توقيع أماكن قياس الترخيم والإنفعال طبقاً لخطاب السيد المهندس الإستشاري والمرفق به كروكيات لأماكن هذه القياسات. كما تم تسجيل قراءات الترخيم والإنفعال كما يلي:


- أ - تسجيل قراءات مرجعية للترخيم والإنفعال وكذلك قياس درجات الحرارة قبل التحميل مباشرة.
- ب - تسجيل قراءات الترخيم والإنفعال ودرجات الحرارة بعد التحميل الكلي مباشرة ثم كل ساعة لمدة ٦ ساعات أو حتى ثبات قراءتين متتاليتين (أيهما أقرب).



٣







- ج - تسجيل قراءات الترخيم والإنفعال ودرجات الحرارة بعد رفع الحمل الكلي مباشرة.
د - تسجيل قراءات الترخيم والإنفعال ودرجات الحرارة كل نصف ساعة بعد رفع الحمل وذلك لمدة ساعتين أو ارتداد ٧٥ % من القيمة القصوى أثناء التحميل (أيهما أقرب).

٣- أجهزة القياس المستخدمة

٣-١- أجهزة قياس الترخيم

تم قياس الترخيم مساحياً باستخدام جهاز محطة الرصد المتكاملة (Topcon GPT - 7502 total station) بقرأ حتى ١ مم وبدقة رصد للزوايا تصل الى ($2'' 0' 0''$) ودقة قياس للمسافات تساوي ($2mm + 2PPM * distance(mm)$). تم تحديد أماكن نقاط الترخيم أسفل كميرات الكوبري لكل تجربة وتم رصد قيم الترخيم بالنقاط المختلفة أسفل كميرات الكوبري والمثبت بها عواكس. كما تم مراعاة أن تكون نقاط الثوابت المرجعية بعيدة بالقدر الكافي عن منطقة التحميل لضمان عدم تأثرها بأي غيوط يحدث مع رصد النقطة الواحدة عدة مرات وأخذ المتوسط الحسابي. مرفق في ملحق (أ) شهادة معايرة الجهاز.




شكل رقم (٣-١): جهاز محطة الرصد المتكاملة المستخدم لقياس الترخيم والعاكس أسفل الكميرات






٢-٣ - أجهزة قياس الإنفعال

تم قياس الإنفعال الطولي كهربيًا على السطح الخرساني العلوي للكوبري بتهيئة مقاييس انفعال كهربية (من طراز Kyowa يابانية الصنع) بطول قياس ٦٠ مم (مرفق شهادة إختيار مقاييس الإنفعال في ملحق (ب))، وتم توصيل جميع هذه المقاييس الكهربية بصندوق توصيل (Channel box) وكذلك مبين لقراءات الإنفعال (Strain indicator) (مرفق مواصفات جهاز مبين قراءات الإنفعال في ملحق (ج)) ، كما في الشكل رقم (٢-٣). ولتهيئة مقاييس الإنفعال الكهربية (Strain gauges) على السطح الخرساني العلوي للكوبري تم تجليخ السطح الخرساني بطول حوالي ٢٠٠ مم في الإتجاه الطولي للكوبري وبعرض حوالي ٢٠٠ مم و تنظيف المكان و السطح ذلك. وتم تهيئة مقاييس الإنفعال على السطح الخرساني بواسطة مادة لائحة شديدة التماسك، كما في الشكل رقم (٢-٣). وفيما يلي تفاصيل تحميل الباكيات المختبرة ونتائجها.

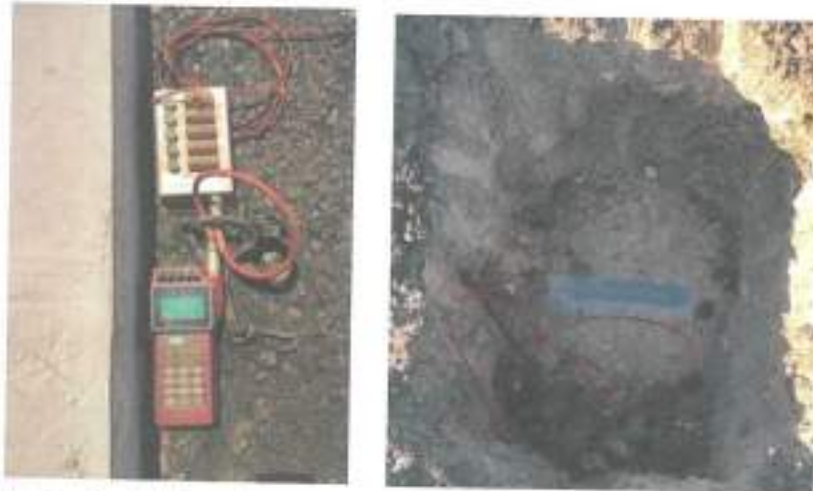

شكل رقم (٢-٣): صندوق التوصيل ومبين القراءات وكيفية تهيئة مقاييس الإنفعال أعلى السطح الخرساني العلوي للكوبري





٤- توصيف واختبار ونتائج تجربة تحميل الباكية A2-A3

٤-١- وصف الكوبري

يتكون النظام الإنشائي للباكية المختبرة بين محوري (A2-A3) من قطاع صندوقي ثنائي الغرف، بعنق إجمالي ٢,٠٠ متر، وممك بلاطة علوية ٢٥ سم إلى ٤٠ سم أعلي الجذوع، وممك الجذوع ٤٠ سم إلى ٦٥ سم، وممك البلاطة السفلية ٢٠ إلى ٣٢ سم. يرتكز القطاع الصندوقي في الاتجاه الطولي علي أعمدة خرسانية كما هو موضح بالشكل رقم (٤-١). الباكية المختبرة ذات بحر حوالي ٣٢ متر وعرض ٣٨,٩٢ متر مع وجود فاصل طولي في منتصف عرض الكوبري وبكامل طوله.




شكل رقم (٤-١): النظام الإنشائي للباكية المختبرة

٤-٢- موقع التجربة


تم تحديد موقع تجربة التحميل بمعرفة للمكتب الاستشاري للمالك وهي كما هو موضح بالأشكال من رقم (٤-٢) وحتى رقم (٤-٣). كما توضح هذه الأشكال ايضاً أماكن إيقاف عربات التحميل وأماكن قبس الترخيم والإنفعال أثناء الاختبار.



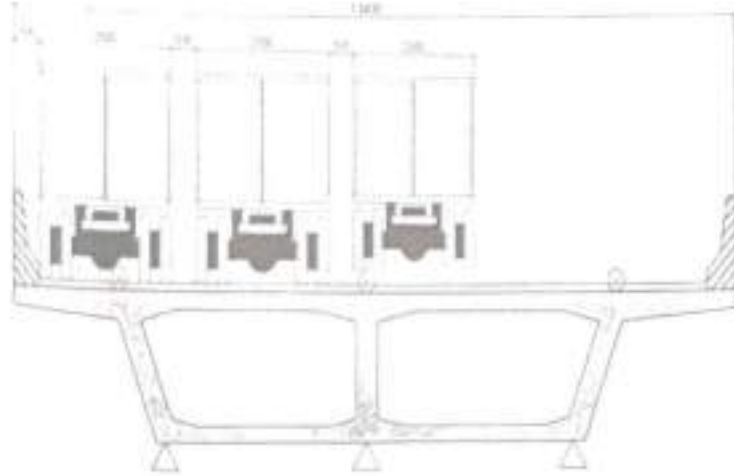

D: نقاط قياس ترخيم S: نقاط قياس إنفعال

شكل رقم (٤-٢): أماكن عربات التحميل وأماكن قياس الإنفعال والترخيم على قطاع الكوبري العرضي

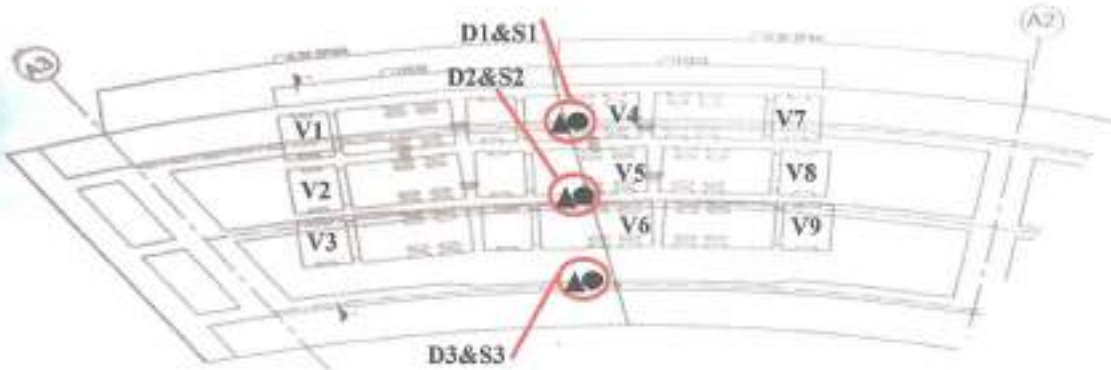

D: نقاط قياس ترخيم S: نقاط قياس إنفعال
V: عربات التحميل

Electric strain gauge
Deflectometer

شكل رقم (٤-٣): أماكن عربات التحميل وأماكن قياس الإنفعال والترخيم على المسقط الأفقي للبلاكية المختبرة

٤-ج- طريقة التحميل

تم تحميل البلاكية الخرسانية بين المحورين (A2-A3) بعدد تسعة سيارات نقل قلاب (Trucks) محملة بالرمل وموزعة طبقاً لتعليمات المكتب الاستشاري للمشروع كما هو مبين بالأشكال من رقم (٤-١) وحتى رقم (٤-٤) (وقد تم وزن كل عربة على حدة بواسطة ميزان بسكول إلكتروني بمعرفة الشركة المنفذة للمشروع كما تم مراجعة شهادات الوزن لكل عربات التحميل بالموقع وذلك قبل إجراء تجربة التحميل. وقد بدأت التجربة في حوالي الساعة الرابعة إلا ثلث عصرًا يوم الإثنين الموافق ٢٠٢٤/٣/٢٤. وكانت أوزان العربات كالتالي:





الوزن (طن)	رقم السيارة	كود العربة
٣٢,٨١٣	٧٣٢٦	V1
٣٥,٩٩٧	١٥٨٤	V2
٣٣,٨٧٣	٧١٢٥	V3
٣٣,٢٦٢	٤٥٣٤	V4
٤٧,٩٤١	١٩٤٦	V5
٣٧,٠٦٦	٥٧١٤	V6
٣١,٦٢٥	٧٥٧١	V7
٣٥,٤٧١	٦٧٣٥	V8
٣٣,٠٠٣	٤٦٩٧	V9



Handwritten signature

شكل رقم (٤-٤): أماكن عربات التحميل على الباكيت المختبرية أثناء مراحل التحميل المختلفة





٤-٥ - نتائج تجربة التحميل

توضح الجداول المرفقة قيم الميوط أسفل الصندوق الخرساني ، وقيم الإنفعال على سطح البلاطة الخرسانية أعلي البلاطة الخرسانية نتيجة أحمال التجربة بالنسبة للمواضع المختلفة. كما توضح الأشكال من رقم (٤-٥) وحتى رقم (٤-٦) والجداول (٤-١) و(٤-٢) التغير في قيم الترخيم والإنفعال بالنسبة للمواضع المختلفة خلال خطوات التحميل.

جدول رقم (٤-١) - نتائج قياس الترخيم


قيم الترخيم أسفل الصندوق الخرساني للنقاط D1-D3

Readings	Time	Temp	Deflection (mms)		
			D1	D2	D3
Initial (Before loading)	15:40	23° C	0	0	0
Just after loading	15:50	23° C	10	9	9
0.5 hour after full loading	16:20	23° C	10	9	9
1 hour after full loading	16:50	23° C	10	9	9
1.5 hours after full loading	17:20	23° C	11	10	10
2 hours after full loading	17:50	23° C	11	10	10
Just after unloading	17:55	23° C	0	2	3
0.5 hour after unloading	18:25	23° C	0	2	3

** -ve sign indicates upward displacement

Handwritten signature



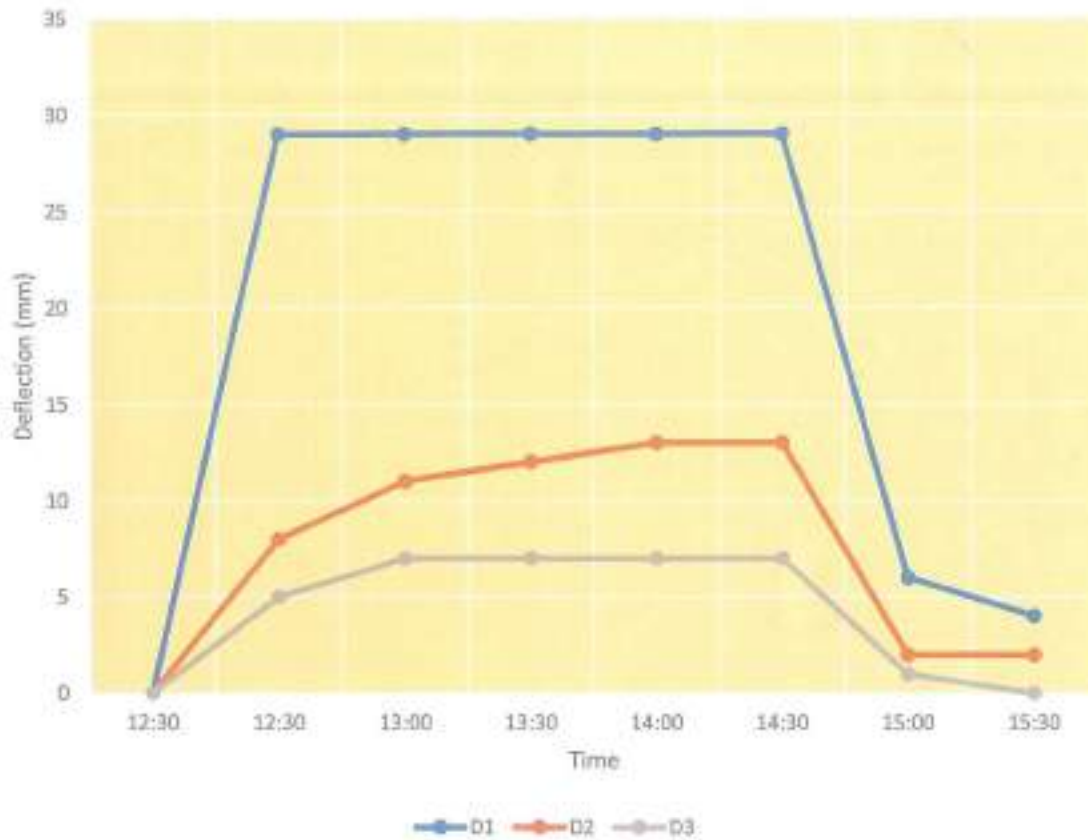

شكل رقم (٤-٥): التغير في قيم الترخيم للكمرة الأولى خلال خطوات التحميل المختلفة

مدير مركز الأبحاث
الهندسة

مدير مركز الأبحاث
الهندسة






جدول رقم (٢-٤) - نتائج قياس الإنفعال

قيم قياس الإنفعال على السطح الخرساني العلوي للكوبري أعلى البلاطة الخرسانية

Readings	Time	Temp	Strains (x10 ⁻⁶)		
			S1	S2	S3
Initial (Before loading)	15:40	23 ⁰ C	0	0	0
Just after loading	15:50	23 ⁰ C	-131	-96	-68
0.5 hour after full loading	16:20	23 ⁰ C	-147	-102	-76
1 hour after full loading	16:50	23 ⁰ C	-147	-102	-74
1.5 hours after full loading	17:20	23 ⁰ C	-147	-103	-75
2 hours after full loading	17:50	23 ⁰ C	-147	-104	-76
Just after unloading	17:55	23 ⁰ C	-8	-5	-2
0.5 hour after unloading	18:25	23 ⁰ C	-7	-4	-2

** -ve sign indicates compression strains



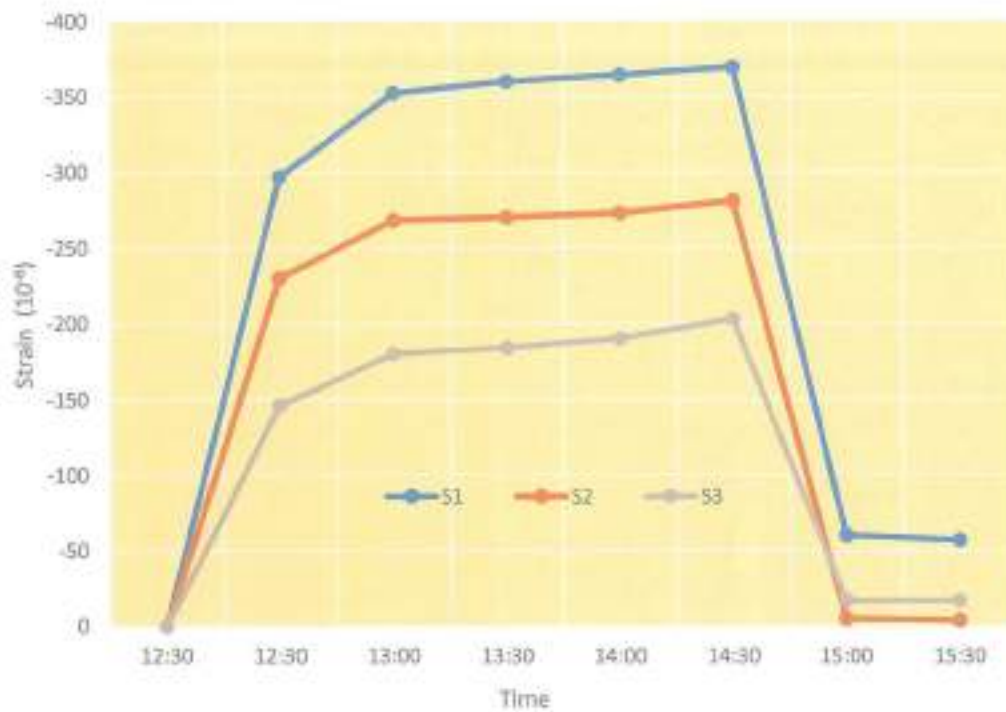

شكل رقم (٤-٦): التغير في قيم الإنفعال أعلى الكمرتين خلال خطوات التحميل المختلفة







٤-٥- ملخص نتائج التجربة

فيما يلي ملخصاً للقيم القصوى لكل من نتائج الترخيم والإنفعال ، والتي تم قياسها أثناء إجراء تجربة التحميل، وكذلك ملخصاً لقيم كل من نتائج الترخيم والإنفعال المتبقية بعد إزالة الحمل.

٤-٥-١ نتائج الإنفعال

- بملاحظة نتائج قياس الإنفعال على السطح الخرساني العلوي للكوبري يتبين أن أقصى قيمة للإنفعال قد حدثت عند النقطة (S1) والمبينة بالجدول رقم (٤-٢) وملخص نتائج الإنفعال كما يلي:
- أقصى انفعال أثناء التحميل $= 1.47 \times 10^{-6}$ (إنضغاط)
- الإنفعال المتبقي بعد إزالة الحمل بنصف ساعة $= 8 \times 10^{-6}$ (إنضغاط)
- نسبة الإنفعال المتبقي بعد إزالة الحمل بنصف ساعة / الإنفعال الأقصى $= 0.54\%$

٤-٥-٢ نتائج الترخيم

- بملاحظة قيم قياس الترخيم للكميرات الخرسانية يتبين أن أقصى قيمة للتخيم قد حدثت عند النقطة (D1) والمبينة بالجدول رقم (٤-١)، وكان ملخص نتائج الترخيم كما يلي:
- أقصى ترخيم أثناء التحميل $= 11.00$ مم
- الترخيم المتبقي بعد إزالة الحمل بنصف ساعة $= 0.00$ مم
- نسبة الترخيم المتبقي بعد إزالة الحمل بنصف ساعة / الترخيم الكلي $= 0.00\%$
- نسبة الترخيم الكلي الى طول الباكية (٤٢,٠٠ متر) $= 0.26\%$
- $= 381811$ من طول بحر الباكية

مدير مركز الأبحاث
الهندسة
أ.د. محمد عبد الله

أ.د. محمد عبد الله



٥- توصيف واختبار ونتائج تجربة تحميل الباكية A3-A4

٥-أ- وصف الكوبري

يتكون النظام الإنشائي للباكية المختبرة بين محوري (A3-A4) من عدد أربعة كمرات خرسانية علي شكل حرف T ذات عمق إجمالي ٢,٠٠ متر وتحمل فوقها بلاطة خرسانية مسلحة بسمك ٠,٢٥ متر. ترتكز الكمرات علي القطاع الصندوقي من جهة وعلي إطار خرساني من الجهة الأخرى كما هو موضح بالشكل رقم (٥-١). الكمرات المختبرة ذات طول إجمالي حوالي ٣١,٠٥ متر بين محور الركائز.




شكل رقم (٥-١): النظام الإنشائي للباكية المختبرة

٥-ب- موقع التجربة


تم تحديد موقع تجربة التحميل بمعرفة المكتب الاستشاري للمالك وهي كما هو موضح بالأشكال من رقم (٥-٢) وحتى رقم (٥-٣). كما توضح هذه الأشكال أيضاً أماكن إيقاف عربات التحميل وأماكن قياس الترخيم والإنفعال أثناء الاختبار.



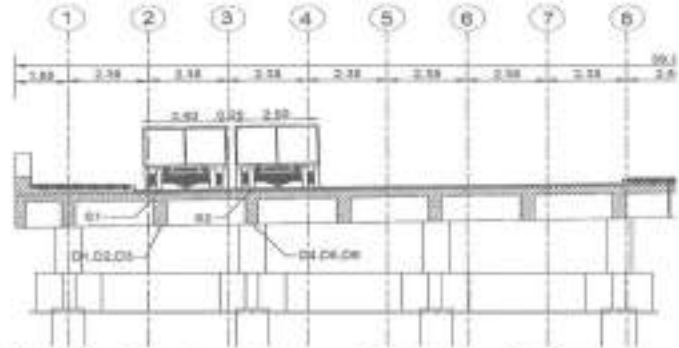

D : نقاط قياس الترخيم S : نقاط قياس الانفعال

شكل رقم (٥-٢): أماكن عربات التحميل وأماكن قياس الإنفعال والترخيم على قطاع الكوبري العرضي

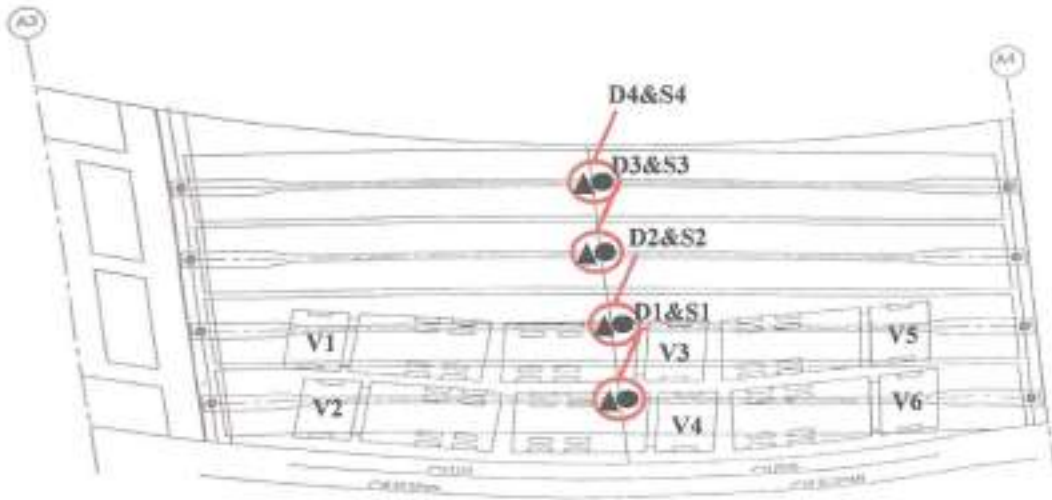

D : نقاط قياس الترخيم S : نقاط قياس الانفعال V : عربات التحميل

● Electronic strain gauge
▲ Deflectometer

شكل رقم (٥-٣): أماكن عربات التحميل وأماكن قياس الإنفعال والترخيم على المسقط الأفقي للباكية المختبرة

٥-ج- طريقة التحميل

تم تحميل الباكبة الخرسانية بين المحورين (A3-A4) بعدد ستة سيارات نقل قلاب (Trucks) محملة بالرمال وموزعة طبقاً لتعليمات المكتب الاستشاري للمشروع كما هو مبين بالأشكال من رقم (٥-٢) وحتى رقم (٥-٤) (وقد تم وزن كل عربة على حدة بواسطة ميزان بسكول إلكتروني بمعرفة الشركة المنفذة للمشروع كما تم مراجعة شهادات الوزن لكل عربات التحميل بالموقع وذلك قبل إجراء تجربة التحميل. وقد بدأت التجربة في حوالي الساعة الثانية عشر والنصف ظهراً يوم الاثنين الموافق ٢٠٢٤/٠٣/٠٣. وكانت أوزان العربات كالتالي:





الوزن (طن)	رقم السيارة	كود العربة
٣٥,٩٩٧	١٥٨٤	V1
٣٣,٢٦٢	٤٥٣٤	V2
٣٣,٨٧٣	٧١٢٥	V3
٣٣,٠٠٣	٤٦٩٧	V4
٣١,٦٢٥	٧٥٧١	V5
٣٧,٠٦٦	٥٧١٤	V6



شكل رقم (٥-٤): أماكن عربات التحميل على الباكية المختبرة أثناء مراحل التحميل المختلفة

فصلنامه علمی پژوهشی
فصلنامه علمی پژوهشی

[Handwritten signature]





٥-٥ - نتائج تجربة التحميل


توضح الجداول المرفقة قيم الإنفعال على سطح البلاطة الخرسانية والترخيم أسفل الكمرات الخرسانية نتيجة أحمال التجربة بالنسبة للمواضع المختلفة، كما توضح الأشكال من رقم (٥-٥) وحتى رقم (٦-٥) والجداول (١-٥) و(٢-٥) التغير في قيم الترخيم والإنفعال بالنسبة للمواضع المختلفة خلال خطوات التحميل.

جدول رقم (١-٥) - نتائج قياس الترخيم أسفل الكمرات الخرسانية للنقاط D1-D4

Readings	Time	Temp	Deflection (mms)			
			D1	D2	D3	D4
Initial (Before loading)	12:30	23° C	0	0	0	0
Just after loading	12:30	23° C	29	8	5	0
0.5 hour after full loading	13:00	23° C	29	11	7	0
1 hour after full loading	13:30	23° C	29	12	7	0
1.5 hours after full loading	14:00	23° C	29	13	7	0
2 hours after full loading	14:30	23° C	29	13	7	0
Just after unloading	15:00	23° C	6	2	1	0
0.5 hour after unloading	15:30	23° C	4	2	0	0
1 hour after unloading	16:00	23° C	2	1	0	0

** -ve sign indicates upward displacement.



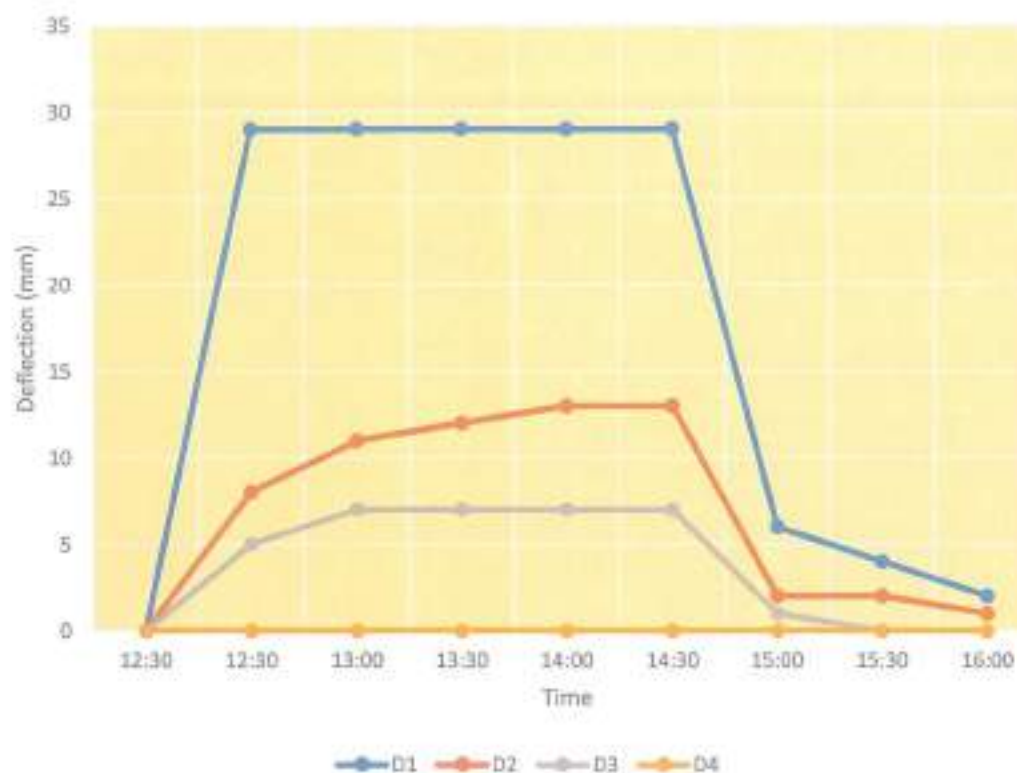

شكل رقم (٥-٥): التغير في قيم الترخيم للكمرات خلال خطوات التحميل المختلفة



[Handwritten signature]






جدول رقم (٢-٥) - نتائج قياس الإنفعال
قيم قياس الإنفعال على السطح الخرساني العلوي للكوبري أعلى الكمرات الخرسانية

Readings	Time	Temp	Strains ($\times 10^{-6}$)			
			S1	S2	S3	S4
Initial (Before loading)	12:30	23° C	0	0	0	0
Just after loading	12:30	23° C	-297	-230	-146	-119
0.5 hour after full loading	13:00	23° C	-352	-268	-180	-141
1 hour after full loading	13:30	23° C	-360	-270	-184	-149
1.5 hours after full loading	14:00	23° C	-364	-273	-190	-158
2 hours after full loading	14:30	23° C	-369	-281	-203	-161
Just after unloading	15:00	23° C	-60	-5	-17	-7
0.5 hour after unloading	15:30	23° C	-57	-4	-17	-5
1 hour after unloading	16:00	23° C	-40	-4	-15	-4

** -ve sign indicates compression strains



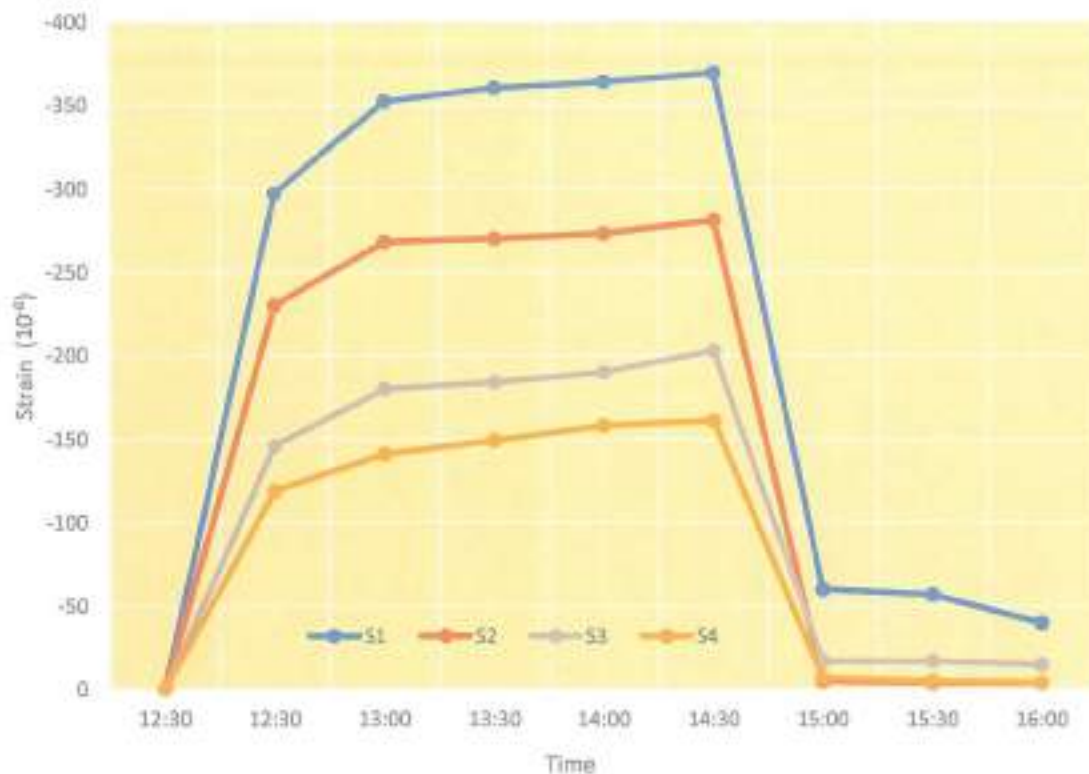

شكل رقم (٥-٦): التغير في قيم الإنفعال أعلى الكموتين خلال خطوات التحميل المختلفة



Signature: _____





٥-٥- ملخص نتائج التجربة

فيما يلي ملخصاً للقيم القصوى لكل من نتائج الترخيم والإنفعال ، والتي تم قياسها أثناء إجراء تجربة التحميل، وكذلك ملخصاً لقيم كل من نتائج الترخيم والإنفعال المتبقية بعد إزالة الحمل.

٥-٥-١ نتائج الإنفعال

- بملاحظة نتائج قياس الإنفعال على السطح الخرساني العلوي للكوبري يتبين أن أقصى قيمة للإنفعال قد حدثت عند النقطة (S1) والمبينة بالجدول رقم (٥-٢) وملخص نتائج الإنفعال كما يلي:
- أقصى انفعال أثناء التحميل $= 369 \times 10^{-6}$ (انضغاط)
- الإنفعال المتبقي بعد إزالة الحمل $= 40 \times 10^{-6}$ (انضغاط)
- نسبة الإنفعال المتبقي بعد إزالة الحمل / الإنفعال الأقصى $= 10.84\%$

٥-٥-٢ نتائج الترخيم

- بملاحظة قيم قياس الترخيم للكميرات الخرسانية يتبين أن أقصى قيمة للتخيم قد حدثت عند النقطة (D1) والمبينة بالجدول رقم (٥-١)، وكان ملخص نتائج الترخيم كما يلي:
- أقصى تخيم أثناء التحميل $= 29,00$ مم
- التخيم المتبقي بعد إزالة الحمل $= 2,00$ مم
- نسبة التخيم المتبقي بعد إزالة الحمل / التخيم الكلي $= 6.90\%$
- نسبة التخيم الكلي الى بحر الباكية (٣١,٠٥٠ متر) $= 0.093\%$
- $= 107.01$ من طول بحر الباكية

أ.م.د. محمد عبد الله
مدير مركز الأبحاث

أ.م.د. محمد عبد الله
مدير مركز الأبحاث





ملحق (أ): شهادة المعايرة لجهاز محطة الرصد

United Consultations Group (UCG)



Specialists in Land Surveying, GPS and GIS

CALIBRATION CERTIFICATE

Instrument	:	SOKKIA Electronic Total Station
Model	:	
Serial No.	:	101543
Owner	:	Surveying Unit, Ain Shams University
Date	:	12 / 7 / 2023
Date of next calibration	:	12 / 1 / 2024

The UCG Laboratory certifies that this surveying instrument has been calibrated based on leveling and measurement aspects.

Calibration Items

Item	Before Calibration	After Calibration
Circular bubble	OK	OK
Longitudinal bubble	3 divisions	OK
Index error	+7"	Zero
Horizontal circle	±04"	Zero

- The calibrated instrument can be used properly for all linear and angular measurements in single face till the next calibration date under the conditions of proper use.
- The UCG Laboratory certifies that the tested device operates within the limits of factory accuracy.

Calibrated by: Eng. Mohammed Sardeena
Checked by : Eng. Adel A. Saber

Approved by UCG
Prof. Dr. Eng. Tamer F. Sorour


Dr. Tamer Sorour

296 Omar Ibn Elkhatab St, Giza Elshez, Cairo Egypt
(+0111) 1070983 (+0122) 3522747










ملحق (ب): شهادة اختبار مقاييس الإنفعال

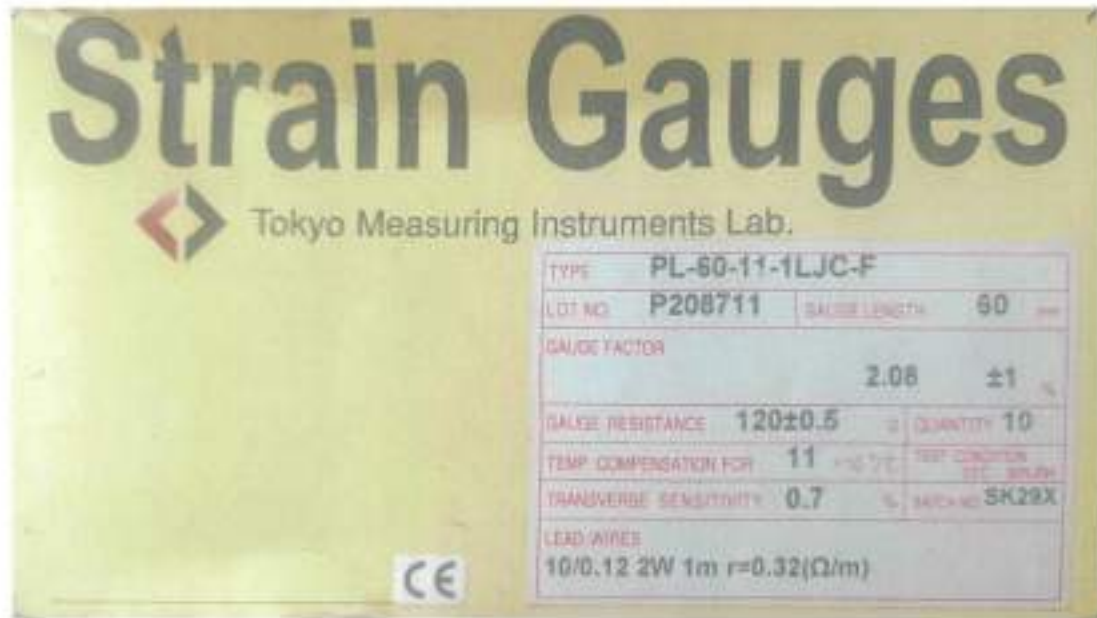

مختبر أبحاث الخرسانة المسلحة
جامعة عين شمس
الهندسة المدنية

أ.م.د. محمد عبد الله
أ.م.د. محمد عبد الله





STRAIN GAUGE TEST DATA

GAUGE TYPE: FL-60-11

LOT NO: P208711

GAUGE FACTOR: 2.08 $\pm 1\%$

ADHESIVE: P-2

TESTED ON: SS-400

COEFFICIENT OF THERMAL EXPANSION: 11.8 $\times 10^{-6}/^{\circ}\text{C}$


TEMPERATURE COEFFICIENT OF G.F.: $+0.05 \pm 0.05 \%/^{\circ}\text{C}$

DATA NO.: CB0012

THERMAL OUTPUT (e.g. mm) APPARENT STRAIN

$\epsilon_{app} = -2.90 \times 10^{-4} + 3.11 \times 10^{-4} T + 4.10 \times 10^{-6} T^2 + 4.10 \times 10^{-6} T^3 - 1.04 \times 10^{-9} T^4$ ($\mu\text{m}/\text{m}$)

TOLERANCE: ± 0.05 ($\mu\text{m}/\text{m}/^{\circ}\text{C}$) 1 TEMPERATURE

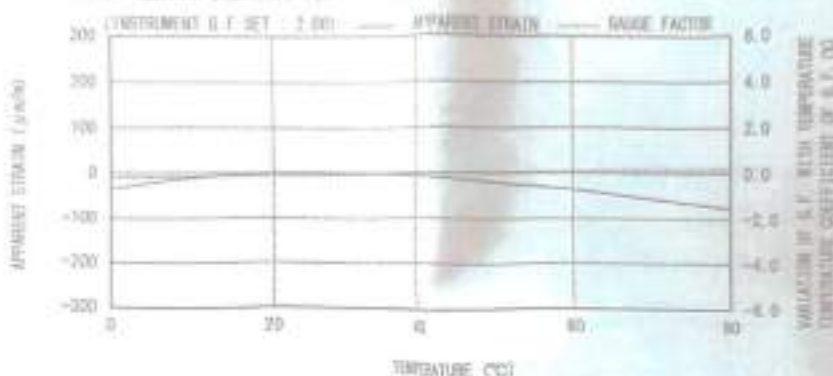

ひずみゲージ取扱いの注意事項

- 上記の特性データは、リード線の取付けによる影響を考慮してありません。表面取付のリード線の製造誤差の影響を受けて修正してください。
- ひずみゲージの使用温度は、接着剤の耐熱温度などにより異なります。
- 絶縁抵抗などの点検は、所定電圧300V以下にて行ってください。
- ゲージリードに無理な力を加えないでください。
- ひずみゲージの表面に接着剤を塗布して接着してください。
- ひずみゲージの表面は絶縁処理してありますので、油などにより汚染しないでください。
- ゲージの包装と開封後は、乾燥した場所で保管してください。
- ご使用に際して、ご不明な点などがございましたら、本誌までお問い合わせください。

株式会社東京測器研究所

〒140-8560 東京都品川区南大井4-1-2
TEL: 03-3783-5611
URL: <http://www.tml.jp>

CAUTIONS ON HANDLING STRAIN GAUGES

- The above characteristic data do not include influence due to lead wires. Correct the data in accordance with the influence of lead wires on measured values measured instead.
- The service temperature of strain gauge depends on the operating temperature of adhesives etc.
- Check of insulating resistance etc. should be made at a voltage of less than 300V.
- Do not apply an excessive force to the gauge leads.
- Apply an adhesive to the back of a strain gauge and stick the gauge to a specimen.
- As the back of strain gauge has been degreased and washed, do not contaminate it.
- After unpacking, store strain gauges in a dry place.
- If you have any questions, please feel free to contact us or your local agents.

Tokyo Measuring Instruments Laboratory Co., Ltd.

5-2, Minami-Chu 1-chome, Minagawa-Ku,
Tokyo 145-8560, JAPAN

TEL: 03-3783-5611



Tokyo Measuring Instruments Lab.

MADE IN JAPAN
日本製





ひずみゲージの取扱い方法

基本的な接着手順

1. 接着剤の選択 使用する条件に合った、エポキシ樹脂系の接着剤を選びます。
 2. 表面処理 接着剤の乾燥に合わせ、表面を粗くし、120〜180番(175〜220番)のサンドペーパーで磨き、油やセメントなどで汚染して、接着剤の接着を妨げないでください。
 3. ゲージ検査 接着剤の乾燥と明瞭を確認してください。
 4. キューリング 接着剤の乾燥と明瞭を確認してください。
 5. 点検 ひずみゲージのリード線が、試験体表面の位置に正確に付いているかを確認してください。
 6. 終了 リード線はゲージ端子を保護して、はんだ付けで接続してください。
- ・必要に応じてコーティングを施してください。

リード線の測定値への影響

- リード線の温度変化による影響。
2線式回路では、温度影響はありません。
1. $R = R_0(1 + \alpha \Delta T)$ (式1)
2. $R = R_0(1 + \alpha \Delta T)$ (式2)
3. $R = R_0(1 + \alpha \Delta T)$ (式3)
4. $R = R_0(1 + \alpha \Delta T)$ (式4)
5. $R = R_0(1 + \alpha \Delta T)$ (式5)
6. $R = R_0(1 + \alpha \Delta T)$ (式6)
7. $R = R_0(1 + \alpha \Delta T)$ (式7)
8. $R = R_0(1 + \alpha \Delta T)$ (式8)
9. $R = R_0(1 + \alpha \Delta T)$ (式9)
10. $R = R_0(1 + \alpha \Delta T)$ (式10)

リード線の経路によるゲージ値の修正

- 2線式の場合
 $K_u = \frac{R}{R + r + L} \times K$ (式2)
 - 3線式の場合
 $K_u = \frac{R}{R + \frac{r + L}{2}} \times K$ (式3)
- K_u = 修正したゲージ値

HANDLING METHOD OF STRAIN GAUGES

Basic Bonding Procedures

1. Select adhesive Select an adhesive most suitable for test conditions.
2. Surface treatment Remove grease, rust, paint, etc. from the bonding surface of a specimen. Slightly polish with an abrasive paper of #120 ~ #180 (#220 ~ #320 for aluminum), wipe with acetone, etc., and mark gauge installation position.
3. Gauge installation Refer to the operation manual of adhesive.
4. Adhesive curing Refer to the operation manual of adhesive.
5. Gauge installation check Check gauge resistance and insulation resistance.
6. Lead wire attachment Solder lead wires to the strain gauges through connecting terminals. If necessary, apply waterproof coating.

リード線1m当りの往復抵抗値
Total Resistance per Meter of Lead Wires

構成(心数/径)	ポリイミド	7/0.12	7/0.16	7/0.18	10/0.12	10/0.16	10/0.18
Lead wires (Core/Diameter)	Polyimide	7/0.12	7/0.16	7/0.18	10/0.12	10/0.16	10/0.18
リード線の直径または断面積 Standard or cross-sectional area of lead wires	φ0.14mm φ0.15mm	0.009mm ²	0.016mm ²	0.025mm ²	0.011mm ²	0.020mm ²	0.025mm ²
1m当りの往復抵抗 Total resistance per meter	2.5Ω/m 1.0Ω/m	0.44Ω/m	0.24Ω/m	0.20Ω/m	0.32Ω/m	0.13Ω/m	0.27Ω/m

Influence of Lead Wires on Measured Values

- Influence of temperature variation of lead wires (2-wire system is independent of temperature.)
 $R = R_0(1 + \alpha \Delta T)$ (Equation 1)
where:
1. R = resistance of lead wire
2. R_0 = resistance of lead wire at 0°C
3. α = temperature coefficient of resistance of lead wire
4. ΔT = temperature variation
5. R = gauge factor
6. R_0 = gauge resistance

Gauge Factor Correction due to Lead Wire Attachment

- In case of 2-wire system
 $K_u = \frac{R}{R + r + L} \times K$ (Equation 2)
 - In case of 3-wire system
 $K_u = \frac{R}{R + \frac{r + L}{2}} \times K$ (Equation 3)
- where: K_u = corrected gauge factor

Tokyo Measuring Instruments Lab.

CamScanner





ملحق (ج): مواصفات جهاز مبيت قراءات الإنفعال

TML

TM-31K (S238C)

Digital Strainmeter

TC-31K

TYPE S238C



PC card flash memory
available 8~128MB
(PC Card standard Type II)

New



CSW-5A

CSW-5A-05

CE

TML

Tokyo Sokki Kenkyujo Co., Ltd.



SWITCHING BOX

Specifications

Application Measurement	TC-31K (See 3.6K or later)
See of Element	3
General Measurement	
Quartz Probe with 3 wires	TC-31K, 2.942K to 3.000K
Heat probe	2.920 to 3.000K
Fuel probe	2.970 to 3.000K
Flaming jet sensor array	3.00K
Measurement Range	Confirms to TC-31K
Service Cells Expansion (Heat probe and sensor array)	Cells total resistance of 2.920 or less
DC Voltage Measurement	
Measurement Range	Confirms to TC-31K
High-impedance	1.6K or more
Temperature Measurement	
Measurement Range	Confirms to TC-31K
PN JTD Measurement	
Measurement Range	Confirms to TC-31K
Measurement Method	3-wire method
Measurement Point No.	Fixed (CH) to (CH)
Measurement Point Indicators	Fixed JTD for each pole
Indicator	Special sealed relay
Operating Temperature & Humidity	-10°C to 50°C, 60% RH (No condensation) derated from TC-31K
Power Supply	

Dimensions	75 (H) × 41.34 × 20 (D) (mm) (printed parts)
Weight	41.7 (g)
Standard Accessories	* 1 Tool connector cable Approx. 85% Tool connector metal 5% CR-603 Swelching Hot Cement Case Operator Manual





DIGITAL STRAINMETER TC-31K



DIGITAL STRAINMETER TC-31K

TC-31K TYPE 5330C is an upgraded model adopting Flash memory card. It succeeds the originality of former model such as fundamental functions including splash proofing construction (IP-54) and easy mounting connector. In addition to strain, dc voltage, thermocouple and Pt-RTD measurements, it can be used as a digital multi-meter for measurement of resistance and insulation resistance. Interval timer with sleep function is also provided. Measurement data can be stored using PC card (PCMCIA Type II, B - 128MByte) on the market. Measured data can easily be processed and analyzed by application software such as MS-Excel. Ten units of five-channel switching box: CSW-5A can be connected at maximum (for 50 channels) as same as former model. Control and data transfer are also available by connecting personal computer using exclusive connection cable.

Design

Designed specifically for field measurement

◆ Use of Flash memory card

A Compact memory card (PCMCIA Type II) which is enough plastic PC card is equipped as a standard item. Although for its shock, memory can be used. A card having capacity of 128 (128MByte) should be used. No RAM card which is accepted by former model of TC-31K cannot be used.



◆ COMPACT AND LIGHTWEIGHT

Weighing only 850g, the weight is perfect for a portable.

◆ DURABLE

The instrument is light proof, protects the instrument with the IP-54 proof class from incidental operation environment in the field, and it is shock resistant as well. Construction materials are supported with anti shock up to long-term vibration.

◆ SUPERB PORTABILITY

Everything about the design and construction is designed to be portable in the field. Lightweight, long to go, and battery powered.

Easy to Use

Convenience at your fingertips

◆ QUICK MOUNT TERMINALS

Using terminals, terminals allow you to quickly and easily connect and disconnect different sensors - an essential feature for measurement and checking in the field.



The optional terminal input cable can be used to connect the TC-31K to a PC. The terminal input cable is a standard 15-pin D-sub connector. The terminal input cable is a standard 15-pin D-sub connector. The terminal input cable is a standard 15-pin D-sub connector.

◆ EASY TO READ DISPLAY

◆ Liquid crystal display with backlight

The display screen shows not only the measurement data, but also the measurement unit, the measurement range, the measurement mode, the measurement status, and the measurement error. The display screen is a liquid crystal display with a backlight. The display screen is a liquid crystal display with a backlight.



◆ LONG BATTERIES

The battery is a 6V 100Ah lead-acid battery. The battery is a 6V 100Ah lead-acid battery. The battery is a 6V 100Ah lead-acid battery. The battery is a 6V 100Ah lead-acid battery.

◆ Automatic power off

The instrument automatically powers off after about 10 minutes of inactivity to save battery power.





القائم بالعمل:

م. أسامة علوان ياسر برك

مراجعة:

د. رهام التحيوي

القائم بأعمال مدير معمل أبحاث الخرسانة المسلحة:

أ.د. أيمن حسين

يعتمد
مدير مركز الاستشارات الهندسية
أ.م.د. ياسر مجاهد

13/3/24

3
19

